S
624.25
H3b
1968

AUG 29 1969
STATE DOCUMENTS

MONTANA HIGHWAY COMMISSION

19 ·· BRIDGE CONDITION ·· 68

Montana State Library
3 0864 1006 6181 1

PREPARED BY

MONTANA STATE HIGHWAY COMMISSION
PLANNING SURVEY SECTION

IN COOPERATION WITH

U. S. DEPARTMENT OF TRANSPORTATION
FEDERAL HIGHWAY ADMINISTRATION
BUREAU OF PUBLIC ROADS

DECEMBER 31, 1968

Cover Photo: Missouri River Bridge On
I-15 North Of Wolf Creek

Digitized by the Internet Archive
in 2015

https://archive.org/details/bridgecondition1968mont

TABLE OF CONTENTS

Introduction I
Federal Aid Interstate and Primary System Map IV
Federal Aid Secondary System Map V

Bridge Condition by F.A. Routes Statewide
    Federal Aid Interstate 1
    Federal Aid Primary 35
    Federal Aid Secondary State Maintained 119
    Federal Aid Secondary 125

Bridge Condition by Construction Divisions
    Missoula Division
        Federal Aid Systems and Routes 169
        Remarks - Critical Conditions 188
        Photographs - Critical Conditions 190

    Kalispell Division
        Federal Aid Systems and Routes 193
        Remarks - Critical Conditions 203
        Photographs - Critical Conditions 205

    Butte Division
        Federal Aid Systems and Routes 207
        Remarks - Critical Conditions 231
        Photographs - Critical Conditions 235

    Bozeman Division

        Federal Aid Systems and Routes 237
        Remarks - Critical Conditions 252
        Photographs - Critical Conditions 254

Great Falls Division

Federal Aid Systems and Routes 257
Remarks - Critical Conditions 274
Photographs - Critical Conditions 279

Havre Division

Federal Aid Systems and Routes 281
Remarks - Critical Conditions 294
Photographs - Critical Conditions 298

Glendive Division

Federal Aid Systems and Routes 301
Remarks - Critical Conditions 316
Photographs - Critical Conditions 317

Wolf Point Division

Federal Aid Systems and Routes 319
Remarks - Critical Conditions 337
Photographs - Critical Conditions 342

Billings Division

Federal Aid Systems and Routes 347
Remarks - Critical Conditions 367
Photographs - Critical Conditions 374

Miles City Division

Federal Aid Systems and Routes 375
Remarks - Critical Conditions 388
Photographs - Critical Conditions 389

Lewistown Division

Federal Aid Systems and Routes 391
Remarks - Critical Conditions 411
Photographs - Critical Conditions 415

INTRODUCTION

This report indicates the condition of all major and minor structures located on the Interstate and Primary Systems. Structures on both the Present Traveled Way and the constructed sections of the Interstate System are listed.

The condition of all major structures on the approved Federal Aid Secondary System has also been indicated.

Condition ratings for each structure have been obtained from a field inspection conducted during the period from September 1968 through January 1969. Detailed photographs of particularly faulty conditions were taken during the inspection. These photographs are included in this report and the originals are on file in the Planning Survey office.

EXPLANATION OF BRIDGE CONDITION COLUMNS

Column A: Bridge Number

Federal Aid System: I= Interstate, M=State Maintained, P=Primary, S=Secondary

Federal Aid Route Number:

Section Number: Approximate mileage or milepost from beginning of route to beginning of section in miles and tenths. Interstate and Primary - between junctions. Secondary - entire route.

Location (Bridge No) Approximate mileage or milepost from beginning of route to bridge in miles and tenths.

Descriptive Letter:
A = Adjacent opening of preceding structure
P = Parallel or dual structure
R = Section direction traffic only
S = Opposite to section direction traffic only
T = Opposing traffic lane of preceding structure

Column B: Total length rounded off to even feet.

Column C: Material and Type Maximum Span

ABBREVIATION	EXPLANATION
Cont St Girder	Cantilever Steel Girder
Comb T & I Beam	Combination T & I Beam
Conc & Steel	Concrete & Steel
Conc & Timber	Concrete & Timber
Conc Sl St I Bm	Concrete Slab & Steel I Beam
Cont Conc Gir	Continuous Concrete Girder
Cont Conc Slab	Continuous Concrete Slab
Cont Conc T Beam	Continuous Concrete T Beam
Cont D St Truss	Continuous Deck Steel Truss
Cont D Pl Gir	Continuous Deck Plate Girder
Cont Pl Girder	Continuous Plate Girder
Cont Roll St Bm	Continuous Rolled Steel Beam
Cont Steel Beam	Continuous Steel Beam
Cont St Girder	Continuous Steel Girder
Cont St I Beam	Continuous Steel I Beam
Cont St Plate	Continuous Steel Plate
Cont St Truss	Continuous Steel Truss
Double Conc Box	Double Concrete Box
Pre Conc Beam	Prestressed Concrete Beam
Pre Conc Girder	Prestressed Concrete Girder
Reinf Concrete	Reinforced Concrete
Reinf Conc Gir	Reinforced Concrete Girder
Reinf Conc Slab	Reinforced Concrete Slab
Riv St Pl Girder	Riveted Steel Plate Girder
St Howe Truss	Steel Howe Truss
St Plate Girder	Steel Plate Girder
St Queen Truss	Steel Queen Truss
St Pony Truss	Steel Pony Truss
St Pratt Truss	Steel Pratt Truss
St Warren Truss	Steel Warren Truss
Thru St Truss	Through Steel Truss
T King Truss	Timber King Truss
T Pony Truss	Timber Pony Truss
T Queen Truss	Timber Queen Truss
T & St Truss	Timber & Steel Truss
T T Arch	Treated Timber Arch
T T & Conc	Treated Timber & Concrete
T T Trestle	Treated Timber Trestle
Unt Log Trestle	Untreated Log Trestle
Unt Pile Tres	Untreated Pile Trestle
Unt T & Conc	Untreated Timber & Concrete
Unt T Howe Truss	Untreated Timber Howe Truss
Unt T King Truss	Untreated Timber King Truss
Unt T Pony Truss	Untreated Timber Pony Truss
Unt T Trestle	Untreated Timber Trestle
Welded Pl Gir	Welded Plate Girder

Column D: Name of feature crossed

ABBREVIATION	EXPLANATION
CA	Canal
CH	Channel
COU	Coulee
CO RD	County Road
CR	Creek
DR	Drainage
DRY CRS	Dry Course
E	East
FK	Fork
INT	Interchange
JR INT	Junior Interchange
MID	Middle
N	North
OF	Overflow
RR	Railroad
RY	Railway
RES	Reservoir
R	River
SEP	Separation
SL	Slough

Column D: Name of feature crossed (continued)

ABBREVIATION	EXPLANATION	ABBREVIATION	EXPLANATION
IRR CA	Irrigation Canal	S	South
IRR DT	Irrigation Ditch	STK	Stockpass
JR GR SEP	Junior Grade Separation	W	West

Columns E through Z: Condition Rating -- The condition of all items pertaining to the structure are rated by the bridge inspector with the following code:

E = Excellent
G = Good
F = Fair
P = Poor
C = Critical

Column Z1: N = New R = To be removed U = Unable to inspect

Column Z2: Remarks: X = Indicates written explanation of the following:

1. Critical rated item

2. Condition that code will not indicate

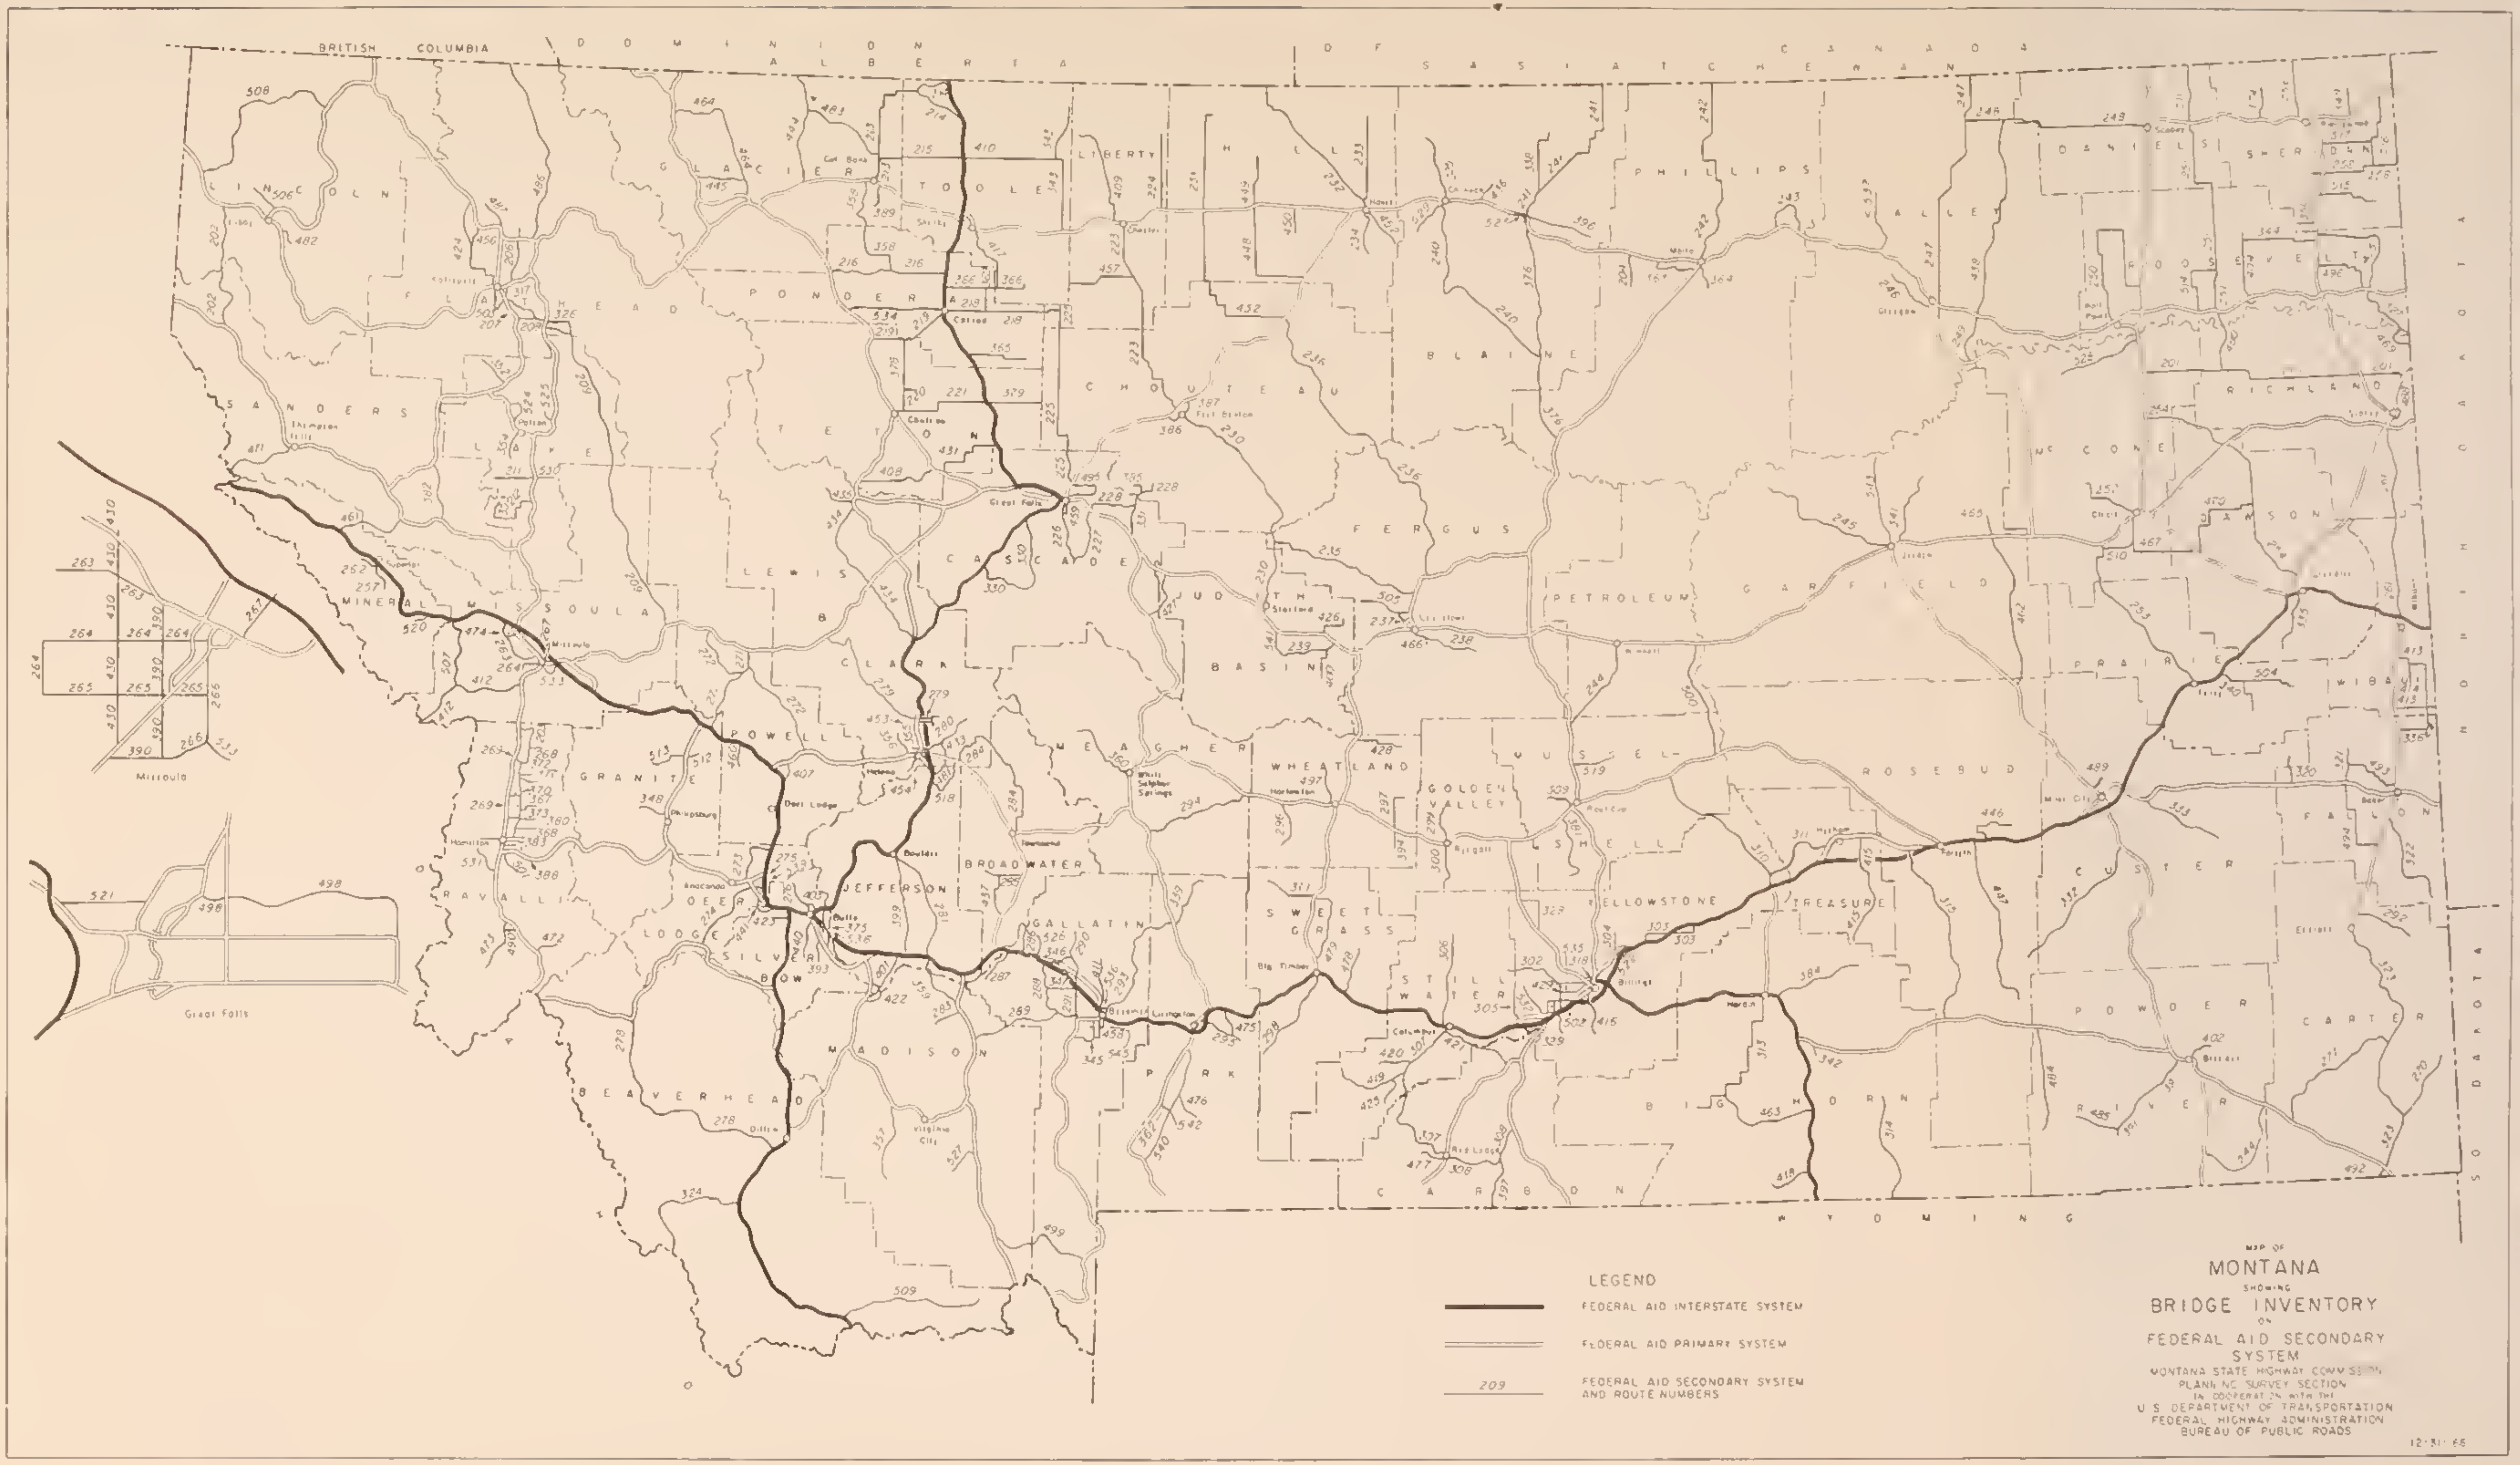

LEGEND

▬	FEDERAL AID INTERSTATE SYSTEM
═	FEDERAL AID PRIMARY SYSTEM
209	FEDERAL AID SECONDARY SYSTEM AND ROUTE NUMBERS

MAP OF
MONTANA
SHOWING
BRIDGE INVENTORY
ON
FEDERAL AID SECONDARY SYSTEM

MONTANA STATE HIGHWAY COMMISSION
PLANNING SURVEY SECTION
IN COOPERATION WITH THE
U S DEPARTMENT OF TRANSPORTATION
FEDERAL HIGHWAY ADMINISTRATION
BUREAU OF PUBLIC ROADS

12-31-66

FEDERAL AID INTERSTATE ROUTES

(CONSTRUCTED & PRESENT TRAVELED WAY)

A	FEET B	C	D	END FILL E	F	BENTS G	PIERS H	WINGWALL I	BACKWALL J	ICE BREAKERS K	L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	Q	R	CURB S	T	U	V	W	X	Y	Z	NO	REMARK 22
I 15 0000 0015	281	PRE CONC BEAM	UP RR	G		E		E	E					E			P	E	E	E	E	E	F	F	G		X
I 15 0000 0095	17	SPPAC CULVERT	JR INT CO RD	G				G																	G		
I 15 0000 0147	450	ST PLATE GIRDER	UP RR	G		G		E	E					E			P	E	E	E	E	E	G	F	G		X
I 15 0000 0151	118	PRE CONC BEAM	LIMA INT-CO RD	G		E		E	E					E			G	E	E	E	E	E	E	G	E		
I 15 0000 0198	108	PRE CONC BEAM	GOSMAN LANE-SEP	E		E		E	E					E			E	E	E	E	E	E	E	E	E		
I 15 0000 0232	22	CONCRETE SLAB	BIG SHEEP CR	G		G		G	G		G	G	G					F	G	G		P		G	G		X
I 15 0000 0310	22	CONCRETE SLAB	DRAINAGE	G		G		F	F				G						G	G	G	G			G		
I 15 0000 0383	143	PRE CONC BEAM	RED ROCK RIVER	G		E	E	E	E	E	E	E	G	E			E	E	E	E	E	E	G	G	E		
I 15 0000 0386	107	PRE CONC BEAM	SEP-CO RD	E		E		E	E					E			E	E	E	E	E	E		G	E		
I 15 0000 0443		UNDERPASS	INT-OR 324	G		E		E	E					E			P	E	E	E	E	E	G	G	E		X
I 15 0000 0448	173	PRE CONC BEAM	BEAVERHEAD RIVER	G		E	E	E	E	E	E	E	G	E			E	E	E	E	E	E	G	E	E		
I 15 0000 0458	401	WELDED PL GIR	BEAVERHEAD RIVER	G		P	E	E	E		E	G	E	G	G			G	E	E	E	E	G	E	E		X
I 15 0000 0499	163	PRE CONC BEAM	BEAVERHEAD RIVER	G		E	E	E	E	E	G	E	G	E			E	E	E	E	E	E	G	E	E		
I 15 0000 0526	188	PRE CONC BEAMS	BEAVERHEAD R	G		E	E	E	E	E	E	E	G	E			E	E	E	E	E	E		E	E		
I 15 0000 0529	163	PRE CONC BEAMS	BEAVERHEAD R	G		E	E	E	E	E	E	E	G	E			E	E	E	G	E	E		E	E		X
I 15 0000 0559	123	PRE CONC BEAMS	BARRATT INT-CO R	E		E		E	E					E			E	E	E	E	E	E		E	E		
I 15 0000 0605	140	CONT ST I BEAM	BEAVERHEAD RIVER	G		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
I 15 0000 0610	143	CONCRETE T BEAM	UP RR	G		F			G					F			F	G	G	G	G	G	G		G		X
I 15 0000 0611	77	CONCRETE T BEAM	POINDEXTER SL	F		G			G		G		G	G			G	G	G	G	G	G			G		

BRIDGE CONDITION REPORT

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I 15 0644 0655	150	CONT ST I BEAM	BEAVERHEAD R	G		G	G		G	G	G	G	F	G			G	G	G	G	G	G	G	G	G		
I 15 0644 0691	29	CONCRETE T BEAM	IRR CA	G		G		G	G		G		G	G			G	G	G	G	G	F			G		
I 15 0644 0700	66	CONCRETE T BEAM	FRY PAN CR	G		G		G	F		G	F	F	G				F	F	G	F	F			F		X
I 15 0644 0873	23B	STEEL TRUSS	BIG HOLE R	F		P	P		F	G	G	G	G		G	G	F	P	G	F	G	G	F	E	P		X
I 15 1042 1223		UNDERPASS	VICTOR INT-OR423	E		E		E	E					E			E	E	E	E	E	E	E	F	E		
I 15 1042 1223A		UNDERPASS	VICTOR INT-OR423	E		E		E	E					E			E	E		E	E	E	E	E	E		
I 15 1042 1231	614	STEEL GIRDER	3RY-CLARK FORK	G		E		E	E		G		G	E			E	E	E	E	E	E	G	G	G		
I 15 1042 1231P	599	STEEL GIRDER	3RY-CLARK FORK	G		E		E	E		G		G	E			E	E	E	E	E	E	G	G	E		
I 15 1042 1237			UNDERPASS																							N	
I 15 1042 1237A			UNDERPASS																							N	
I 15 1237 1237			UNDERPASS																							N	
I 15 1237 1237A			UNDERPASS																							N	
I 15 1237 1249	11B	PRE CONC BEAM	ROCKER INT-CO-RD																							N	
I 15 1237 1249P	118	PRE CONC BEAM	ROCKER INT-CO-RD																							N	
I 15 1237 1264	133	CONCRETE T BEAM	BA&P RY	G		G			G					G			G	G	G	G			F		G		
I 15 1237 1264P	133	CONCRETE T BEAM	BA&P RY	G		G			G					G			G	G	G	G			F		G		
I 15 1266 126BS		UNDERPASS	W BUTTE INT-I115	G		E		E	E				E			E	P	E	E	E	E	E	G	E	E		X
I 15 1266 1270	301	PRE CONC BEAM	BA&P-CMSTP&P RR	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
I 15 1266 1270P	321	PRE CONC BEAM	BA&P-CMSTP&P RR	G		E		E	E					E			E	E	E	E	E	E	G	G	E		

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Columns E thru Z
E = Excellent
G = Good
F = Fair
P = Poor
C = Critical

Column Z1
N = New
R = To be Removed
U = Unable to inspect

Column Z2
X = Written Explanation

CONTROL BRIDGE NUMBER					DESCRIPTIVE FEATURES			CONDITION RATING																							
								SUBSTRUCTURE										SUPERSTRUCTURE													
F. A. SYSTEM	F. A. ROUTE NUMBER	CONTROL-JUNCTION MILEPOST TO TENTHS	BRIDGE LOCATION-MILEPOST TO TENTHS	DESCRIPTIVE	TOTAL LENGTH FEET	MATERIAL & TYPE MAXIMUM SPAN Also Structures not carrying road by type of facility, Underpass, Tunnel, Ferry	NAME OF FEATURE CROSSED (River, Creek, Canal, Irrigation Ditch, Drainage, Railroad, Highways, Interchanges and Separations, Etc.)	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION JOINTS	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
A					B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I	15	1266	1272		442	RIVETED ST GIR	NP RY	G		E		E	E		G	G	G	E			E	E	E	E	E	E	G	G	E		
I	15	1266	1272P		489	RIVETED ST GIR	NP RY	G		E		E	E		G	G	G	E			E	E	E	E	E	E	G	G	E		
I	15	1266	1281		472	STEEL GIRDER	CMSTP&P RR-NP RY	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
I	15	1266	1281P		472	STEEL GIRDER	CMSTP&P RR-NP RY	G		E		E	E					E			E	E	E	E	E	E	G	E	E		
I	15	1266	1287		168	STEEL GIRDER	MONT S INT-US 10	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
I	15	1266	1287P		168	STEEL GIRDER	MONT S INT-US 10	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
I	15	1287	1291			UNDERPASS	LEXINGTON ST SEP	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1287	1291A			UNDERPASS	LEXINGTON ST SEP	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1287	1296			UNDERPASS	OREGON ST SEP	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1287	1296A			UNDERPASS	OREGON ST SEP																								
I	15	1287	1303		210	PRE CONC BEAM	HARRISON AVE INT	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1287	1303P		210	PRE CONC BEAM	HARRISON AVE INT	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1303	1311			UNDERPASS	SHERIDAN ST-SEP	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1303	1311A			UNDERPASS	SHERIDAN ST-SEP	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1303	1314			UNDERPASS	9MILE SEP-OR 375	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1303	1314A			UNDERPASS	9MILE SEP-OR 375	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1314	1318			UNDERPASS*	E BUTTE INT-I90	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1314	1319			UNDERPASS*	E BUTTE INT-I90	E		E		E	E					E			E	E		E	E	E	G	E	E		
I	15	1314	1323		230	STEEL GIRDER	NPRY	E		E		E	E					E			E	E		E	E	E	G	E	E		

P[illegible] [illegible]EY BRIDGE CONDITION REPORT

RATINGS

Column Z | Column Z1 | Column Z2
Good | New | X With Explanation
Fair | To be Removed |
Poor | Unable to Inspect |
Critical | |

CONTROL BRIDGE NUMBER					DESCRIPTIVE FEATURES			CONDITION RATING SUBSTRUCTURE											SUPERSTRUCTURE													
F. A. SYSTEM	F. A. ROUTE NUMBER	CONTROL JUNCTION MILEPOST TO TENTHS	BRIDGE LOCATION MILEPOST TO TENTHS	DESCRIPTIVE	TOTAL LENGTH FEET	MATERIAL & TYPE MAXIMUM SPAN Also - Structures not carrying road by type of facility, Underpass, Tunnel, Ferry	NAME OF FEATURE CROSSED (River, Creek Canal, Irrigation Ditch, Drainage, Railroad, Highways Interchanges and Separations Etc.)	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION JTS	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
A					B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I	15	1359	1447		31	STEEL I BEAM	BISON CREEK	G		F		P	G		G		G	G				P	G	G	G	F		F	F		
I	15	1359	1482		81	CONCRETE T BEAM	BISON CREEK	F		G	F	G	G		G	P	G	F			F	F	G	G	G	G			F		
I	15	1359	1484		99	CONCRETE T BEAM	BISON CREEK	G		G		F	G		G		G	G				P	G	G	G	F			G		
I	15	1359	1503		31	CONCRETE T BEAM	BISON CREEK	G		G		F	G		G		G	G				P	G	G	G	F			G		
I	15	1359	1527			UNDERPASS	GN RY	G		G	G		G					G			G		G	G	G				G		
I	15	1359	1538		43	CONCRETE T BEAM	BOULDER R	G		F		F	G		G	F	G	G				P	G	F	G	F			F		
I	15	1359	1547		22	CONCRETE SLAB	RED ROCK CR	G		G		F	G		G		G					F	G	G	G	F			G		
I	15	1359	1580		23	CONCRETE SLAB	BASIN CR	G		G		G	G		G	G	G					G	G	G	G	G		F	G		
I	15	1359	1590		79	CONCRETE T BEAM	CATARACT CR	G		F		G	G		G	G	G	G				P	G	G	F	F			F		
I	15	1359	1606			UNDERPASS	GN RY	G	F	F	G		G					G			G			G	G				G		
I	15	1359	1607		149	CONCRETE T BEAM	BOULDER R	G		F	G	F	G	G	G	G	G	G			G	P	G	F	F	F	G		F		
I	15	1359	1625		138	CONCRETE T BEAM	BOULDER R	G		G	F	F	G	G	G	G	G	G			G	P	G	F	G	F	G		F		
I	15	1359	1680		7	T T TRESTLE	STOCKPASS	G	G	G		F	G		G				G			P	F	G	G				G		
I	15	1359	1693		7	T T TRESTLE	STOCKPASS	G	G	G		F	G		G				G			P	F	G	G				G		
I	15	1359	1702		7	T T TRESTLE	STOCKPASS	G	G	G		F	G		G				G			P	F	G	G				G		
I	15	1359	1708		7	T T TRESTLE	STOCKPASS	G	G	G		F	G		G				F			P	F	G	G				G		X
I	15	1359	1717		7	T T TRESTLE	STOCKPASS	G	G	G		F	G		G				G			P	F	G	G				G		
I	15	1359	1730		7	T T TRESTLE	STOCKPASS	G	G	G		F	G		G				F			F	P	G	G				G		X
I	15	1359	1830		31	CONCRETE T BEAM	PRICKLY PEAR CR	G		G		G	G		G		G	G				G	G	G	G	F			G		

A	B	C	D	E	F	G	H	I	J	K		M	N	O	P	Q	R	S	T		V	W			Z	Z1	
	FEET																										
I 15 1359 1887	133	PRE CONC BEAM	SEP FRONT RD																							N	
I 15 1359 1887P	133	PRE CONC BEAM	SEP FRONT RD																							N	
I 15 1359 1902	231	PRE CONC BEAM	GN RY																							N	
I 15 1359 1902P	231	PRE CONC BEAM	GN RY																							N	
I 15 1359 1909		UNDERPASS	MONT CITY INT																							N	
I 15 1359 1909A		UNDERPASS	MONT CITY INT																							N	
I 15 1359 1926		UNDERPASS	SEP OR 481																							N	
I 15 1359 1926A		UNDERPASS	SEP OR 481																							N	
I 15 1359 1953		UNDERPASS*	CAPITOL INT-US12	G		E		E	E					E			F	E		E	E	E	G	G	E		
I 15 1359 1953A		UNDERPASS	CAPITOL INT-US12	G		E		E	E					E			E	E		E	E	E	E	G	G	E	
I 15 1953 1953		UNDERPASS*	CAPITOL INT-US12	G		E		E	F					E			E	E		E	E	E	E	E	G	E	
I 15 1953 1953A		UNDERPASS	CAPITOL INT-US12	G		E		E	E					E			E	E		E	E	E	E	E	G	E	
I 15 1953 1961	798	RIV PL GIRDER	GN&NP RY-AVENUE	G		E		E	E					E			E	E	G	E	E	E	E	E	G	E	
I 15 1953 1961P	810	RIV PL GIRDER	GN&NP RY-AVENUE	G		E		E	E					E			E	E	E	E	E	E	E	E	G	E	
I 15 1953 1965		UNDERPASS	CEDAR ST INT	G		E		E	E					E			P	E		E	E	E	E	E	G	E	X
I 15 1953 1965A		UNDERPASS	CEDAR ST INT	G		E		E	E					E			P	E		E	E	E	E	E	G	E	X
I 15 1953 1971		UNDERPASS	YORK SEP-OR 280	G		E		E	E					E			E	E		E	E	E	E	E	G	E	
I 15 1953 1971A		UNDERPASS	YORK SEP-OR 280	G		E		E	E					E			E	E		E	E	E	E	E	G	E	
I 15 1953 1992	50	PRE CONC BEAM	TEN MILE CREEK	G		E		E	E		G		G	E			E	E		E	E	E		G	E	E	

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS			
Columns E thru Z		Column Z1	Column Z2
E = Excellent	P = Poor	N = New	X = Written Explanation
G = Good	C = Critical	R = To be Removed	
F = Fair		U = Unable to Inspect	

CONTROL BRIDGE NUMBER					DESCRIPTIVE FEATURES			CONDITION RATING																							
								SUBSTRUCTURE										SUPERSTRUCTURE													
F. A. SYSTEM	F. A. ROUTE NUMBER	CONTROL-JUNCTION MILEPOST TO TENTHS	BRIDGE LOCATION-MILEPOST TO TENTHS	DESCRIPTIVE	TOTAL LENGTH FEET	MATERIAL & TYPE MAXIMUM SPAN - Also - Structures not carrying road by type of facility, Underpass, Tunnel, Ferry	NAME OF FEATURE CROSSED (River, Creek, Canal, Irrigation Ditch, Drainage, Railroad, Highways, Interchanges and Separations, Etc.)	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION JOINTS	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
A					B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I	15	1953	1992	T	50	PRE CONC BEAM	TEN MILE CREEK	G		E		E	E		G		G	E			E	E		E	E	E		G	E		
I	15	1953	2001		118	PRE CONC BEAM	SEP-CO RD	G		E		E	E					E			E	E		E	E	E	E	G	E		
I	15	1953	2001	P	118	PRE CONC BEAM	SEP-CO RD	E		E		E	E					E			E	E		E	E	E	F	G	E		
I	15	1953	2032			UNDERPASS*	LINCOLN INT-US 9	G		E		E	E					E			E	E		E	E	E	G	G	E		
I	15	1953	2032	A		UNDERPASS	LINCOLN INT-US 9	G		E		E	E					E			E	E		E	E	E	G	G	E		
I	15	2032	2122		118	PRE CONC BEAM	INT-CO RD	G		E		E	E					E			E	E		E	E	E	G	G	E		
I	15	2032	2122	P	118	PRE CONC BEAM	INT-CO RD	G		E		E	E					E			E	E		E	E	G	G	G	E		
I	15	2032	2196		133	PRE CONC BEAM	SIEBEN INT-CO RD	G		G		G	G					G			G	G	G	G		G	G		G		
I	15	2032	2196	P	133	PRE CONC BEAM	SIEBEN INT-CO RD	G		G		G	G					G			G	G	G	G		G	G		G		
I	15	2032	2215		519	STEEL GIRDER	LIT PRICKLY CR C	G		G		G	G		G		G	G			G	G	G	G		G	F	G	G		
I	15	2032	2215	P	519	STEEL GIRDER	LIT PRICKLY PR C	G		G		G	G		G		G	G			G	G	G	G		G	F	G	G		
I	15	2032	2223		539	PRE CONC BEAM	SPR CR INT-GN RY	G		G		G	G		G		G	G			G	G	G	G		G	F	G	G		
I	15	2032	2223	P	539	PRE CONC BEAM	SPR CR INT-GN RY	G		G		G	G		G		G	G			G	G	G	G		G	F	G	G		
I	15	2032	2236		133	PRE CONC BEAM	LYONS CR SEP	G		G		G	G		G		G	G			G	G	G	G		G		G	G		
I	15	2032	2236	P	133	PRE CONC BEAM	LYONS CR SEP	G		G		G	G		G		G	G			G	G	G	G		G		G	G		
I	15	2032	2298		113	PRE CONC BEAM	WOLF CR INT	G		G		G	G					G			G	G	G	G		G		G	G		
I	15	2032	2298	T	113	PRE CONC BEAM	WOLF CR INT	G		G		G	G					G			G	G	G	G		G		G	G		
I	15	2032	2317			UNDERPASS*	AUGUSTA INT	G		G		G	G					G			G			G		G		G	G		
I	15	2032	2317	A		UNDERPASS*	AUGUSTA INT	G		G		G	G					G			G			G		G		G	G		

PLANNING SURVEY [illegible]

A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z		Z
I	15	2317	2374	123	PRE CONC BEAM	CRAIG INT-CO RD	G		G		G	G					G			G	G		G		G		G	G		
I	15	2317	2374P	123	PRE CONC BEAM	CRAIG INT-CO RD	G		G		G	G					G			G	G		G		G		G	G		
I	15	2317	2391	365	PRE CONC BEAM	GN RY	G		G		G	G					G			G	G	G	G		G	G	G	G		
I	15	2317	2391T	365	PRE CONC BEAM	GN RY	G		G		G	G					G			G	G	G	G		G	G	G	G		
I	15	2317	2394	770	WELDED PL GIR	MISSOURI R	G		G		G	G	G		G	G	G	G		G	G		G	G	G	G	G	G		
I	15	2317	2394T	770	WELDED PL GIR	MISSOURI R	G		G		G	G	G		G	G	G	G		G	G		G	G	G	G	G	G		
I	15	2317	2400	60	CAST CONC GIR	STICKNEY CR																							N	
I	15	2317	2400T	60	CAST CONC GIR	STICKNEY CR																							N	
I	15	2317	2484			UNDERPASS																							N	
I	15	2317	2484T			UNDERPASS																							N	
I	15	2317	2519	154	WELDED PL GIR	MISSOURI R																							N	
I	15	2317	2519T	154	WELDED PL GIR	MISSOURI R																							N	
I	15	2317	2527	62	PRE CONC BEAM	HARDY CR																							N	
I	15	2317	2527T	62	PRE CONC BEAM	HARDY CR																							N	
I	15	2317	2537	133	PRE CONC BEAM	INT-CO RD	P		G		G	G					G			G	G		G		G	F	F	G		X
I	15	2317	2554	82	PRE CONC BEAM	SEP-CO RD	G		G		E	E					E			G	G		G		G	G	G	G		
I	15	2317	2589	138	PRE CONC BEAM	S CASCADE INT	P		G		G	G					G			G	G		G		G	G	G	G		
I	15	2599	2614	123	PRE CONC BEAM	N CASCADE INT	F		G		G	G					G			G	G		G		G	G	G	G		
I	15	2614	2688	100	CONT CONC T BM	LITTLE MUDDY CR	P		G		G	G			F		G			G	G	G	G		G		P	G		X

A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
				FEET				PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS								REMARKS
I	15	2614	2688P	100	CONT CONC T 8M	LITTLE MUDDY CR	P		G		G	G			F		G			G	G	G	G		G		P	G		
I	15	2614	2754	130	CONT CONC T 8M	ULM INT	F		G		G	G					G			G	G		G		G		P	G		
I	15	2614	2827		UNDERPASS	GORE HILL INT	G		G		G	G					G			G	G	G	G		G			G		
I	15	2614	2827A		UNDERPASS	GORE HILL INT	G		G		G	G					G			G	G	G	G		G			G		
I	15	2614	2839		UNDERPASS*	SPUR INT-I 315	G		G		G	G					G			G			G		G	G	G	G		
I	15	2614	2839A		UNDERPASS*	SPUR INT-I 315	G		G		G	G					G			G			G		G	G	G	G		
I	15	2839	2842		UNDERPASS	CO RD SEP	G		G		G	G					G			G			G		G	G	G	G		
I	15	2839	2842A		UNDERPASS	CO RD SEP	G		G		G	G					G			G			G		G	G	G	G		
I	15	2839	2849	483	PRE CONC 8M	SUN R	G		G	G	G	G	G	G	G	G	G			G	G		G		G	G	G	G		
I	15	2839	2849P	483	PRE CONC 8M	SUN R	G		G	G	G	G	G	G	G	G	G			G	G		G		G	G	G	G		
I	15	2839	2850	123	PRE CONC 8M	5TH AVE SEP	G		G		G	G						G		G	G		G		G	G	G	G		
I	15	2839	2850P	123	PRE CONC 8M	5TH AVE SEP	G		G		G	G						G		G	G		G		G	G	G	G		
I	15	2839	2855		UNDERPASS	CENTRAL AVE INT	G		G		G	G					G			G			G		G			G		
I	15	2839	2855A		UNDERPASS	CENTRAL AVE INT	G		G		G	G					G			G			G		G			G		
I	15	2839	2869		UNDERPASS	34TH ST SEP	G		G		G	G					G			G			G		G			G		
I	15	2839	2869A		UNDERPASS	34TH ST SEP	G		G		G	G					G			G			G		G			G		
I	15	2839	2874	354	PRE CONC 8M	EMERSON INT-GNRY	G		G		G	G					G			G	G		G		G	G	G	G		
I	15	2839	2874P	359	PRE CONC 8M	EMERSON INT-GNRY	G		G		G	G					G			G	G		G		G	G	G	G		
I	15	2874	2900	17	CONCRETE SLA8	JR GR SEP	G				G	G									G		G		G		G	G		

A				B FEET	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I	15	2874	2900P	17	CONCRETE SLAB	JR GR SEP	G				G	G									G		G		G		G	G		
I	15	2874	2913	108	PRE CONC BEAM	INT-CO RD	G		G		G	G					G			G	G		G		G	G	G	G		
I	15	2874	2913P	108	PRE CONC BEAM	INT-CO RD	G		G		G	G					G			G	G		G		G	G	G	G		
I	15	2874	2941	17	CONCRETE SLAB	JR GR SEP	G				F	G									G		G				G	G		X
I	15	2874	2941P	17	CONCRETE SLAB	JR GR SEP	G				F	G									G		G				G	G		
I	15	2874	2954		UNDERPASS*	VAUGHN INT-US 89	G		G		G	G						G		G			G				G	G		
I	15	2874	2954A		UNDERPASS	VAUGHN INT-US 89	G		G		G	G						G		G			G				G	G		
I	15	2954	3231	346	PRE CONC BEAM	TETON R	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G		
I	15	2954	3326		UNDERPASS	BRADY INT-OR 365	G		G	G	G	G					G			G			G				G	G		
I	15	2954	3339		UNDERPASS	SEP-CO RD	G		G		G	G					G			G			G				G	G		
I	15	2954	3420	25	CONCRETE T BEAM	IRR CA	F		F			F					G						F		F			F		
I	15	2954	3469	113	CONCRETE T BEAM	DRY FK MARIAS R	F		G	F	F	F	F	G	F	F	G				F	G	G	G	F		P	F		X
I	15	2954	3524	64	CONCRETE T BEAM	IRR CA	F	F	G		G	G		G		G	G				G	G	G	G	F			G		
I	15	2954	3627	541	CONT ST PLATE	MARIAS R	F		G	F		G	F	F	F	G	G	G		G	G	F	F	G	F	G	F	F		X
I	15	2954	3690	360	STEEL BEAMS	INT US2 & GN RY	E		E		E	E					E			E	E		E	E	E	E	G	E		
I	15	2954	3690P	360	STEEL BEAMS	INT US2 & GN RY	E		E		E	E					E			E	E		E	E	E	E	G	E		
I	15	3690	3703		UNDERPASS*	N SHELBY INT	G		E		E	E					E			E	E	G	E	E	E	G	G	E		
I	15	3690	3703A		UNDERPASS	N SHELBY INT	G		E		E	E					E			E	E	G	E	E	E	G	G	E		
I	15	3703	3748		UNDERPASS	INT-CO RD	G		E		E	E					E			E	E	G	E	E	E		E	E		

A				B TOTAL LENGTH FEET	C MAX MUM SPAN	D	E END FILLS	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TRUSS	R SHOES	S CURBS	T MARKERS	U DECK	V BRACING	W RAILING	X EXPANSION	Y PAINT	Z GENERAL CONDITION	Z1 NOT INSPECTED	Z2 REMARKS
I	15	3703	3858	118	PRE CONC BEAM	KEVIN INT-OR 215	G		E		E	E					E			E	E	G	E	E	E		E	E		
I	15	3703	3954	168	PRE CONC BEAM	SUNBURST INT	F		E		E	E					E			E	E	G	E	E	E	P	G	E		
I	15	3703	3957	313	STEEL GIRDER	GN RY	G		G		G	G					G	G		G	G	G	G		G	G	G	G		
I	15	3703	4035		UNDERPASS	SWEETGRASS INT	E		E		E	E					E			E	E	G	E	E	E	F	G	E		
I	15	3703	4035A		UNDERPASS	SWEETGRASS INT	E		E		E	E					E			E	E	G	E	E	E	F	G	E		
I1	15	4038	4040R	244	STEEL GIRDER	W BUTTE INT-I 90	G		E		E	E				E			E	P	E	E	E	E	E	G	E	E		X
I1	15	4038	4047	12	CONCRETE BOX	JR GR SEP-TR RD	G		G		G	E		G		G					G	G	G	G				G		
I1	15	4038	4047P	12	CONCRETE BOX	JR GR SEP-TR RD	G		G		G	G		G		G					G	G	G	G				G		
I1	15	4038	4050	156	CONCRETE T BEAM	EXCELSIOR ST SEP	G		G			G					G				G	G	G	G	G		F	G		
I1	15	4038	4050T	156	CONCRETE T BEAM	EXCELSIOR ST SEP	G		G			G					G				G	G	G	G	G		F	G		
I3	15	4050	4055P	206	STEEL BM	GN RY	G		G		G	G					G			G	G	G	G		G	G	G	G		
I3	15	4050	4050	296	PRE CONC BM	SPUR INT- I 15	G		G		G	G					G			G	G		G		G	G	G	G		
I3	15	4050	4050T	296	PRE CONC BM	SPUR INT- I 15	G		G		G	G					G			G	G		G		G	G	G	G		
I3	15	4050	4053	148	PRE CONC BM	BRIDGE ST SEP	G		G		G	G					G			G	G	G	G		G	G	G	G		
I3	15	4050	4053P	148	PRE CONC BM	BRIDGE ST SEP	G		G		G	G					G			G	G	G	G		G	G	G	G		
I3	15	4050	4055	174	CONT ST GIR	GN RY	G		G		G	G					G			G	G	G	G		G	G	G	G		

PLANNING SURVEY BRIDGE [illegible] REPORT

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	7	Z
I 90 0000 0024	42	STEEL GIRDER	ST REGIS R	G		G		G	G		G	G	G	G	G		G	G	F	G		G	G		G		
I 90 0000 0068	23	STEEL I BEAM	RANDOLPH CR	G		G		G	G		G	G	G	G	G			G	F	G		P	G		G		
I 90 0000 0082	100	CANT ST GIRDER	ST REGIS R	G		G	G		G		G	G	G	G			G	P	G	G		F		P	F		
I 90 0000 0109	100	CANT ST GIRDER	ST REGIS R	G		G	G		G		G	F	G	G			G	P	P	G		G		P	G		
I 90 0000 0224	42	CONCRETE T BEAM	TWELVE MILE CR	G		G		G	G		G	G	G	G				G	G	G	G	G		F	G		
I 90 0000 0343	190	CONT ST GIRDER	ST REGIS R	G		G	G		N		G	P	G	G			G	P	F	G		F	F	F	F		
I 90 0000 0346	787	STEEL TRUSS	CLARK FK & NP RY	G		G	G		G	G	G		G	G	G	G	G	G	G	G		G	P	P	G		
I 90 0000 0391	482	ST PLATE GIRDER	CMSTP&P RR	G		G			G				G	G			G	G	G	G		F	F	P	G		
I 90 0000 0456	621	RIV PL GIRDER	CLARK FK	G		G	G		G		G		G	G	G		G	G	G	G	G	G	G	F	E		
I 90 0000 0466	17	CONCRETE SLAB	JR GR SEP-CO RD	G		G		G	G									G		G		G		G	E		
I 90 0000 0479	153	PRE CONC BEAM	SUPERIOR INT	G		G		G	G					G			E	E	G	E	E	E	G	P	E		
I 90 0000 0479P	153	PRE CONC BEAM	SUPERIOR INT	G		G		G	G					G			E	E	G	E	E	E	G	P	E		
I 90 0000 0495	168	PRE CONC BEAM	CEDAR CR	G		E		E	E		E	E	E	E			E	E		E	E	E	E	G	E		
I 90 0000 0495P	168	PRE CONC BEAM	CEDAR CR	G		E		E	E		E	E	E	E			E		E	E	E	E	E	G	E		
I 90 0000 0498	801	WELDED PL GIR	CLARK FK	G		E	E	E	E	E	E	E	E	E	E		E	E	E	E	E	E	G	F	E		
I 90 0000 0498P	801	RIV PL GIRDER	CLARK FK	G		E	E	E	E	E	E	P	E	E	E		E	E	E	E	E	E	E	G	E		
I 90 0000 0542	757	WELDED PL GIR	CLARK FORK	G		E	E	E	E	E	E	E	E	E	E		E	E	E	E	E	E	E	E	E		
I 90 0000 0542P	757	WELDED PL GIR	CLARK FORK	G		E	E	E	E	E	E	E	E	E	E		E	E	E	E	E	E	E	E	E		
I 90 0000 0545		UNDERPASS	NP RY	E		E	E	E	E						E		E	E	P	E	E	E		E	E		

A	B TOTAL LENGTH FEET	C	D	E	F PILES	G BENTS	H PIERS	I WINGWALLS	J	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P	Q	R SHOES	S CURBS	T	U	V	W	X	Y	Z	Z1	Z2
I 90 0000 0545A		UNOERPASS	NP RY	E		E	E	E	E						E		E	E	P	E	E	E		E	E		
I 90 0000 0559	128	PRE CONC BM	LOZEAU INT-CO RO	G		E		E						E			E	E		E		E	E	G	E		
I 90 0000 0559P	128	PRE CONC BM	LOZEAU INT-CO RO	G		E		E						E			E	E		E		E	E	G	E		
I 90 0000 0579	296	PRE CONC 8M	NP RY	F		E	E	E	E					E			E	E		E		E	E	G	E		
I 90 0000 0579P	296	PRE CONC 8M	NP RY	F		E	E	E	E					E			E	E		E		E	E	G	E		
I 90 0000 0590	826	WELOEO PL GIR	CLARK FORK	E		E	E	E	E	E	E	E	E		E		E	E	E	E	E	E	E	E	E		
I 90 0000 0590P	826	WELOEO PL GIR	CLARK FORK	E		E	E	E	E	E	E	E	E		E		E	E	E	E	E	E	E	E	E		
I 90 0000 0592		UNOERPASS	CMSTP&P RR	E		E	E	E	E						E		E		P	E	E		G	E	E		
I 90 0000 0592A		UNOERPASS	CMST P&P RR	E		E	E	E	E						E		E		P	E	E		G	E	E		
I 90 0000 0603	17	CONCRETE SLAB	JRGR SEP-CO RO	E		E		E	F									E		E		E		G	E		
I 90 0000 0603S	17	CONCRETE SLA8	JR GR SEP-CO RO	E		E		E	F									E		E		E		P	E		
I 90 0000 0620	128	PRE CONC BEAM	TARKIO INT-CO RO	E		E		E	E						E		E	E	E	E		E	G	P	E		
I 90 0000 0620P	128	PRE CONC 8EAM	TARKIO INT-CO RO	E		E		E	E						E		E	E	E	E		E	G	P	E		
I 90 0000 0663	445	STEEL GIROER	CMST P&P RR-CO R	E		E		E	E						E		E	E		E		E	G	F	E		
I 90 0000 0669	807	WELOEO PL GIR	CLARK FORK	E		E	E	E	E	E	E	E	E	E	E		E	E		E		E	E	G	E		
I 90 0000 0671	338	STEEL GIROER	NP RY	E		E	E	E	E					E	E		E	E		E		E	E	G	E		
I 90 0000 0675		UNOERPASS	FISH INT-OR 520	E		E	E	E	E						E		E	E	E	E		E	E	E	E		
I 90 0000 0708	190	PRE CONC 8EAM	NP RY	F		E	E	E	E						E		E	E		E		E	E	E	E		X
I 90 0000 0710	762	CONT PL GIROER	CYR INT & CLARK	E		E	E	E	E	E	E	E	E	E	E		E	E		E		E	E	E	E		

PLANNING [illegible] BRIDGE CONDITION [illegible]

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O		O	R	S	T	U		W		Y	Z	Z1	Z2
	FT																										
I 90 0000 0760		UNDERPASS	ALBERTON INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I 90 0000 0760A		UNDERPASS	ALBERTON INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I 90 0000 0784	128	PRE CONC BEAM	SEP-OR507	E		E	E	E	E					E			E		E	E	E	E	E	P	E		
I 90 0000 0802	17	CONCRETE SLAB	JR GR SEP-CO RD	E		E		F	E									E		E		E		F	E		
I 90 0000 0812	879	WELDED PL GIR	CLARK FORK	E		E	E	E	E	E	E	E	E	E	E		E	E	G	E	E	E	G	G	E		
I 90 0000 0827	982	WELDED PL GIR	CLARK FK & RR	E		E	E	E	E	E	E	E	E	E	E		E	E	G	E	E	E	E	G	E		
I 90 0000 0827	982	WELDED PL GIR	CLARK FK & RR	E		E	E	E	E	E	E	E	E	E	E		E	E	G	E	E	E	E	G	E		
I 90 0000 0835	123	PRE CONC BEAM	9 MILE INT-CO RD	E		E	E	E	E						E		E	E		E		E		F	E		
I 90 0000 0835P	123	PRE CONC BEAM	9 MILE INT-CO RD	E		E	E	E	E						E		E	E		E		E		F	E		
I 90 0000 0970		UNDERPASS*	DESMET INT-10A	E		E	E	E	E						E		E	E	E	E		E	E	E	E		
I 90 0000 0970A		UNDERPASS*	DESMET INT-10A	E		E	E	E	E						E		E	E	E	E		E	E	E	E		
I 90 0970 0987	163	PRE CONC BEAM	NPRY	E		E	E	E	E						E		E	E		E		E		E	E		
I 90 0970 0987P	163	PRE CONC BEAM	NPRY	E		E	E	E	E						E		E	E		E		E		E	E		
I 90 0970 0991	138	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E						E		E	E		E		E		E	E		
I 90 0970 0991P	138	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E						E		E	E		E		E		E	E		
I 90 0970 1023	195	PRE CONC BEAM	RESERVE ST-INT	E		E	E	E	E			E	E		E		E	E		E		E		E	E		
I 90 0970 1023P	195	PRE CONC BEAM	RESERVE ST-INT	E		E	E	E	E			E	E		E		E	E		E		E		E	E		
I 90 0970 1037	138	PRE CONC BEAM	SEP-CO RD	G		E	E	E	E					E			E	E		E		E		G	E		
I 90 0970 1037P	138	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E			E	E		E		E		G	E		

A				B FEET TOTAL LENGTH	C DESC	D	E END FILLS	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TR	R	S	T	U	V	W	X	Y	Z	21	22
I	90	0970	1054	179	PRE CONC BEAM	ORANGE ST INT	E		E	E	E	E					E			E	E		E		E		E	E		
I	90	0970	1054T	179	PRE CONC BEAM	ORANGE ST INT	E		E	E	E	E					E			E	E		E		E		E	E		
I	90	1054	1061	245	PRE CONC BEAM	RATTLESNAKE CR	E		E	E	E	E		E	E	E	E			E	E		E		E	E	E	E		
I	90	1054	1061T	245	PRE CONC BEAM	RATTLESNAKE CR	E		E	E	E	E		E	E	E	E			E	E		E		E	E	E	E		
I	90	1054	1063	165	PRE CONC BEAM	VAN BUREN ST INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I	90	1054	1063T	165	PRE CONC BEAM	VAN BUREN ST INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I	90	1054	1079	194	PRE CONC BEAM	E MISSOULA INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I	90	1054	1079T	194	PRE CONC BEAM	E MISSOULA INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I	90	1079	1089	455	ST PLATE GIRDER	CLARK FORK	E		E	E	E	E	G	E	E	E	E			E	E		E	E	E	G	E	E		
I	90	1079	1089P	455	ST PLATE GIRDER	CLARK FORK	E		E	E	E	E	E	E	E	E	E			E	E		E	E	E	E	E	E		
I	90	1079	1099	143	PRE CONC BEAM	SEP--OR 533	E		E	E	E	E					E			E			E		E		E	E		
I	90	1079	1099P	143	PRE CONC BEAM	SEP--OR 533	E		E	E	E	E					E			E			E		E		E	E		
I	90	1079	1100	409	ST PLATE GIRDER	CLARK FORK-SEP	G		E	E	E	E	E	E	G	E	E			E	E		E	E	E	E	E	E		
I	90	1079	1100P	399	ST PLATE GIRDER	CLARK FORK--SEP	G		E	E	E	E	E	E	G	E	E			E	E		E	E	E	G		E		
I	90	1079	1108		UNDERPASS	BONNER INT-APPR	E		E	E	E	E					E			E	E		E		E	E	E	E		
I	90	1079	1108A		UNDERPASS	BONNER INT--APPR	E		E	E	E	E					E			E	E		E		E	E	E	E		
I	90	1079	1111	342	STEEL GIRDER	NP RY	E		E	E	E	E					E			E	E		E		E	E	F	E		
I	90	1079	1111P	342	STEEL GIRDER	NP RY	E		E	E	E	E					E			E	E		E		E	P	F	E		
I	90	1079	1113	343	WELDED PL GIR	BLACKFOOT R	E		E	E	E	E	E	E	E	E	E			E	E		G	E	E	E	G	E		

A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S					W	X			Z	Z
I	90	1079	1113P	343	WELDED PL GIR	BLACKFOOT R	E		E	E	E	E	E	E	E	E	E			E	E		G	E	E	E	G	E		
I	90	1079	1120	153	PRE CONC BEAM	CMSTP&P RR	E		E	E	E	E					E			E			G		E		E	E		
I	90	1079	1120P	153	PRE CONC BEAM	CMSTP&P RR	E		E	E	E	E					E			E			G		E		E	E		
I	90	1079	1127	118	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E			E			E		E		G	E		
I	90	1079	1127P	118	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E			E			E		E		G	E		
I	90	1079	1150	118	PRE CONC BEAM	TURAH INT	E		E	E	E	E					E			E			E		E		G	E		
I	90	1079	1150P	118	PRE CONC BEAM	TURAH INT-US 10	E		E	E	E	E					E			E			E		E		G	E		
I	90	1150	1181	128	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E			E			E		E		G	E		
I	90	1150	1181P	128	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E			E			E		E		G	E		
I	90	1150	1197	351	STEEL GIRDER	NP RY	E	E	E	E	E	E					E			E			E		E		E	E		
I	90	1150	1197P	355	STEEL GIRDER	NP RY	E		E	E	E	E					E			E			E		E		E	E		
I	90	1150	1555	123	PRE CONC BEAM	W DRUMMOND INT	E		E	E	E	E					E			E	E		G	E	E	E	G	G		
I	90	1150	1555T	123	PRE CONC BEAM	W DRUMMOND INT	E		E	E	E	E					E			E	E		G	E	E		G	G		
I	90	1555	1559	128	PRE CONC BEAM	MAIN ST SEP	E		E	E	E	E				E	E		E	E	E		E	E	E		G	E		
I	90	1555	1559T	128	PRE CONC BEAM	MAIN ST SEP	E		E	E	E	E				E	E		E	E	E		E	E	E		G	E		
I	90	1555	1564	133	PRE CONC BEAM	E DRUMMOND INT	F		E	E	G	E				E	E		E	E	E		E	E	E		G	E		
I	90	1555	1564P	133	PRE CONC BEAM	E DRUMMOND INT	F		E	E	G	E				E	E		E	E	E		E	E	E		G	E		
I	90	1564	1579	128	PRE CONC BEAM	SEP-OR 271	F		E	E	G	E									E		E	E	E		G	E		
I	90	1564	1579P	128	PRE CONC BEAM	SEP-OR 271	F		E	E	G	E									E		E	E	E		G	E		

		A		B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z22
				FEET			END F[illegible]S	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	[illegible]	[illegible]	[illegible]SHOES	CURB	MARKER	DECK	[illegible]	RA[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	REMARK
I	90	1564	1591	17	CONCRETE SLAB	JR GR SEP-CO RO	E		E	E	E	E									E		E	E	E		G	E		
I	90	1564	1591P	17	CONCRETE SLAB	JR GR SEP-CO RO	E		E	E	E	E									E		E	E	E		G	E		
I	90	1564	1609	17	CONCRETE SLAB	JR GR SEP-CO RD	E		E	E	E	E									E		E	E	E		G	E		
I	90	1564	1609P	17	CONCRETE SLAB	JR GR SEP-CO RO	E		E	E	E	E									E		E	E	E		G	E		
I	90	1564	1625	17	CONCRETE SLAB	JR GR SEP-CO RO	G		E		E	G									E		E		E		G	E		
I	90	1564	1625P	17	CONCRETE SLAB	JR GR SEP-CO RO	G		E		E	G									E		E		E		G	E		
I	90	1564	1631	17	CONCRETE SLAB	JR GR SEP-CO RO	G		E		E										E		E		E		G	E		
I	90	1564	1631P	17	CONCRETE SLAB	JR GR SEP-CO RO	G		E		E										E		E		E		G	E		
I	90	1564	1639	113	PRE CONC BEAM	JENS INT-CO RO	G		E		E	E					E			E	E		E		E	G	G	E		
I	90	1564	1639P	113	PRE CONC BEAM	JENS INT-CO RO	G		E		E	E					E			E	E		E		E	G	G	E		
I	90	1564	1671	17	CONCRETE SLAB	JR GR SEP	G		E		E										E		E		E		G	E		
I	90	1564	1671P	17	CONCRETE SLAB	JR GR SEP	G		E		E										E		E		E		G	E		
I	90	1564	1679	153	PRE CONC BEAM	GOLO C INT-OR460	G		E		E	E					E			E	E	G	E		E	G	G	E		
I	90	1564	1679P	153	PRE CONC BEAM	GOLO C INT-OR460	G		E		E	E					E			E	E	G	E		E	G	G	E		
I	90	1765	1767	204	CONT ROLL BM	NP RY	F		G		G	G					G			G	G	G	G	G	G	F	F	G		X
I	90	1765	1771	141	CONT T BEAM	LIT BLACKFOOT R	G		G	G		G	G	G	F	G	G			G	G	G	G	G	G	G	F	G		
I	90	1765	1821	20	CONCRETE SLAB	JR GR SEP-CO RO	G		G		G	E									E		E	G	E		G	E		X
I	90	1765	1850	20	CONCRETE SLAB	JR GR SEP-CO RO	G		E		E	E									E		E	E	E		G	E		
I	90	1765	1865	123	PRE CONC BEAM	N O-L INT-US 10	G		E		E	E					E			E	E		E	E	E	G	G	E		

PLANNING SURVEY BRIDGE CONDITION REPORT

A				B FEET	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z		
I	90	1865	1876	118	PRE CONC BEAM	SEP-MILWAUKEE AV	G		E		E	E					E			E	E		E	E	E	P	F	G		X
I	90	1865	1886	168	PRE CONC BEAM	SEP-CO RD	G		E		E	E					E			E	E	F	E	E	G	F	G	G		
I	90	1865	1893	153	PRE CONC BEAM	CLARK FORK	G		E		E	E	E	G	G	G	E			E	E	G	E	E	E	G	G	G		
I	90	1865	1893P	153	PRE CONC BEAM	CLARK FORK	G		E		E	E	E	G	G	G	E			E	E	G	E	E	E	G	G	G		
I	90	1865	1895		UNDERPASS*	S D-L INT-US 10	G		E		E	E					E			E	E		E	E	E	E	G	G		
I	90	1865	1895A		UNDERPASS	S D-L INT-US 10	G		E		E	E					E			E	E		E	E	E	E	G	G		
I	90	1895	1905	35	CONCRETE T BEAM	POWELL CR	G		G		G	G		G		F	G				G	G	F	G	G			G		
I	90	1895	1937	62	CONCRETE SLAB	DEMPSEY CR	G	F	G		G	G		G	P	G					G	G	G	G	G			F		
I	90	1895	1956	35	CONCRETE T BEAM	RACE TRACK CR	G		G		G	G		G	F	G	G				G	G	G	G	G			G		
I	90	1895	1967	182	CONCRETE T BEAM	CMSTP&P RR	F		F			G					G				G	F	G	F	G	G		F		
I	90	1895	2004	35	CONCRETE T BEAM	LOST CR	G		G		G	G		G		G	G				G	G	G	G	G			G		
I	90	1895	2031	27	CONCRETE T BEAM	WARM SPRINGS CR	G		G		G	G		G		G	G				G	G	G	G	G			G		
I	90	2039	2059	31	CONCRETE T BEAM	DR	G		G		G	G		G	F	G	G				G	G	G	G	G			G		
I	90	2039	2064	35	CONCRETE T BEAM	DR	G		G		G	G		G	F	G	G				G	G	G	G	G			G		
I	90	2039	2070	35	CONCRETE T BEAM	WILLOW CR	G		G		G	G		G	F	G	G				G	G	G	G	G			G		
I	90	2039	2073	75	CONCRETE T BEAM	CLARK FORK	G		G		G	G	G	G	F	G	G				G	G	G	G	G			G		
I	90	2039	2083		UNDERPASS	SEP-DR 275	G		E		E	E					E			E	E		E	E	E	E	E	E		
I	90	2039	2083A		UNDERPASS	SEP-DR 275	G		E		E	E					E			E	E		E	E	E	E	E	E		
I	90	2039	2092		UNDERPASS*	INT-US 10A	G		E		E	E					E			E	E		E	E	E	G	E	E		

A				TOTAL LENGTH FEET B	MATERIAL & TYPE MAXIMUM SPAN C	NAME OF FEATURE D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKER T	DECK U	V	W	X	Y	GENERAL Z	NOT INSPECTED Z1	REMARKS Z2
I	90	2039	2092A		UNDERPASS	INT-US 10A	G		E		E	E					E			E	E		E	E	E	G	E	E		
I	90	2092	2115	211	PRE CONC 8EAM	CMSTP&P RR	G		E		E	E					E			E	E		E	E	E	G	E	E		
I	90	2092	2115P	211	PRE CONC 8EAM	CMSTP&P RR	G		E		E	E					E			E	E		E	E	E	G	E	E		
I	90	2092	2126		UNDERPASS	GREGSON INT-441	G		E		E	E					E			E	E	E	E	E	E	E	E	E		
I	90	2092	2126A		UNDERPASS	GREGSON INT-441	G		E		E	E					E			E	E	E	E	E	E	E	E	E		
I	90	2092	2171P	158	PRE CONC 8M	8A & P RY	G		E		E	E					E			E	E	E	E	E	E	E	E	E		
I	90	2092	2171A	158	PRE CONC 8M	8A & P RY	G		E		E	E					E			E	E	E	E	E	E	E	E	E		
I	90	2092	2177		UNDERPASS	RAMSEY INT-CO RD	G		E		E	E					E			E	E	E	E	E	E	E	E	E		
I	90	2092	2177A		UNDERPASS	RAMSEY INT-CO RD	G		E		E	E					E			E	E	E	E	E	E	E	E	E		
I	90	2092	2201	303	PRE CONC 8EAM	INT I15 NISSLER																							N	
I	90	2092	2201P	293	PRE CONC 8EAM	INT I15 NISSLER																							N	
I	90	2278	2279		UNDERPASS	9MILE SEP-OR375	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I	90	2278	2279A		UNDERPASS	9MILE SEP-OR375	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I	90	2278	2284	193	STEEL GIRDER	E 8UTTE INT-I 15	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I	90	2278	2284P	193	STEEL GIRDER	E 8UTTE INT-I 15	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I	90	2278	2288		UNDERPASS	SEP-CO RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I	90	2278	2288A		UNDERPASS	SEP-CO RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I	90	2278	2346		UNDERPASS	HOMESTAKE INT-CO	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I	90	2278	2346A		UNDERPASS	HOMESTAKE INT-CO	G		E		E	E					E			E	E	E	E	E	E	E	G	E		

A	B	C	D		F		H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X		Z		
I 90 2278 2434	123	PRE CDNC 8EAM	PIPESTDNE INT-CD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2434P	123	PRE CDNC 8EAM	PIPESTDNE INT-CD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2447	315	STEEL GIRDER	NPRY	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2447P	315	STEEL GIRDER	NPRY	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2465	108	PRE CONC 8EAM	SEP-CD RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2465P	108	PRE CONC 8EAM	SEP-CD RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2504	128	PRE CDNC 8EAM	WHITEHALL INT	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2504P	128	PRE CDNC 8EAM	WHITEHALL INT	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2511		UNDERPASS	SEP CD RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2511A		UNDERPASS	SEP CD RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2546	214	PRE CDNC 8EAM	SEP-FRTG RD																							N	
I 90 2278 2546P	199	PRE CDNC BEAM	SEP-FRTG RD																							N	
I 90 2278 2576	138	PRE CONC 8EAM	CARDWELL INT																							N	
I 90 2278 2576P	138	PRE CDNC BEAM	CARDWELL INT																							N	
I 90 2278 2581	112	PRE CDNC 8EAM	8OULDER R																							N	
I 90 2278 2581P	112	PRE CDNC BEAM	8DULDER R																							N	
I 90 2702 2758	102	PRE CDNC BEAM	MILLIGAN CR																							N	
I 90 2702 2772	7	TT TRESTLE	STOCKPASS	G	F	F		G	G						F			P	G	F	F				F		X
I 90 2702 2779	7	TT TRESTLE	STDCKPASS	F	F	F		P	G						F			P	G	F	F				F		X

A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
				FEET			END FILLS	PILES	BENTS	PIERS	WINGWALLS	BULKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAIL	EXPANSION	PAINT	GENERAL COND	NOT INSPECTED	REMARKS
I	90	2702	2790	7	T T TRESTLE	STOCKPASS	F	F	F		F	G						F			F	G	F	F				F		
I	90	2702	2793	7	T T TRESTLE	STOCKPASS	F	F	F		F	G						F			F	G	F	F				F		
I	90	2801	2801	247	CONT ST GIRDER	JEFFERSON R	G		G	G	G	G	G	G	G	G	G			G	G	G	F	G	G	G	G	G		
I	90	2801	2818	208	STEEL GIRDER	CMSTP&P RR	F		F			G					G			G	G	G	G	G	F	F	G	G		
I	90	2838	2842	735	PRE CONC BEAM	2 RR-MADISON R	G		E	E	E	E	E	G	E	G	E			E	E	G	E	E	E	F	E	E		
I	90	2838	2842P	624	PRE CONC BEAM	2 RR-MADISON R	G		E	E	E	E	E	G	E	G	E			E	E	G	E	E	E	F	E	E		
I	90	2838	2849	144	PRE CONC BEAM	MID FK MADISON R	G		E	E	E	E	E	E	E	G	E			E	E		E	E	E		E	E		
I	90	2838	2849P	144	PRE CONC BEAM	MID FK MADISON R	G		E	E	E	E	E	E	E	G	E			E	E		E	E	E		E	E		
I	90	2838	2855	92	PRE CONC BEAM	E FK MADISON R	G		E	E	E	E	E	E	E	G	E			E	E		E	E	E		E	E		
I	90	2838	2855P	92	PRE CONC BEAM	E FK MADISON R	G		E	E	E	E	E	E	E	G	E			E	E		E	E	E		E	E		
I	90	2838	2857	128	PRE CONC BEAM	SEP-CO RD	G		E		E	E				E			E	E		E	E	E		E	E	E		
I	90	2838	2857P	128	PRE CONC BEAM	SEP-CO RD	G		E		E	E				E			E	E		E	E	E		E	E	E		
I	90	2838	2888P	143	PRE CONC BEAM	LOGAN INT-CO RD	G		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2942		UNDERPASS	INT-OR 288	E		G		E	E					E			E	E		E		E	E	E	E		
I	90	2838	2942A		UNDERPASS	INT-OR 288																								
I	90	2838	2946	158	PRE CONC BEAM	CMSTP&P RR	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2946P	158	PRE CONC BEAM	CMSTP&P RR	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2948	163	PRE CONC BEAM	NP RY	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2948P	163	PRE CONC BEAM	NP RY	E		E		E	E					E			E	E		G		E		G	E		

A				B	C	D	E	F	G	H		J	K	L	M	N	O	P	Q	R	S				W		Y	Z	Z	Z
I	90	2838	2962	82	PRE CONC 8EAM	CAMP CR	E		E	E	E	E	E	E	E	E	E			E	E		G		E		G	E		
I	90	2838	2962P	82	PRE CONC 8EAM	CAMP CR	E		E	E	E	E	E	E	E	E	E			E	E		G		E		G	E		
I	90	2838	2963	92	PRE CONC 8EAM	8AKER CR	E		E	E	E	E	E	E	E	E	E			E	E		G		E		G	E		
I	90	2838	2963P	92	PRE CONC 8EAM	8AKER CR	E		E	E	E	E	E	E	E	E	E			E	E		G		E		G	E		
I	90	2838	2971	113	PRE CONC 8EAM	HEE8 LANE SEP-CO	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2971P	113	PRE CONC 8EAM	HEE8 LANE SEP-CO	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2980	205	PRE CONC BEAM	W GALLATIN R	E		E	G	E	E	G	G	E	F	E			E	E		G		E		G	E		
I	90	2838	2980P	205	PRE CONC 8EAM	W GALLATIN R	E		E	G	E	E	G	G	E	F	E			E	E		F		E		G	E		
I	90	2838	2990	113	PRE CONC BEAM	CENTRAL PARK SEP	E		E		E	E					E			E	E		E		E		G	E		
I	90	2838	2990P	113	PRE CONC 8EAM	CENTRAL PARK SEP	E		E		E	E					E			E	E		E		E		G	E		
I	90	2838	3038		UNDERPASS	8ELGRADE INT-291	E		E		E	E					E			E	E		E		E	G	G	E		
I	90	2838	3038A		UNDERPASS	8ELGRADE INT-291																								
I	90	2838	3091	113	PRE CONC 8EAM	SEP CO RD	E		E		E	E					E			E	E		E		E		E	E		
I	90	2838	3091P	113	PRE CONC 8EAM	SEP CO RD	E		E		E	E					E			E	E		E		E		E	E		
I	90	2838	3125S	245	PRE CONC 8EAM	W 8OZEMAN INT	E		E		E	E					E			E	E		G		E	E	E	E		
I	90	2838	3132	351	WLD PL 136 GRD	NPRY & ROUSE ST																						E	N	
I	90	2838	3132P	351	WLD PL 136 GRD	NPRY & ROUSE ST																						E	N	
I	90	2838	3135	188	PRE CON 8M 70	MILW RY																						E	N	
I	90	2838	3135P	188	PRE CON 8M 70	MILW RY																						E	N	

A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
	NUMBER	CONTROL SECTION	BRIDGE NUMBER	TOTAL LENGTH FEET	MATERIAL & TYPE MAXIMUM SPAN	NAME OF FEATURE	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
I	90	2838	3136	143	PRE CON 8M 60	L ST																						E	N	
I	90	2838	3136P	143	PRE CON 8M 60	L ST																						E	N	
I	90	3137	3191	113	PRE CONC 8EAM	INT-CO RD	G		E		E	E					E			G	G	G	G	E	G	F	G	E		
I	90	3137	3191P	113	PRE CONC 8EAM	INT-CO RD	G		E		E	E					E			G	G	G	G	E	G	F	G	E		
I	90	3137	3197	338	ST GIRDER	NP RY	G		G		E	E					G			G	G	G	G	E	G	F	F	G		
I	90	3137	3197P	328	ST GIRDER	NP RY	G		G		E	G					G			G	G	G	G	E	G	F	F	G		
I	90	3137	3225	128	PRE CONC 8EAM	INT-CO RO	G		G		E	E					G			G	G	G	G	G	F	F	F	G		
I	90	3137	3225P	128	PRE CONC 8EAM	INT-CO RO	G		G		E	E					G			G	G	G	G	G	F	F	F	G		
I	90	3137	3367	113	PRE CONC 8EAM	W INT-US 10	G		G		G	G					G			G	G	G	G		F	F	F	G		
I	90	3137	3367P	113	PRE CONC 8EAM	W INT-US 10	F		G		G	G					G			G	G	G	G	G	G	F	F	G		
I	90	3367	3386	251	PRE CONC 8EAM	S INT-US 89	G		G		G	G					G			E	G	G	G	G	G		F	G		
I	90	3367	3386P	251	PRE CONC 8EAM	S INT-US 89	G		G		G	G					G			E	G	G	G	G	G		F	G		
I	90	3386	3392	730	RIV PL GIRDER	YELLOWSTONE R	G		G	G	G	G	F	F		G	G			G	G	G	F	G	G	F	F	G		
I	90	3386	3392P	730	RIV PL GIRDER	YELLOWSTONE R	G		G	G	G	G	F	F		G	G			G	G	G	F	G	G	F	F	G		
I	90	3386	3415	15	CONCRETE SLA8	JR GR SEP	G		G		E	E									E		E		G		G	G		
I	90	3386	3415P	15	CONCRETE SLA8	JR GR SEP	G		G		E	E									E		E		G		G	G		
I	90	3386	3425	128	PRE CONC 8EAM	SEP-OR 295	G		G		G	G					G			G	G	G	G	G	G	G	F	G		
I	90	3386	3425P	128	PRE CONC 8EAM	SEP-OR 295	G		G		G	G					G			G	G	G	G	G	G	G	F	G		
I	90	3386	3436		UNDERPASS*	E INT-US 89	G		G		G	G					G			G	G	G	F	G	G	F	G	G		

A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I	90	3386	3436A		UNDERPASS	E INT-US 89																								
I	90	3436	3461		UNDERPASS*	INT-US 89	F		F		G	G					G			F	G	G	G	G	G	G	F	G		
I	90	3436	3461A		UNDERPASS	INT-US 89																								
I	90	3461	3472	118	PRE CONC 8EAM	MISSION CR	G		G	G	G	E		G		G	G			G	G		G	G	G		F	G		
I	90	3746	3754	286	ST PLATE GIRDER	8OULDER R	G		G	F		F	F	P	G	G	F			F	G	G	F	F	G	F	F	F		
I	90	3746	3755	25	T T TRESTLE	8OULDER R OF	F	F	F		F	F		G	F	G		F		F	F	G	F	G	F		F	F		
I	90	3746	3796	57	T T TRESTLE	DRY CR	G	G	G	G	G	G		G	F	G		G		G	F	G	G	G	G		F	C		
I	90	3746	3801	11	T T TRESTLE	STOCKPASS	G	F	G		G	G			G	G		G		G	P	G	F	G	F		F	F		
I	90	3746	3803	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G		G	P	G	G	G	F		F	G		
I	90	3746	3810	19	T T TRESTLE	STOCKPASS	G	G	G		F	F						G		G	F	G	G	G	G		F	G		
I	90	3746	3817	39	CONCRETE I 8EAM	UPPER DEER CR	F		P		P	C		P	F	P	G	F		P	P	G	F	F	P		G	P		X
I	90	3746	3833	39	STEEL I 8EAM	LOWER DEER CR	F		G		F	G		F	F	G	G			G	G	G	G	G	G			G		
I	90	3746	3836	25	T T TRESTLE	STK & SPRING CR	F	G	F		F	F		F	F	F		G			F	G	G	G	F		F	F		
I	90	3746	3907	95	CONCRETE T 8EAM	8RIDGER CR	F		F	F		G		G	F	G	F				F	G	F		P			F		
I	90	3746	3942	67	CONCRETE T 8EAM	WORK CR	F		G			F		F	P	G	F				P	G	F		F			F		
I	90	3746	3954	29	CONCRETE T 8EAM	HUMPH CR	F		G		F	G		G	F	G	G				P	G	G		F			F		
I	90	3746	3970	102	PRE CONC 8EAM	SEP-CO RD	P		G	G	G	G					G			G	G		G	G	G		F	G		
I	90	3746	3980	133	PRE CONC 8EAM	INT-CO RD	F		E		E	E					E			E	E		E		E	F	G	G		X
I	90	3746	3980P	133	PRE CONC 8EAM	INT-CO RD	G		E		E	E					E			E	E		E		E	P	G	G		

							E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	Y	Y	Z	Z	ZZ
I	90	3746	4022	21	CONCRETE SLAB	JR INT-CO RD	G		E		F	E									E		E		G		G	G		X
I	90	3746	4031	16	CONC SLAB	JR GR SEP CO RD	G		E		F	E									E		E		G		G	G		X
I	90	3746	4033	558	RIV PL GIRDER	YELLOWSTONE R	G		E	E	E	E	E	E	E	E	E			E	G	G	F	E	G	E	G	E		X
I	90	3746	4037	249	STEEL GIRDER	NP RY	G		E		E	E					E			E	E		G		E	G	G	E		
I	90	3746	4046	16	CONC SLAB	JR GR SEP CO RD	F		E		G	E									E		E		E		G	E		
I	90	3746	4057	102	PRE CONC BEAM	BERRY CREEK	F		E		E	E		G	G	G	E			E	E		F		E	G	G	G		
I	90	3746	4140	76	CONCRETE T BEAM	KEYSER CR	G		G			G		G	G	G	G				P		G		F		P	G		
I	90	3746	419B	96	CONCRETE T BEAM	BROWN CR	G		G			G		G	G	G	G			G	G	G	G		G			G		
I	90	3746	4204	84	STEEL I BEAM	HENSLEY CR	F		F			F		G		G		G			G	G	G		G		P	F		
I	90	3746	4226	23	STEEL T BEAM	COVE IRR DT	F		G		F	G		G		G		G			G	G	G		F		P	G		
I	90	3746	4254	21	STEEL I BEAM	ALLEN CR	G		G		G	G		G	G	G		G			G	G	G		F		F	G		
I	90	3746	426B	100	CONT CONC T BM	BIG DITCH	F		G			G		G	G	G	G				G	G	G		G		F	G		
I	90	3746	4311	108	STEEL I BEAM	VALLEY CR	F		F			G		G	G	G		G			F	G	G		F		P	G		
I	90	3746	432B	123	PRE CONC BM	PARK CITY INT-10	E		E					E		E	E				E		E		E		E	E		
I	90	3746	432BP	123	PRE CONC BM	PARK CITY INT-10	E		E					E		E	E				E		E		E		E	E		
I	90	432B	4333	123	PRE CONC BM	SEP-CO RD	E		E					E		E	E				E		E		E		E	E		
I	90	432B	4333P	123	PRE CONC BM	SEP-CO RD	E		E					E		E	E				E		E		E		E	E		
I	90	432B	4375	123	PRE CONC BM	SEP-CO RD	E		E					E		E	E				E		E		E		E	E		
I	90	432B	4375P	123	PRE CONC BM	SEP-CO RD	E		E					E		E	E				E		E		E		E	E		

PLANNING SURVEY BRIDGE CONDITION REPORT

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z'
I 90 4328 4392	491	PRE CONC 8M	W LAUREL INT-RY	E		E			E		E		E	E			E	E		E		E	E	E	E		
I 90 4328 4392P	487	PRE CONC 8M	W LAUREL INT-RY	E		E			E		E		E	E			E	E		E		E	E	E	E		
I 90 4328 4396		UNOERPASS	SEP-CO RD	E		E							E	E											E		
I 90 4328 4396A		UNOERPASS	SEP-CO RO	E		E							E	E											E		
I 90 4328 4403	364	RIV PL GIR	S LAUREL INT-212	E		E	E				E		E	E				E		E		E		E	E		
I 90 4328 4403P	364	RIV PL GIR	S LAUREL INT-212	E		E	E				E		E	E				E		E		E		E	E		
I 90 4403 4417		UNOERPASS	SEP-CO RO	G		E			E					E			E			E		E	E	G	E		
I 90 4403 4417A		UNOERPASS	SEP-CO RO	G		E			E					E			E			E		E	E	G	E		
I 90 4403 4437	118	PRE CONC 8EAM	INT-US 10	G		E			E					E			E	E		E		E	E	G	E		
I 90 4403 4437P	118	PRE CONC 8EAM	INT-US 10	G		E			E					E			E	E		E		E	E	G	E		
I 90 4437 4442	40	PRE CONC 8EAM	88WA CANAL	G		E	E		E		G		G	E				E		E		E		G	E		
I 90 4437 4442P	40	PRE CONC 8EAM	88WA CANAL	G		E	E		E		G		G	E				E		E		G		G	E		
I 90 4437 4465	153	PRE CONC 8EAM	SEP-OR 502	G		E			E					E			E	E		G		G	G	G	G		
I 90 4437 4465P	153	PRE CONC 8EAM	SEP-OR 502	G		E			E					E			E	E		G		G	F	G	G		
I 90 4437 4489		UNOERPASS	SEP-OR 429	F		G			G					E			G	G		G			G	F	G		
I 90 4437 4489A		UNOERPASS	SEP-OR 429	F		G			G					E			G	G		G			G	F	G		
I 90 4437 4491	153	PRE CONC 8EAM	CANYON CR	F		G			G		G	G	G	G			G	G		G		G	G	F	G		
I 90 4437 4491P	153	PRE CONC 8EAM	CANYON CR	F		G			G		G	G	G	G			G	G		G		G	G	F	G		
I 90 4437 4517	82	PRE CONC 8EAM	HOGAN SL	G		G			G		G		G	G			G	G		G		G	G	G	G		

							E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
I	90	4437	4517P	82	PRE CONC BEAM	HOGAN SL	G		G			G		G		G	G			G	G		G		G	G	G	G		
I	90	4437	4522	185	PRE CONC BEAM	W BILLINGS INT	G		E			E					E				E		G		E		E	E		
I	90	4437	4522P	185	PRE CONC BEAM	W BILLINGS INT	G		E			E					E				E		G		E		E	E		
I	90	4522	4524	195	PRE CONC BEAM	W BILLINGS INT	G		E			E					E				E		G		E		E	E		
I	90	4522	4524P	195	PRE CONC BEAM	W BILLINGS INT	G		E			E					E				E		G		E		E	E		
I	90	4522	4534		UNDERPASS	BILLINGS BLV SEP	G		E			E					E											E		
I	90	4522	4534A		UNDERPASS	BILLINGS BLV SEP	G		E			E					E											E		
I	90	4522	4555		UNDERPASS	SUGAR AVE SEP	G		E			E					E											E		
I	90	4522	4555A		UNDERPASS	SUGAR AVE SEP	G		E			E					E											E		
I	90	4522	4563		UNDERPASS*	27TH ST INT-SR 3	G		E			E					E											E		
I	90	4522	4563A		UNDERPASS*	27TH ST INT--SR 3	G		E			E					E											E		
I	90	4563	4568	148	PRE CONC BEAM	MT POWER RR SPUR	G		E			E					E				E		E		E		E	E		
I	90	4563	4568P	148	PRE CONC BEAM	MT POWER RR SPUR	G		E			E					E				E		E		E		E	E		
I	90	4563	4583	945	RIV PL GIRDER	YELLOWSTONE R	G		E	E		E		G	G	G	E			E	E	E	F		E	E	G	E		
I	90	4563	4583P	945	RIV PL GIRDER	YELLOWSTONE R	G		E	E		E		G	G	G	E			E	E	E	F		E	E	G	E		
I	90	4563	4591S	276	PRE CONC BEAM	LOCKWOOD INT--I94	G		E			E					E				E		E				E	E		
I	90	4591	4606	57	UNT T TRESTLE	DRY CR	G	G	G			G		G	F			P			F		G		F		F	F		X
I	90	4591	4698	69	CONCRETE SLAB	PRYOR CR	G		F		F	G		G	F			G			E		G		G		F	G		
I	90	4591	4700	55	CONCRETE SLAB	E FK PRYOR CR	G		G			G		G	F			G			E		G		G		F	G		

[illegible]

				FEET						PIERS										SHOES	CURBS		DECK				PAINT			
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z
I	90	4591	4B66	19	T T TRESTLE	STOCKPASS & OR	F	F	F		G	P						F			F		G		G		P	G		
I	90	4591	4907	57	UNT T TRESTLE	FLY CR	G	G	G			G		G	G			P			F		G		G		P	G		X
I	90	4591	4945	233	CONCRETE T BEAM	CB & Q RY	G		P			G					G			P	G		G		F	P		F		X
I	90	4591	4959	19	T T TRESTLE	STOCKPASS & OR	G	G	G		G	G				G		F			G		G		G		F	G		
I	90	4591	5005	38	T T TRESTLE	PERISTA CR	G	G	F		F	G		G		G		F			F		G	G	G		F	G		X
I	90	4591	5015	19	T T TRESTLE	STOCKPASS & OR	F	G	G		G	G		G		G		F			G		G		G		F	G		X
I	90	4591	5052	31	CONCRETE T BEAM	TWO LEGGIN CA	G	G	G			G		G	F	G					F		G		F			G		
I	90	5065	5086	578	STEEL TRUSS	BIG HORN R	G		G	G		G		G		G		G	G	G	F	G	G	G	G	P	P	G		X
I	90	5065	5137	11B	PRE CONC BEAM	INT-CO RO	F		E			E					E			E	E		G		E		F	E		
I	90	5065	5137P	11B	PRE CONC BEAM	INT-CO RO	F		E			E					E			E	E		G		E		F	E		
I	90	5065	5146	15	CONCRETE SLAB	JR GR SEP	G		E		P	E					E			E	E		G		E		F	G		X
I	90	5065	5196	133	PRE CONC BEAM	INT-CO RO	F		E			E					E			E	E		G		E		P	G		
I	90	5065	5196P	133	PRE CONC BEAM	INT-CO RO	G		E			E					E			E	E		G		G		P	G		
I	90	5065	5201	165	PRE CONC BEAM	LITTLE BIGHORN R	G		E	E		E	E	G	G	G	E			E	E		G		E		F	E		
I	90	5065	5201P	130	CONT ST GIRDER	LITTLE BIGHORN R	G		G	G	G	G	G	G	G	G	G			F	G	F	G		G	F	F	G		
I	90	5065	5214		UNDERPASS*	INT-US 212	F		E			E					E			E			E				G	E		
I	90	5065	5214A		UNDERPASS	INT-US 212	F		E			E					E			E			E				G	E		
I	90	5214	5221	156	CONCRETE T BEAM	LITTLE BIGHORN R	G			G		G	G	G	G	G	G			G	G	F	G		G		G	G		
I	90	5214	5280	156	CONCRETE T BEAM	LITTLE BIGHORN R	P			G		G	G	G	G	G	G			G	G	G	G		F		F	G		

A	B			E	F	G	H		J	K	L	M	N	O	P		R	S	T	U		W			Z	Z	ZZ
I 90 5214 5338	136	CONCRETE T 8EAM	LITTLE BIGHORN R	P			G		G	G	G	G	G	G			G	G	F	G		G		G	G		
I 90 5214 5409	64	CONCRETE T BEAM	LODGE GRASS CR	G			G		G	G	G	G	G	G			G	G	P	G		G		F	G		
I 90 5214 5501	120	CONT ST GIROER	LITTLE 8IGHORN R	F		G	G		G	G	G	G	G	G			F	G	F	G		G	F	P	G		
I 90 5214 5585	65	CONT ST GIRDER	PASS CR	F	G	G	G		G		G	G	G	G			G	G	G	G		G		G	G		
I 90 5214 5592	65	CONT ST GIROER	PASS CR	F	G	G	G		G		G	G	G	G			G	G	G	G		G		G	G		
I 94 0000 0000		UNDERPASS	INT-190 & US 87	E		E			E					E										E	E		
I 94 0000 0000A		UNDERPASS	INT-I 90 & US 87	E		E			E					E										E	E		
I 94 0000 0024	150	PRE CONC BM	JOHNSON LANE-SEP	G		E			E					E				E		E		E		E	E		
I 94 0000 0024P	150	PRE CONC BM	JOHNSON LANE-SEP	G		E			E					E				E		E		E		E	E		
I 94 0000 0037		UNOERPASS	PINE HILL INT	E		E			E					E										E	E		
I 94 0000 0037A		UNOERPASS	PINE HILL INT	E		E			E					E										E	E		
I 94 0000 0045	153	PRE CONC BM	SEP-CO RD	E		E			E					E				E		E		E		E	E		
I 94 0000 0045P	163	PRE CONC 8M	SEP-CO RO	E		E			E					E				E		E		E		E	E		
I 94 0000 0095		PRE CONC BM	HUNTLEY INT	E		E			E					E										E	E		
I 94 0000 0095P		PRE CONC BM	HUNTLEY INT	E		E			E					E										E	E		
I 94 0000 0098	313	PRE CONC BEAM	PRYOR CR																							N	
I 94 0000 0098P	313	PRE CONC 8EAM	PRYOR CR																							N	
I 94 0000 0106	92	PRE CONC BM	PRYOR CR	E		E		E	E			E		E				E		E		E		E	E		

PLANNING SURVEY BRIDGE CONDITION REPORT

A				B FEET	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	ZZ
I	94	0000	0107	70	PRE CONC BM	HUNTLEY CANAL	E		E		E	E			E		E				E		E		E		E	E		
I	94	0000	0135	78	CAST CONC SLAB	SEP-CO RD																							N	
I	94	0000	0135P	78	CAST CONC SLAB	SEP-CO RD																							N	
I	94	0000	0181	128	PRE CONC BEAM	BALLANTINE INT																							N	
I	94	0000	0181P	128	PRE CONC BEAM	BALLANTINE INT																							N	
I	94	0000	0198	448	PRE CONC BEAM	CB & GRR-CO RD																							N	
I	94	0000	0198P	446	PRE CONC BEAM	CB & GRR-CO RD																							N	
I	94	0000	0207	154	PRE CONC BEAM	SEP-CO RD																							N	
I	94	0000	0207P	154	PRE CONC BEAM	SEP-CO RD																							N	
I	94	0000	0228	128	PRE CONC BEAM	SEP-CO RD																							N	
I	94	0000	0228P	118	PRE CONC BEAM	SEP-CO RD																							N	
I	94	0000	0237	107	PRE CONC BEAM	HUNTLEY CA																							N	
I	94	0000	0237P	117	PRE CONC BEAM	HUNTLEY CA																							N	
I	94	0000	0245		UNDERPASS	SEP-CO RD																							N	
I	94	0000	0245A		UNDERPASS	SEP-CO RD																							N	
I	94	0000	0265		UNDERPASS	POMPEYS PILLAR																							N	
I	94	0000	0265A		UNDERPASS	INT US 10																							N	
I	94	0265	0287	125	T T TRESTLE	FLY CR	G	G	G	F		G	F	G		G		G			G	G	G	F	G		G	G		
I	94	0265	0306	57	T T TRESTLE	SAND CR	G	G	G			G		G	G	F		G			P	F	G	G	G		G	G		

								E	F	G	H		J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z?
I	94	0265	0330	57	T T TRESTLE	MILL CR		G	G	G			G		G	G	G		F			F	F	G	G	G		G	G		X
I	94	0265	0345	57	T T TRESTLE	KAISER CR		G	G	G			G		G	G	G		G			F	G	G	G	G		G	G		
I	94	0265	0361	57	T T TRESTLE	DRAINAGE		G	G	G			G		G		G		G			F		G	G	G		G	G		
I	94	0265	0376	57	T T TRESTLE	SPRING CR		G	G	G			G		G	G	G		G			G	F	G	G	G		G	G		
I	94	0265	0406	106	STEEL GIRDER	AUTOMATIC CR		G		G			G		G	G	G	G			G	G	G	G		G	F	F	G		
I	94	0535	0558	580	RIV PL GIRDER	BIG HORN R		G		E	E		E	E	G	G	G	E			E	E	E	E	E	E	E	G	E		
I	94	0535	0568		UNDERPASS	INT-CO RD		G		E			E					E			E							G	E		
I	94	0535	0716	143	PRE CONC BM	HYSHAM INT-US 10		G		E			E					E			G	G		G		E		G	E		
I	94	0716	0754	188	PRE CONC BM	SARPY CR		E		E		E	E	E	E			E			E			E		E		E	E		
I	94	0716	0757		UNDERPASS	SARPY INT-OR 415		E		E			E					E			E							E	E		
I	94	0716	0856	180	PRE CONC BM	SEP-CO RD-RES CR		G		E			E		G	G	G	E			E	E		E		E		E	E		
I	94	0716	0913		UNDERPASS	COLSTRIP INT-315		F		E			E					E			E	E		E		E		E	E		
I	94	0716	0918	394	PRE CONC BM	NP RY-ARMELLS CR		F		E			E		G	E	G	E			E	E		E		E		E	E		
I	94	0716	0959	220	PRE CONC BM	SMITH CR		G		E			E		G	E	G	E			E	E		E		E		E	E		
I	94	0972	1079	123	ST PONY TRUSS	ROSEBUD CR		G		G	G		G		G		G		G	G	F	G		G	G	F		G	G		
I	94	0972	1097	76	T T TRESTLE	BUTTE CR		F	F	F			G		G	G	G		F			F	G	G	F	F		F	F		
I	94	0972	1154	114	T T TRESTLE	SWEENEY CR		F	F	F			F		G		G		F			F	E	G	G		F	F	F		
I	94	0972	1182	95	T T TRESTLE	COAL CR		G	G	F			F		G	G	G		F			F	G	G	G	F		F	F		
I	94	0972	1194	17	CONCRETE SLAB	JR GR SEP-STK		F		E		G	E									E		E		E		G	E		

PLANNING SURVEY BRIDGE CONDITION REPORT

A				B FEET	C	D	E END F	F	G BENTS	H PIERS	I WINGWALLS	J	K ICE BREAKERS	L	M	N SCOUR	O	P	Q	R SHOES	S CURBS	T	U	V	W	X	Y PAINT	Z GENERAL	Z1	Z2
I	94	0972	1229	82	PRE CONC BEAM	GRAVEYARD CR	G		E			E		G	G	G	E			E	E		E		E	F	G	E		
I	94	0972	1305		UNDERPASS	INT--CO RD	G		E			E					E			E	E		E		E	G	G	E		
I	94	0972	1330		UNDERPASS	INT--CO RD	G		E			E					E			E	E		E		E	G	G	E		
I	94	0972	1381	17	CONCRETE SLAB	JR GR SEP--STK	G		E		E	E									E		E		E		G	E		
I	94	0972	1391	17	CONCRETE SLAB	JR GR SEP--STK	G		E		E	E									E		E		E		G	E		
I	94	0972	1398		UNDERPASS*	W INT-US 10	G		E			E					E			E	E		E		E		G	E		
I	94	0972	139BA		UNDERPASS	W INT-US 10	G		E			E					E			E	E		E		E		G	E		
I	94	1398	1408	17	CONCRETE SLAB	JR GR SEP-STK	G		E		E	E									E		E		E		G	E		
I	94	1398	1413	290	RIV PL GIRDER	TONGUE R	G		E	E		E	E	G	G	G	E	E		E	E		E	E	E	G	G	E		
I	94	1398	1422	153	PRE CONC BEAM	SEP-CO RD	G		E			G					E			G	F		E		E	F	G	E		
I	94	1398	1425	158	PRE CONC BEAM	INT-US 312	G		E			E					E			G	E		E		E	F	G	E		X
I	94	1425	1431	21	CONCRETE SLAB	JR GR SEP--CO RD	G		E		E	E									E		E		E		G	E		
I	94	1425	1443	21	CONCRETE SLAB	JR GR SEP-CO RD	G		E		E	E									E		E		E		G	E		
I	94	1425	1450	14	CONC SLAB	JR GR SEP	G		E		E	E									E		G		E		F	G		
I	94	1425	1454		UNDERPASS*	BAKER INT-US 12	G		E			E					E			E	G		E		E	G	G	E		
I	94	1454	1489	15	CONCRETE SLAB	JR GR SEP--STK	G		E		E	E									E		E		E		G	E		
I	94	1454	1505	21	CONCRETE SLAB	JR GR SEP--CO RD	G		E		E	E									E		E		E		G	E		
I	94	1531	1625	171	T T TRESTLE	COTTONWOOD CR	G	F	F			G		G	G	G		F			G	G	G	F	F		P	F		
I	94	1531	1639	57	T T TRESTLE	MILES CR	G	G	G					P		P		G			G	G	G	G	F		F	G		

A	B	C		E	F	G	H	I	J	K		M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
I 94 1531 1659	38	T T TRESTLE	MACKS CR	G	G	G			G		G	G	G		G			G	G	G	G	G		F	G
I 94 1531 1668	95	T T TRESTLE	WILLIAMS COU	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
I 94 1531 1695	57	T T TRESTLE	CAMP CR	G	G	G	G	G	G	N	P	G	F	N	G	N	N	G	G	G	G	G	N	F	F
I 94 1531 1732	633	CONT ST TRUSS	POWDER R	F	N	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G
I 94 1531 1761	57	T T TRESTLE	CONNS COU	G	E	E	N	E	E	N	E	G	E	N	E	N	N	E	E	E	E	G	N	G	E
I 94 1531 1779	19	T T TRESTLE	STOCKPASS & DR	F	E	E	N	E	E	N	E	E	E	N	E	N	N	E	E	E	E	G	N	G	E
I 94 1531 1787	38	T T TRESTLE	DRAINAGE	F	E	E	N	E	E	N	E	E	E	N	E	N	N	E	E	E	E	G	N	G	E
I 94 1531 1799	38	T T TRESTLE	DRAINAGE	F	E	E	N	E	E	N	E	E	E	N	E	N	N	E	E	E	E	G	N	G	E
I 94 1531 1835		UNDERPASS	CMSTP&P RR	E	N	G	N	G	G	N	N	N	N	G	N	N	G	N	G	G	N	N	N	P	G
I 94 1531 1888	220	CONT ST GIRDER	O FALLON CR	F	N	P	G	G	P	G	G	G	G	G	N	N	P	G	G	F	N	G	P	G	F
I 94 1531 1891	146	CONCRETE T BEAM	NP RY	P	N	G	N	G	G	N	N	N	N	G	N	N	F	G	G	G	N	G	F	N	G
I 94 1531 1910	1142	STEEL TRUSS	YELLOWSTONE R	G	N	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	F	G	G	G	G
I 94 1531 1933	65	STEEL I BEAM	HATCHET CR	G	G	G	N	N	G	N	G	F	F	G	N	N	G	G	G	G	N	G	N	G	G
I 94 1531 1964	165	STEEL I 8EAM	8AD ROUTE CR	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	G	G	G
I 94 1531 2011	165	STEEL I BEAM	CRACKER BOX CR	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	G	G	G
I 94 1531 2059	65	STEEL I BEAM	USRS CANAL	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	G	G	G
I 94 1531 2060	190	STEEL I BEAM	CLEAR CR	P	G	G	N	N	P	N	G	G	G	G	N	N	G	G	G	G	N	G	G	G	F
I 94 1531 2063	31	STEEL I BEAM	CANAL	G	N	G	N	N	G	N	G	N	G	G	N	N	G	G	G	G	N	G	N	G	G
I 94 1531 2086	65	STEEL I BEAM	WHOOPUP CR	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	N	G	G

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Columns E thru Z

E - Excellent
G - Good
F = Fair

P = Poor
C - Critical

Column Z1

N = New
R - To be Removed
Unable to inspect

CONTROL BRIDGE NUMBER	TOTAL LENGTH FEET	MATERIAL & TYPE MAXIMUM SPAN	NAME OF FEATURE	SUBSTRUCTURE																							
A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U		W	X		Z	Z	Z2
I 94 1531 2109	40	STEEL I BEAM	USRS CANAL	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	N	G	G		
I 94 1531 2110	90	STEEL I BEAM	SAND CR	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	N	G	G		
I 94 1531 2112	21	CONCRETE T BEAM	USRS CANAL	G	N	G	N	N	G	N	G	N	G	G	N	N	N	G	G	G	N	G	N	N	G		
I 94 1531 2138	21	CONCRETE T BEAM	USRS CANAL	F	N	G	N	N	G	N	F	N	F	G	N	N	N	G	G	G	N	G	N	N	G		
I 94 1531 2154	120	CONT CONC T BM	UPPER 7 MILE CR	E	N	E	E	E	E	N	E	E	G	E	N	N	E	E	G	G	N	E	N	G	G		
I 94 1531 2154P	120	CONT CONC T BM	UPPER 7 MILE CR	E	N	E	E	E	E	N	E	E	G	E	N	N	E	E	G	G	N	E	N	G	G		
I 94 2162 2163	120	CONT CONC T BM	DRY CR	G	N	E	N	E	E	N	E	E	E	E	N	N	E	E	G	G	N	E	N	G	G		
I 94 2162 2163P	120	CONT CONC T BM	DRY CR	G	N	E	N	E	E	N	E	E	E	E	N	N	E	E	G	G	N	E	N	G	G		
I 94 2169 2175	1318	CONCRETE GIRDER	YELLOWSTONE R	G	N	E	E	E	G	G	E	E	G	E	N	N	E	E	G	E	E	E	G	G	G		
I 94 2169 2265	106	CONT ST GIRDER	GRIFFITH CR	G	N	G	G	E	E	N	E	G	G	E	N	N	E	G	G	G	N	G	G	G	G		
I 94 2169 2355	123	PRE CONC BEAM	HODGES SEP-CO RD	P	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	E	N	E	N	E	E		
I 94 2169 2460		UNDERPASS*	W INT-SR 7	G	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	G	N	E	G	G	E		
I 94 2460 2463	286	PRE CONC BEAMS	BEAVER CR	G	N	E	E	E	E	G	G	E	G	E	N	N	E	E	G	G	N	E	G	G	E		
I 94 2460 2466		UNDERPASS*	E INT-SR 7	G	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	G	N	E	G	G	E		

FEDERAL AID PRIMARY ROUTES

A	B	C	D	E		G	H	I	J		L	M	N	O	P		R	S	T			W				
P 1 0000 0063	210	STEEL GIRDER	YAAK R	G		G	G	G	G		G		G	G			G	G	G	F	G	G	G	G	G	X
P 1 0000 0116	939	STEEL TRUSS	KOOTENAIR-GN RY	F		G	G	G	G	G	G	G	G		G	G	G	G	G	G	G	G	G	P	G	X
P 1 0000 0145	187	ST PONY TRUSS	CALLAHAN CR	G		F	F	G	G		P	P	G		G	G	G	G	G	G	G	G	G	G	G	X
P 1 0000 0153	175	CONT STEEL BEAM	LAKE CR	G		G		F	F		G		G	G			G	G	G	G	G	P	G	P	G	X
P 1 0000 0278	39	CONCRETE T BEAM	CEDAR CR	G		G		G	G		G		F	G					P	G		G		G	G	
P 1 0000 0311	22	CONCRETE SLAB	PARMENTER CR	G		G		G	G		G		G						G	G		F		G	G	
P 1 0000 0322	22	CONCRETE SLAB	FLOWER CR	G		G		G	G		G		G						G	G		G		G	G	
P 1 0323 0353	179	STEEL BEAM	GRANITE CR	P		F		G	G		P		G	G	G		G	F	P	P	G	F	P	P	F	X
P 1 0323 0412	38	T T TRESTLE	GETNER CR	F	G	G		G	G		P		G		G			G	G	G	G	G		P	G	
P 1 0323 0447	140	STEEL TRUSS	LIBBY CR	F		G		G	G		G	G	G			G	G	G	G	G	G	G	G	G	G	
P 1 0323 0461	30	T T & CONC	SWAMP CR	G	G	G		G	G		G		G		G			G	G	G	G	G			G	
P 1 0323 0467	30	T T & CONC	SWAMP CR	G	G	G		G	G		G		G		G			G	G	G	G	G			G	
P 1 0323 0483	45	T T & CONC	SWAMP CR	G	G	G		G	G		G		G		G			G	G	G	G	G			G	
P 1 0323 0487	19	T T TRESTLE	SWAMP CR	F	G	G		G	G		G		F		G			G	G	G	G	P			G	
P 1 0323 0567	23	T T & CONC	MILLER CR	G	G	G		G	G		G		G		G			G	G	G	G	G			G	
P 1 0323 0571	180	THRU ST TRUSS	FISHER R	G		G		G	G		G	G	G			G		G	G	G	G	G		G	G	
P 1 0323 0689	75	T T TRESTLE	PRIVATE RD	G	G	G		G	G						G			G	G	G	G	G		G	G	
P 1 0323 0711	38	T T TRESTLE	FISHER R	F	G	G		G	G	G	G	F	G		G			G	G	G	G	F		F	G	
P 1 0323 0804	38	T T TRESTLE	LANG CR	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G	

				TOTAL LENGTH	DESCRIPTION OF STRUCTURE	NAME OF FEATURE CROSSED	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHIELDS	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
		A		FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	1	0323	0962	19	T T TRESTLE	LIT BITTEROOT R	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	0323	1052	75	T T TRESTLE	ASHLEY CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	1	0323	1139	41	CONCRETE T BEAM	ASHLEY CR	F		G		G	G		G	G	G	G				G	G	G		G			G		
P	1	0323	1146	41	CONCRETE T BEAM	ASHLEY CR	G		G		G	G		G	G	G	G				F	F	G		F			G		
P	1	1209	1216		UNDERPASS	GN RY	G		G		G	G					G			G	G		G				G	G		
P	1	1209	1216A		UNDERPASS	GN RY	G		G		G	G					G			G	G		G				G	G		
P	1	1209	1224	182	PRE CONC BEAM	STILLWATER R	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G		
P	1	1209	1224P	182	PRE CONC BEAM	STILLWATER R	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G		
P	1	1209	1235	92	PRE CONC BEAM	SPRING CR	G		G		G	G		G	G	G	G			G	G	G	G		G		G	G		
P	1	1209	1248	898	STEEL TRUSS	FLATHEAD R	G		G	G	G	G	G	F		F			F	F	P	G	F	G	F	G	F	F		X
P	1	1383	1400	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	1	1383	1422	590	STEEL GIRDER	S FK FLATHEAD R	G		G		G	G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
P	1	1383	1444	22	CONCRETE SLAB	MARTIN CR	G		G		G	G		G		G					G	G	G		G			G		
P	1	1532	1610	115	T T TRESTLE	DEER LICK CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G			G		
P	1	1532	1647	363	STEEL GIRDER	GN RY	G		G		G	G					G			G	G	G	G	G	G		P	G		
P	1	1532	1675	209	CONCRETE T BEAM	GN RY	G		G		G	G					G			G	G	G	G	G	G		F	G		
P	1	1532	1805	744	PRE CONC GIRDER	MID FK FLATHEAD																								N
P	1	1532	1825	144	ST PONY TRUSS	SNOWSLIDE GULCH	G		F		F	F		G		G			G	G	P	G	F	G	F	G	P	G		
P	1	1532	1841		UNDERPASS	GN RY	G		G		G	G					G						G				F	G		

				FEET			E	F	G	H	I	J	K		M	N	O			R									Z	ZZ
P	1	1532	1863	122	PRE CONC BEAM	BEAR CR	F		G		G	G		F	G	G	G				G	P	G		G			G		
P	1	1532	1895	26	CONCRETE SLAB	DEVIL CR	G		G		F	G		G		G					G	P	G		G			G		
P	1	1532	1922	112	PRE CONC BEAM	BEAR CR	G		G	G	G	G		G	G	G	G				G		G	G	G			G		
P	1	1532	2091	142	CONCRETE T BEAM	MIDVALE CR	G		G			G		G	G	G	G			G	P		F	G	P	F		F		X
P	1	2093	2102	760	CONT ST TRUSS	TWO MEDICINE CR	G		G	G	G	G		G		G		G	G	G	G	G	G	G	F	G	P	G		X
P	1	2093	2204	127	CONCRETE T BEAM	GN RY	G		G			G					G				G	G	G	G	F			G		
P	1	2093	2214	20	STL GIRDER	DRAINAGE	G		G		G	G		G		F	G				G	G	G				F	G		
P	1	2218	2232	144	CONCRETE T BEAM	GN RY	G		F		G	F					P				F	G	F	F	P			P		X
P	1	2240	2290	38	T T TRESTLE	WILLOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	U		
P	1	2240	2294	38	T T TRESTLE	WILLOW CR OF	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
P	1	2240	2541	314	CONT ST GIRDER	CUT BANK CR	F		G			G	G	G	P	F	G	G		G	G	F	G	G	G	F		G		
P	1	2240	2784		UNDERPASS*	SHELBY INT-I 15	E		E		E	E					E			E	E		E	E	E	E	G	E		
P	1	2240	2784A		UNDERPASS	SHELBY INT-I 15	E		E		E	E					E			E	E		E	E	E	E	G	E		
P	1	2784	2784		UNDERPASS*	SHELBY INT-I 15	E		E		E	E					E			E	E		E	E	E	E	G	E		
P	1	2784	2784A		UNDERPASS	SHELBY INT-I 15	E		E		E	E					E			E	E		E	E	E	E	G	E		
P	1	2794	3001	57	T T TRESTLE	W FK WILLOW CR	G	G	G		G	G		G	G	G		G			G	F	G	G	G		F	G		
P	1	2794	3030	100	T T TRESTLE	N FK WILLOW CR	G	G	G		G	G		F	P	F		G			G	G	G	F	G		F	G		
P	1	2794	3224	57	T T TRESTLE	COTTONWOOD CR	G	G	G		G	G		G		G		G			G	G	G	F	G		G	G		
P	1	2794	3266	7	T T TRESTLE	STOCKPASS	F	F			G	G						G			F	G	G	F				G		

PLANNING [illegible] BRIDGE CONDITION [illegible]

A				B TOTAL LENGTH FEET	C MATERIAL & TYPE	D NAME	E END	F PI	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TRUSS	R SHOES	S CURBS	T MARKERS	U DECK	V BRACING	W RAILING	X EXPA	Y PAINT	Z GENERAL	Z1 NOT IN	Z2 REMARKS
P	1	2794	3538	120	CONCRETE T BEAM	SAGE CR	G		E	E	E	E	G	G	G	G	E			E	E	G	G		G		G	E		
P	1	2794	3763	146	CONT CONC T BM	BIG SANDY CR	P		G	G	G	G	G	G	F	G	G			G	G	G	G	G	G		F	G		
P	1	2794	3780	312	STEEL BEAM	GN RY	F		G		G	G					G	G		G	G	G	G	G	G	P	F	G		X
P	1	3791	3862	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G		G	G	G		G	G		
P	1	3791	3893	100	T T TRESTLE	BOX ELDER CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	1	3791	3897	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		G	G		
P	1	3791	3904	38	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			F		G	G	G		G	G		
P	1	3791	3924	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	P	G		P			G		X
P	1	3791	3927	38	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	G	G	F	G		G	G		
P	1	3791	3934	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	1	3791	3960	57	T T TRESTLE	CLEAR CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	1	3791	3971	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	1	3791	3977	242	ST PONY TRUSS	MILK R	G		G	G	G	G	G	F	G	G			G	G	G	G	G	G	G	G	G	G		
P	1	3791	4006	19	T T TRESTLE	CANAL	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	1	3791	4018	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	1	3791	4022	57	T T TRESTLE	RED ROCK CR	G	G	G		P	G		G	G	G		G			F	G	G	G	G		G	G		
P	1	3791	4027	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4041	57	T T TRESTLE	RED ROCK CR OF	G	G	G		G	G		G	F	G		G			F	G	G	G	G		G	G		
P	1	3791	4043	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		

		A		B		D	E	F		H		J	K		M	N	O		Q	R	S				W			Z		
P	1	3791	4045	94	CONCRETE T 8EAM	LODGE CREEK	G		G	G	G	G		P		F	G			G	G	G	G		G			G		X
P	1	3791	4053	57	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	1	3791	4056	152	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	1	3791	4060	11	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G			G	G		
P	1	3791	4068	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4070	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4079	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	1	3791	4084	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4099	196	THRU ST TRUSS	8ATTLE CR	G		G	G	G	G		G	F	G		G	G	G	G	G	G	G	G	G	G	G		X
P	1	3791	4120	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4128	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	1	3791	4138	108	CONT ST GIRDER	FIFTEEN MILE CR	G		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
P	1	3791	4256	25	STL & CONC	MAIN IRR CA																							N	
P	1	3791	4279	213	PRE CONC 8EAM	MILK R																							N	
P	1	3791	4324	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G	G	G		G		F	G		
P	1	3791	4428	119	CONCRETE SLA8	WHITE BEAR CR	F	G	G	G		G	G	G		G		G			G	G	G	G	F			G		
P	1	3791	4470	57	T T TRESTLE	PEOPLES CR OF	F	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4471	57	T T TRESTLE	PEOPLES CR OF	F	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4474	125	T T TRESTLE	PEOPLES CR	F	F	G	P		G	G	G		G		G			F	G	F	G	F		F	F		X

	DESCRIPTION OF STRUCTURES			CONDITION RATING																							
				SUBSTRUCTURE																							
	FEET	MATERIAL & TYPE MAX MUM SPAN	NAME	END FILLS	PILES	BENTS	PIERS	WINGWA	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TR	SHOES	CURBS	MAR	DECK	BRA	RA	EX	PAINT	GE	NOT INSPECTED	R
A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P 1 3791 4513	63	T T TRESTLE	DODSON CR CA	G	G	G		G	G		F		F		G			G	G	G	G	G		F	G		
P 1 3791 4517	240	STEEL TRUSS	MILK R	G	G	G	F		G	G	G		G		G	G	F	F	G	G	G	F		F	G		
P 1 3791 4535	75	T T TRESTLE	DODSON CR	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P 1 3791 4540	57	T T TRESTLE	USRS CANAL	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P 1 3791 4541	57	T T TRESTLE	DODSON CR OF	G	G	G			G		G		G		G			F	G	G	G	G		G	G		
P 1 3791 4560	57	T T TRESTLE	DODSON CR OF	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P 1 3791 4576	57	T T TRESTLE	SPRING CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P 1 3791 4583	186	CONCRETE T 8EAM	GN RY	G		G			G								P	F	F	F		F	P		F		X
P 1 3791 4676	76	T T TRESTLE	EXETER CR	G	G	G			G		G	F	G					F	G	G	G	F		G	G		
P 1 3791 4716	240	STEEL GIRDER	MILK R	G		G	G		G	G	F	G	G	G			G	G	G	G		G	G	F	G		
P 1 4718 4857	102	PRE CONC 8M	NELSON CANAL	F	E	E		E	E		F		G	E			G	E	G	E		E		E	E		
P 1 4718 4905	90	CONT CONC SLA8	DRAINAGE	F		G		E	E		G	E	G					E		E		E		E	E		
P 1 4718 4918	90	CONT CONC SLAB	DRAINAGE	F		G		E	E		G	E	G					E		E		E		E	E		
P 1 4718 4927	163	CONC PRE 8EAM	8EAVER CREEK	G		E	E	G	E		F	E	G	E			G	G	G	G		G		G	G		
P 1 4718 4989	150	CONT ST 8EAM	BEAVER CR	G		G	F		G	G	F	F	G	G			F	F	F	G	G	G	F	F	G		
P 1 4718 5004	114	T T TRESTLE	8EAVER CR OF	G	G	G			G		G	F	G		P			G	F	G	G	G		F	G		X
P 1 4718 5009	190	T T TRESTLE	8EAVER CR OF	G	F	F			G		F	F	G		G			G	F	G	F	G		P	G		
P 1 4718 5013	133	T T TRESTLE	8EAVER CR OF	G	G	G			G		G	F	G		G			G	G	G	G	G		P	G		
P 1 4718 5019	38	T T TRESTLE	USRS CANAL	G	G	G		G	F		G	F	G		G			F	F	G	G	G		P	G		

A	FEET E	C	D	E	F	G	H		J	K	L	M	N	O	P	Q	R	S	T	U	V	W			Z	Z	Z2
P 1 4718 5066	38	T T TRESTLE	USRS CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 1 4718 5088	172	PRE CONC BEAM	BEAVER CR	F		G	G	G	G	G	G	G	G				G	G	G	G	G	G		G	G		
P 1 4718 5145	355	PRE CONC BEAM	MILK R	G		E	E	E	E	E	G	G	G	E			E	E	E	E	E	E	G	G	E		
P 1 4718 5147	144	PRE CONC BEAM	MILK R OF	G		E		E	E		G	G	G	E			E	E	E	E	E	E		G	E		
P 1 4718 5156	76	T T TRESTLE	MILK R OF	G	G	G			G		G		G		G			G	G	G	G	G		F	G		
P 1 4718 5157	38	T T TRESTLE	CANAL	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P 1 4718 5178	95	T T TRESTLE	CANAL	G	G	G			G		G		G		G			G	G	F	G	G		F	G		
P 1 4718 5200	19	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		
P 1 4718 5223	95	T T TRESTLE	BEAR CR OF	G	G	G			G		G	G	G		P			G	G	G	G	G		G	G		X
P 1 4718 5225	114	T T TRESTLE	BEAR CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P 1 4718 5258	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 1 4718 5270	95	T T TRESTLE	UNGER CR	G	G	G			G		G	G	G		G			F	G	G	G	F		G	G		
P 1 4718 5281	152	T T TRESTLE	LIME CR	G	G	G			G		G	G	G		G			G	G	G	G	G		P	G		
P 1 4718 5333	95	T T TRESTLE	CHAPMAN COULEE	G	G	G			G		G	G	G		G			G	G	F	G	F		P	G		
P 1 4718 5342	95	T T TRESTLE	MOONEY COULEE	G	G	G			G		G	G	G		P			G	G	F	G	F		P	G		X
P 1 4718 5375	57	T T TRESTLE	RICHARDSON COU	G	G	G			G		G	G	G		G			F	G	G	G	F		P	G		
P 1 4718 5380	57	T T TRESTLE	ONEIL CR	G	G	G			G		G	G	G		G			G	G	F	G	F		P	G		
P 1 4718 5398	114	T T TRESTLE	CHERRY CR OF	G	G	G			G		G	G	G		F			F	G	G	G	F		P	G		
P 1 4718 5402	114	T T TRESTLE	CHERRY CR	G	G	G			G		G	G	G		G			F	G	F	G	F		F	G		

				B		D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
P	1	5416	5461	38	T T TRESTLE	GOUDGE COULEE	G	G	G		G	G		G		G		F			G	G	G	G	G		F	G		
P	1	5416	5484	50	T T TRESTLE	WHATLEY CR	G	G	G		G	G		G		G		G			G	G	G	G	F		P	G		
P	1	5416	5513	57	T T TRESTLE	ESPEIL COULEE	G	G	G		G	G		G		G		F			F	G	G	G	G		F	G		
P	1	5416	5518	95	T T TRESTLE	SPRING CR	G	G	G		G	G		G		G		G			G	G	G	G	F		P	G		
P	1	5416	5565	152	CONT CONC T BM	PORCUPINE CR	F		G	G		G	G	F	G	G	G			G	G	F	G		G		P	G		
P	1	5416	5573	120	CONT CONC T 8M	PORCUPINE CR OF	F		G	G		G	G	G	G	G	G			G	G	F	G		G		P	G		
P	1	5416	5717	204	PRE CONC BEAM	LIT PORCUPINE CR	F		G	G		G		G	G	G	G			G	G	G	G		G		P	G		
P	1	5416	5727	25	T T TRESTLE	INDIAN SERV CA	F	G	G		G	G		G		G		F			G	G	G	G	G		F	G		
P	1	5416	5795	63	T T TRESTLE	OSWEGO CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
P	1	5416	5819	57	T T TRESTLE	FLYNN CR	G	G	G		G	G		G		G		G			F	G	G	G	G		P	G		
P	1	5416	5888	152	CONT CONC T BM	WOLF CR	F		G	G		G	G	G	G	G	G			G	G	F	G		G		P	G		
P	1	5905	5916	63	T T TRESTLE	MOSQUITO CR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	1	5905	5926	100	T T TRESTLE	LITTLE WOLF CR	G	G	G		G	G		G	G	G		G			G	G	G	F	G		F	G		
P	1	5972	6013	120	CONCRETE T BEAM	TULE CR	F		G	G		G	G	G	G	G				G	G	G	G		G		G	G		
P	1	5972	6110	294	STEEL GIRDER	POPLAR R	G		G	G		G	G	G	P	G	G			P	F	G	G		G	P	F	F		X
P	1	5972	6264	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	1	5972	6291	75	T T TRESTLE	BOX ELDER CR	F	G	F		G	G		G	G	G		P			G	G	G	G	F		F	G		X
P	1	5972	6312	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	5972	6323	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		

PLANNING SURVEY [illegible]

				FEET			E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z
P	1	5972	6391	163	CONT ST GIRDER	BIG MUDDY R	G		G	G	G	G	G	G	G	G	G			F	G	G	G	F		P	G	G		X
P	1	6445	6456	57	T T TRESTLE	SHEEP CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	6445	6483	90	CONT CONC SLAB	CLOVER CR	F		E			E		G	G	G					E	G	E		E		G	E		
P	1	6445	6590	76	T T TRESTLE	SHOTGUN CR	G	G	G			G		G		G		G			F	G	G	G	F		F	G		
P	1	6671	6672		UNDERPASS	GN RY	G		G		G	G					G				G		G		G		G	G		
P	1	6671	6673	433	WELDED PL GIR	MID FK FLATHEAD	G		G	G	G	G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
P	1	6674	6675		UNDERPASS	GN RY	G				G	G											G	G	G		P	G		
P	1	6674	6698	140	PRE CONC BEAM	TWO MEDICINE CR	E		E	E	E	E		G		G	E			E	E		E	E	E		E	E		
P	2	0970	0970	321	PRE CONC BEAM	DE SMET INT	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	2	0970	0977		UNDERPASS	NP RY	G	F	F		F	F					G	G		G			G	F			P	F		
P	2	0970	1026		UNDERPASS	INT OR 430																							N	
P	2	1060	1061	65	PRE CONC BEAM	RATTLESNAKE CR	G	G			G	G		G	G	G	G	G		G			G	G	G		G	G		
P	2	1060	1079		UNDERPASS	NP RY																								
P	2	1060	1081		UNDERPASS*	E MISSOULA INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
P	2	1081	1126	354	CONT ST GIRDER	BIG BLACKFOOT R	G		G	G	G	G		G		G	G			G	G	F	G	G	G	G	F	G		
P	2	1126	1139	88	CONCRETE T BEAM	CMSTP&P RR																								
P	2	1126	1161		UNDERPASS*	TURAH INT-I 90	E		E	E	E	E					E			E	E	E	E		E	E	G	E		
P	2	1126	1162		UNDERPASS*	TURAH INT-I 90	E		E	E	E	E					E			E	E	E	E		E	E	G	E		

				TOTAL ENG FEET	MAXIM M P		END F	P ES	BENTS	P ERS	W NG WA LS	BA K WA LS	ICE BREAKERS	OR F	RIP RAP	SCOUR	G RA RS	S	TH	SH ES	CURBS	MARKE	DE K	BRAC	RA	E	P	GE E	N CE E	REV E S
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	2	1574	1574S		UNDERPASS*	W DRUMMOND INT	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	2	1575	1587S		UNDERPASS*	E DRUMMOND INT	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	2	1575	1588S		UNDERPASS*	E DRUMMOND INT	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	2	1891	1891		UNDERPASS	N D L INT I 90	G		E		E	E					E			E	E		E	E	E	G	G	E		
P	2	1891	1901	23	CONCRETE SLAB	COTTONWOOD CR	G		G		F	G		G		G					G	F	G	G	G			G		
P	2	1891	1920	130	CONT ST GIRDER	CLARK FORK	G		G	G		G	G	G	F	G	G			G	G	G	G	G	F	G	G	G		
P	2	1891	1926S	256	PRE CONC BEAM	S D L INT I 90	G		E		E	E					E			E	E		E	E	E	E	G	G		
P	2	2254	2258	36	CONCRETE SLAB	CLARK FORK	F		F	P	P	P		G		G					P		F	F	P			P		
P	2	2254	2259		UNDERPASS	NP RY	G		G		F	G					G			G		F	F	G			F	F		
P	2	2254	2260		UNDERPASS*	MONT S INT I 15	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
P	2	2258	2258		UNDERPASS*	MONT S INT I 15	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
P	2	2258	2280	33	CONCRETE SLAB	DRAINAGE	G		G	F	G	G		G		G					G	G	G	F	G			G		
P	2	2280	2441	6	T T TRESTLE	STOCKPASS	G	G	G		F		G		G		G	G			F	G	G	G				G		
P	2	2280	2449	6	T T TRESTLE	STOCKPASS	G	G	G		F		G		G		G	G			F	G	G	G				G		
P	2	2280	2467	7	T T TRESTLE	STOCKPASS	G	G	G		F		G		G		G	G			F	G	G	G	F		F	G		
P	2	2280	2469	95	T T TRESTLE	RADER CR	G	G	F		F	G		G	G	G		G			F	G	G	G	F		P	F		
P	2	2280	2472	7	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			F	G	G	F	F		P	G		
P	2	2481	1610		UNDERPASS	I90 SEP																							N	
P	2	2481	1611		UNDERPASS	I90 SEP																							N	

PLAN[illegible] [illegible] REPORT

		A		FEET B		D	E	F	G	H	I		K	L	M	N	O			R	S				W			Z		
P	2	2481	1642		UNDERPASS	CARDWELL INT I90																							N	
P	2	2481	1643		UNDERPASS	CARDWELL INT I90																							N	
P	2	2481	2492	38	T T TRESTLE	COLBERT CR	G	G	G		G	G		G		G		G			F	G	G	F	F		P	G		
P	2	2481	2517	7	T T TRESTLE	STOCKPASS	F	G	G		G	G		G	G	G		G			F	G	G	G	F		P	G		
P	2	2481	2526	76	T T TRESTLE	BIG PIPESTONE CR	F	G	G		G	G		G	G	G		G			F	G	G	G	F		P	G		
P	2	2481	2529	7	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	F		P	G		
P	2	2481	2530	113	CONCRETE T BEAM	NP RY	F		G		G	G					G				G	G	G	G	P			G		
P	2	2481	2580	64	CONC T BEAM	WHITETAIL CR																							N	
P	2	2909	2909	235	PRE CONC BEAM	INT I-90	G		E		E	E					E			E	E		E	E	E	G	E	E		X
P	2	2909	2915	220	CONT ST GIRDER	MADISON R	G		G	G		G	G	G	F	G	G			G	G	G	G	G	G	G	G	G		
P	2	2909	2922	100	CONCRETE SLAB	MID FK MADISON R	G		P		F	G		G	F	G					P	G	F	F	P		P	P		
P	2	2909	2928	80	CONCRETE SLAB	E FK MADISON R	G		P		P	G		G	F	G					P	G	F	F	P		P	P		
P	2	2909	2936	80	CONCRETE SLAB	REY CR	G		P		F	F		G		G					P	G	F	F	P		P	P		
P	2	2909	2959	77	CONCRETE T BEAM	SEP-CO RD	G		G		G	G					G				G	G	G	G	F			G		
P	2	2909	2960	343	CONCRETE T BEAM	NP RY	G		G			G					G			P	F	F	G	G	F	G	F	F		X
P	2	2909	2993	22	CONCRETE SLAB	DRAINAGE	E		G		G	E		E		E					G		E		G			E		
P	2	2909	3029	280	CONCRETE GIRDER	NP RY	F		F		P	G					E			G	F	G	G		P	G	G	G		
P	2	2909	3038	41	CONCRETE T BEAM	CAMP CR	E				G	E		E	G	G	E				G	E	G		G			E		
P	2	2909	3040	52	CONCRETE T BEAM	BAKER CR	E		E	E	E	E	G	E	G	G	E				G	E	E		G			E		

				TOTAL LENGTH FEET			END FLOORS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSSES	SHOES	CURBS	MARKERS	DECK						NOT	REM
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	2	2909	3055	247	STEEL GIRDER	W GALLATIN R	G		E	E	E	E	E	G	E	G	E			E	E	E	G	E	E	E	G	E		
P	2	2909	3175	19	T T TRESTLE	DRAINAGE	G	E	E		E	F		E		E		E			E	E	E	E	G		F	E		
P	2	2909	3192	209	CONCRETE T 8EAM	NP RY	G		G		G	E					G			N	P	G	G		F	G		G		
P	2	2909	3198	245	PRE CONC 8EAM	W 8OZEMAN INT 90	E		E		E	E					E			E	E		E	E	E	E	E	E		
P	2	2909	3198P	245	PRE CONC 8EAM	W 8OZEMAN INT 90	E		E		E	E					E			E	E		G	E	E	E	E	E		
P	2	3466	3466		UNOERPASS*	W INT- I 90	G		G		G	G					G			G	G	G	G	G	F	F	F	G		
P	2	3466	3467		UNDERPASS*	W INT- I 90	F		G		G	G					G			G	G	G	G	G	G	F	F	G		
P	2	3490	3507	500	CONT ST GIROER	YELLOWSTONE R	G		F	F	F	G	F	F		P	G			F	F	F	P	G	P	F	F	F		
P	2	3490	3528	279	CONT ST GIROER	E INT- I90	G		G		G	G					G			G	G	G	F	G	G	F	G	G		
P	2	4387	4387		UNOERPASS*	PARK CITY INT 10	E		E					E		E					E							E		
P	2	4387	4388		UNOERPASS*	PARK CITY INT 10	E		E					E		E					E							E		
P	2	4387	4389	34	STEEL I BEAM	8IG DITCH	G		G		F	G		G		G		G			G	G	G		G		P	G		
P	2	4387	4392	27	STEEL I 8EAM	COVE IRR DT	G		G		G	G		G		G		G			P	G	G		P		F	G		
P	2	4387	4409	25	STEEL I 8EAM	COVE IRR DT	G		G		G	G		G		G		G			G	G	G		P		F	G		
P	2	4387	4426	63	CONCRETE T BEAM	8IG OITCH	F		F		F	F		G		G	G				G	G	G		G			F		
P	2	4467	4500	269	STEEL GIROER	NP RY	G		C			F					G			P	G	F	F		G	P	P	P		X
P	2	4467	4503		UNOERPASS	INT-I 90	G		E			E					E			E	E						E	E		
P	2	4467	4504		UNOERPASS	INT-I 90	G		E			E					E			E	E						E	E		
P	2	4595	4595		UNDERPASS*	W 8ILLINGS INT	E		E			E					E			E	E						E	E		

		A		B		D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z		
P	2	4595	4595A		UNDERPASS	W BILLINGS INT	E		E			E					E			E	E						E	E		
P	2	4595	4596		UNDERPASS	W BILLINGS INT	E		E			E					E			E	E						E	E		
P	2	4595	4596A		UNDERPASS*	W BILLINGS INT	E		E			E					E			E	E						E	E		
P	2	4595	4598		UNDERPASS	SEP OR 305	G		E			E					E			E	E						E	E		
P	2	4595	4598A		UNDERPASS	SEP OR 305	G		E			E					E			E	E						E	E		
P	2	4595	4599		UNDERPASS	SEP OR 305	G		E			E					E			E	E						E	E		
P	2	4595	4599A		UNDERPASS	SEP OR 305	G		E			E					E			E	E						E	E		
P	2	4611	4613	1711	PRE CONC BEAM	NP RY & US BYP	F		E		F	E					E			E	G		G		G	G	G	G		X
P	2	4611	4613P	1711	PRE CONC BEAM	NP RY & US BYP	F		E		F	E					E			E	G		G		G	G	G	G		X
P	2	4682	4688	63	T T TRESTLE	FIVE MILE CR	G	G	G			G		G	G	G		G			F	G	G	G	G		G	G		
P	2	4682	4695	67	T T TRESTLE	BL&I IRR DT	G	G	G	G		G		G	G	G		G			G	F	G	G	G		G	G		
P	2	4682	4699	11	T T TRESTLE	STOCK PASS	G	G	G		G	G						G			G		G	G	G		G	G		
P	2	4682	4704	59	T T TRESTLE	BL&I IRR DT	G	G	G	G		G		G	G	G		G			F	G	G	G	G		G	G		
P	2	4682	4705	11	T T TRESTLE	STOCK PASS	G	G	G		G	G						G			F		G	G	G		G	G		
P	2	4682	4710	25	T T TRESTLE	SEVEN MILE CR	G	G	G			G		G	G	G		G			F	G	G		G		G	G		
P	2	4682	4748	100	T T TRESTLE	TWELVE MILE CR	G	G	G			G		G		G		G			F	F	G	G	G		F	G		
P	2	4682	4770	1022	STEEL GIRDER	YELLOWSTONE R	G		G	G		G	G	G	G	G	G			G	G	G	G	G	F	F	P	G		
P	2	4682	4805	25	STEEL I BEAM	CUSTER COU	G		G		G	G		G		G		G			G	G	G	G	G			G		
P	2	4682	4814	14	CONCRETE SLAB	DRAINAGE	G		G			G		G	G	G		G					G				P	G		

				FEET B	C		E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	2	4682	4869	24	STEEL I BEAM	ARROW CR.	G		F		F	F		G		G		G					G		F		P	G		X
P	2	4682	4941	268	ST. PONY TRUSS	NP RY	F		F			G					G	G	G	F	F	F	G	G	G	F	P	G		X
P	2	4682	4943	259	CONT STEEL BM	INT I-94																							N	
P	2	5383	5383R		UNDERPASS	HYSHAM INT I 94	E		G			E					E			E							E	E		
P	2	5383	5413	25	T T TRESTLE	IRR DT	F	G	G			G		G		G		G			F		G	G	G		F	G		
P	2	5383	5425	19	T T TRESTLE	STOCKPASS	F	G	G		P	G		G		G		F			P		G	G	P		P	G		X
P	2	5383	5428	19	T T TRESTLE	DRAINAGE	G	G	G		F	G		P		G		G			F		G	G	G		F	G		
P	2	5383	5442	57	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			F		G	G	F		F	G		
P	2	5383	5446	38	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		F			G		G	G	F		F	G		X
P	2	5383	5451	95	T T TRESTLE	SARPY CR	G	G	G	G		G	G	G		G		F			F	G	G	G	F		F	G		X
P	2	5383	5456	38	T T TRESTLE	DRAINAGE	F	G	G			G		G	P	G		F			G		G	G	F		G	G		X
P	2	5383	5460	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		F			G		G	G	F		G	G		X
P	2	5383	5491	76	T T TRESTLE	IRR DT	F	G	G			G		G		G		F			G		G	F	F		G	G		X
P	2	5383	5502	19	T T TRESTLE	STOCKPASS	F	G	G		P	F						G			F		G	G	F		G	G		
P	2	5383	5507	57	T T TRESTLE	IRR DT	G	G	G			F		G		G		F			G		G	G	F		F	G		X
P	2	5383	5508	19	T T TRESTLE	STOCKPASS	F	G	G			G		G		G		G			G		G	G	F		F	G		
P	2	5383	5511	19	T T TRESTLE	STOCKPASS	F	G	G			G		G	F	G		G			F		G	G	G		P	G		
P	2	5383	5536	19	T T TRESTLE	DRAINAGE	F	G	G			G		G		G		G			G		G	G	G		G	G		
P	2	5383	5546	19	T T TRESTLE	DRAINAGE	G	G	G			F		G	G	G		G			F		G	G	F		F	G		

		A		B			E	F	G	H		J	K		M	N	O	P	Q	R					W			
P	2	53B3	5552	100	T T TRESTLE	RESERVATION CR	G	G	G	G		G	G	G	G	G		G			F	G	G	G	G		G	G
P	2	53B3	5566	19	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			F		G	G	F		F	G
P	2	53B3	5594	65	STEEL I BEAM	WYANT COV	F		G			G		G	G	G	G				F	G	G		F			G
P	2	53B3	5614	129	CONC T BEAM	ARMELLS CR	G		G	G		G	G	G	G	G	G				G	G	G		G			G
P	2	53B3	5630	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		G	G
P	2	53B3	5643	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		F	G
P	2	53B3	5655	89	STEEL I BEAM	SMITH CR	G		G			G		G	G	G	G				G	G	G		G		G	G
P	2	6096	6096	268	STEEL GIRDER	W INT-I 94	G		E			E					E			E	E		E		E		G	E
P	2	6096	6104	311	ST PLATE GIRDER	NP RY	G		G			G					G			G	G	F	G	G	G	G	G	G
P	2	6096	6118	300	STEEL GIRDER	TONGUE R	F		G	G		G	G	G	F	G	G	G		G	G	G	G	G	G	F	P	G
P	2	6123	6126		UNDERPASS	NPRY	F		F		F	F						G		G	F	F		G	F		F	F
P	2	6146	6161	168	PRE CONC BEAM	BAKER INT-I 94	G		E			E					E			E	G		E		E	G	G	E
P	2	6161	6169	57	T T TRESTLE	KIRCHER CR	G	G	G			F		G	F	G		G			G	G	G	G	G		G	G
P	2	6161	6186	57	T T TRESTLE	DRY WASH	F	G	G			F		G	F	G		G			G		G	G	G		G	G
P	2	6161	6194	76	T T TRESTLE	BENSLEY CR	G	G	G					G	G	G		G			G	G	G	G	F		G	G
P	2	6161	6243	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		G	G
P	2	6161	6274	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G		G	G	G		G	G
P	2	6161	6291	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		F	G
P	2	6161	6298	76	T T TRESTLE	MEADOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G

	NUMBER A			TOTAL FEET B	C	D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	Q	R	CURBS S	T	U	V	W	X	Y	Z	Z	Z2
P	2	6161	6305	76	T T TRESTLE	ASH CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P	2	6161	6322	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G		G	G	G		F	G		
P	2	6161	6328	38	T T TRESTLE	LI COTTONWOOD CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	2	6161	6336	7	T T TRESTLE	STOCKPASS	G	G	F		G	G						G			G		G	G	G		F	G		
P	2	6161	6340	76	T T TRESTLE	COTTONWOOD CR	G	G	G			F		G		G		G			G		G	G	G		G	G		
P	2	6161	6374	57	T T TRESTLE	S FK SMITH CR	G	G	G			G		G	F	G		G			G		G	G	G		F	G		
P	2	6161	6380	95	T T TRESTLE	SMITH CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	2	6161	6402	57	T T TRESTLE	DRY WASH	G	G	G			G		G		G		G			G		G	G	F		P	G		
P	2	6161	6417	76	T T TRESTLE	SMITH CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	2	6161	6419	554	STEEL TRUSS	POWDER R	F		F	F		G	G	G	G	G		G	F	F	G	G	G	P	G	F	P	F		
P	2	6161	6688	200	STEEL GIRDER	O FALLON CR	G		G	G		G	G	G	G	G		G		G	G	G	G	G	G	F	F	G		
P	2	6161	6716	57	T T TRESTLE	HAY CR	G	G	G			G		G	F	G		G			G	G	G	G	G		G	G		
P	2	6161	6779	140	STEEL GIRDER	SANDSTONE COU	G	N	G	F	F	F	G	G	G	F	G	N	N	G	F	G	G	N	F	F	F	F		
P	2	6161	6807	133	STEEL GIRDER	SANDSTONE CR	F	N	G	F	G	G	G	G	G	F	G	N	N	G	F	G	G	N	F	F	F	F		
P	2	6161	6823	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	F	G		
P	2	6161	6829	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	F	G	G	N	G	N	N	G	G	G	G	F	N	F	G		
P	2	6161	6847	50	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	P	G		
P	2	6161	6859	19	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	P	G		
P	2	6161	6863	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	F	N	G	G	G	N	G	N	N	G	G	G	G	G	N	P	G		

PLANNING SURVEY [illegible]

			A	FEET B		C	E	F	G	H		J	K		M	N	O	P		R	S			V	W				
P	2	6161	6874	76	T T TRESTLE	TIMBER CR	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	P	G	
P	2	6161	6898	57	T T TRESTLE	RED BUTTE CR	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G	
P	2	6161	6914	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	P	G	
P	2	6161	6924	57	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	F	N	G	N	N	G	G	G	G	G	N	F	G	
P	2	6930	6956	213	PRE CONC BEAM	CMSTP&P RR	E	N	E	N	E	E	N	N	N	N	E	N	N	E	E	N	E	N	E	N	G	E	
P	2	7060	7062	162	STEEL GIRDER	BA&P CMSTP&P RR	G		G			G					G			G	G	G	G	G	G	G	F	G	
P	2	7060	7068		UNDERPASS	CMSTP&P RR	G		G		G	G					G			G		G	G	G	G		F	G	
P	2	7081	7083		UNDERPASS	NP RY	G		G		G	G					G			G		G	G	G	G		F	G	
P	2	7081	7096		UNDERPASS*	HARRISON AVE INT	E		E		E	E					E			E	E		E	E	E	G	F	E	
P	2	7081	7096A		UNDERPASS	HARRISON AVE INT	E		E		E	E					E			E	E		E	E	E	G	F	E	
P	2	7096	7096		UNDERPASS*	HARRISON AVE INT	E		E		E	E					E			E	E		E	E	E	G	F	E	
P	2	7096	7096A		UNDERPASS	HARRISON AVE INT	E		E		E	E					E			E	E		E	E	E	G	F	E	
P	2	7128	7130S		UNDERPASS*	I 90 PTW-US 10			E								E			E	E		E					E	
P	2	7128	7131S		UNDERPASS*	I 90 PTW--US 10			E								E			E	E		E					E	
P	2	7145	7155		UNDERPASS	NP RY	G		G		G	G					G			G	F				G		F	G	X
P	3	1276	1290	157	STEEL BEAM	NP RY	F		G			G					G			P	P		G	G	F	G	G	F	X
P	3	1276	1291	158	T T TRESTLE	CLARK FORK	G	G	G			G		G		G		P			P		G	G	G			G	X
P	3	1276	1292	145	CONT STEEL BEAM	NP RY	G		F			G					G			P	P		G	G	G	G	G	G	X

	A			FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	3	1276	1299	126	STEEL GIRDER	GN RY	G		G			G					G			G	G	G	G	G	G	G	F	G		
P	3	1276	1300	25	CONCRETE T BEAM	DRY WASH	G		G		G	G		F	G	G	G				G	G	G	G	G			G		
P	3	1935	1935	261	STEEL GIRDER	CAPITOL INT-I 15	G		E		E	E					E			F	E		E	E	E	G	G	G		X
P	3	1935	1935P	261	STEEL GIRDER	CAPITOL INT-I 15	G		E		E	E					E			F	E		E	E	E	G	G	G		X
P	3	1958	1960	83	CONCRETE T BEAM	GN RY	G		G		G	F					F				G	G	G	G	G			G		
P	3	1958	1961	119	CONCRETE T BEAM	NP RY	G		F		P	P					G			G	G	G	G	F	G			F		X
P	3	1966	1972	23	STEEL & CONC	HELENA VALLEY CA	G		G		G	G		G		G					G	G	G	G	G		G	G		
P	3	1966	1978	67	CONCRETE T BEAM	TEN MILE CR	G		G		F	G		G		G	F			G	G	G	G	G	G			G		
P	3	1966	2036	205	PRE CONC BEAM	LINCOLN INT-I 15	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
P	3	2620	2620S		UNDERPASS*	S CASCADE INT	P		G		G	G					G			G	G		G		G		G	G		
P	3	2620	2637S		UNDERPASS*	N CASCADE INT	F		G		G	G					G			G	G		G		G		G	G		
P	3	2877	2878	396	STEEL TRUSS	SUN R	G		G	G	G	G		G		G		F	F	F	P	P	P	F	P	F	C	P		X
P	3	2877	2882		UNDERPASS	GN RY	G		G		G	G					G	G		F	G		G				P	G		
P	3	2889	2921		UNDERPASS*	EMERSON JCT INT	G		G		G	G					G	G		G			G		G					
P	3	2921	2921		UNDERPASS*	EMERSON JCT INT	G		G		G	G					G	G		G			G		G					
P	3	2996	2996	219	STEEL GIRDER	VAUGHN INT-I 15	G		G		G	G					G	G		G	G		G		G	G	G	G		
P	3	2996	2997	138	CONCRETE T BEAM	CMSTP&P RR-GN RY	F		G		G	G					G	G		G	G	G	G	G	G	F	G			
P	3	2996	2998	146	CONCRETE GIRDER	MUDDY CR	G		G	G	G	G	G	G	G	G	G	G		G	G	G	G		G	G	G	G		
P	3	3070	3074	19	T T TRESTLE	IRRIGATION CANAL	P	G	G		G	G						N			G	G	G	N	G		G	G		

		A		B	C		E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	
P	3	3070	3079	76	T T TRESTLE	MILL COULEE CR	G	G	G		G	G		P	F	G		G			G	G	G	G	G		G	G	
P	3	3070	3100	76	T T TRESTLE	MILL COULEE CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P	3	3070	3135	25	T T TRESTLE	ASHUELUT CANAL	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G	
P	3	3070	3144	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G	
P	3	3070	3169	60	PRE CONC BEAM	GREENFIELD S CA	G		G		G	G		G	G	G	G			G	G	G	G		G		G	G	
P	3	3070	3199	57	T T TRESTLE	IRRIGATION CA	G		G		G	G		G		G	G				G	G	G	G	G		G	G	
P	3	3070	3335	11	T T TRESTLE	STOCKPASS	G	G	G		G	G					G				G	G	G	G	G		G	G	
P	3	3070	3342	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						F			G	G	G	G	G		G	G	X
P	3	3070	3348	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G	
P	3	3070	3358	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G	
P	3	3070	3378	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G	
P	3	3070	3385	227	ST PONY TRUSS	TETON R	G		G	G	G	G	G	G	G	G		G	G	F	F	G	F	G	P		F	G	X
P	3	3402	3495	20	CONCRETE SLA8	DRAINAGE	G	G	G		G	G		G		G		S			G	G	G		G		G	G	
P	3	3402	3525	45	T T TRESTLE	FOSTER CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	3	3402	3546	285	T T TRESTLE	BIG MUDDY CR	G	G	G		G	G		P	F	G		G			G	G	G	G	F		G	G	
P	3	3402	3567	57	T T TRESTLE	JONES COU	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P	3	3402	3582	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	3	3402	3588	57	T T TRESTLE	DRAINAGE	G	F	G		G	G		G		G		G			G	G	G	G	F		G	G	X
P	3	3402	3592	38	T T TRESTLE	8YNUM CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	

				FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	3	3402	3622	57	T T TRESTLE	FARMERS COU	G	G	G		G	G		G		G		G			G	G	G	G	F		G	G		
P	3	3402	3643	38	T T TRESTLE	WALENSTEIN COU	G	P	P		P	P			F			G			P	G	F	G	P		P	P		
P	3	3402	3653	9	T T TRESTLE	STOCKPASS	G	P	P		P	P						F			P	P	F	P			F	P		X
P	3	3402	3675	114	T T TRESTLE	HINES COU	G	G	G		G	G						G			G	G	G	G	F		F	G		
P	3	3402	3697	57	T T TRESTLE	DRY FK MARIAS R	G	G	G		G	G			F	G		G			F	G	G	G	G		G	G		
P	3	3402	3699	75	T T TRESTLE	DRY FK MARIAS R	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	3	3402	3725	95	T T TRESTLE	MATCHETT COU	G	G	G		G	G				G		G			G	G	G	G	G		G	G		
P	3	3402	3743	190	UNT T TRESTLE	DUPUYER CR	F	F	F		F	F		F		F		F			P	F	F	F	P		P	F		
P	3	3402	3746	122	PRE CONC BEAM	DUPUYER CR OF	E		E	E	E	E	E	G	E	G	E			E	E	G	E	E	E		E	E		
P	3	3402	3749	57	UNT T TRESTLE	SHEEP CR	G	P	P		P	F		G		G		F			P	G	F	P	P		P	P		
P	3	3402	3778	82	PRE CONC BEAM	VALIER CANAL	E		E	E	E	E	E	E		G	E			E	E	E	E	E	E		E	E		
P	3	3402	3823	18	UN TR TRESTLE	DRAINAGE	F	P	P		P	P			F	P		P			F	G	G	G	G		G	P		X
P	3	3402	3842	213	PRE CONC BEAM	BIRCH CR	E		E	E	E	E	E	G	E	G	E			E	E	G	E	E	E		E	E		
P	3	3402	3861	142	PRE CONC BEAM	BLACKTAIL CR	E		E	E	E	E	E	E	E	G	E			E	E	E	E	E	E		E	E		
P	3	3402	3952	70	PRE CONC BEAM	AGENCY CR	E		E		E	E		E	E	E	E			E	E		E	E	E		E	E		
P	3	3402	3955	306	PRE CONC BEAM	BADGER CR	E		F	E	E	E	E	G	E	G	E			E	E	G	E	E	E	E	E	E		
P	3	3402	4007	265	STEEL GIRDER	TWO MEDICINE CR	P		G	G	G	G	G	P		G	E			G	G	F	G	E	G	G	F	G		
P	3	3402	4014	50	T T TRESTLE	TWO MEDICINE CA	G	G	G		G	G	G	F		G		G			G	F	G	G	F		P	G		
P	3	4116	4160	16	ST GIR	DRAINAGE	G		G		G	G		G		G	G				G	G	G				P	G		

PLANNING SURVEY LIST OF CONDITION REPORT

P	3	4250	4254	42	CONCRETE ARCH	DRAINAGE	G				F	G		F		G	G					G	G	G	P			G	
P	3	4250	4259	53	CONCRETE ARCH	S FK CUT BANK CR	G				F	G		G		G	G					G	G	G	F			G	
P	3	4250	4302	120	STEEL TRUSS	N FK CUT BANK CR	F		F		G	G		F		P		G	G	G	F	F	G	G	G	P	P	G	X
P	3	4250	4340	48	CONCRETE ARCH	DRAINAGE	F					G		G		G	G					G	G	G	P			G	X
P	3	4250	4516	312	CONT ST GIRDER	ST MARYS R	G		G	G		G	G	G	G	G	E			G	G	F	G	G	G	G	F	G	X
P	3	4250	456B	122	PRE CONC BEAM	KENNEDY CR	E		E	E	E	E	E	G	E	G	F			E	G	G	E	G	E	G	G	E	
P	3	4646	4655	2093	STEEL GIRDER	MISSOURI R-GN RY	F		G	G	G	G	G	G		G	G	G		G	G	G	F		G	G	P	G	X
P	4	0000	0005	57	T T TRESTLE	USRS FRANNIE CA	G	G	G			G		G		G		G			G	G	G	G	G		G	G	
P	4	0000	0042	76	T T TRESTLE	SAGE CR	G	G	G		G	G	G	G		G		P			G	G	G	G	G		F	G	X
P	4	0000	0121	142	CONCRETE T BEAM	CB&Q RR	G		G			G					G				G		G		G			G	
P	4	0000	0225	19	T T TRESTLE	DRAINAGE	G	G	G		F	G		G		G		G			F		G		G		G	G	
P	4	0000	0235	57	T T TRESTLE	BRIDGER CR	G	G	G			F		G		G		F			G		G	G	G		F	G	X
P	4	0000	0237	300	STEEL GIRDER	CLARK-FK YELLO R	G		G	G		G	G	G		G	G			G	G	G	G	G	G	G	F	G	
P	4	0000	0242	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			F		G		G		F	G	
P	4	0000	0245	19	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			G		G		G		G	G	
P	4	0247	0256	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	F	G		F			F		G		F		F	G	
P	4	0247	0290	57	T T TRESTLE	SAND CR	F	G	G			F		G	F	G		G			G		G	P	F		F	G	X
P	4	0247	0306	19	T T TRESTLE	DRAINAGE-STK	G	G	G		G	G						G			F		F		F		F	G	

				FEET B	C		E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	4	0247	0424	139	CONCRETE T BEAM	ROCK CR	E		E			E		E	E	E	E			G	E		G		E			E		X
P	4	0427	0526		UNDERPASS	NP RY	G		G		G	G					G	G		G	G	G					G	G		
P	4	0427	0529	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G		G		E	G		
P	4	0427	0535	496	STEEL TRUSS	YELLOWSTONE R	G		F	F		F	G	G		G			G	G	G	G	G	G	F		F	G		X
P	4	0427	0541		UNDERPASS*	LAUREL INT-I 90	E		E			E					E			E	E							E		
P	4	0541	0541		UNDERPASS*	LAUREL INT-I 90	E		E			E					E			E	E							E		
P	4	0541	0545		UNDERPASS	NPRY	G		G		P	G					G	G			P				F		P	G		X
P	5	0000	0000	321	PRE CONC BEAM	DE SMET INT I90	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	5	0000	0096	173	PRE CONC BEAM	NP RY	G		G	E	E	E					E			E	E	F	E		G		C	G		
P	5	0000	0189	104	CONCRETE T BEAM	JOCKO R	F		G			G		G		G	F				G	G	F		G		F	G		X
P	5	0275	0377	51	CONCRETE T BEAM	POST CR	G		G		G	G		F	F	G	G				G	G	G		G		G	G		
P	5	0275	0407	76	T T TRESTLE	NINE PIPES RES	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
P	5	0275	0510	20	CONCRETE SLAB	DRAINAGE	G		G		G	G		G		G						G	G		F			G		
P	5	0275	0570	82	CONT CONC T BM	PABLO FEEDER CA	G	G	G		G	G		G	G	G	G			G	G	G	G		G		P	G		
P	5	0590	0611	1536	PRE CONC BEAM	FLATHEAD R	G	G	G		G	G		G	G	G	G			G	G		G		G	G	G	G		
P	5	0775	0823	61	CONCRETE T BEAM	DAYTON CR	F		F		G	G		G	F	G	G				F	G	F		F			F		
P	5	1126	1161	155	CONCRETE T BEAM	STILLWATER R	F		G	G	G	G	G	G		G	G			G	G	F	G		G	G	F	G		
P	5	1254	1281	215	STEEL BEAM	WHITEFISH R	G		P		G	G		G		G	G			P	G		G	G	P	P	F	F		X

							E	F		H				L	M	N	O			R	S	T	U		W			Z	Z1	Z2
		A																												
P	5	1254	1447		UNDERPASS	GN RY	G		G		G	G					G			G			G				F	G		
P	5	1254	1580	60	CONCRETE T BEAM	STILLWATER R	F		G	G	G	G		G		G	G				G	P	G		G		F	G		
P	5	1254	1702	57	CONCRETE T BEAM	GRAVES CR	F		G	G	G	G	G	G		G	G			G	G	G	G		G			G		
P	5	1254	1705	43	CONCRETE T BEAM	DRAINAGE	F		F		G	G		F		G	G				G	G	G		G			G		
P	5	1809	1822	11	T T TRESTLE	DRAINAGE	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	5	1809	1843	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	5	1809	1870	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	6	0000	0109	162	STEEL GIRDER	BULL R	E		E			E	E	E	E	E	E			E	E	G	E	E	E	E	P	E		
P	6	0000	0127	346	STEEL GIRDER	NPRY	E		E		E	E					E			E	E		E	E	E	E	P	E		
P	6	0000	0170	315	CONT D PL GIR	NP RY	E		E	E	E	E					E			E	E	C	E	E	E	E	P	E		
P	6	0000	0281	1061	CONT D PL GIR	CLARK FORK	G		E	E	E	E	E	E		E	E	E	E	E	E		E	E	E	E	P	E		
P	6	0000	0313		UNDERPASS	NP RY	G		G	G		G					E			E		G	G		E		P	E		
P	6	0000	0335	230	STEEL BEAM	BEAVER CR	F		G	G	F	G		G		G	G			G	C	G	F		P		G	F		X
P	6	0000	0492	949	RIV PL GIRDER	CLARK FORK	G		E	E		E	E	E		E	E	E		E	E	G	F		E	F	P	E		
P	6	0000	0533	156	STEEL GIRDER	NP RY	G	G	F	G	F	G						F			P	G	F	G	F	F	P	F		
P	6	0000	0562	427	STEEL TRUSS	THOMPSON R	G		G	G	G	G				G	G	G	G	G	F	G	G	G	F	G	P	G		
P	6	0000	0730	83	CONCRETE T BEAM	LYNCH CR	G		G	G	F	G	G	G	G	G	G					F	F		P			F		
P	6	0766	0767	51	CONCRETE T BEAM	BOYER CR	G		G	G	F	G		G	G	G	G				G	G	G		G			G		

PLANNING SURVEY BRIDGE CONDITION REPORT

[illegible]

CONTROL BRIDGE NUMBER A	TOTAL LENGTH FEET B	MAXIMUM SPAN C	NAME OF FEATURE D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BR V	RAILINGS W	EXPANSION X	PAINT Y	GENERAL CONDITION Z	NOT INSPECTED Z1	REMARKS Z2
P 6 0766 0827	970	STEEL TRUSS	CLARK FORK	G		G	G		G	G	G	P	G	G	G	G	G	G	F	G	G	F	F	C	F		X
P 6 0766 0848	455	STEEL TRUSS	CLARK FORK	F		E	E	G	E	E	E	P	E		E	E	E	E	G	G	E	E	E	G	E		
P 6 0766 0923	31	STEEL I BEAM	SEEPAY CR	G		G		G	G		G		F	G	G			E	G		E		G		G		
P 6 0766 1012	39	STEEL I BEAM	MAGPIE CR	G		G		G	G		G		F	G				E	G	G		E		G	E		
P 6 0766 1059	19	CONCRETE SLAB	REVALS CR	G		P		F	P		G	G	G	G				G	G	G	G		F	F			X
P 6 0766 1159	332	CONCRETE T BEAM	NP RY & JOCK R	G		G	G	G	G	G	G		G	G			G	G	G	G	G	G	G		G		
P 7 0001 0106	7	TT TRESTLE	ANDREWS CR STK	G		G		F	G		G		G						C	G		F		C	G		
P 7 0001 0129	140	STEEL BEAM	E FK BITTERROOT	G		G	G		G		G		G		G		G	G	F	G	G	G	G	C	G		
P 7 0001 0155	130	CONT STEEL BEAM	E FK BITTERROOT	G		G	G		G		G		G		G		G	F	F	F	G	G	G	P	G		
P 7 0001 0181	130	CONT ST GIRDER	E FK BITTERROOT	G		G	G		G		G		G		G		G	P	F	G	G	G	G	C	G		
P 7 0001 0259	76	T T TRESTLE	RYE CR	G	G	G	G		G		G	F	F		G			G	F	P		F		C	F		X
P 7 0001 0264	182	PONY TRUSS	BITTERROOT R	G		G	F	G	G	F	G		G		G	G	G	G	F	G	G	P	G	C	G		
P 7 0001 0270	19	T T TRESTLE	DRAINAGE	G	G	G			G						G			F	F	G		P		C	G		
P 7 0001 0292	209	T T TRESTLE	FERN CR	G	G	G	G		G		G	F	G		G			F	P	G		F		C	G		
P 7 0001 0298	57	T T TRESTLE	TINCUP CR	F	G	G	G		G		G	P	G		G			P	P	F		F		C	F		
P 7 0001 0337	19	T T TRESTLE	DRAINAGE	G	G	G			G			F	G		G			F	P	G		P		C	G		
P 7 0001 0349	95	CONCRETE T BEAM	ROCK CR	P		G	G		G		F		F	G			G	G	F	G		G	F		G		
P 7 0001 0369	76	T T TRESTLE	LICK CR	G	G	G	G		G		G	G	G		G			F	F	G	G	F		C	G		

		A		B	C	D	E	F	G	H		J	K		M	N	O			R					W		Y		Z
P	7	0001	0377	137	CONCRETE T BEAM	LOST HORSE CR	F		G	G	G	G		G	P	F		G		G	G	F	G		G	G		G	
P	7	0001	0388	19	T T TRESTLE	DRAINAGE	G	G				G		G		G		G			F	P	G		F		C	G	
P	7	0001	0399	38	T T TRESTLE	CAMAS CR	G	G	G	G		G		G	G	G		G			G	P	G		F		C	F	
P	7	0001	0418	100	T T TRESTLE	GOLD CR	P	G	G	G		P			P	G		G			F	F	G	G	C		G	P	
P	7	0001	0436	300	STEEL GIRDER	BITTERROOT R	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G		G	
P	7	0445	0450	57	T T TRESTLE	SKALKAHO CR	F	G	G	G		P	G	F	P	F		G			F	G	G		F		F	F	
P	7	0445	0486	36	CONCRETE T BEAM	CORVALLIS CR	G		G			G		G		G	G				G	G	G		G			G	
P	7	0445	0495	392	CONT ST TRUSS	BITTERROOT R	G		G	G		G	G	G	G	G		G	G	G	G	G	G	G	G	G	G	P	G
P	7	0445	0499	25	T T TRESTLE	IRRIGATION CA	G	G	G			G		G	G	G		G			G	F	G		G		P	G	
P	7	0445	0503	49	T T TRESTLE	BLODGETT CR	G	G	G	G		G		F	G	G		G			F	F	F		G		P	G	
P	7	0445	0504	11	T T TRESTLE	STOCKPASS	G	G	G			G						G			G	F	F		G		P	G	
P	7	0445	0508	25	T T TRESTLE	MILL CR	G	G	G			G		G	G	G		G			G	F	F		G		P	G	
P	7	0445	0545	88	T T TRESTLE	SHEAFMAN CR	G	G	G	G		G		G	G	G		G			G	G	F		G		P	G	
P	7	0445	0570	100	T T TRESTLE	S FK BEAR CR	G	G	G	G		G		F	F	G		G			G	G	G	G	G		P	G	
P	7	0445	0583	38	T T TRESTLE	N FK BEAR CR	G	G	G	G		G		P	G	G		G			G	G	G	G	G		P	G	
P	7	0445	0597	81	T T TRESTLE	SWEATHOUSE CR	G	G	G	G		F		G	F	G		G			G	G	G	G	G		P	G	
P	7	0445	0616	114	T T TRESTLE	BIG CR	G	G	G	G		F		G	F	G		G			G	G	G		G		P	G	
P	7	0445	0650	38	T T TRESTLE	MCCALLA CR	G	G	G	G		G		G	G	G		G			G	G	G		G		P	G	
P	7	0445	0660	57	T T TRESTLE	MCCALLA CR	G	G	G	G		G		G	G	G		G			G	G	G		G		P	G	

PLANNING SURVEY BRIDGE CONDITION REPORT

		A		FEET B	C	D	END FILLS E	PILES F	BENTS G	PIERS H	I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	P	Q	SHOES R	S	T	U	V	W	X	Y	Z	Z1	REMARKS Z2
P	7	0445	0662	75	T T TRESTLE	KOOTENAI CR	E	G	G	G		G		G	G			G			G	G	G	G	G		P	G		
P	7	0445	0829	122	PRE CONC BEAM	LOLO CR																								X
P	7	0B35	0903	346	PRE CONC 8M	BITTERROOT R																							N	
P	7	0835	0903P	346	PRE CONC 8M	8ITTERROOT R																							N	
P	7	0940	0942	972	RIV PL GIRDER	CLARK FORK & RR	G		E	E	E	E	E	G	E	G	E	E		E	E		E	E	G	E	G	E		
P	7	0940	0942T	972	RIV PL GIRDER	CLARK FORK & RR	G		E	E	E	E	E	G	E	G	E	E		E	E		E	E	G	E	G	E		
P	7	0946	0958	209	CONCRETE T 8EAM	CMSTP&P RR	F		G	G		G					G			G	F		P		G	G	F	F		
P	7	0946	0959	503	DECK TRUSS	CLARK FORK	F		G	G		G	G	G	G	G		G	G	G	G		F	G	G	G	F	G		
P	7	0960	0965		UNDERPASS	NP RY	G		G		G	G					F			G	G		G	G	G	G	F	G		X
P	7	0960	0968		UNDERPASS	ORANGE ST INT-90	E		E		E	E					E			E	E		E	E	E		E	E		
P	7	0965	0971	552	ST PLATE GIRDER	CLARK FORK & RR	G		G	G	G	G	G	G	G	G	G	G		G	G		G	G	G	G	G	G		
P	8	0000	0062	462	STEEL GIRDER	LIT 8LFT R-NP RY	G		G	G		G	G	G		G	G			P	G	G	G	G	G	G	F	G		X
P	8	0000	0118	107	CONCRETE T BEAM	LIT BLACKFOOT R	F		P		G	F		G	F	G	F				P	G	G	F	P			P		X
P	8	0000	0132	95	CONCRETE T BEAM	LIT BLACKFOOT R	F		P		G	F		G	F	G	F				P	G	G	F	P			P		
P	8	0000	0222	59	CONCRETE T BEAM	LIT 8LACKFOOT R	F		P		G	F		G	F	G	F				P	G	G	F	P			P		X
P	8	0000	0369	102	CONCRETE T 8EAM	TENMILE CR	G		G		F	G		G	G	G	G			G	G	G	G	G	G			G		
P	8	0454	047B	149	CONCRETE T BEAM	GN RY	G		G			G					G			G	G	G	G	G	G	G		G		
P	B	0454	0479	212	CONCRETE T 8EAM	NP RY	G		G			G					G			G	F	G	G	G	G	G		G		

PLANNING [illegible] REPORT

A	B		D	E	F		H		J	K	L	M	N	O		Q	R	S				W			Z		
P 8 0454 0492	65	CONCRETE T 8EAM	PRICKLY PEAR CR	G		G		G	G		G		G	G				G	G	G	G	G			G		
P 8 0454 0592	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	F		G	G		
P 8 0454 0607	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	F		G	G		
P 8 0454 0763	500	CONT PL GIRDER	MISSOURI R	G		G	G		G	G	G		G	G	G		G	G	G	G	G	G	G	F	G		
P 8 0775 0788	22	CONCRETE SLAB	IRRIGATION CA	F		G		G	G		G		G					G	P	G	G	G			G		
P 8 0775 0800	66	CONCRETE T 8EAM	DEEP CR	G		F		G	G		G		G	G				G	P	F	G	G			F		
P 8 0775 0806	22	CONCRETE SLA8	DEEP CR OF	G		G		F	G		G		G					G	F	G	G	G			G		
P 8 0775 0872	22	CONCRETE SLA8	SIX MILE CR	G		G		G	G		G		G					G	F	G	G	G			G		
P 8 0775 0880	386	CONCRETE T 8EAM	NP RY	F		G			G					G			G	G	F	G	G	G	G	G	G		
P 8 0775 0882	690	STEEL GIRDER	MISSOURI R	G		G	G		G	G	G	G	G	G			G	G	F	G	G	G	G	F	G		
P 8 0775 1079	295	CONT CON GIRD	INT I90 FUTURE																							N	
P 8 1093 1095	206	PRE CONC 8EAM	GN RY	G		G		G	G					G			G	G		G	G	G		F	G		
P 8 1093 1095P	206	CONCRETE T BEAM	GN RY	G		F			G					G			G	G		G	F	G	G		G		
P 9 0000 0000	190	STEEL GIRDER	AUGUSTA RD INT	G		G		G	G					G			G	G	G	G		G	G	G	G		
P 9 0000 0130	294	RIV PL GIRDER	DEAR8ORN R	G		G	G	G	G	G	F	G	G	G			G	G	G	G		G	G	G	G		
P 9 0201 0236	57	T T TRESTLE	FLAT CR	F	G	G	G	G	G	G	G	F	G		G			G	G	G	G	G		G	G		
P 9 0201 0283	7	T T TRESTLE	STOCKPASS	G	G	F		G	G						G			G	C	G	G	C		G	F		X
P 9 0201 0287	7	T T TRESTLE	STOCKPASS	F	F	P		G	G						G			G	P	G		C			P		X

	FEET B		D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	ZZ
P 9 0201 0313	19	T T TRESTLE	STOCKPASS	P	G	G		G	P						G			G	G	G	G	G		G	G		
P 9 0201 0316	38	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	F	G		G	G		
P 9 0201 0321	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G				G			G	G	G	G	G		G	G		
P 9 0201 0326	38	T T TRESTLE	DRY CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 9 0201 0372	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 9 0201 0380	41	CONCRETE T BEAM	S FK SUN R	G		G		G	G		G		G		G			G	G	G		G			G		
P 9 0201 0381	57	T T TRESTLE	SLOUGH	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		X
P 9 0399 0401	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 9 0399 0431	315	STEEL GIRDER	N FK SUN R	P		G	G	G	G	G	P		G	G			G	G	G	G	G	G	G	F	G		
P 9 0399 0433	93	T T TRESTLE	FLOWEREE CANAL	G	G	G		G	G		G				G			G	G	G	G	G		G	G		
P 9 0399 0448	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 9 0399 0467	100	T T TRESTLE	USRS CANAL	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 9 0399 0586	57	T T TRESTLE	DRY WASH	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 9 0399 0596	19	T T TRESTLE	DRAINAGE	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 9 0399 0616	183	PRE CONC BEAM	DEEP CR	G		G	G	G	G	G	F	G	G	G			G	G	G	G		G	G	G	G		
P 9 0399 0618	7	T T TRESTLE	DRAINAGE	G	G	G		G	G		G				G			G	G	G	G	G		G	G		
P 9 0399 0635	200	T T TRESTLE	TETON R	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		G	G		
P 10 0002 0004	965	CONCRETE ARCH	MISSOURI R	G		F	F	F	F		F		G	P				P	G	P		P			P		X

A	B		D	E	F	G	H		J	K		M	N	O			R	S							Z	
P 10 0002 0006		UNOERPASS	GN RY	G		G		G	G					G			G	G		G		G		G	G	X
P 10 0008 0014		UNOERPASS	GN RY	G		G		G	G					G			G			G				G	G	
P 10 0008 0015		UNOERPASS	CMSTP&P RR	G		G		G	G					G			G			G				G	G	
P 10 0015 0020	1130	CONCRETE ARCH	MISSOURI R	F		F	F	F	F		G		G	F	G			C	G	P		P			P	X
P 10 0032 0403	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G	
P 10 0032 045B	126	CONCRETE T BEAM	GN RY	F		G		G	G					F			P	F	G	G		F	P		F	X
P 10 0032 0517	1151	CONT ST TRUSS	MARIAS R & GN RY	G		G	G	G	G	G	G		F	G	G	G	G	G	F	G	G	G	G	P	G	X
P 10 0032 0619	19	T T TRESTLE	STOCKPASS	G	G	G		F	G						G			F	G	G	G	F		G	G	
P 10 0032 0639	114	T T TRESTLE	SPRING COULEE	F	F	G		F	G		G		G		G			G	G	G	G	F		G	G	
P 10 0032 0690	95	T T TRESTLE	ORY COURSE	G	G	G		F	G		G	G	G		G			G	G	G	G	G		G	G	
P 10 0032 0699	95	T T TRESTLE	ORY COURSE	G	G	G		F	G		G	P	P		G			G	G	G	G	G		G	G	
P 10 0032 0727	95	CONCRETE T BEAM	GN RY	P		G		G	G					G				G	G	G		G	G		G	
P 10 0032 0829	95	T T TRESTLE	BIG SANOY CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P 10 0032 0849	57	T T TRESTLE	ORY COURSE	G	G	G		G	G		G	F	G		G			G	G	G	G	F		G	G	
P 10 0032 0897	76	T T TRESTLE	BOX ELDER CR	G	G	G		G	F	G	F	F	F		G			G	G	G	G	G		G	G	
P 10 0032 0996	95	T T TRESTLE	GRAVELLY COULEE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P 10 0032 1071	122	PRE CONC BEAM	BEAVER CR	E		E	E	E	E	E	E	E	E	E			E	E		E	E	E		E	E	
P 10 1120 1130	1126	RIV PL GIROER	MISSOURI R-GN RY	G		P	G	G	G	G	G		G	G	G		G	G	F	F		G	G	G	G	X
P 10 1120 1130T	1126	RIV PL GIROER	MISSOURI R-GN RY	G		P	G	G	G	G	G		G	G	G		G	G	F	P		G	G	G	G	X

A	FEET B	C	D	END FI E	PILES F	BENTS G	PIERS H	WINGWA_S I	J	ICE BREA ERS K	DR FT L	RIP RAP M	S OUR N	G RDERS O	STF N P	TR Q	H R	CURBS S	T	U	V	W	X	Y	GE Z	Z1	Z2
P 10 1120 1131		UNDERPASS	GN RY	G		G		G	G					G	G		G	G	P	G		G		G	G		
P 10 1120 1131A		UNOERPASS	GN RY	G		G		G	G					G	G		G	G	P	G		G		G	G		
P 10 1120 1132		UNOERPASS	SMELTER AVE	G		G		G	G					G	G		G	G		G		G	G	G	G		
P 10 1120 1132A		UNDERPASS	SMELTER AVE	G		G		G	G					G	G		G	G		G		G	G	G	G		
P 11 0000 0002	409	STEEL TRUSS	YELLOWSTONE R	P		C	F	F	F		G	G	G	F	G	G	F	F	P	F	G	F	F	F	F		X
P 11 0000 0204	450	ST PLATE GIRDER	YELLOWSTONE R	F		G	F	G	G	F	G	G	G	G			G	G	G	G	G	G	F	F	G		
P 11 0000 0240	90	CONT CONC T BM	BIG CR	F		G	G	F	G		F	G	G	G			G	F	G	G	G	F	G	F	G		
P 11 0000 0530		UNOERPASS*	S INT-I 90	G		G		G	G					G			E	G	G	G	G	G		F	G		
P 11 0000 0530A		UNDERPASS	S INT-I 90	G		G		G	G					G			E	G	G	G	G	G		F	G		
P 11 0530 0530		UNOERPASS*	S INT-I 90	G		G		G	G					G			E	G	G	G	G	G		F	G		
P 11 0530 0530A		UNDERPASS	S INT-I 90	G		G		G	G					G			E	G	G	G	G	G		F	G		
P 11 0605 0605	210	PRE CONC BEAM	MISSION INT-I 90	F		F		G	G					G			F	G	G	G	G	G	G	F	G		
P 11 0605 0606	128	CONCRETE T BEAM	NP RY	G		G	G	G	G					G			F	G	G	F	F	G	F	F	G		
P 11 0605 0615	390	CONT STEEL GIR	YELLOWSTONE R	G		G	F	G	G	F	F	G	F	G			F	G	G	F	G	G	F	F	G		
P 11 0605 0632	60	CONCRETE SLAB	DRAINAGE	G		G	G	F	G		G	G	G					P	G	G		F			G		
P 11 0605 0650	11	T T TRESTLE	STOCKPASS	G	F	G		G	F						G		G	F	G	G	G	F		F	G		
P 11 0605 0655	19	T T TRESTLE	STOCKPASS	F	F	F		F	F						G		G	F	G	G	F	F		F	F		
P 11 0605 0673	19	T T TRESTLE	STOCKPASS	G	F	F		F	G						G		G	F	G	G	G	G		F	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

F A SYS	F A RTE NUMBER	CONTROL JUNCT MILE POST TO TENTH	BRIDGE MILE POST TO TENTH	DESC	TOTAL LENGTH FEET	DESCRIPTION		FOOTINGS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSSES	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION	PAINT	GENERAL CONDITION	NOT INSP	REMARKS
A					B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	11	0605	0677		38	T T TRESTLE	WILLOW CR	G	F	F	F	F	G		G	F	G		G		G	F	G	G	G	G		F	G		
P	11	0605	0686		19	T T TRESTLE	DRAINAGE	G	F	G		F	F		G	E	G		G		G	F	G	G	G	G		F	G		
P	11	0605	0697		11	T T TRESTLE	DRAINAGE-STK	G	F	F		F	F		G	F	G		F		F	F	G	F	G	G		F	G		
P	11	0605	0702		38	T T TRESTLE	DRAINAGE	G	G	G	G	F	F		G	F	G		G		G	F	G	G	G	F		F	G		
P	11	0605	0712		141	ST PONY TRUSS	SHIELDS R	G	G	F	F	F	F	G	G	F	F		G	G	F	P	G	F	G	G		P	F		
P	11	0605	0723		59	STEEL I BEAM	ROCK CR	G		F	F	F	F	F	G	P	G		F		P	P	G	F		P		P	F		
P	11	0605	0767		128	STEEL GIRDER	SHIELDS R	G	G	G	G	G	F	G	G	F	G		G		G	F	G	F	F	F		F	G		
P	11	0605	0810		19	T T TRESTLE	DRAINAGE	G	F	F		F	F		G	G	G		F		G	G	G	G	F	F		P	G		
P	11	0605	0845		55	STEEL I BEAM	FLATHEAD CR	F		F	F	F	F		G	P	F		F		P	P	P	F		F			F		
P	11	0605	1024		7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G			G	G		
P	11	0605	1037		38	T T TRESTLE	LOST CR	F	G	G		P	P		G		G		G			G	G	G	G	G		G	G		
P	11	0605	1044		38	T T TRESTLE	S FK 16 MILE CR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	11	0605	1050		245	CONT ST GIRDER	CMSTP&P RR-CR	F		G		G	G		G	G	G	G			G	F	G	F	G	G	G	F	F		
P	11	0605	1122		57	T T TRESTLE	S FK SMITH R	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	11	0605	1124		19	T T TRESTLE	STOCKPASS	G	G	G		G	F		G		G		G			G	G	G	G	G		G	G		
P	11	0605	1131		57	T T TRESTLE	S FK SMITH R	G	G	G		G	G	G	G		G		G			G	G	G	G	G		G	G		
P	11	0605	1142		7	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G				G	G	G				G		
P	11	1175	1176		76	T T TRESTLE	S FK SMITH R	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	11	1175	1185		19	T T TRESTLE	STOCKPASS-DR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		

							E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z		Z
P	11	1175	1204	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	11	1291	1295	38	T T TRESTLE	N FK SMITH R	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	11	1291	1471	69	T T TRESTLE	SHEEP CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	11	1291	1639	100	CONCRETE T BEAM	BELT CR	G		F		G	G		G	G	G	G				F	G	G		G			G		
P	11	1291	1693	100	CONCRETE T BEAM	BELT CR	G		G		G	G		G	G	G	G				G	G	G		G			G		
P	11	1291	1712	140	PRES CONC BEAM	BELT CR	G		G		G	G		G	G	G	G			G	G		G		G		G	G		
P	11	1291	1942	164	PRE CONC BEAM	BELT CR																							N	
P	11	1291	1956	158	PRE CONC BEAM	BELT CR																							N	
P	11	1291	1965	182	PRE CONC BEAM	BELT CR																							N	
P	11	1291	2003	163	PRE CONC BEAM	BELT CR																							N	
P	11	2008	2011	156	CONCRETE T BEAM	BELT CR	G		G	G	G	G	G	P	G	G	G			G	G	P	G		G		P	G		
P	11	2008	2123	40	CONCRETE T BEAM	BOX ELDER CR	G		G		G	G		G	G	G	G				P	F	G		P			G		X
P	11	2008	2129	11	T T TRESTLE	STOCKPASS	G		G		G	G						G			G	G	G		G		P	G		
P	11	2008	2157		UNDERPASS	GN RY	F		G								G			G		F	G				P	G		
P	12	0000	0044	60	REIN CONC GIR	S FK MADISON R	G		G	G		G	G	G	P	G	G				G	G	G	G	G			G		
P	13	0000	0081	260	PRE CONC GIRDER	MADISON R	G		G	G	F	G	F	G	P	G	F			F	G	G	F	G	G		F	G		
P	13	0000	0308	83	CONCRETE T BEAM	INDIAN CR	F		G	G	G	G	G	G	G	F	G			G	F	G	G	G	G			G		

PLANNING SURVEY BRIDGE CONDITION REPORT

A	FEET B	C	D	FR E	PILE F	BENT G	PIERS H	WINGWALLS	BACKWALLS J	ICE BREAKERS K	DR L	RIP RAP M	SCOUR N	O	TR P	R Q	SHOES R	CURBS S	MA	DECK	BRACING V	RAILING W	EXPANSION X	PAINT Y	GENERAL CON Z	NOT INS Z1	REMARKS Z2
P 13 0000 0475	8	T T TRESTLE	STOCKPASS	G	G	G		G	G						G		G	G	G	G	F	G		G	G		
P 13 0000 0481	122	CONCRETE T BEAM	ODELL CR	F		G	C	F	G	C	G	F	G	F			C	G	G	G	G	F			F		X
P 13 0000 0483	107	CONCRETE T BEAM	MADISON R OF	F		F	C	F	G	F	G	G	G	F			F	G	G	G	G	P			F		X
P 13 0000 0484	81	CONCRETE T BEAM	MADISON R OF	G		G	F	F	G	G	G	G	G	F			F	G	G	G	G	G			G		
P 13 0000 0485	107	CONCRETE T BEAM	MADISON R OF	F		F	G	G	G	G	G	G	G	F			F	F	G	G	G	F	F		G		
P 13 0000 0486	290	THRU ST TRUSS	MADISON R	G		G	F	G	G	F	G	G	G		G	G	F	F	G	G	G	G	F	E	G		
P 13 0491 0564	19	T T TRESTLE	N MEADOW CR	G	G	G		G	G		G	G	G		G			F	G	G	G	G		F	G		
P 13 0491 0567	7	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		F			G	G	G	G	G		F	G		
P 13 0491 0611	19	T T TRESTLE	STOCKPASS	G	F	G		G	G		G		F		G			F	G	G	F	F		F	G		
P 13 0491 0652	38	T T TRESTLE	WARM SPRINGS CR	G	F	G		F	F		G		G		G			F	G	G	F	F		F	F		
P 13 0491 0671	19	T T TRESTLE	STOCKPASS	G	F	G		G	G		G		G		G			F	G	G	G	F		F	G		
P 13 0491 0679	38	T T TRESTLE	DRAINAGE	G	F	G		F	F		G		G		G			F	G	G	G	F		F	G		
P 13 0491 0688	19	T T TRESTLE	STOCKPASS	G	F	G		F	F		G		G		G			F	G	G	G	F		F	G		
P 13 0491 0693	19	T T TRESTLE	STOCKPASS	F	F	G		F	G		G		G		G			F	G	G	F	F		G	G		
P 13 0491 0704	19	T T TRESTLE	STOCKPASS	G	F	G		F	G		G		G		G			F	G	G	F	G		F	G		
P 13 0491 0713	19	T T TRESTLE	STOCKPASS	G	F	G		F	F		G		G		C			F	G	G	F	F		F	F		X
P 13 0491 0714	19	T T TRESTLE	NORWEGIAN CR	G	F	G		F	G		G		G		G			G	G	G	F	F		F	G		
P 13 0491 0735	76	T T TRESTLE	DRY HOLLOW CR	G	F	G		F	F		G		G		G			F	G	F	F	F		F	F		
P 13 0491 0751	38	T T TRESTLE	S WILLOW CR	G	F	G		G	G		G		G		G			F	G	G	G	F		F	G		

A	B	C	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X		Z	Z	Z
P 13 0491 0760	19 T T TRESTLE	N WILLOW CR	G	F	G		F	F		G	F	G		G			G	G	G	F	G		F	G		
P 13 0491 0824	370 STEEL GIRDER	NP RY-CMSTP&P RR	F		G		G	G					G			G	F	G	F	G	G		F	G		
P 13 0491 0830	395 THRU ST TRUSS	JEFFERSON R	F		G	F	G	G	G	G		G	G		G	F	F	G	G	P	F	G	E	G		
P 14 0000 0065	7 T T TRESTLE	STOCKPASS	G	F	F		G	G						P			F	G	G	F	F		F	P		X
P 14 0000 0073	7 T T TRESTLE	STOCKPASS	G	G	G		F	G						P			G	G	G	P	G		F	P		X
P 14 0000 0090	7 T T TRESTLE	STOCKPASS	G	F	P		F	G						F			F	G	F	F	F		F	P		X
P 14 0000 0111	57 T T TRESTLE	DEEP CR	G	G	F		G	G	G	G		G		G			G	G	G	P	F		G	F		
P 14 0000 0117	19 UNT T TRESTLE	DRAINAGE	G	G	P		P	P		G		G		F			F	G	G	P	F		F	P		X
P 14 0000 0119	38 T T TRESTLE	DEEP CR	G	F	G		G	G	G	F		G		G			F	G	G	G	P		F	F		X
P 14 0000 0148	19 T T TRESTLE	DEEP CR	G	G	G		F	G		G		G		G			F	G	G	G	F		F	G		X
P 14 0000 0151	39 T T TRESTLE	DEEP CR	G	F	G		F	G		G		G		F			F	G	G	F	F		F	F		X
P 14 0000 0173	39 T T TRESTLE	DEEP CR	G	G	G		F	G		F	G	G		G			F	G	G	F	F		F	F		X
P 14 0000 0196	19 T T TRESTLE	DEEP CR	F		G		F	F		G		G		G			F	G	G	G	F		F	F		X
P 14 0000 0198	19 T T TRESTLE	DEEP CR	G		G		G	G		G		G		G			F	G	G	G	F		F	G		X
P 14 0000 0240	7 T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0000 0246	7 T T TRESTLE	STOCKPASS	G	G	G		G							F			G	G	G	G	G		G	G		X
P 14 0000 0295	7 T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0000 0304	7 T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		

PLANNING SURVEY BRIDGE [illegible] REPORT

A	B	C	D	E	F		H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W		Y	Z	Z	Z
P 14 0449 0489	25	T T TRESTLE	FOUR MILE CR	G	G	G		G	G		G	G	G		G			G	F	G	G	G		G	G		
P 14 0449 0530	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0661	76	T T TRESTLE	FLAGSTAFF CR	G	G	F		G	G		G		G		G			G	G	G	G	G		G	G		X
P 14 0449 0667	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		G	G		
P 14 0449 0682	76	T T TRESTLE	COOPER CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 14 0449 0695	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 14 0449 0707	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		G	G		
P 14 0449 0730	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		G	G		
P 14 0449 0763	95	T T TRESTLE	N FK MUSSELSHELL	G	G	G		G	G	G	F		G		G			G	G	G	G	G		G	G		
P 14 0449 0764	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		X
P 14 0449 0773	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0778	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0784	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0789	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0794	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0802	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0808	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0812	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0822	57	T T TRESTLE	DAISY DEAN CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		

				FEET B			F	F	G	H		J	K	L	M	N	O	P	Q	R	S		U	V	W	X	Y	Z	Z	
P	14	0449	0848	57	T T TRESTLE	WILLIS COU	F	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	14	0449	0881	65	CONT CONC SLAB	HAYMAKER CR	G		G		G	G		G	G	G					G	G	G		G		G	G		
P	14	0995	1005	204	CONT STEEL BEAM	CMSTP&P RR	P		G		G	G			G		G			G	G	G	G	G	G	G	G	G		
P	14	1008	1092	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	P	G		G	G		
P	14	1008	1106	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	P	G		G	G		
P	14	1008	1322	38	T T TRESTLE	DRAINAGE	P	G	G		G	G		G		G		G			G	G	G	F	F		G	G		
P	14	1008	1336	114	T T TRESTLE	CARELESS CR	P	G	G		G	G	G	P		P		G			G	G	G	G	G		G	G		X
P	14	1008	1337	7	T T TRESTLE	STOCKPASS	P	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1008	1344	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1008	1352	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1008	1358	57	T T TRESTLE	DRAINAGE	P	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	14	1008	1393	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1008	1397	57	T T TRESTLE	NINE MILE CR	G	G	G		G	G		G	P	G		G			G	G	G	G	G		G	G		
P	14	1008	1398		UNDERPASS	GN RY	G		G		G	G					G			G		G	G	G			G	G		
P	14	1008	1403	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	14	1008	1431	76	T T TRESTLE	FIVE MILE CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	14	1008	1444	95	T T TRESTLE	DRAINAGE	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	14	1460	1462	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1460	1474	57	T T TRESTLE	TWIN COULEE	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		

PLANNING SURVEY [illegible]

FAS SYSTEM	FAS ROUTE NUMBER	CONTROL JUNCTION MILE TO TENTHS	BRIDGE MILEPOST TO TENTHS	TOTAL FEET	DESCRIPTION	NAME	E	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIPRAP	N	O GIRDERS	P STRINGERS	Q	R HOOKS	S CURBS	T	U DECK	V BRACING	W RAILING	X	Y PAINT	Z GENERAL CONDITION	Z NOT INSPECTED	Z REMARKS
P	14	1460	1476	57	T T TRESTLE	TWIN COULEE	P	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1486	76	T T TRESTLE	DRAINAGE	P	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1523	76	T T TRESTLE	DEAN CREEK	P	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1531	7	T T TRESTLE	STOCKPASS	P	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1460	1547	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1613	95	T T TRESTLE	CURRANT CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1641	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1460	1658	75	T T TRESTLE	POLE CR	G		P		G	G		G	G	G	G				G	G	G	G	G		G	P		X
P	14	1694	1746	76	T T TRESTLE	WILLOW CR	P	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1755	76	T T TRESTLE	MUSSELSHELL R	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1763	76	T T TRESTLE	MUSSELSHELL R	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1771	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	14	1694	1774	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1790	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1806	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1820	11	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1694	1824	19	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1694	1828	76	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1840	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	G		G			G	G	G	P	F		G	G		

									E	F	G	H			K	L	M		O	P	Q	R	S	T	U	V	W			Z	
P	14	1694	1854	11	T	T	TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	14	1694	1860	57	T	T	TRESTLE	DRAINAGE	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	14	1694	1871	11	T	T	TRESTLE	STOCKPASS	P	G	G		G	G			F			G			G	G	G	G	G		G	G	
P	14	1694	1888	57	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G				G	G	G	G		G	G	
P	14	1694	1896	11	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G		G	G	
P	14	1694	1903	25	T	T	TRESTLE	IRRIGATION CANAL	G	G	G		G	G		G		G		G				G	G	G	G		G	G	
P	14	1694	1913	57	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G				G	G	G	G		G	G	
P	14	1694	1919	76	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G				G	G	G	G		G	G	
P	14	1694	1930	57	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G				G	G	G	G		G	G	
P	14	1694	1945	95	T	T	TRESTLE	DRAINAGE	P	G	G		G	G		G		G		G				G	G	G	G		G	G	X
P	14	1694	1954	19	T	T	TRESTLE	STOCKPASS	G	G	G		G	G			G			G				G	G	G	G		G	G	
P	14	1694	1956	19	T	T	TRESTLE	DRAINAGE & STK P	F	G	G		G	G		G	G	G		G				G	G	G	G		G	G	
P	14	1694	1964	57	T	T	TRESTLE	DRAINAGE	P	G	G		G	G		G	G	G		G				G	G	G	G		G	G	X
P	14	1694	1966	11	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G		G	G	X
P	14	1694	1993	11	T	T	TRESTLE	STOCKPASS & DR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	14	1694	2000	38	T	T	TRESTLE	DRAINAGE	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	14	1694	2015	57	T	T	TRESTLE	OLD RIVER CH	G	G	G		G	G		G	P	G		G			G	G	G	G	G		G	G	
P	14	1694	2030	19	T	T	TRESTLE	STOCKPASS	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	14	1694	2039	76	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	X

PLANNING [illegible] CONDITION REPORT

A			E	F	G						M	N	C				R	S							
P 14 1694 2052	38 T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G
P 14 1694 2071	224 CONT ST GIRDER	MUSSELSHELL R	G		G	G	G	G	G	G	F	G	G			G	G	G	G	G	G	G	G	G
P 14 1694 2079	38 T T TRESTLE	DRAINAGE	G	G	G			G		G	G	F		G			G		G	G	F		G	G
P 14 1694 2094	95 T T TRESTLE	HOME CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G
P 14 1694 2160	11 T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G		G	G	G		G	G
P 14 1694 2161	57 T T TRESTLE	HOME CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G
P 14 1694 2165	57 T T TRESTLE	HOME CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G
P 14 1694 2168	57 T T TRESTLE	HOME CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G
P 14 1694 2170	38 T T TRESTLE	HOME CR	G	G	G			G		G		G		G			G	G	G	G	G		G	G
P 14 1694 2199	57 T T TRESTLE	DRY WASH	G	G	G			G		G		G		F			F	G	G	G	G		G	G
P 14 1694 2237	38 T T TRESTLE	DRAINAGE	G	G	G			G		G	F	G		G			F		G	G	G		G	G
P 14 1694 2246	57 T T TRESTLE	DRAINAGE	G	G	G			G		G	G	F		G			F		G	G	G		F	G
P 14 1694 2273	57 T T TRESTLE	DRY WASH	G	G	G			G		G	G	G		F			G		G	G	G		G	G
P 14 1694 2293	25 T T TRESTLE	DRAINAGE	G	G	G			G		G	F	F		G			F		G	G	G		G	G
P 14 1694 2359	57 T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		G	G
P 14 1694 2381	38 T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		G	G
P 14 1694 2389	57 T T TRESTLE	DRAINAGE	G	G	G			G		G	F	G		G			G		G	G	G		G	G
P 14 1694 2398	57 T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		G	G
P 14 1694 2437	57 T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G

PLANNING SURVEY BRIDGE CONDITION REPORT

CONDITION RATING

SUBSTRUCTURE

				E	F	G	H	I	J	K		M	N	O	P		T	U	V	W		Z
P 14 1694 2453	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G	F		G	G	G	G	G
P 14 1694 2463	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G	F		G	G	G	F	G
P 14 1694 2505	100	T T TRESTLE	HORSE CR	G	G	G			G		G	G	G		G	G	G	G	G	G	G	G
P 14 1694 2521	57	T T TRESTLE	ANDERSON CR	G	G	G			G		G	F	G		G	G	G	G	G	G	G	G
P 14 1694 2530	38	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G	F		G	G	F	G	G
P 14 1694 2545	19	T T TRESTLE	DRAINAGE-STK P	F	G	G			G		G	G	G		G	G		G	G	G	G	G
P 14 1694 2570	19	T T TRESTLE	STOCKPASS	F	G	G			G						G	F		G	G	G	G	G
P 14 1694 2572	122	STEEL GIRDER	PORCUPINE CR	G	G	G	G		G	G	G	G	G	G	G	F	G	G	G	G	G	G
P 14 1694 2574	57	T T TRESTLE	DRAINAGE	G	G	F			G		G	G	G		G	F		G	G	G	G	G
P 14 1694 2583	19	T T TRESTLE	STOCKPASS	F	G	G			G		G	G	G		G	F		G	G	G	G	G
P 14 1694 2585	11	T T TRESTLE	STOCKPASS	F	G	G		G	G		G		G		G	G		G	G	G	G	G
P 14 1694 2598	38	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G	F		G	G	F	G	G
P 14 1694 2603	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G	G		G	G	G	G	G
P 14 1694 2615	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G	G		G	G	G	G	G
P 14 1694 2620	19	T T TRESTLE	DRAINAGE	G	G	F			F		G	G	G		G	F		G	G	F	F	G
P 14 1694 2625	95	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G	G		G	G	F	F	G
P 14 1694 2626	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G	F		G	G	F	G	G
P 14 1694 2628	19	T T TRESTLE	GREASEWOOD CR	F	G	G			G		G	G	G		G	F	G	G	G	F	F	G
P 14 1694 2648	38	T T TRESTLE	MCGRAWS COULEE	G	G	G			G		G	G	G		G	F	F	G	G	F	F	G

PLANNING [illegible] BRIDGE CONDITION REPORT

							E	F	G	H		J	K		M	N	O	P	Q	R	S	T			W				Z	
P	14	1694	2703	825	STEEL GIRDER	YELLOWSTONE R-RR	G		E	E		E	G	G	G	G	E	E		E	G	G	E	E	G	G	F	E		
P	15	0000	0002	123	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	F	G		P	G	G	G		X
P	15	0000	0005	118	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G		
P	15	0000	0008	118	PRE CONC BEAM	OTTER CR	F		G		X	G		G	G	G	G			G	G	G	G		G	G	G	G		X
P	15	0000	0015	102	PRE CONC BEAM	OTTER CR	F		G		G	G		G	G	G	G			G	G	P	G		G	G	G	G		X
P	15	0000	0019	102	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	P	G		P	G	G	G		X
P	15	0000	0022	92	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	G	G		G	G	G	G		
P	15	0000	0025	92	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	F	G		G	G	G	G		X
P	15	0000	0030	102	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	F	G		F	G	G	G		X
P	15	0000	0036	102	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	P	G		G	G	G	G		X
P	15	0000	0085	82	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	G	G		G	G	G	G		
P	15	0000	0093	82	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	G	G		G	F	G	G		
P	15	0000	0103	82	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	G	G		G	F	G	G		
P	15	0000	0108	82	PRE CONC BEAM	OTTER CR	G	G	G		G	G		G	G	G	G			G	G	G	G		G		G	G		
P	15	0000	0219	57	T T TRESTLE	MCCARTHY CR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	15	0000	0241	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	15	0000	0262	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		G	G		
P	15	0000	0267	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

	FEET B				D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	7	72
P 15 0000 0291	7	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 0000 0292	57	T	T	TRESTLE	FOX COU	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0000 0303	19	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 15 0000 0308	57	T	T	TRESTLE	SURPRISE CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0000 0317	57	T	T	TRESTLE	SUN CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0000 0336	11	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P 15 0000 0349	57	T	T	TRESTLE	WOLF CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0363	11	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P 15 0000 0372	38	T	T	TRESTLE	N FK SKULL CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0374	38	T	T	TRESTLE	S FK SKULL CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0389	57	T	T	TRESTLE	COYOTE CR	G	G	G		G	G		G		G		G			F	G	G	G	G		G	G		
P 15 0000 0394	11	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P 15 0000 0400	57	T	T	TRESTLE	WILLOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0422	38	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0000 0431	38	T	T	TRESTLE	SAGE CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0442	38	T	T	TRESTLE	DRAINAGE	C	G	G		G	G		G	F	G		G			G	G	G	G	F		G	G		X
P 15 0000 0457	38	T	T	TRESTLE	DRY CR	P	G	G		G	G		G	P	G		G			G	G	G	G	G		G	G		
P 15 0000 0460	19	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 0000 0488	19	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		

A	B	C	D	E	F	G	H	I	J	K		M	N	O	P		R	S	T		V	W			Z	Z1	Z2
P 15 0000 0569	123	CONCRETE T BEAM	GN RY	G		G		G	G					G			G	G	G	G		G		G	G		
P 15 0000 0582	159	CONCRETE T BEAM	JUDITH R	F		G	P	G	G	G	P	F	G	G			G	G	G	G		G			F		X
P 15 0000 0625	120	CONCRETE T BEAM	ROSS FORK CR	P		G	G	G	G	G	G	F	G	G			G	G	G	G		G			G		X
P 15 0000 0631	38	T T TRESTLE	OLSON CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0638	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P 15 0649 0694	38	T T TRESTLE	DRY COU	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0649 0696	38	T T TRESTLE	ROCK CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0649 0719	38	T T TRESTLE	LITTLE ROCK CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0649 0726	57	T T TRESTLE	KING COU	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0649 0739	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P 15 0649 0741	57	T T TRESTLE	BEAVER CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0649 0751	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G			G		G	G		
P 15 0649 0755	75	T T TRESTLE	COTTONWOOD CR	F	G	G		G	G		F	G	G		G			G	G	G	G	G		G	G		
P 15 0793 0796	165	CONCRETE T BEAM	CMSTP&P RR	F		F		G	G					F			F	F	G	F		G			F		X
P 15 0793 0822	30	STEEL & CONC	BIG SPRING CR	G		N		N	N						N			G		G					G		X
P 15 0823 0824	25	CONCRETE T BEAM	MILL DITCH	G		F		F	F		G		G	G				P		F		G			G		X
P 15 0823 0842	57	T T TRESTLE	BOYD CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0823 0862	57	T T TRESTLE	BOYD CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0823 0872	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		

[illegible] SURFACE BRIDGE CONDITION REPORT

							E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
P	15	0823	0909	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			P	G	G	G			G	G
P	15	0823	0955	38	T T TRESTLE	DRAINAGE	G	G	G		F	G	G			G		G			F	G	G	G			G	G
P	15	0823	0996	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G				G	G	G			G	G
P	15	0823	1008	57	T T TRESTLE	DRAINAGE	G	G	G		F	G				G		G			G	G	G	G			G	G
P	15	0823	1038	25	T T TRESTLE	DRAINAGE	G	G	G		G	G			G	G		G			G	G	G	G			G	G
P	15	0823	1053	57	T T TRESTLE	N FK MCDONALD CR	G	G	G		G	G			G	G		G			G	G	G	G			G	G
P	15	0823	1067	38	T T TRESTLE	DRAINAGE	G	G	G		G	G			G	G		G			G	G	G	G			G	G
P	15	0823	1074	57	T T TRESTLE	DRAINAGE	G	G	G		G	G			G	G		G			G	G	G	G			G	G
P	15	0823	1078	100	T T TRESTLE	IRRIGATION RES	G	G	G		G	G			G			G			G	G	G	G	G		G	G
P	15	0823	1094	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G
P	15	0823	1105	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G
P	15	0823	1107	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G
P	15	0823	1110	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G
P	15	0823	1118	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G
P	15	0823	1125	100	T T TRESTLE	S FK MCDONALD CR	G	G	G		G	G		F	G	G		G			G	G	G	G	G		G	G
P	15	1129	1172	92	PRE CONC BEAM	MCDONALD CR	G		G	G	G	G	G	F	G	G	G			G	G	G	G	G	G	G	G	G
P	15	1129	1200	76	T T TRESTLE	BRIGGS COU	G	G	G		G	G		G		G		G				G	G	G	G	G	G	G
P	15	1129	1453	184	CONCRETE T BEAM	BOX ELDER CR	P		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G
P	15	1129	1579	38	T T TRESTLE	DRAINAGE	F	G	G		G	G			G	G		G			G	G	G	G	G		G	G

P	15	1129	1584	436	STEEL TRUSS	MUSSELSHELL R	F		G	F	G	G	G	G	G	G			G	F	F	G	F	G	G	G	G	G		X
P	15	1129	1613	114	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	15	1129	1698	132	PRE CONC BEAM	CALF CR	E		E	E	E	E	E	E	E	E	E			E	E	E	E		E		E	E		
P	15	1129	1735	57	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	F	G	G	G		G	G		
P	15	1129	1750	57	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	15	1129	1772	38	T T TRESTLE	DRAINAGE	P	G	G		G	G		G	P	G		G			G	G	G	G	G		G	G		
P	15	1129	1792	19	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		
P	15	1129	1800	19	T T TRESTLE	STOCKPASS	F	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	15	1129	1816	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	15	1129	1832	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	15	1129	1842	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	15	1129	1846	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		F	G		
P	15	1129	1849	7	T T TRESTLE	STOCKPASS	P	G	G		G	G						G			G	G	G	G	G		G	G		
P	15	1129	1878	95	T T TRESTLE	DUGOUT COU	G	G	G		G	G			G			G			G	G	G	G	G		P	G		
P	15	1129	1891	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		F	G		
P	15	1129	1903	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		F	G		
P	15	1129	1910	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	15	1129	1912	95	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	15	1129	1923	114	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		

				TOTAL LENGTH FEET	MAXIMUM SPAN		END FL	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DE	BRA	RAI	EXPAN	PA	GENERA	NOT N	REMA
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	15	1129	1934	95	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
P	15	1129	1942	95	T T TRESTLE	ORAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
P	15	1129	1969	95	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P	15	1129	1973	38	T T TRESTLE	ORAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P	15	1129	1989	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P	15	1129	2001	162	STEEL GIRDER	8IG ORY CR	G	G	G	G	G	G	G	G	G	G	G	G		G	G	G	G	G	G	G	P	G		
P	15	1129	2007	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P	15	1129	2025	76	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P	15	1129	2035	19	T T TRESTLE	ORAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		F	G		
P	15	1129	2050	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		F	G		
P	15	1129	2056	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		P	G		
P	15	1129	2063	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		F	G		
P	15	1129	2078	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P	15	1129	2087	76	T T TRESTLE	ORAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P	15	1129	2092	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		F	G		
P	15	1129	2105	95	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P	15	1129	2112	114	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P	15	2121	2123	161	STEEL BEAM	8IG DRY CR	P	G	G	G	G	G	F	G	G	G	G	G		G	G	G	G	G	G	P	P	G		
P	15	2121	2152	63	T T TRESTLE	VALE CR	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

A							E	F	G	H		J	K	L	M	N	O		Q	R	S				W		Y	
P	15	2121	2177	63	T T TRESTLE	DRY WASH	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G
P	15	2121	2198	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G
P	15	2121	2212	63	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G
P	15	2121	2224	63	T T TRESTLE	DRY WASH	G	G	G		G	G		G	E	G		G			G	G	G	G	G		F	G
P	15	2121	2235	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G
P	15	2121	2265	396	CONT STEEL BEAM	BIG DRY CR	G	G	G	G	G	G	G	G	G	G	G	G		F	G	G	G	G	G	P	F	G
P	15	2121	2275	125	T T TRESTLE	L-S CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G
P	15	2121	2299	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G
P	15	2121	2310	57	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	G	F	D	G	G	N	G	G
P	15	2121	2325	25	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	F	D	G	G	N	G	G
P	15	2121	2327	76	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	F	D	G	G	N	G	G
P	15	2121	2345	101	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	G	G	G	G	N	G	G
P	15	2121	2356	93	T T TRESTLE	DRAINAGE	G	F	F	N	N	G	N	G	G	G	N	F	N	N	G	G	G	G	G	N	G	G
P	15	2121	2392	404	STEEL BEAM	LITTLE DRY CR	G	G	G	F	N	G	G	G	F	F	G	F	N	F	F	G	G	G	G	F	F	F
P	15	2121	2474	95	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G
P	15	2486	2488	125	T T TRESTLE	TIMBER CR	G	G	G	G	G	G	G	G	F	F	N	G	N	N	G	F	G	G	G	N	G	G
P	15	2486	2497	123	T T TRESTLE	SKULL CR	G	G	G	G	G	G	G	G	P	F	N	G	N	N	G	F	G	G	G	N	G	G
P	15	2486	2530	57	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G
P	15	2486	2533	85	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

CONTROL A				TOTAL LENGTH FEET B	DESCRIPTION OF STRUCTURES MATERIAL & TYPE MAXIMUM SPAN C	NAME OF FEATURE CROSSED D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKER T	DECK U	B V	RAILING W	EXPANSION X	PAINT Y	GENERAL Z	NOT INSPECTED Z1	Z2
P	15	2486	2547	85	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	F	N	N	G	G	G	G	G	N	G	G		
P	15	2486	2548	76	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	15	2486	2553	95	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2571	75	T T TRESTLE	COULEE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2579	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2588	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2601	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2615	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2618	38	T T TRESTLE	DIRTY CR	G	G	G		G	G	N	P	F	F	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2670	63	T T TRESTLE	COTTER CR	G	G	G		G	G	N	G	F	F	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2702	76	T T TRESTLE	STONEY BUTTE CR	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2716	76	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	F	F	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2733	57	T T TRESTLE	ANTELOPE CR	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2756	95	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	F	G	G	G	N	G	G		
P	15	2486	2765	114	T T TRESTLE	DL CH REDWATER R	G	G	G	G	G	G	N	G	F	F	N	G	N	N	G	F	G	G	G	N	F	G		
P	15	2486	2775	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	F	N	G	N	G	N	N	G	F	G	G	G	N	F	G		
P	15	2795	2800	267	STEEL BEAM	REDWATER R	G		G	G		G	G	G		G	G			G	G	G	G	G	G	G	G	G		
P	15	2807	2836	92	PRE CONC BEAM	BUFFALO SPR CR	P	N	E	E	E	E	N	G	E	G	E	N	N	E	E	G	E	N	E	N	G	G		
P	15	2807	2981	57	T T TRESTLE	HAY CR	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	G	G	G	G	N	G	G		

P	15	2807	2992	76	T T TRESTLE	HAY CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	F	G		
P	15	2807	3004	57	T T TRESTLE	SAND CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	F	G		
P	15	2807	3017	57	T T TRESTLE	DRAINAGE	G	G	G	G	F	F	N	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	15	2807	3069	112	PRE CONC BEAM	N FK UPPER 7MI C	G	N	E	E	E	E	N	G	G	G	E	N	N	E	G	G	G	N	E	N	G	E		
P	15	2807	3139	102	PRE CONC BEAM	UPPER 7 MI CR	G	N	E	E	E	E	N	G	G	G	E	N	N	E	G	G	G	N	E	N	G	E		
P	15	3554	3554	163	PRE CONC BEAM	W INT-I 94	G	N	E	N	E	E	N	N	N	N	E	N	N	E	G	G	G	N	G	G	G	G		
P	15	3558	3559	276	CONT ST GIRDER	BEAVER CR	G	N	G	G	G	G	G	G	G	G	G	N	N	G	G	G	F	N	G	G	F	G		
P	15	3558	3563	173	PRE CONC BEAM	E INT-I 94	G	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	G	N	G	G	G	G		
P	16	1039	1039	276	PRE CONC BEAM	LOCKWOOD INT I90	G		E			E					E				E		E				E	E		
P	16	1039	1039T	276	PRE CONC BEAM	LOCKWOOD INT I90	G		E			E					E				E		E				E	E		
P	16	1039	1045	262	CONT STEEL BEAM	NP RY	G		G			G					G			P	F		G	F	F	P	P	F		
P	16	1039	1047	540	CONT STEEL TRUS	YELLOWSTONE R	G		F	G		G	G	G		G		G	G	G	F	F	F	F	F	F	F	F		X
P	16	1039	1049	35	CONC T BEAM	SEWER DT	G		G			G					G				F		G					G		X
P	16	1088	1091	57	T T TRESTLE	FIVE MILE CR	G	F	G			G		F		G		G			F	G	G	G	F		F	G		
P	16	1088	1097	39	STEEL I BEAM	88WA CA	G	F	G			F		G		G		G			P	F	G		F		F	G		
P	16	1088	1143	31	STEEL I BEAM	ELEVEN MILE CR	G	G	G			G		G		G		G			F		G		F		G	G		
P	16	1088	1148	38	T T TRESTLE	MID FK 12 MI CR	F	G	G			F		G		G		G			F		G		F		G	G		
P	16	1088	1151	38	T T TRESTLE	N FK 12 MILE CR	F	G	G			F		G		F		G			F		G	G	F		G	G		

PLANNING SAFETY BRIDGE CONDITION REPORT

A				FEET B	C	D	END FL E	P LE F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	R P RAP M	SCOUR N	GIR O	STR P	Q	R	S	T	U	V	W	X	Y	Z	Z1	ZZ
P	16	1088	1203	57	T T TRESTLE	S FK CROOKED CR	G	G	G			F		G		G		G			F		F	G	F		G	G		
P	16	1088	1210	57	T T TRESTLE	N FK CROOKED CR	G	G	G			F		G		G		G			F		G	G	F		G	G		
P	16	1088	1245	57	T T TRESTLE	DRY WASH	G	G	G			F		G	G	G		G			F		G	G	F		G	G		
P	16	1088	1285	57	T T TRESTLE	DRAINAGE	G	G	G			F		G	G	G		G			F		G	G	F		G	G		
P	16	1088	1287	57	T T TRESTLE	DRAINAGE	G	G	G			F		G	F	G		G			F		G	G	F		G	G		
P	16	1088	1308	38	T T TRESTLE	DRAINAGE	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		X
P	16	1088	1318	57	T T TRESTLE	DRAINAGE	F	G	G		P	G		G		G		G			G	G	G	G	G		G	G		X
P	16	1088	1332	19	T T TRESTLE	DRAINAGE & STK P	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	16	1088	1336	75	T T TRESTLE	RAZOR CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	16	1088	1515	229	CONT STEEL BEAM	MUSSELSHELL R	G		G	G	G	G	G	P	P	P	G			G	G	G	G	G	G	G	G	G		
P	16	1088	1519	168	STEEL TRUSS	CMSTP&P RY	G		G		G	G							G	G	G	G	G	G	G	P	F	G		
P	16	1539	1612	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	F		G	G		
P	16	1539	1621	76	T T TRESTLE	S WILLOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	16	1539	1633	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	16	1539	1642	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	16	1539	1687	95	T T TRESTLE	WILLOW CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	16	1539	1729	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		
P	16	1539	1924	57	T T TRESTLE	ELK CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	16	1991	1998	92	PRE CONC BEAM	MCDONALD CR	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G		

					F		H		J	K	L	M		O			R					W				
P 16 1991 2009	82	PRE CONC BEAM	CHIPPEWA CR	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G	
P 16 1991 2047	92	PRE CONC BEAM	FORDS CR	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G	
P 16 1991 2070	82	PRE CONC BEAM	LIT BOX ELDER CR	G		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G	
P 16 1991 2103	92	PRE CONC BEAM	S FK BEAR CR	G		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G	
P 16 1991 2160	82	PRE CONC BEAM	N FK BEAR CR	G		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G	
P 16 2206 2211	75	T T TRESTLE	OF BOX ELDER CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P 16 2206 2405	173	PRE CONC BEAM	ARMELLS CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G	G	G	G	
P 16 2206 2420	698	STEEL GIRDER	MISSOURI R	P		G	G	G	G	G	F	G	G	G			G	G	G	G	G	G	G	F	G	X
P 16 2206 2731	57	T T TRESTLE	BEAVER CR	F	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G	
P 16 2206 2785	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G	
P 16 2206 2790	63	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G	
P 16 2206 2795	138	T T TRESTLE	LITTLE WARM CR	G	G	G			G	G	F	G	G		G			G	G	G	G	G		G	G	
P 16 2206 2839	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G	
P 16 2206 2874	100	T T TRESTLE	BIG WARM CR	F	G	G		G	G	G	G	F	F		G			G	G	F	G	G		G	G	
P 16 2206 2901	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G	G	G	G	G		G	G	
P 16 2206 2905	57	T T TRESTLE	WILD HORSE CR OF	G	G	G		G	G	G	G	F	G		P			G	G	G	G	G		G	F	X
P 16 2206 2907	100	T T TRESTLE	WILD HORSE CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P 16 2206 2910	100	T T TRESTLE	WILD HORSE CR	F	G	G		G	G	G	G		F		F			G	G	G	G	G		G	G	
P 16 2206 2940	57	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

R = To be Removed

CONTROL				DESCRIPTION OF FEATURES			CONDITION RATINGS																						
				TOTAL FEET	MATERIAL & TYPE	NAME OF FEATURE	END FILL	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DR	RIP RAP	SCOUR	GIRDERS	STRINGERS											
				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	
P	16	2206	2943	57	T T TRESTLE	DRAINAGE	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		G	G	
P	16	2206	2973	100	T T TRESTLE	W ALKALI CR	F	G	G		G	G	G	F	G	F		P			G	G	G	G	G		G	F	X
P	16	2206	2979	75	T T TRESTLE	BLACK COU	F	G	G		G	G	G	F	G	F		G			G	G	G	G	G		G	G	
P	16	2206	3000	76	T T TRESTLE	HALFWAY COU	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P	16	2206	3033	157	ST PONY TRUSS	ALKALI CR	F	G	G			F	G	G	G	G	G	G		F	G	G	G	G	G	P	G	G	
P	16	2206	3039	57	T T TRESTLE	DESJARDIN COU	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P	16	2206	3082	75	T T TRESTLE	S FK TAYLOR CR	F	G	G		G	G		G	G	G		C			G	G	G	G	G		G	F	X
P	16	2206	3084	100	T T TRESTLE	N FK TAYLOR CR	F	G	G		G	G		G	F	G		G			G	G	G	G	G		F	G	
P	16	2206	3108	100	T T TRESTLE	DODSON SO CANAL	G	G	G			G		G	F	G		P			G	G	G	G	G		G	F	X
P	16	2206	3114		UNDERPASS	GN RY	G		G		G	G					G				G	G	G		G		F	G	
P	18	0000	0010	971	STEEL GIRDER	YELLOWSTONE R	F		G	G	G	G	G	F	G	G	G	G		G	G	P	G		G	F	F	G	
P	18	0000	0039	164	CONCRETE BEAM	S FK SUNDAY CR	G		G	G		G	G	G	G	G	G			G	G	E	G		G		G	G	
P	18	0000	0110	122	PRE CONC BEAM	N FK SUNDAY CR	F		G			G		G	G	G	G			G	G	E	G	G	G		G	G	
P	18	0000	0178	102	PRE CONC BEAM	GRIMES CR	G		G			G		G	G	G	G			G	G	E	G	G	G	G	G	G	
P	18	0000	0251	95	T T TRESTLE	DRY HOUSE CR	G	P	P			F	G	G	G	G		F			F	E	F	F	G		G	F	
P	18	0000	0351	38	T T TRESTLE	ROCK SPRINGS CR	F	F	F			F		G	G	G		F			F		F	F	G		G	G	
P	18	0000	0434	95	T T TRESTLE	RED BUTTE CR	G	G	G	G	N	G	G	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G	
P	18	0000	0439	57	T T TRESTLE	DRAINAGE	G	F	G	N	N	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G	

P 18 0000 0450	76	T T TRESTLE	DRAINAGE	F	G	F	N	N	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G
P 18 0000 0463	57	T T TRESTLE	DRAINAGE	F	G	G	N	N	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G
P 18 0000 0478	95	T T TRESTLE	THOMPSON CR	G	G	G	N	N	G	G	G	G	G	N	G	N	N	F	G	G	G	G	N	G	G
P 18 0000 0490	38	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	G	G	G	G	N	G	G
P 18 0000 0518	57	T T TRESTLE	DRAINAGE	F	F	G	N	N	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P 18 0000 0524	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	N	N	N	G
P 18 0000 0527	57	T T TRESTLE	DRAINAGE	G	F	G	N	N	G	N	G	F	F	N	G	N	N	G	G	G	G	G	N	F	G
P 18 0000 0540	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	N	N	N	N	G	N	N	G	G	G	G	N	N	N	G
P 18 0000 0590	171	STEEL I BEAM	LITTLE DRY CR	F	G	G	G	N	G	G	G	F	F	G	F	N	N	F	G	G	G	G	N	F	G
P 18 0000 0592	57	T T TRESTLE	WHITE HORSE CR	F	F	F	F	N	G	N	G	N	F	N	G	N	N	F	G	G	G	G	N	F	F
P 18 0000 0614	57	T T TRESTLE	RED HORSE CR	F	G	G	G	N	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	F	G
P 18 0000 0779	153	CONCRETE T BEAM	SAND CREEK	G		G	G	G	G	G	G	G	G	G			G	G	G	G	G	G	G	F	G
P 19 0000 0000	276	PRE CONC BEAM	ANACONDA INT-I90	G		E		E	E					E			E	E	E	E	E	E	G	E	E
P 19 0000 0000T	276	PRE CONC BEAM	ANACONDA INT-I90	G		E		E	E					E			E	E	E	E	E	E	G	E	E
P 19 0000 0003	148	PRE CONC BEAM	NP RY	G		E		E	E					E			E	E	E	E	E	E		E	E
P 19 0000 0003P	148	PRE CONC BEAM	NP RY	G		E		E	E					E			E	E	E	E	E	E		E	E
P 19 0000 0005	70	PRE CONC BEAM	CLARK FORK	G		E		E	E		G	E	G	E			E	E	E	E	E	E		E	E
P 19 0000 0005P	70	PRE CONC BEAM	CLARK FORK	G		E		E	E		G	E	G	E			E	E	E	E	E	E		E	E

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Columns E thru Z
E = Excellent
G = Good
F = Fair
P = Poor
C = Critical

Column Z
N = New
R = To be Removed
U = Unable to Inspect

Column Z2
X = Written Explanation

CONTROL BRIDGE NUMBER F.A. SYSTEM A	F.A. ROUTE NUMBER	CONTROL JUNCTION MILEPOST TO TENTHS	BRIDGE LOCATION MILEPOST TO TENTHS DESCRIPTIVE	TOTAL LENGTH FEET B	DESCRIPTIVE FEATURES: MATERIAL & TYPE MAXIMUM SPAN - Also Structures not carrying road by type of facility, Underpass, Tunnel, Ferry C	NAME OF FEATURE CROSSED (River, Creek, Canal, Irrigation Ditch, Drainage, Railroad, Highways, Interchanges and Separations, Etc.) D	SUBSTRUCTURE: END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	SUPERSTRUCTURE: GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILING W	EXPANSION JOINTS X	PAINT Y	GENERAL CONDITION Z	NOT INSPECTED Z1	REMARKS Z2
P	19	0055	0105	41	CONCRETE T BEAM	WARM SPRINGS CR	G		G		G	G		G		G	G				G	G	G	G	G			G		
P	19	0055	0169	41	CONCRETE T BEAM	WARM SPRINGS CR	G		G		G	G		G		G	G				G	G	G	G	G			G		
P	19	0316	0353	63	CONCRETE T BEAM	FRED BURR CR	G	G		G		G		G	F	G	G				G	F	G	G	G			G		
P	19	0316	0490	71	CONCRETE T BEAM	BOULDER CR	F	F		P		G		F	P	F	G				F	G	G	G	F	G		F		X
P	19	0316	0533	114	CONCRETE T BEAM	FLINT CR	G			F		F		G	F	G	G			G	G	G	G	G	G	G		G		X
P	19	0316	0597	39	STEEL I BEAM	WILLOW CR	G		G		G	G		G		G	G				G	G	G	G	F		F	G		
P	19	0316	0631	301	PRE CONC BEAM	CLARK FORK	E		E	E	E	E	E	G	G	G	E			E	E	G	E	E	E	E	G	E		
P	19	0316	0633	163	PRE CONC BEAM	CMSTP& P RR	G		E	E	F	E					E		E		E	G	E	E	E	E	G	E		
P	19	0316	0637	188	PRE CONC BEAM	NP RR	G		E	E	F	E					E		E	E		G	E	E	E	E	G	E		
P	20	0000	0043	112	PRE CONC BEAM	DEER CR	E	N	E	E	E	E	N	E	E	E	E	N	N	E	E	G	E	N	E	N	E	E		
P	20	0000	0100	132	PRE CONC BM	LOWER 7 MILE CR	E	N	E	E	E	E	N	E	E	E	E	N	N	E	E	G	E	N	E	N	E	E		
P	20	0000	0124	122	PRE CONC BM	MORGAN CR	E	N	E	E	E	E	N	E	E	E	E	N	N	E	E	G	E	N	E	N	E	E		
P	20	0000	0156	190	T T TRESTLE	THIRTEEN MILE CR	G	G	G	G	G	G	N	G	N	G	G	G	N	N	G	G	G	G	G	N	G	G		
P	20	0000	0178	57	T T TRESTLE	LINDEN CR	G	G	G	G	G	G	N	G	N	G	G	G	N	N	G	G	G	G	G	N	G	G		
P	20	0000	0250	150	T T TRESTLE	BURNS CR	G	G	G	G	G	G	G	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	20	0000	0292	57	T T TRESTLE	BEEF SLOUGH	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	20	0000	0312	57	T T TRESTLE	GARDEN COULEE	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	G	G	G	G	N	F	G		
P	20	0000	0322	75	T T TRESTLE	USRS CANAL	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	F	G	G	P	N	F	G		

PLANNING [illegible]

A				E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
P 20 0000 0325	95	T T TRESTLE	DUNLAP CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P 20 0000 0328	63	T T TRESTLE	USRS CANAL	P	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P 20 0000 0375	75	T T TRESTLE	USRS CANAL	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P 20 0000 0378	57	T T TRESTLE	SEARS CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	F	G
P 20 0000 0466	76	UNT T TRESTLE	FOX CR	G	G	G	P	N	G	G	G	G	G	N	P	N	N	P	F	P	G	P	N	F	P
P 20 0000 0499	38	T T TRESTLE	DITCH	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	F	G
P 20 0500 0516	114	T T TRESTLE	LONE TREE CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	F	G	G	G	N	F	G
P 20 0525 0595	114	T T TRESTLE	FIRST HAY CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P 20 0525 0600	95	T T TRESTLE	SECOND HAY CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P 20 0525 0608	76	T T TRESTLE	THIRD HAY CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P 21 0749 0752	382	STEEL BEAM	GN RY	F		G			G					G			G	F		G	G	F	F	F	G
P 21 0749 0768	276	STEEL GIRDER	N SHELBY INT	G		E		E	E					E			E	E	G	E	E	E	G	G	E
P 22 0000 0142	76	T T TRESTLE	N FK EAGLE CR	F	G	G			F		G	F	G		G			G	G	G	G	F		F	G
P 22 0000 0153	19	T T TRESTLE	GAINES CR	G	G	G		F	G		G		G		G			G	G	G	G	F		F	G
P 22 0000 0204	76	T T TRESTLE	N FK EAGLE CR	G	G	G			G		G	F	F		G			G	G	G	G	G		F	G
P 22 0000 0215	95	T T TRESTLE	EAGLE CR	F	G	G			G	G	F	F	G		G			G	G	G	G	G		F	G
P 22 0000 0238	76	T T TRESTLE	REDSTONE CR	G	G	G			G		G		G		G			G	G	G	F	G		G	G

F	NUMBER	JUNCT. MILEPOST	BP MILE TO END	FEET					FNDN	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILS	EXPANSION	PAINT	GEN.	NOT	Z2
		A		B				D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
P	22	0000	0254	125	T	T	TRESTLE	BIG MUDDY CR	G	G	G			G	G	F	F	G		G			F	G	G	G	G		F	G		
P	22	0000	0262	38	T	T	TRESTLE	DRAINAGE	G	G	G			G		G	F	G		G			F	G	G	G	F		F	G		
P	22	0000	0278	19	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		F	G		
P	22	0000	0288	19	T	T	TRESTLE	ARCHER COULEE	G	G	G		G	G		G		G		G			F	G	G	G	G		F	G		
P	22	0000	0300	19	T	T	TRESTLE	DRAINAGE	F	G	G		G	G		G	P	G		G			F	G	G	G	F		F	G		
P	22	0000	0315	19	T	T	TRESTLE	STOCKPASS	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	22	0000	0323	11	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P	22	0000	0366	114	T	T	TRESTLE	PLENTYWOOD CR	F	G	G			P	G	F	G	F		G			G	G	G	G	F		F	G		
P	22	0000	0384	114	T	T	TRESTLE	MCCOY CR	F	G	G			P	G	F	G	G		G			F	G	G	G	F		F	G		
P	22	0000	0426	19	T	T	TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			F	G	G	G	F		P	G		
P	22	0000	0433	76	T	T	TRESTLE	MARRON CR	G	G	G		G	G		G	G	G		G			F	G	G	G	P		P	G		
P	22	0435	0446	38	T	T	TRESTLE	DRAINAGE	G	G	G			G		G	F	G		G			F	G	G	G	F		F	G		
P	22	0435	0456	19	T	T	TRESTLE	STOCKPASS	G	G	G			G			F			G			F	G	G	G	G		F	G		
P	22	0435	0463	95	T	T	TRESTLE	ATOR CR	G	G	F			P		F	G	G		G			F	G	F	G	F		F	F		
P	22	0435	0467	19	T	T	TRESTLE	STOCKPASS	F	G	P		G	G		G	F	G		G			G	G	G	G	G		G	F		X
P	22	0435	0470	7	T	T	TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	22	0435	0481	19	T	T	TRESTLE	STOCKPASS	F	G	G		G	G		G	F	G		G			F	G	G		F		F	G		
P	22	0435	0513	114	T	T	TRESTLE	ANTELOPE CR	F	F	F			G	G	F	F	G		G			F	G	F	G	F		F	F		
P	22	0435	0655	95	T	T	TRESTLE	MEDICINE LAKE OF	F	G	F			G	G	G	G	G		G			F	G	G	G	P		F	F		

PLANNING [illegible]

A	FEET B			E	F	G	H		J	K		M	N	O	P	Q	R	S	T		V	W			Z	
P 22 0435 0656	190	T T TRESTLE	MEDICINE LAKE	F	G	F			G	G	G	G	G		G			F	G	G	G	F		F	F	
P 22 0435 0698	7	T T TRESTLE	STOCKPASS	F	F	F		F	P			F	F		G			G	G	G		G		F	F	X
P 22 0435 0709	38	T T TRESTLE	HOMESTEAD CR	F	G	G			G				F		G			F	G	G	G	F		F	G	
P 22 0435 0719	38	T T TRESTLE	MCCABE CR	G	G	G			G		G	F	F		G			F	G	G	G	F		F	G	
P 22 0435 0728	57	T T TRESTLE	LOST CR	F	G	G			F		G	G	G		G			G	G	G	G	F		F	G	
P 22 0435 0758	106	PONY TRUSS	SHEEP CR	G		G			G		G		G	G			F	F	G	G	G	F	P	P	F	
P 22 0886 0895	264	STEEL GIRDER	SPRING CR-GN RY	G		G			G					G			G	G	F	G		G	G	G	G	
P 22 0886 0918	1169	THRU ST TRUSS	MISSOURI R	F		G	G		G	G	F		F	G	G	P	G	G	G	F	G	G	F	G	G	X
P 22 0886 0924	95	T T TRESTLE	MISSOURI R OF	G	G	G			G		G		G		G			G	G	G	G	G		G	G	
P 22 0886 0933	76	T T TRESTLE	DRY CR	F	G	G			G		G	F	G		G			G	G	G	G	F		F	G	
P 22 0886 0957	19	T T TRESTLE	WALLACE COULEE	G	G	G		G	G		G		G		G			F	G	G	G	F		F	G	
P 22 0886 1004	76	T T TRESTLE	CHERRY CR	F	G	G		G	G		G	F	G		G			F	G	G	G	F		F	G	
P 22 0886 1012	38	T T TRESTLE	MID FK CHERRY CR	G	G	G		G	G		G	G	G		G			F	G	G	G	F		F	G	
P 22 0886 1020	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G	
P 22 0886 1022	38	T T TRESTLE	HACKLEY COULEE	F	G	G		G	G		G	G	G		G			F	G	G	G	F		F	G	
P 22 0886 1031	76	T T TRESTLE	S FK CHERRY CR	G	G	G		G	G		G	G	G		G				G	G	F	F		F	G	
P 22 0886 1044	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		G	G	
P 22 0886 1094	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		G	G	
P 22 0886 1120	76	T T TRESTLE	N FK 1ST HAY CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G	

A	FEET B	C	D	EN… E	PILES F	BENTS G	PIERS H	WINGW…LS I	BA… J	ICE BRE… K	DR… L	RIP RAP M	SCO… N	GIR… O	STR… P	TR… Q	SH… R	CUR… S	MAR… T	DE… U	B… V	R… W	X	Y	Z	Z1	REM… Z2
P 22 0886 1126	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	N	N	G	N	N	G	G	G	G	G	N	G	G		
P 22 0886 1153	95	T T TRESTLE	S FK 1ST HAY CR	G	G	G	G	G	G	N	G	F	G	N	G	N	N	G	P	G	G	G	N	G	G		
P 22 0886 1156	38	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	P	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 22 0886 1229	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 22 0886 1243	19	T T TRESTLE	STOCKPASS	F	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 22 0886 1250	75	T T TRESTLE	USRS CANAL	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	G	G		
P 23 0000 0021		UNDERPASS*	INT-I 94	G		E			E					E			G	E		E		E	F	G	E		
P 23 0021 0027	50	T T TRESTLE	IRRIGATION CANAL	G	G	G	F		G		F	P	G		G			G		G	G	G		F	G		
P 23 0021 0033	19	UNT T TRESTLE	STOCKPASS	G	G	G			G		G	G	G		G			G		G	G	G		F	G		
P 23 0021 0067	57	T T TRESTLE	COWLES CR	G	G	G			G		G	G	G		G			G		G	G	G		F	G		
P 23 0021 0073	38	T T TRESTLE	IRRIGATION CANAL	G	G	G	F		G		F	G	G		G			G		G	G	G		F	G		
P 23 0021 0082	50	T T TRESTLE	IRRIGATION CANAL	G	G	G	F		G		G	F	F		G			G		G	G	G		P	G		
P 23 0021 0087	95	T T TRESTLE	LOG CR	G	G	G			G		F	F	G		G			G		G	G	G		F	G		
P 23 0021 0095	76	T T TRESTLE	MILLS CR	G	G	G			G	G	G		F		G			G		G	G	G		F	G		
P 23 0021 0103	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		F	G		
P 23 0021 0108	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		F	G		
P 23 0021 0112	76	T T TRESTLE	SQUAW CR	G	G	G			G		G	G	G		G			G		G	G	G		F	G		
P 23 0021 0159	138	PRE CONC BEAM	PUMPKIN CR	E		E			E		G	G	G	E			E	E	E	E		E		G	E		

P	23	0021	0282	38	T	T	TRESTLE	DRAINAGE	G	G	G			G		F	P	G	G	G		G	G	F	F	G
P	23	0021	0293	7	T	T	TRESTLE	STOCKPASS	G	G	G		G	G					G	G		G	G	G	F	G
P	23	0021	0300	57	T	T	TRESTLE	FIRE CR	G	G	G			G		G	G	G	G	G		F	G	G	F	G
P	23	0021	0313	38	T	T	TRESTLE	DRAINAGE	G	G	G			G		G	G	G	G	G		G	G	G	G	G
P	23	0021	0328	38	T	T	TRESTLE	DRAINAGE	G	G	G			G		F		F	F	G		F	G	G	G	G
P	23	0021	0338	57	T	T	TRESTLE	MAGGIE CR	G	F	G			F		G	P	G	G	G	G	G	G	G	F	G
P	23	0021	0343	7	T	T	TRESTLE	STOCKPASS	G	G	G		G	G					G	G		G	G	G	F	G
P	23	0021	0352	57	T	T	TRESTLE	DRAINAGE	F	G	G			F		G	F	G	G	G		G	G	G	F	G
P	23	0021	0358	7	T	T	TRESTLE	STOCKPASS	G	G	G		G	G					G	G		F	G	G	F	G
P	23	0021	0367	38	T	T	TRESTLE	DRAINAGE	G	G	G			G		G		G	G	G		G	G	G	G	G
P	23	0021	0383	19	T	T	TRESTLE	DRAINAGE	F	G	G			G		G		F	G	G		G		G	F	G
P	23	0021	0389	38	T	T	TRESTLE	DRAINAGE	F	F	F			F		G	G	G	G	G		F	G	G	E	F
P	23	0021	0400	57	T	T	TRESTLE	969 CR	G	G	G			G		G		G	G	G		F		G	F	G
P	23	0021	0404	7	T	T	TRESTLE	STOCKPASS	G	G	G		G	G					F	G		G	G	G	G	G
P	23	0021	0412	57	T	T	TRESTLE	BETZ CR	F	G	G			G		G	G	G	G	G		G	G	G	F	G
P	23	0021	0421	38	T	T	TRESTLE	COTTONWOOD CR	G	G	G			G		G	G	G	G	G		G	G	G	F	G
P	23	0021	0431	57	T	T	TRESTLE	BASIN CR	F	G	G			F		G		G	G	G		F	G	G	G	G
P	23	0021	0434	7	T	T	TRESTLE	STOCKPASS	F	G	G		G	G					G	G		F	G	G	G	G
P	23	0021	0445	95	T	T	TRESTLE	PUMPKIN CR	G	G	G	G		G	G	F	G	F	G	G	G	F	G	G	F	G

A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	23	0021	0451	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			G		F	G	G		F	G		
P	23	0021	0475	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G		G	G	G		E	G		
P	23	0021	0582	76	T T TRESTLE	DRAINAGE	F	G	G			G		G		G		G			G		G	G	G		G	G		
P	23	0021	0601	38	T T TRESTLE	LOST SOLDIER CR	G	G	G			G		G		G		G			G		G	G	G		G	G		
P	23	0021	0614	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	23	0021	0643	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		G	G		
P	23	0021	0668	57	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G			G	G		
P	23	0021	0698	114	T T TRESTLE	MIZPAH CR	G	G	G	G		G	G	G	G	G		G			G	G	F	G	G		F	G		
P	23	0021	0706	57	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		F	G		
P	23	0021	0728	38	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	23	0762	0791	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			F		P	G	P		P	F		
P	23	0762	0795	57	T T TRESTLE	DRAINAGE	G	G	G					G	G	G		G			G		F	G	G		F	G		
P	23	0762	0805	592	CONT ST TRUSS	POWDER R	F		G	G		G	G	F	G	G		G	G	G	F	G	G	G	G	G	P	G		
P	23	0831	0844	19	T T TRESTLE	DRAINAGE	G	G	G		F	F		G		G		G			G		G	G	G		F	G		
P	23	0831	0868	297	STEEL TRUSS	LITTLE POWDER R	G	G	G	G		G	G	G	G	G		F	F	G	F	F	G	F	F	G	F	G		
P	23	0831	0872	114	T T TRESTLE	E FORK CR	G	G	G	F		F	G	G	G	G		G			F		G	F	F		F	F		
P	23	0831	1264	92	CONCRETE GIRDER	WILLOW CR	G	G	G			G		G		G	G			G	G	F	G		G		F	G		
P	23	0831	1344	102	PRE CONC BEAM	THOMPSON CR	F		E	E	E	E	E	G	G	G	E			E	E	E	E		E		E	E		
P	23	0831	1361	142	PRE CONC BEAM	LIT MISSOUR R	F		E	E	E	E	E	G	G	G	E			E	E	G	G		E		G	E		

A		C	D	E	F	G			J	K		M	N	O	P	Q	R	S	T	U	V	W			
P 24 0000 0055	361	CONT ST GIRDER	BLACKFOOT R	G		G	G	G	G	G	G	E	E	E			E	E	G	G		E	E	G	E
P 24 0000 0090	75	T T TRESTLE	WEST TWIN CR	G		G	G		G		G		G		G			F	F	G		C		C	F
P 24 0000 0093	75	T T TRESTLE	EAST TWIN CR	G		G	G		G		G		G		G			F	F	G		C		C	F
P 24 0000 0112	446	CONT D ST TRUSS	BLACKFOOT R	G		G	G		G	G	G		F		G	G	G		F	P	G	F	G	C	G
P 24 0000 0229	11	T T TRESTLE	STOCKPASS	G	G	G			G						G			C	G	G		C		C	F
P 24 0000 0245	11	T T TRESTLE	STOCKPASS	G	G	G			G						G			C	G	G		C		C	F
P 24 0000 0253	55	T T TRESTLE	ELK CR	G	G	G	G		G		G	F	G		G			P	G	G	F	P		C	G
P 24 0000 0267	244	PLATE GIRDER	BIG BLACKFOOT R	G		G	G	G	G	G	G	G	G		G	G		G	F	G	F	G	C	G	G
P 24 0000 0271	11	T T TRESTLE	STOCKPASS	E	E	E		E	E						E			F	E	G		G		G	E
P 24 0000 0280	11	T T TRESTLE	STOCKPASS	E	E	E		E	E						E			F	E	G		G		G	E
P 24 0000 0302	11	T T TRESTLE	STOCKPASS	E	E	E		E	E						E			F	E	F		F		P	G
P 24 0000 0313	113	CONT STEEL BEAM	CLEARWATER R	G		G	G		G	E	E	E	E	E			E	G	G	G		G	F	G	G
P 24 0000 0314	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			F	G	G		G		G	G
P 24 0000 0415	100	T T TRESTLE	MONTURE CR	G	G	G	G		G	E	F	F	G		G			F	G	F	F	G		C	G
P 24 0000 0496	182	CONT CONC T BM	N FK BLACKFOOT R	G		E	E		E	E	E	E		E			E	E	E	G		G		P	E
P 24 0000 0579	57	T T TRESTLE	ARRASTRA CR	G	G	G	G	G	G		P		G		G			F	G	G		G		G	G
P 24 0000 0579	57	T T TRESTLE	ARRASTRA	G	G	G		G	G		F		G	G	G			G	P	G	G	G		G	G
P 24 0000 0689	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G			G	G			G	G	G	G	G		G	G
P 24 0000 0695	19	T T TRESTLE	BEAVER CR	G	G	G		G	G		G	F	G	G	G			G	P	G	G	G		G	G

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

[illegible]

N New
R [illegible] be [illegible] moved

BRIDGE NUMBER (F.A. SYSTEM, NUMBER, CONTROL JUNCTION, MILE, BRIDGE, DEPT.) A	TOTAL LENGTH FEET B	DESCRIPTIVE FEATURES: MATERIAL & TYPE, MAXIMUM SPAN C	NAME OF FEATURE CROSSED (River, Creek, Canal, Irrigation or Drainage, Railroad, Highways, Interchanges and Separations, Etc.) D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILING W	EXPANSION X	PAINT Y	GENERAL Z	NOT INSPECTED Z1	REMARKS Z2
P 24 0000 0697	38	T T TRESTLE	KEEP COOL CR	G	G	G		G	G		G	G	G	G	G			G	F	G	G	G		G	G		
P 24 0000 0701	38	T T TRESTLE	SPRING CR	G	G	G		G	G		G	G	G	G	G			G	G	G	G	G		G	G		
P 24 0000 0710	25	T T TRESTLE	SPRING CR OF	G	G	G		G	G		G	G	G	G	G			G	G	G	G	F		G	G		
P 24 0000 0767	11	T T TRESTLE	STOCKPASS	G	G	G		G	G					G	G			G	G	G	G	G		G	G		
P 24 0000 0778	178	CONT ST I BEAM	LANDERS FORK	F		G	G	G	G	G	F		F	G	G		G	P	F	G	G	G	G	G	G		
P 24 0000 0784	30	T T TRESTLE	DRAINAGE	G	G	G		F	G		G	G	G	G	G			G	G	G	G	G		G	G		
P 24 0000 0794	30	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	F		G	G		
P 24 0000 0808	30	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	F		G	G		
P 24 0000 0820	30	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 24 0000 0829	75	T T TRESTLE	ALICE CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 24 0000 0855	38	T T TRESTLE	CADOTTE CR	G	G	G		G	G		G	G	G		G			G	G	G	F	G		G	G		
P 24 0000 0973	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 0000 0979	101	T T TRESTLE	MID FK DEARBORN	G	G	G		G	G	G		G		G			G	G	G	G	G			G	G		
P 24 0000 0984	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 24 0000 0990	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 24 0000 0995	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 24 0000 1002	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 24 0000 1025	185	CONT ST GIRDER	DEARBORN R	G		G	G	G	G	G	G		G	G			G	G	G	G	G	G	P	G	G		X
P 24 0000 1042	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	F	G	G	G		G	G		

A			C	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z		
P 24 0000 1078	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1096	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1112	75	T T TRESTLE	FLAT CR	G	G	F		G	G	G					G			G	F	G	G	G		G	G		
P 24 1090 1125	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1139	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1144	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1159	11	T T TRESTLE	STOCKPASS	P	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1179	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1194	63	T T TRESTLE	DRAINAGE	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1212	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1219	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1242	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1252	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1259	25	T T TRESTLE	IRRIGATION CANAL	G	G	G		G	G						G			G	G	G	G	C		G	G		X
P 24 1274 1385	284	STEEL TRUSS	SUN R	G		G	F	G	G	G	G		G		G	G	G	G	G	F	G	G	G	P	G		X
P 24 1274 1390	57	T T TRESTLE	MILL COULEE	G	F	F		G	F		G	G	G		G			G	G	G	G	G		G	G		
P 24 1397 1407	150	T T TRESTLE	SIMMS CR	G	G	G		G	G	G	G	G	G		G			G	F	G	F	G		G	G		X
P 24 1397 1416	39	CONCRETE T BEAM	IRRIGATION CANAL	G		G		G	G		G	G	G	G				G	F	G		G			G		
P 24 1397 1426	57	T T TRESTLE	HEPPLER COULEE	G	G	G		G	G		G	F	G		G			F	G	G	G	G		G	G		

P 24 1397 1431	19	T T TRESTLE	STOCKPASS	G	G	G		G	G				G		G			G	G	G	G	G		G	G	
P 24 1397 1460	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	F	G	G	G		G	G	X
P 24 1397 1485	19	T T TRESTLE	STOCKPASS-DR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G	
P 24 1397 1513	76	T T TRESTLE	DRY CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P 24 1397 1561	95	T T TRESTLE	SPRING COULEE CR	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		G	G	
P 24 1397 1597	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P 24 1397 1602	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P 24 1397 1604	79	CONCRETE T BEAM	S FK SUN R	G		G	G	G	G		G		G	G			G	G	G	G		P	G		G	X
P 24 1397 1605	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			P	G	G	G	G		G	G	
P 25 0000 0002	114	T T TRESTLE	HORSE CR	P	F	F	F	P	P	G	F	F	P	N	G	N	N	G	G	G	F	G	N	G	F	
P 25 0000 0009	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	P	N	G	N	G	N	N	G	F	G	G	G	N	G	G	
P 25 0000 0017	38	T T TRESTLE	LONE TREE CR	G	G	G	G	G	G	N	G	F	G	N	G	N	N	G	F	G	G	G	N	G	G	
P 25 0000 0024	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	F	F	N	G	N	N	G	F	G	G	G	N	F	G	
P 25 0000 0055	76	T T TRESTLE	LOST CR	F	G	G	G	N	G	N	G	F	F	N	G	N	N	G	F	G	G	F	N	F	F	
P 25 0000 0085	76	T T TRESTLE	S FK BUFFALO CR	G	G	G	G	N	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	F	G	
P 25 0000 0102	76	T T TRESTLE	N FK BUFFALO CR	G	G	G	G	N	G	N	G	F	G	N	G	N	N	G	G	G	F	F	N	P	G	
P 25 0000 0126	11	T T TRESTLE	STOCKPASS	G	G	G	N	N	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	F	G	
P 25 0000 0141	11	T T TRESTLE	STOCKPASS	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	F	G	G	F	N	P	G	

PLANNING [illegible]

A	FEET B			C	D	E	F	G	H		J	K	L	M	N	O	P	Q	R	S	T		V	W		Y	Z	Z	Z
P 25 0000 0149	76	T	T	TRESTLE	DUCK CR	G	G	G	G	N	F	N	G	P	P	N	G	N	N	G	F	G	G	G	N	P	F		
P 25 0000 0185	57	T	T	TRESTLE	DRAINAGE	G	G	G	F	N	F	N	G	F	P	N	G	N	N	G	F	F	F	G	N	G	F		
P 25 0000 0202	114	T	T	TRESTLE	COW CR	G	G	G	G	N	G	F	G	G	G	N	G	N	N	G	F	G	F	G	N	F	G		
P 25 0000 0212	57	T	T	TRESTLE	DRAINAGE	F	G	G	N	N	G	N	G	G	G	N	G	N	N	F	F	G	G	G	N	G	G		
P 25 0000 0227	11	T	T	TRESTLE	STOCKPASS	G	G	G	N	N	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 25 0000 0242	19	T	T	TRESTLE	STOCKPASS	G	G	G	N	N	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 25 0000 0253	57	T	T	TRESTLE	E FK WOLF CR	F	G	G		G	G		G	G	G		G			F	G	G	G	G		F	G		
P 25 0000 0262	11	T	T	TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G		G		G	G		
P 25 0000 0268	11	T	T	TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			F	G	G		G		G	G		
P 25 0000 0277	114	T	T	TRESTLE	WOLF CR		G	G		G	G	G	F	G	G		G			G	G	G	G	G		F	G		
P 25 0000 0294	76	T	T	TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G	G	G	G	F		F	G		
P 25 0000 0315	57	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 25 0000 0342	57	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			F	G	G	G	G		F	G		
P 25 0000 0354	25	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G	F	F		G			G	G	G	G	G		G	G		
P 25 0000 0387	57	T	T	TRESTLE	SHEEP CR	F	G	G		G	G		G	G	G		G			F	G	G	F	G		G	G		
P 25 0000 0397	19	T	T	TRESTLE	DRAINAGE	G	G	G		F	F		G	F	G		G			G	G	G	F	G		G	G		
P 25 0000 0413	19	T	T	TRESTLE	STOCKPASS	G	G	G		G	G		G	G	G		G			G	G	G	G	F		F	G		
P 25 0000 0418	19	T	T	TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			F	G	G	G	F		F	G		
P 25 0000 0420	38	T	T	TRESTLE	DRAINAGE	F	G	G		F	F		G	F	G		G			G	G	G	G	F		G	G		

A	FEET B	C	D	E	F	BENTS G	PIERS H	WINGWALL I	J	ICE BREAKER K	L	RIP RAP M	SCOUR N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P 25 0000 0422	19	T T TRESTLE	STOCKPASS	G	G	G			F		G	F	G		G			F	G	G	G	F		G	G		
P 25 0000 0450	7	T T TRESTLE	STOCKPASS	G	G	G			F						G					G					G		
P 25 0000 0465	1074	ST THRU TRUSS	MISSOURI R	G		F	F		F	G	G		G		G	G	F	F	G	F	G	F	F	F	F		
P 25 0469 0503	76	T T TRESTLE	LITTLE WOLF CR	G	G	G			G		G	P	G		F			F		G		F		F	G		
P 25 0469 0513	57	T T TRESTLE	MOSQUITO CR	G	G	G			G		G	F	G		G			G	G	G	G	G		G	G		
P 25 0469 0528		UNDERPASS	GN RY			F			F					G				F		P		G		F	F		
P 26 0000 0003	57	T T TRESTLE	DITCH	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 26 0000 0012	1231	STEEL TRUSS	YELLOWSTONE R	G	N	G	G	F	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	F	G		
P 26 0000 0022	57	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 26 0000 0061	113	CONCRETE T BEAM	BENNIE PEER CR	G	N	G	F	G	G	G	G	G	F	G	N	N	G	G	G	G	N	G	N	N	F		
P 27 0000 0013	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	N	G	N	P	N	N	G	G	G	G	G	N	G	F		
P 27 0000 0023	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	P	G	N	G	N	N	G	G	G	G	G	N	G	F		
P 27 0000 0050	57	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	F	G	F	G	G	N	G	G		
P 27 0000 0060	95	T T TRESTLE	LITTLE BEAVER CR	P	G	G	G	G	G	G	G	F	P	N	G	N	N	G	G	G	G	G	N	G	G		
P 27 0000 0064	57	T T TRESTLE	COLLINS CR	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 27 0000 0072	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	N	N	N	N	G	N	N	G	G	G	G	G	N	G	G		
P 27 0000 0080	57	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

A				B	C			D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
				FEET				NAME																						
P	27	0000	0095	11	T	T	TRESTLE	STOCKPASS	P	G	G	N	G	G	N	F	N	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0000	0114	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	F	F	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0000	0151	11	T	T	TRESTLE	STOCKPASS	P	G	G	N	G	F	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0000	0173	11	T	T	TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0000	0183	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0000	0202	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0000	0214	57	T	T	TRESTLE	DRAINAGE	F	G	G	N	G	G	N	G	F	F	N	G	N	N	F	G	G	G	G	N	G	G
P	27	0000	0351	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	F	G	G	G	G	N	F	G
P	27	0354	0358	63	T	T	TRESTLE	SANDSTONE CR	G	G	G	N	G	G	N	G	G	F	N	G	N	N	G	G	G	G	G	N	F	G
P	27	0354	0550	75	T	T	TRESTLE	ASH CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	F	G	G	G	G	N	G	G
P	27	0354	0574	38	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0354	0608	45	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0354	0620	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	F	G	F	G	G	N	G	G
P	27	0354	0654	19	T	T	TRESTLE	DR & STOCKPASS	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0354	0670	19	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0354	0680	45	T	T	TRESTLE	DRAINAGE	G	F	F	N	G	G	N	G	G	G	N	G	N	N	G	G	F	G	G	N	G	F
P	27	0354	0726	76	T	T	TRESTLE	DRAINAGE	G	F	G	F	G	G	N	G	F	F	N	G	N	N	G	G	F	G	G	N	G	F
P	27	0354	0783	150	T	T	TRESTLE	BEAVER CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P	27	0354	0796	150	STEEL GIRDER			BEAVER CR	G	N	G	G	G	G	G	G	G	G	G	N	N	G	G	G	G	N	G	G	F	G

							E	F	G	PIERS H		J	K	L	M	N	O	P	Q	R		T	U	V	W	X	Y	Z	
P	27	0354	0799		UNDERPASS	NP RY	G	N	G	N	N	G	N	N	N	N	G	N	N	G	G	F	N	N	G	N	P	G	
P	28	0000	0057	25	CONCRETE T BEAM	DRAINAGE	G		G			G		G		G	G				G		G		G			G	
P	28	0000	0072	63	CONCRETE T 8EAM	W FK ROCK CR	G		G			G		G	G	G	G				G		G		G			G	
P	28	0000	0243	122	CONCRETE T BEAM	ROCK CR	G		G			G		G	G	G	G				G	G	G		G			G	
P	28	0000	0343	123	STEEL I BEAM	ROCK CR	F	F	P	F	F	P	G	F	G	G	G	P			G		G		G		F	C	X
P	28	0000	0348	38	T T TRESTLE	DRAINAGE	F	F	G			G		G		G		F			G		G	G	G		F	G	X
P	29	0000	0021	25	T T TRESTLE	WEBER IRRIGATION	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P	29	0000	0166	45	T T TRESTLE	HERMAN GULCH	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G	
P	29	0000	0178	38	T T TRESTLE	GRANITE CR	G	G	G		G	G		G	F	G		G			P	G	G	G	F		F	G	
P	29	0000	0182	38	T T TRESTLE	MCNEAL GULCH	G	G	G		G	G		G	F	G		G			P	G	G	G	F		F	G	
P	29	0000	0187	57	T T TRESTLE	WATER GULCH	G	G	G		G	G		G	P	F		F			G	G	G	F	F		F	F	
P	29	0000	0258	38	T T TRESTLE	ALOER CR	G	G	G		G	G		G		G		G			G	G	G	G	F		F	G	
P	29	0000	0267	19	T T TRESTLE	CALIFORNIA CR	G	G	G		G	G		G		G		G			G	G	G	G	F		F	G	
P	29	0000	0284	38	T T TRESTLE	RAMSHORN CR	G	G	G		G	G		G	F	G		G			G	G	G	G	F		F	G	
P	29	0000	0303	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	F	F		F	G	
P	29	0000	0341	19	T T TRESTLE	INOIAN CR	G	G	G		F	G		G	G	G		G			G	G	G	G	F		F	G	
P	29	0000	0343	19	T T TRESTLE	INOIAN CR	G	G	G		F	G		G	G	G		G			G	G	G	G	F		F	G	

PLANNING SURVEY

F.A. SYS	F.A. RT. NUMBER	CONTROL JUNCTION	MILE POST TO TENTHS	TOTAL FEET	C	D NAME	E END FILLS	F PILES	G BENTS	H PIERS	I WING WALLS	J BACK WALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TRUSS	R SHOES	S CURBS	T	U DECK	V BRACING	W RAILING	X EXPANSION	Y PAINT	Z GENERAL	Z1 NOT INSP.	Z2 REMARKS
P	29	0000	0372	57	T T TRESTLE	WISCONSIN CR	G	G	G		F	G		G	G	G		G			G	G	G	G	F		F	G		
P	29	0428	0498	358	ST PONY TRUSS	JEFFERSON R	G		G	F		G	G	G		G		G	G	G	G	G	G	G	G	G	G	G		
P	29	0428	0499	25	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G		G		F			F	G	G	G	F		P	G		
P	29	0428	0503	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		F			G	G	F	F	G		P	F		X
P	29	0428	0507	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		F			F	G	G	F	F		P	F		
P	29	0428	0509	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		F			P	G	G	F	F		P	F		
P	29	0428	0513	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	F	F		P	G		
P	29	0428	0516	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	P	F	F		P	F		
P	29	0428	0519	25	T T TRESTLE	DRY WASH	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
P	29	0428	0521	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	29	0428	0522	25	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	29	0428	0531	19	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	29	0428	0533	25	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	29	0428	0536	25	T T TRESTLE	CHERRY CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	29	0428	0549	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
P	29	0428	0550	19	T T TRESTLE	CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P	29	0428	0553	19	T T TRESTLE	CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P	29	0428	0557	19	T T TRESTLE	CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P	29	0428	0564	19	T T TRESTLE	CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		

	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z		
P 29 0428 0571	57	T T TRESTLE	LITTLE CHERRY CR	G	G	G		G	G		G	F	G		G			G	G	G	G	F		P	G		
P 29 0428 0573	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
P 29 0428 0598	57	T T TRESTLE	FISH CR	G	G	G		G	G		G	F	F		G			G	G	G	G	G		P	G		
P 29 0428 0632	136	STEEL BEAM	CMSTP&P RY	G		G			G				G				G	G	G	G	G	G	G		G		
P 29 0428 0655	76	T T TRESTLE	LIT PIPESTONE CR	G	G	G		G	G		G		G		G			G	G	G	G	F		P	G		
P 30 0000 0113	57	T T TRESTLE	DAHL CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 30 0000 0143	95	T T TRESTLE	MAIN CR	F	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P 30 0000 0153	25	T T TRESTLE	DRY CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 30 0000 0163	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		F	G		
P 30 0000 0170	76	T T TRESTLE	SHALLOW CR	G	G	G			G		G	G	G		G			G	G	G		G		P	G		
P 32 0037 0081	89	CONCRETE T BEAM	TULE CR	F		P			G		G	F	G	G			F	F	G	G		G			F		X
P 32 0037 0120	38	T T TRESTLE	BITTNER COULEE	G	G	G			F						G			G	G	G	G	G		F	G		
P 32 0037 0147	57	T T TRESTLE	S FK CHELSEA CR	G	G	G			G			F	G		G			G	G	G	G	G		F	G		
P 32 0037 0153	76	T T TRESTLE	CHELSEA CR	G	G	G			G			G	F		F			G	G	G	G	G		F	G		
P 32 0037 0203	95	T T TRESTLE	BOX ELDER CR	G	G	G			G	G	G	G	F		G			G	G	G	G	G		G	G		
P 32 0037 0217	38	T T TRESTLE	N FK BOX ELDER C	G	G	G			F		G	G	F		G			G	G	G	G	G		G	G		
P 32 0037 0275	76	T T TRESTLE	SPRAGUE COULEE	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

RATING

F A SYST	F A R NUMBER	CONTR JUNCT MILEPOST TO TENTHS	BRIDGE MILEPOST TO TENTHS	TOTAL LENGTH FEET	DESCRIPTION MAT TYPE	NAME	EN F S	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIPRAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MA	DECK	BRACING	RAILING	EXPAN	PAINT	GENERAL	NOT INSP	REMARKS
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	32	0037	0300	57	T T TRESTLE	MIDWAY COULEE	F	G	G			G			P	G		G			G	G	G	G	F		G	G		
P	32	0037	0336	76	T T TRESTLE	W FK POPLAR R	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P	32	0037	0341	114	T T TRESTLE	W FK POPLAR R OF	F	G	G			G	G	G	F	F		G			G	G	G	G	G		F	G		
P	32	0037	0343	185	ST PONY TRUSS	W FK POPLAR R	F		G	G		G	G	G	G	G	G		G	P	G	G	G	G	G	P	P	G		X
P	32	0037	0381	38	T T TRESTLE	NELSON COULEE	F	G	G			G		G	G	G		G			G	G	G	G	F		F	G		
P	32	0037	0409	57	T T TRESTLE	BELKNAP CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P	32	0037	0439	38	T T TRESTLE	DICKINSON COULEE	G	G	G			G		G	G	G		G			F	G	G	G	F		G	G		
P	32	0037	0450	76	T T TRESTLE	BRICKER COULEE	G	G	G			G		G	G	G		G			G	G	G	G	F		F	G		
P	32	0037	0466	185	STEEL TRUSS	POPLAR R	F		G	G		G	G	G	G	G	G	G	G	G	G	G	F	G	G	F	P	G		X
P	32	0037	0472	19	T T TRESTLE	STOCKPASS	G	G	G			G						G			G	G	G	G	P		F	G		
P	32	0037	0481	57	T T TRESTLE	MANTERNACH COU	G	G	G			G		G	F	F		G			G	G	G	G	F		G	G		
P	32	0513	0555	143	CONC T BEAM	E FK POPLAR R	G		G	G		G	G	G	G	G	G			G	G	F	G		G		G	G		
P	32	0513	0595	143	CONC T BEAM	E FK POPLAR R	G		G	G		G	G	G	G	G	G			G	G	G	G		G		G	G		
P	32	0513	0626	50	T T TRESTLE	COW CR	F	G	G		G	G	G	G	P	G		G			G	G	G	G	G		P	G		
P	33	0000	0005	271	CONT STEEL BEAM	GN RY	G		G		G	G					G	G		G	G		F	G	G	G	F	G		
P	33	0000	0008	698	RIV PL GIRDER	KOOTENAI R	G		G	G	G	G	G	G	G	G	G	G		G	G	P	G	G	G	G	G	G		
P	33	0000	0300	17	ENCASED GIRDER	BRISTOW CR	G		G		G	G		G		G						G	G		G			G		
P	33	0000	0366	12	CONCRETE SLAB	ROSEY CR	G		G		G	G		G		G						G	G		P			G		

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W			Z	Z	Z2
P 33 0000 0388	12	CONC SLAB	GRIBLER CR	G		G		G	G		G		G						G	G		G			G		
P 33 0000 0422	24	ENCASED GIR	PARSNIP CR	G		G		G	G		G		G						F	G		G			G		
P 33 0000 0423	12	CONC SLAB	N FK RAINY CR	G		G		G	G		G		G						G	G		F			G		
P 33 0000 0471	60	STEEL GIRDER	BIG CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G		P	G		
P 33 0000 0586	483	STEEL TRUSS	KOOTENAI R	F	P	F	P	F	F	P	G	F	G			F	F	F	G	F	F	P	F	P	F		X
P 33 0000 0622	130	ST PONY TRUSS	TABACCO R	F		G		G	G		G	F	G			G	G	G	G	G	G	G	G	F	G		
P 35 0000 0010	25	T T TRESTLE	REPUBLICAN DT	G	G	G		G	G		G		G		G			G		F	G	G		P	G		
P 35 0000 0017	25	T T TRESTLE	HEDGES CANAL	F	G	G		G	G		G		G		G			G		F	G	G		P	G		
P 35 0000 0029	76	T T TRESTLE	SKALKAHO CR	G	G	G		G	G	G	F		G		G			G		F	G	G		P	G		
P 35 0000 0036	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G		P	G	G		F	G		
P 35 0000 0043	19	T T TRESTLE	WARD CANAL	G	G	G		G	G		G		G		G			G		G	G	G		P	G		
P 35 0000 0046	50	T T TRESTLE	BRI CANAL	G	G	G		F	F	G	G		G		G			G		P	G	G		P	G		
P 35 0000 0052	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G												
P 35 0000 0364	45	ST PONY TRUSS	W FK ROCK CR	G		F		P	P		G		G	F	F	F	F	F		F	F	F		C	F		
P 35 0000 0397	45	ST PONY TRUSS	W FK ROCK CR	P		P		C	C				P		G	G	F	P		P	F	F		C	P		
P 35 0000 0423	140	CONCRETE T BEAM	ROCK CR	G		G	P		G		G	G	G	G	G		G	P	F	G	G	F	G		F		
P 36 0000 0012	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

RATING

P - Poor

F A SYSTEM	F A ROUTE NUMBER	CONTROL-JUNCTION MILEPOST TO TENTHS	BRIDGE MILEPOST TO TENTHS DESCR	TOTAL LENGTH FEET	DESCRIPTION MATERIAL AND TYPE	FEATURE	ENDWALLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	FLOOR F	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MAR	DECK	BRACING	RAILING	EXPANSION	PAINT	GEN RAL COND	NOT INSPECTED	REMARKS
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
P	36	0000	0030	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	36	0000	0140	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	36	0189	0198	50	PRE CONC BEAM	HOT SPRINGS CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G		G	G		
P	36	0189	0267	57	T T TRESTLE	LIT BITTERROOT R	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	36	0189	0290	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	36	0189	0307	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	36	0189	0311	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	36	0189	0312	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	36	0189	0325	38	T T TRESTLE	SULLIVAN CR	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	36	0189	0328	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	36	0189	0339	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	36	0189	0351	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	36	0189	0359	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	37	0000	0000	210	PRE CONC BEAM	INT-I90	F		E			E					E			E	E		E		E		G	E		
P	37	0000	0013	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G	G	G		G			G		G	G	G		G	G		
P	37	0000	0030	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G		G	G	G		G	G		
P	37	0000	0081	76	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		P			G		G	G	G		F	G		X
P	37	0000	0093	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		P			G		G	F	G		F	G		X

A	EET B		D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X		Z	Z	Z2
P 37 0000 0129	95	T T TRESTLE	W FK TULLOCK CR	G	G	G			F		G	G	G		P			G		G	F	G		G	G		X
P 37 0000 0147	76	T T TRESTLE	DRAINAGE	F	G	G			F		G	G	G		P			G		G	G	G		G	G		X
P 37 0000 0156	38	T T TRESTLE	DRAINAGE	G	G	G			F		G	F	G		P			G		G	G	G		G	G		X
P 37 0000 0165	38	T T TRESTLE	DRAINAGE	G	G	G			F		G	G	G		P			G		G	G	G		G	G		X
P 37 0000 0170	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		P			G		G	G	G		G	G		X
P 37 0000 0249	75	T T TRESTLE	ROSEBUD CR	G	G	G			G		G	G	G		F			G	G	G	G	G		G	G		X
P 37 0000 0255	38	T T TRESTLE	8US8Y CR	G	G	G			G		G	G	G		F			G	G	G	G	G		G	G		X
P 37 0000 0278	75	T T TRESTLE	PARK CR	G	G	G			G		G	G	G		F			G		G	G	G		G	G		X
P 37 0000 0283	100	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		F			G		G	G	G		G	G		X
P 37 0000 0293	75	T T TRESTLE	E PORCUPINE CR	G	G	G			G		G	G	G		F			G		G	G	G		G	G		X
P 37 0000 0303	75	T T TRESTLE	TWO MOON CR	G	G	G			G		G	G	G		P			G	G	G	G	G		G	G		X
P 37 0000 0313	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 37 0000 0321	75	T T TRESTLE	KILLSNIGHT CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		X
P 37 0000 0337	75	T T TRESTLE	RIDGEWALKER CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 37 0000 0367	95	T T TRESTLE	MUDDY CR	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P 37 0000 0420	75	T T TRESTLE	LAME DEER CR	F	G	G			G		G	G	G		G			F		F	G	G		F	G		
P 37 0000 0614	200	CONT ST GIRDER	TONGUE R	F		G	G		G	G	G	G	G	G			G	G	G	G		G	G	G	G		
P 37 0000 0631	112	T T TRESTLE	OTTER CR	G	G	G			F		G		G		G			G	G	G	G			F	G		
P 37 0000 0635	7	T T TRESTLE	STOCKPASS	G		G		G	G						G					G		G		G	G		

PLANNING Y CONDITION REPORT

RA C

Co ur s E r

E

P = Poor

ical

F ir

e Removed

nable to Inspect

n t

CONTROL BRIDGE NUMBER F A SYST, F A ROUTE NUMBER, CONTROL JUNCTION MILEPOST TO TENTHS, BRIDGE MILEPOST TO TENTHS, DESCR A	TOTAL LENGTH FEET B	DESCRIPTION MATERIAL & TYPE MAXIMUM structures or by Interpost, ne, erry C	NAME Sc Irrigat- ion Railroad, Highway Changes and Separation, Etc D	FN F LLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSSES Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILING W	EXPANSION X	PAINT Y	GENERAL CONDITION Z	NOT INSP Z	REMARKS ZZ
P 37 0000 0639	7	T T TRESTLE	STOCKPASS	G		G		G	G						G					G		P		F	G		
P 37 0000 0661	10	T T TRESTLE	STOCK PASS	G		F		G	F						G					G					G		
P 37 0000 0670	6	T T TRESTLE	STOCKPASS	G		G		G	G						G					G					G		
P 37 0000 0674	81	T T TRESTLE	E FK OTTER CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 37 0000 0724	38	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 37 0000 0732	7	T T TRESTLE	STOCKPASS	G		G		G	G						G					G					G		
P 37 0000 0735	38	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 38 0000 0016	138	STEEL BEAM	WHITEFISH R	G	G	G	G	G	G	G	G	F	G	G	G			G	F	G	G	P	G	G	G		X
P 38 0000 0079	496	STEEL TRUSS	FLATHEAD R	P		G	G	G	G	G	G		G		G	G	G	G	F	G	G	G	G	G	G		X
P 38 0000 0080	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	F		F	G		
P 38 0000 0085	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	F		F	G		
P 41 0040 0045	109	CONCRETE T BEAM	GN RY	P		P		G	G					P			G	G		G		F	G		P		X
P 41 0040 0046		UNDERPASS*	US BYP	G		G	G							G			G			G	G			G	G		
P 41 0040 0054		UNDERPASS	GN RY	G		G	G	G	G				G	G	G		G			P				F	G		
P 41 0040 0057		UNDERPASS*	US 89	G		G		G	G		G		G	F						F					F		
P 41 0040 0058		UNDERPASS	CMSTP&P RR	G		G		G	G		G		G	G			G			F				F	G		

A	B			E	F	G	H		J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
P 42 0000 0054	205	PRE CONC BEAM	TIMBER CR	G	N	G	G	G	E	G	G	G	G	G	N	N	E	E	G	G	N	E	G	E	E		
P 42 0000 0147	133	PRE CONC BEAM	NELSON CR	G	N	G	G	G	E	N	G	G	G	G	N	N	E	E	G	G	N	E	N	E	E		
P 42 0000 0618	19	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	F		G			G	G	G	G	G		P	G		
P 42 0000 0626	57	T T TRESTLE	BARTON COULEE	F	G	G			G		G	G	G		G			G	G	G	G	G		P	G		
P 42 0000 0634	76	T T TRESTLE	GALPIN COULEE	F	F	P			G		G	G	G		G			G	G	G	G	G		P	F		X
P 42 0000 0651	57	T T TRESTLE	GALPIN COULEE	G	G	G			G		G	G	G		G			G	G	G	G	G		P	G		
P 42 0000 0662	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G				G		
P 42 0000 0692	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G	G	G		G			G	G	G	G	F		P	G		
P 42 0000 0704	38	T T TRESTLE	CANAL	G	G	G	F		G		P		G		G			P	G	G	G	F		P	G		X
P 42 0000 0714	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G	G	G	G	F		P	G		
P 42 0000 0725	152	T T TRESTLE	MILK R OF	F	G	G			F		G	G	G		G			G	G	G	G	F		P	G		
P 42 0000 0727	473	ST THRU TRUSS	MILK R	F	G	G	G		F		G	G	G		G	F	P	G	G	G	G	G	P	P	G		X
P 42 0000 0740	57	T T TRESTLE	SPRAGUE COULEE	G	G	G			G		G		F		G			G	G	G	G	F		P	G		
P 42 0000 0760		UNDERPASS	GN RY			G			G					F				G	G	G				P	G		
P 43 0000 0001	34	CONCRETE SLAB	BIG SPRING CR	G		G		G	G		G		G					G	G	G	G	G		G	G		
P 43 0003 0007	63	CONCRETE T BEAM	BIG SPRING CR	G		P	F	F	F		G	G	F	F				F		F		F			F		X
P 43 0003 0100	38	T T TRESTLE	WARM SPRINGS CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 43 0003 0379	57	T T TRESTLE	BOX ELDER CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		

A				B FEET	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z
P	43	0003	0385	57	T T TRESTLE	BOX ELDER CR	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	45	0000	0008		UNDERPASS	NP RY	G		F		P	G					E			G			G	G	G		F	G		
P	45	0000	0009	11	T T TRESTLE	STOCKPASS	G	G	G		F	F						F			P	E	G	G	F		G	G		
P	45	0000	0010	380	CONT ST GIRDER	YELLOWSTONE R	G		G	G	G	G	G	F	F	G	G			F	G	G	F	G	F	G	F	G		
P	45	0000	0018	137	CONCRETE T BEAM	BIG TIMBER CR	G		F	G	F	G	G	F	F	G	P			F	F	E	G		F	F	P	F		
P	45	0000	0097	57	T T TRESTLE	DRAINAGE	G	F	G	G	F	G		G	G	G		G			F	E	G	G	G		G	G		
P	45	0000	0099	63	T T TRESTLE	SFK TENMILE CR	F	F	G	F	G	G		G	G	G		F			F	E	F	F	G		G	G		
P	45	0000	0114	57	T T TRESTLE	TENMILE CR	G	G	G	G	F	G		G	F	G		G			F	E	G	G	G		G	G		
P	45	0000	0140	63	T T TRESTLE	WHEELER CR	G	G	G	G	F	F		G	G	G		F			F	F	G	G	G		G	G		
P	45	0000	0152	57	T T TRESTLE	DRAINAGE	G	F	G	F	G	F		G	G	G		G			F	E	G	G	G		G	G		
P	45	0000	0163	88	T T TRESTLE	OTTER CR	G	G	G	G	F	F		G	G	G		G			F	E	G	G	G		G	G		
P	45	0000	0181	57	T T TRESTLE	RYE CR	G	G	G		G	F		G	F	G		G			F	E	G	G	G		G	G		
P	45	0000	0182	184	CONT ST GIRDER	SWEET GRASS CR	G		G	G	G	G	G	G	F	G	G			F	G	G	F	G	G	F	G	G		
P	45	0000	0197	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			F	E	G	G	G		G	G		
P	45	0000	0204	38	T T TRESTLE	CAYUSE CR	F	G	G		G	G						G			G	E	G	G	G		G	G		
P	45	0000	0219	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			F	F	G	G	G		G	G		
P	45	0000	0224	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	E	G	G	G		G	G		
P	45	0000	0265	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	E	G	G	G		G	G		

A	B FEET	C	D	E	F PILES	G BENTS	H PIERS	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
P 45 0000 0268	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	E	G	G	G		G	G		
P 45 0000 0291	113	T T TRESTLE	FISH CR	G	G	G		G	G	G	F	G	G		G			G	G	G	G	G		G	G		
P 45 0000 0316	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 45 0000 0328	29	CONC & ST I BM	S FK AMERICAN FK	G		G		G	G		G	G	P		G			G	G	G	G	G		G	G		
P 45 0000 0330	40	CONCRETE T BEAM	AMERICAN FK	G		G		G	G		G	G	F		G			G	G	G	G	G			G		
P 45 0000 0365	25	T T TRESTLE	DRY WASH	G		G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 45 0000 0370	25	T T TRESTLE	LEBO CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 45 0000 0381	25	T T TRESTLE	SPRING CR	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 45 0000 0403	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G				G		
P 45 0000 0434	190	CONT ST CANT	MUSSELSHELL R	F		G	G	G	G	G	G	G	G	G			G	G	G	G	G	G	G	F	G		X
P 45 0000 0437	186	ST PONY TRUSS	CMSTP&P RR	F		G		G	G			G				G	G	G	G	G	G	G	F	F	G		
P 45 0453 0460	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0468	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0487	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0492	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0549	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0621	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0628	200	CONT ST GIRDER	GN RY	P		G		G	G					G			G	G	G	G	G	G	G	G	G		
P 45 0453 0658	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		

A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
				FEET			FND F	PILES	BENT	PIERS	WINGWALLS	BACKW	ICE BREAKERS	DR	RIP		GIRD	S		SHOE	CURBS	MAR	DECK	BRAC	RAIL N	EXPANS	PAIN	GENER		
P	45	0453	0662	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	45	0453	0668	19	T T TRESTLE	ROSS FK	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	45	0453	0687	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	45	0453	0731	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	45	0453	0733	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	45	0453	0754	25	T T TRESTLE	BUFFALO CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	45	0453	0796	57	T T TRESTLE	LITTLE TROUT CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	45	0453	0821	241	CONCT BEAM	CMST P&P RY	F		G		G	G					G			G	G	G	G	G	G			G		
P	45	0453	0825	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	45	0453	0830	19	T T TRESTLE	OLSON CR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	46	0000	0041	19	REINF CONC SLAB	JOSEPH CR	G	E	G		G	G									G		G		G			G		
P	46	0000	0049	19	REINF CONC SLAB	JOSEPH CR	G	G	G		G	G									G		G		G			G		
P	46	0000	0070	19	REINF CONC SLAB	JOSEPH CR	G	G	G		G	G									G		G		G			G		
P	46	0000	0075	38	REINF CONC SLAB	TRAIL CR	G	G	G		G	G									G		G		G			G		
P	46	0000	0090	60	REINF CONC SLAB	TRAIL CR	G		E		E	E		G	E	G					E	G	E	E	E			E		
P	46	0000	0098	60	REINF CONC SLAB	TRAIL CR	G		E		E			G	E	G					E	G	E	E	E			E		
P	46	0000	0141	60	REINF CONC SLAB	TRAIL CR	G		E		E			G	E	G					E	G	E	E	E			E		
P	46	0000	0158	60	REINF CONC SLAB	RUBY CR	G		E		E			G	E	G					E	G	E	E	E			E		

PLANNING SURVEY BRIDGE CONDITION REPORT

CONTROL BRIDGE NUMBER	LENGTH FEET	MATERIAL & TYPE MAXIMUM SPAN	NAME OF FEATURE CROSSED	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSSES	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION JOINTS	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P 46 0000 0258	215	PRE CONC BEAM	BIG HOLE R	G		E	E	E	E	E	E		G	E			E	E	E	E	E	E	G	G	E		
P 46 0000 0276	38	T T TRESTLE	STEEL CR	G	G	G		G	G	G	G		G		G			G	G	G	G	G		G	G		
P 46 0000 0419	235	PRE CONC BEAM	BIG HOLE R	G		E	E	E	E	E	G	G	G	E			E	E	E	E	E	E	G	E	E		
P 46 0000 0485	57	T T TRESTLE	FISHTRAP CR	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		G	G		
P 46 0000 0502	81	T T TRESTLE	LAMARCHE CR	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		G	G		
P 46 0000 0531	38	T T TRESTLE	SEYMOUR CR	G	G	G		G	G	G	G		G		G			G	G	G	G	G		G	G		
P 46 0000 0543	75	T T TRESTLE	DEEP CR	G	G	G		G	G	G	G		G		G			G	G	G	G	G		G	G		
P 46 0000 0580	325	RIV ST PL GIR	BIG HOLE R	G		G	G	E	E	E	G	E	G	E			E	E	E	F	E	G	E	G	F		
P 46 0000 0649	29	STEEL I BEAM	BRANCH OF WISE R	G		G		G	G		G		G	G					F	G	G	F		F	G		
P 46 0000 0651	44	STEEL I BEAM	BRANCH OF WISE R	F		G		G	G		G		G	G					F	G	G	F		F	G		
P 46 0000 0652	43	STEEL I BEAM	BRANCH OF WISE R	G		G		G	G		G		G	G					F	G	G	F		F	G		
P 46 0000 0749	304	PRE CONC BEAM	BIG HOLE R																								N
P 46 0000 0769	38	T T TRESTLE	DIVIDE CR	G	E	G		E	G		G		G		G			G	G	G	G	G		F	G		
P 48 0000 0009	25	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		F			P		G	G	F		P	G		
P 48 0000 0015	68	T T TRESTLE	DRAINAGE	G	G	G					G		F		G			F		G	G	F		P	G		
P 48 0000 0055	31	T T TRESTLE	LOW LINE DITCH	F	F	F			F		G		G		F			F		P		F		F	F		X
P 48 0000 0075	38	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		F	G		
P 48 0000 0080	38	T T TRESTLE	LOW LINE DITCH	G	G	G			G		P		G		G			F		F	G	F		F	G		

F A SYS	F A RD NUMBER	CONTROL JUNCT	MILE TO TENTH	TOTAL FEET	TYPE	NAME	FN F S	PILE	BENT	PIERS	WIN WALLS	BACKWA	ICE BREAKERS	DRIF	RIP RAP	SCOUR	GIRDERS		TR	SHOES	CURBS	MAR	DECK	BRACING	RAILING	F N	PAINT	GEN RAT ON	NOT INSP	REMA
		A		B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
P	48	0000	0083	57	T T TRESTLE	LOW LINE DITCH	G	G	G			G		G		G		G			F		G	G	F		F	G		
P	48	0000	0113	38	T T TRESTLE	DRAIN DITCH	G	G	G	G		G	G	G		F		G			F		G	G	F		G	G		
P	49	0000	0033	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			F	G	G	G	F		G	G		
P	49	0000	0069	25	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G	G	G		G			F	F	F	F	F		G	G		
P	49	0000	0090	38	T T TRESTLE	STONE CR	G	G	G		G	G		G	G	G		G			F	F	F	G	F		G	G		
P	49	0000	0147	150	STEEL GIRDER	BEAVERHEAD R	G		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
P	49	0000	0273	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			F	G	G	G	G		G	G		
P	49	0000	0275	181	STEEL GIRDER	BEAVERHEAD R	G		G	G		G	G	G		G	G			G	G	G	G	G	G	G	F	G		
P	50	0000	0037	134	CONCRETE GIRDER	MADISON R	G	F	F	G	F	G		G	P	G	G			G	G	G	F	G	G	F	F	G		
P	50	0000	0075	36	CONCRETE SLAB	COUGAR CR	G		G		G	G		G	E	G				G	G	G	E		F		F	G		
P	50	0000	0099	105	REINF CONC GIR	GRAYLING CR	G		F	F	F	G	G	G	G	G	F			P	F	G	G	F	F		F	F		
P	50	0000	0236	120	CONT CONC T BM	GALLATIN R	G		G	F	G	G	G	G	G	G	G				G	G	G	G	G		F	G		
P	50	0000	0264	64	CONT CONC T BM	SPECIMEN CR	G		G	G	G	G	G	G	G	G	G				G	G	G	G	F		P	G		
P	50	0000	0327	122	CONCRETE GIRDER	GALLATIN R	G		G	F	G	G	G	G	G	F	G				G	G	G	G	F		F	G		
P	50	0000	0339	70	CANT CONC GIR	TAYLOR FORK	G		G	G	G	G	G	G	G	G	G				G	G	G	G	F		F	G		
P	50	0000	0479	80	CANT CONC GIR	WEST FORK	G		G	G	G	G	G	G	E	G	G				G	G	G	F	F		F	G		
P	50	0000	0498	160	CONCRETE T BEAM	GALLATIN R	G		G	G	G	G	G	G	G	G	G				G	G	G	G	F		F	G		

	FLET B	C		E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	ZZ
P 50 0000 0572	54	REINF CONCRETE	SWAN CR	G		G	G	G	G		G	G	G	G				G	G	G		F		F	G		
P 50 0000 0614	234	STEEL GIRDER	GALLATIN R	G		G	G	G	G	G	G	E	G	G			E	G	G	F	G	G	G	F	G		
P 50 0000 0682	69	CONCRETE T 8EAM	SPANISH CR	G		F	F	F	F	F	G	G	G	G			F	G	G	F		G		F	G		
P 50 0000 0704	260	STEEL GIRDER	GALLATIN R	G		G	G	G	F	G	G	G	G	G			F	G	G	F	G	G	F	F	G		
P 50 0000 0767	20	CONC SLA8	COTTONWOOD CR	G		G		G	G		G		G					E	G	E		G		F	G		
P 50 0000 0776	20	CONC SLA8	FARMERS CANAL	G		G		G	G		G		G					E	G	E		G		F	G		
P 50 0000 0814	20	CONC SLA8	FARMERS CANAL	G		G		G	G		G		G					E	G	E		G		F	G		
P 50 0000 0827	30	CONCRETE GIRDER	MIDDLE CR	G		G		F	F		G	G	G	G			G	G	G	F	G	F		F	G		
P 51 0000 0004	88	T T TRESTLE	8UFFALO SPR CR	F	G	G	G	G	G	N	G	N	G	N	G	N	N	F	F	G	G	F	N	G	G		
P 51 0000 0072	88	T T TRESTLE	COTTONWOOD CR	F	G	G	G	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 51 0000 0105	88	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	N	P	N	G	N	N	G	G	G	G	G	N	G	G		
P 51 0000 0135	88	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 51 0000 0172	57	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 51 0000 0699	75	T T TRESTLE	US8S CANAL	G	G	G	F	F	F	N	G	N	G	N	N	N	N	G	N	G	N	G	N	G	F		
P 52 0000 0310	220	CONT ST GIRDER	SWAN R	G		F	G	G	G	G	G		G	G	G		P	G	G	G	G	G		G	G		X
P 52 0000 0354	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	F		G	G		
P 52 0000 0408	95	T T TRESTLE	MILL CR	F	F	F		G	G		G		G		G			G	G	G	G	F		G	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Columns E thru Z

E - Excellent
G - Good
F - Fair

P = Poor
C = Critical

Column Z

N = New
R = To be Removed
= Unable to Inspect

CONTROL	DESCRIPTION OF FEATURES			E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	
P 53 0000 0000	220	PRE CONC BEAM	27TH ST INT I90	G		E			E					E			E	E		E		E		E	E	
P 53 0000 0000T	220	PRE CONC BEAM	27TH ST INT I90	G		E			E					E			E	E		E		E		E	E	
P 53 0013 0024	35	T T TRESTLE	BL&I CANAL	G	G	G		G	G		G		G		G			G		G		G		G	G	
P 53 0013 0097	95	T T TRESTLE	S FK ALKALI CR	F	G	G			G		G	G	G		G			F		G	G	G		G	G	
P 53 0013 0106	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		F	G	
P 53 0013 0119	57	T T TRESTLE	N FK ALKALI CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G	
P 53 0013 0145	76	T T TRESTLE	S FK FIVE MILE C	G	G	G			G		G	G	G		G			G		G	G	G		G	G	
P 53 0013 0147	57	T T TRESTLE	N FK FIVE MILE C	G	G	G			F		G	G	G		G			G		G	G	G		G	G	
P 53 0013 0347	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P 53 0013 0368	57	T T TRESTLE	DRY WASH	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P 53 0013 0372	25	T T TRESTLE	DRY WASH	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P 53 0013 0392	76	T T TRESTLE	DRY WASH	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	X
P 53 0013 0398	95	T T TRESTLE	PAINTED ROBE CR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G	
P 53 0013 0448	101	PRE CONC BEAM	BIG COULEE CR	F		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G	
P 53 0013 0454	143	PRE CONC BEAM	MUSSELSHELL R	G		G	F	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G	X
P 53 0013 0463	11	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G	

FEDERAL AID SECONDARY ROUTES

(STATE MAINTAINED)

			FEET			E	F	G	H		J	K		M	N	O	P	Q	R	S		U	V	W	X		Z	Z	Z
M208	0000	0058	686	STEEL GIRDER	FLATHEAD R	G		G	G	G	G	G	G	G	G	G	G		G	G	G	G	G	G	G	G	G		
M209	0000	0122	75	T T TRESTLE	MORRELL CR	G	G	G	G	G	G		G		G		G			G	G	G		G		G	G		
M209	0000	0355	57	T T TRESTLE	HOLLAND CR	G		G		G	G		G		G		G		G	G	G	G	G	G		P	G		
M209	0000	0524	69	T T TRESTLE	LION CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
M209	0000	0570	57	T T TRESTLE	GOAT CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
M209	0000	0656	57	T T TRESTLE	LOST CR	G	G	G		G	G		G		G		G			G	G	G	F	G		P	G		
M209	0000	0830	225	PRE CONC BEAM	SWAN R	G		G	G	G	G	G	G	G	G	G			G	G		G		G	G	G	G		
M230	0000	0002	128	CONCRETE T BEAM	GN RY	G		G		G	G					G			G	G	G	G		G	G	G	G		
M230	0000	0024	708	RIV PL GIRDER	MISSOURI R	F		G	G	G	G	G	G	G	G	G			G	G	G	G	G	G	G	F	G		
M230	0000	0040	125	T T TRESTLE	SHONKIN CR	P	G	G		G	G	G	F	P	F		G			G	P	G	G	G		F	G		
M230	0000	0086	75	T T TRESTLE	BOYLE COULEE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
M230	0000	0132	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
M230	0000	0322	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
M230	0000	0331	76	T T TRESTLE	FLAT CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
M230	0000	0341	25	T T TRESTLE	TRIBUTARY FLAT C	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
M230	0000	0416	75	T T TRESTLE	COWBOY STEELE CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
M230	0000	0420	75	T T TRESTLE	BUTTE CR	G	G	G		G	G		G	P	P		G			G	G	G	F	G		G	G		

M230 0000 0467	250	T T TRESTLE	ARROW CR	P	F	F		F	P	F	C		C		G			G	G	G	G	G		G	F	X
M230 0000 0611	57	T T TRESTLE	WOLF CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G	
M232 0000 0001	826	STEEL I BEAM	GN RY	F	P	P		F	F					G	P		P	P		F	P	P	P	P	P	X
M232 0000 0002	287	STEEL TRUSS	MILK R	G	F	F	F		P	G	G		F		F	F		P		F	F	P	F	C	F	X
M244 0000 0024	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		G	G	
M244 0000 0058	133	T T TRESTLE	FLATWILLOW CR	G	G	G		G	G	G	G	F	G		G			G	G	G	G	G		G	G	X
M244 0000 0121	38	T T TRESTLE	PIKE CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
M244 0000 0123	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
M244 0000 0185	76	T T TRESTLE	YELLOW WATER CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
M244 0000 0233	125	T T TRESTLE	MCDONALD CR	G	G	G		G	G	G	F	G	G		G			G	G	G	G	G		G	G	
M247 0000 0066	150	T T TRESTLE	E FK CHERRY CR	G	G	G			G		G		G		F			G	G	G	G	G		P	G	
M247 0000 0254	125	T T TRESTLE	DRY FK CR	G	G	G			G		G		G		G			G	G	G	G	G		P	G	
M247 0000 0281	114	T T TRESTLE	W FK PORCUPINE	G	G	G	F		G	G	G	G	F		G			G	G	G	G	F		G	G	
M247 0000 0351	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G	
M247 0000 0394	100	T T TRESTLE	M FK PORCUPINE	F	G	G			G		G	G	G		G			G	G	G	G	G		G	G	
M247 0000 0400	76	T T TRESTLE	ALKALI CR	G	G	G			G		G	G	G		G			G	G	G	G	F		G	G	

A	B FEET	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	ZZ
M249 0000 0020	369	STEEL GIRDER	MILK R	G		G	G		G	G	G	G	G	G			G	G	F	G		F	F	F	G	
M249 0000 0072	57	T T TRESTLE	DRAINAGE	G	P	P			P		G		G		P			G	G	P	P	F		F	F	X
M249 0000 0098	286	STEEL I BEAM	OF MISSOURI R	G		G			G		G		G	G			G	G		G		G	G	F	G	
M289 0000 0079	250	STEEL TRUSS	MADISON R	G		G	G	G	G	G	G	F	G		G	G	G	F	G	G	G	G	G	F	G	
M289 0000 0096	38	T T TRESTLE	CHERRY CR	G	G	G	G	G	F	G	G	F	G		G		G	F	G	G	G	G		F	G	
M289 0000 0151	21	CONCRETE T BEAM	ELK CR	G		G		G	G	G	G		G		G		G	F	G	G		F		F	G	
M289 0000 0279	120	ST THRU TRUSS	GALLATIN R	F		G		F	G	G	F	G	G		F	F	F	F	G	F	C	P		P	F	X
M289 0000 0282	39	STEEL I BEAM	GALLATIN R	F		G		F	G	G	G	P	G	F			G	F	G	F	F	P		P	F	
M291 0000 0008	235	PRE CONC BEAM	BELGRADE INT I90	E		E		E	E					E			E	E		E		E	G	G	E	
M308 0000 0001	62	STEEL I BEAMS	ROCK CR	G		F	F	G	G		G	G	G	G	G			F		G		P		P	G	X
M308 0147 0158	244	STEEL GIRDER	CLARK FORK	F		G	G		G	G	G	G	G	G			G	G	G	G		G	F	G	G	
M308 0147 0175	57	T T TRESTLE	SILVER TIP CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G	
M308 0147 0183	261	STEEL GIRDER	CLARK FORK	G		G	G		G	G	G	G	G	G			G	G		G		G	G	G	G	
M376 0000 0166	25	T T TRESTLE	LIT PEOPLES CR	F	G	G		G	G		G		G		G			G	F	G	G	G		G	G	
M376 0000 0180	25	T T TRESTLE	LIT PEOPLES CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G	

M376 0000 0223	38	T T TRESTLE	LIT PEOPLES CR	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G	
M376 0000 0263	100	T T TRESTLE	S FK PEOPLES CR	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G	
M376 0000 0316	100	T T TRESTLE	PEOPLES CR	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G	
M376 0000 0409	75	T T TRESTLE	WHITE BEAR CR	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G	
M376 0000 0472	100	T T TRESTLE	THREE MILE COU	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G	
M397 0000 0055	194	STEEL GIRDER	CLARK FORK	F		G	G	F	G		G	G	G	G			G			G		G		G	G	X
M401 0000 0002	76	T T TRESTLE	PIPESTONE CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G	
M401 0000 0084	38	T T TRESTLE	FISH CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G	
M412 0000 0247	84	T T TRESTLE	LOLO CR	G	G	G	G	G	G		G		G		G			G	G	G	G	G		G	G	
M412 0000 0250	63	T T TRESTLE	LOLO CR	G	G	G	G	G	G		G		G		G			G	F	G		G		G	G	
M412 0000 0265	28	T T TRESTLE	LOLO CR	G	G	G		G	G		G		G		G			G	F	G		G		G	G	
M412 0000 0267	28	T T TRESTLE	LOLO CR	G	G	G		G	G		G		G		G			G	F	G		G		G	G	
M499 0000 0077	123	CONCRETE SLAB	BEAVER CR	F	G	G	F	G	G	P	G	F	G					G	G	G	G	G		E	G	
M499 0000 0091	83	CONCRETE T BEAM	CABIN CR	G		G	F	G	G	F	G	G	G	F			F	G	G	G	G	G			G	
M499 0000 0208	75	CONCRETE SLAB	GRAYLING CR	G	G	G	G	G	G	F	F	G	G					G	G	E	G	G			G	

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Columns E thru Z

E = Excellent
G = Good
F = Fair
P = Poor
C = Critical

Column Z

N = New
R = To be Removed
U = Unable to Inspect

= [illegible] E plan [illegible]

CONTROL BRIDGE NUMBER		DESCRIPTIVE FEATURES MATERIAL & TYPE	NAME OF FEATURE	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
M511 0000 0037	76	T T TRESTLE	S FK WHITETAIL C	G	G	G			G		G	F	G		G			G	G	F	G	F		G	G
M511 0000 0063	76	T T TRESTLE	WHITETAIL CR	F	G	G			P		F	G	G		G			G	G	G	G	F		F	G
M511 0000 0070	38	T T TRESTLE	N FK WHITETAIL C	G	G	G			G		G	P	G		G			G	G	G	G	F		F	G

FEDERAL AID SECONDARY ROUTES

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S201 0000 0133	321	CONCRETE T BEAM	REDWATER R	G		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
S201 0000 0588	76	T T TRESTLE	FIRST HAY CR	G	G	G			G		G	G	G		G			G	P	G	G	F		P	G		
S201 0000 0640	57	T T TRESTLE	SECOND HAY CR	G	G	G			G		G	F	G		G			F	P	G	G	G		P	G		
S201 0000 0693	51	T T TRESTLE	MAIN CANAL	F	G	G			G		G		G		G			P		F	G	F		P	G		
S202 0000 0218	79	CONCRETE SLAB	BULL R	G		G	G	G	G		G	F	G					G		G		G			G		
S202 0000 0264	83	T T TRESTLE	BULL R	P	G	G	G	G	G		P		F		G			G		G	G	G		C	G		
S203 0000 0052	374	CONCRETE T BEAM	BITTERROOT R	G		E	E	E	E	E	F	G	G	E			E	G		E	E	G	G	F	E		
S203 0000 0055	38	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	F	G		G		G			G		G		G		G	G		
S204 0000 0013	240	ST PLATE GIRDER	MILK R	F		G	G		G	G	G	G	G	G			F	G	P	G	G	G	G	P	G		
S204 0000 0014	63	T T TRESTLE	USRS CANAL	F	G	G		G	G		G		G		G			G	P	G	G	G		P	G		
S212 0000 0124	75	T T TRESTLE	POST CR-RD PLANS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S214 0000 0001		UNDERPASS	INT-I15 SUNBURST	F		E		E	E					E			E	E	G	E	E	E	P	G	E		
S214 0000 0243	256	PRE CONC BEAM	SW GRASS INT-I15	E		E		E	E					E			E	E	G	E	E	E	F	G	E		

S215 0000 0000		UNDERPASS	KEVIN INT-I15	G		E		E	E					E			E	E	G	E	E	E		E	E		
S216 0000 0053	57	T T TRESTLE	SOBERUP CR	F	F	G		F	F		F	P	C		G			F	G	G	G	F		F	F		X
S216 0000 0095	150	T T TRESTLE	OUPUYER CR	F		G		G	G		G	F	F		G			F		G	F	F		F	F		X
S216 0000 0117	38	T T TRESTLE	IRRIGATION CANAL	G	G	G		G	G		G		G		G			F		G	G	G		F	G		
S218 0000 0011	38	T T TRESTLE	PONDERA COULEE	G	G	G		F	F		G		G		G			F	G	G	G	G		P	G		
S218 0000 0107	60	T T TRESTLE	PONDERA COULEE	G	G	G	G	G	G	G			G		G			G	G	G	G	G		F	G		
S218 0000 0199	23	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G				G	G	G			F	G		
S218 0000 0299	50	T T TRUSS	PONDERA COULEE	F	G	G		P	F		F	P	F		G	F		F		F	G	F		P	F		
S219 0000 0031	57	T T TRESTLE	FARMERS COULEE	G	G	G		G	G						G			G	G	G	G	G		G	G		
S219 0000 0176	38	T T TRESTLE	ORAINAGE	G	G	G		G	G						G			G	G	G	G	G		P	G		
S221 0000 0049	268	STEEL I BEAM	TETON R	F		F	F	G	G	G	P	G	F	G	G		G	G		G	G	G	P	F	G		
S223 0000 0013	298	CONCRETE T 8EAM	TETON R	G		G	G	G	G	G	F	G	G	G			G	G	F	G		G	G	F	G		
S223 0000 0378	346	PRE CONC 8EAM	MARIAS R	E		E	E	E	E	E	E	E	G	E			E	E		E	E	E	E	E	E		
S223 0000 0435	57	T T TRESTLE	DRAINAGE	G	G	G		F	F		G	G	F		G			G		G	G	F		P	G		X

S225	0000	0316	408	PRE CONC BEAM	TETON R	G		G	G	G	G	G	G	G	G	G			G	G	F	G		G	G	G	G		X
S226	0000	0001		UNDERPASS	SPUR FAP 3	G		G	G							G			G			G	G			G	G		
S226	0000	0036	57	T T TRESTLE	SAND COULEE	G	G	G		G	G		G	G	G		G				G	G		G		F	G		
S228	0000	0105	57	T T TRESTLE	RED COULEE	G	G	G		G	G		G	G	G		G			G		G	G	G		G	G		
S228	0000	0164	186	STEEL I BEAM	BELT CR	G		G	F	G	G		G		F	G	G		G	G		G	G	F	G	P	G		
S228	0000	0223	75	T T TRESTLE	HIGHWOOD CR	F	G	G		F	G		G		G		F			G		G	P	G		F	G		
S231	0000	0090	38	T T TRESTLE	OBRIEN COULEE	G	G	G		F	G		G	G	G		G			F		G	G	G		P	G		
S231	0000	0138	38	T T TRESTLE	LITTLE SAGE CR	G	G	G		F	G		G		G		G			F	G	G	G	F		F	G		
S231	0000	0186	57	T T TRESTLE	SAGE CR	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
S234	0000	0020	96	ST PONY TRUSS	SCOTT COULEE CA	G	G	G	G	G	G		G		G		G	G	G	F		F	G	P		P	G		X
S235	0000	0004	50	CONCRETE SLAB	WARM SPRINGS CR																							R	
S235	0000	0033	38	T T TRESTLE	WARM SPRINGS CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S235	0000	0085	38	T T TRESTLE	IRRIGATION CANAL	P	F	F		G	G		F		G		G			G		G	G				G		X
S235	0000	0090	95	T T TRESTLE	WARM SPRINGS CR	P	G	G		G	G		F		G		G			G		G	G	F		P	G		

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	ZZ
S235 0000 0100	95	T T TRESTLE	WARM SPRINGS CR	P	G	G		G	G		G	G	G		G			G		G	G	F		P	G		
S235 0000 0175	177	STEEL GIRDER	JUDITH R	F		G	G	G	G	G	P		G	G			G	G	G	G	G	G	G	G	G		X
S235 0000 0179	175	T T TRESTLE	SAGE CR	G	G	G		G	G		F	F	G		G			G	G	G	F	G		G	G		
S235 0000 0225	57	T T TRESTLE	DRY WOLF CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S235 0000 0299	76	T T TRESTLE	WOLF CR	F	G	G		G	G		G		G		G			G		G	G	G		G	G		X
S235 0000 0364	38	T T TRESTLE	COFFEE CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S236 0000 0042	38	T T TRESTLE	DOG CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
S236 0000 0063	38	T T TRESTLE	LITTLE DOG CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
S236 0000 0095	38	T T TRESTLE	DOG CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
S236 0000 0101	57	T T TRESTLE	DOG CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
S236 0000 0552	98	UNT T TRESTLE	CHIP COULEE	F	F	F		F	F		G		G		F			P		G	P	P		P	F		
S237 0000 0019	50	HOWE ST TRUSS	BIG SPRING CR	G		P		F	F		G		G			F				F	P	P		G	F		X
S238 0000 0004	49	REINF CONC SLAB	MILL DITCH	G	G	G		G	G		G	G	G					G		G		F		P	G		X
S239 0000 0031	65	PRE CONC BEAM	JUDITH R	G		G		G	G		G		G	G			G	G		G		G		G	G		

A	B	C	D	E	F	G	H		J	K		M	N	O	P		R	S			V	W					
S240 0000 0015	213	PRE CONC BEAM	MILK R	F		E	E	E	E	E	P	F	G	E			E	E	G	E		E		G	E		
S240 0000 0029	40	STEEL I BEAM	THREE MILE CR	F	G	G		G	G		G		G		G			G		G	G	F		P	G		
S240 0000 0124	38	T T TRESTLE	BEAN CR	G	G	G	G	G	G	G	G		G		G			G	F	G	F	G		P	G		
S240 0000 0166	38	T T TRESTLE	SNAKE CR	G	G	G	G	G	G	G	G		G		G			F	F	G	G	G		P	G		
S240 0000 0250	57	T T TRESTLE	PEOPLES CR	G	G	G	G	G	G	G	G		G		G			G	F	G	G	G		P	G		
S241 0000 0001	88	T T TRESTLE	THIRTY MILE CR	G	G	G			G		P		P		G			G	F	G	G	P		P	G		
S241 0000 0009	57	T T TRESTLE	BUCKLEY COULEE	F	G	G			G		F	F	G		G			G		G	G	P		P	G		
S241 0000 0075	76	T T TRESTLE	W FK WAYNE CR	F	G	G			G		G	F	F		G			F	P	F	G	F		P	F		
S241 0000 0091	76	T T TRESTLE	WAYNE CR	G	G	G			G		G	P	G		G			F	P	G	G	F		P	G		
S241 0000 0097	57	T T TRESTLE	E FK WAYNE CR	G	G	G			G		G	P	G		G			F	P	G	G	F		P	G		
S241 0000 0110	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G	P	G	G	F		P	G		
S241 0000 0122	57	T T TRESTLE	WEST SAVOY CR	G	G	G			G		G	G	G		G			G	P	G	G	F		P	G		
S241 0000 0375	117	STEEL I BEAM	WOODY ISLAND CR	G		G			G		F		G		G			F		F		P		P	G		
S242 0000 0055	57	T T TRESTLE	CIRCLE DIAMOND	F	G	G			G		G	F	G		P			G	P	G	G	G		F	G		X
S242 0000 0060	114	T T TRESTLE	ASSINIBOINE CR	F	G	G			G		F	F	F		G			G	P	G	G	F		F	G		
S242 0000 0152	100	T T TRESTLE	COTTONWOOD CR	G	F	F			G	G	F	G	F		G			G	P	G	G	G		F	G		X
S242 0000 0174	76	T T TRESTLE	LIT COTTONWOOD C	G	G	G		G	G		F		F		G			G	P	G	G	G		F	G		

A	B TOTAL LENGTH FEET	C MAXIMUM SPAN	D	E END F	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TRUSS	R SHOES	S CURBS	T MARKERS	U DECK	V BRACING	W RAILING	X	Y	Z	Z1 NOT INSPECTED	Z2
S242 0000 0470	100	T T TRESTLE	WHITEWATER CR	G	G	G		G	G	G	G	G	G		G			G	F	F	G	G		F	G		
S243 0000 0059	146	CONC SLAB FORD	MILK R	F																P					P		X
S243 0000 0117	117	STEEL I BEAM	WHITEWATER CR	F	P	F					G	F	G		F			P		F					P		X
S243 0000 0122	62	STEEL I BEAM	WHITE CR	F	G	G			G		G	G	G		F					F		P		P	F		
S243 0000 0160	250	ST PLATE GIRDER	MILK R	F		G	G		G	G	G	G	G	G			G	G	F	G	G	G	G	F	G		
S243 0000 0196	38	T T TRESTLE	DRAINAGE	F	G	G	G		G		G		G		G			F		G	G	F		F	G		
S243 0000 0200	114	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			F		G	G	F		F	G		
S243 0000 0202	38	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			F		G	G	F		F	G		
S243 0000 0204	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			F		G	G	F		F	G		
S243 0000 0205	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			F		G	G	F		F	G		
S243 0000 0206	95	T T TRESTLE	USRS DITCH	F	G	G			G		G	F	G		G			F		G	G	F		F	G		
S243 0000 0207	38	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			F		G	G	G		F	G		
S243 0000 0208	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			F		G	G	G		F	G		
S246 0000 0007	120	CONT CONC T BM	CHERRY CR	P		G	G		G	G	G	G	G	G			G	G	G	G		G		P	G		
S246 0000 0011	75	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			G		G	G	G		P	G		
S246 0000 0021	400	RIV ST PL GIR	MILK R	P		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	P	G		
S246 0000 0067	50	T T PILE	ANTELOPE CR	G	G	G		G	G		G		G		G			G		G	G	G		P	G		

A			D		F	G	H		J	K		M	N		P		R	S				W			Z		
S248 0000 0024	25	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
S248 0000 0029	278	ST PONY TRUSS	E FK POPLAR R	F	G	P			G	G	F	P	F	G	G	G	F	G		G	G	G	P	F	F		X
S248 0000 0031	76	T T TRESTLE	DRAINAGE	G	G	G		G	G	G	G	F	G		F			G	G	G	G	G		G	G		
S248 0000 0035	127	T T TRESTLE	BUTTE CR	G	G	F		G	G	G	F	G	F		G			G	G	G	F	F		F	G		
S248 0000 0092	25	T T TRESTLE	DRAINAGE	G	G	G		G	G	G	G	G	G		G			G	P	G	G	G		G	G		
S248 0000 0105	75	T T TRESTLE	SPRING CR	G	G	F		G	G		G	G	F		G			G	G	G	G	C		G	F		X
S248 0000 0219	57	T T TRESTLE	DRAINAGE	G	G	F		G	G		G	G	G		F			G	G	G	G	G		P	G		X
S248 0000 0224	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			F	G	G	G	G		P	G		
S248 0000 0242	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
S248 0000 0288	75	T T TRESTLE	DRAINAGE	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		P	G		
S248 0000 0289	50	T T TRESTLE	OLD OF CHANNEL	G	G	G		G	G		G	G	G		G			G	G	G	F	G		P	G		
S248 0000 0290	200	T T TRESTLE	W FK POPLAR R	G	G	G		G	G	G	F	G	F		C			G	G	F	F	G		P	G		X
S248 0000 0292	75	T T TRESTLE	OF W FK POPLAR R	G	G	G		G	G	G	G	G	G		G			G	F	G	G	G		P	G		
S248 0000 0293	19	T T TRESTLE	IRRIGATION CANAL	G	G	G		G	G						C			G	F	G	G	F		P	F		X
S248 0000 0315	50	T T TRESTLE	SPRING CR	G	G	G		G	F		G		G		G			G	P	G	G	F		P	G		
S251 0000 0118	25	T T TRESTLE	DRAINAGE	F	G	G			G		G		G		F			G		G	G	G		G	G		
S251 0000 0155	25	T T TRESTLE	DRAINAGE	F	G	G			G		G		G		G			G		G	G	F		G	G		
S251 0000 0178	25	T T TRESTLE	KIRN COULEE	G	G	G			G		G		G		G			G	P	G	G	G		F	G		

NUMBER A	TOTAL LENGTH FEET B	C	D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWA I	BACKW J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TR Q	R	S	MARKER T	U	V	W	X	Y	Z	Z1	Z2
S251 0000 0207	25	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		C			G		G	G	G		G	G		X
S251 0000 0217	38	T T TRESTLE	HAY CR	G	G	G			G		G		G		G			G	F	G	G	G		G	G		
S251 0000 0409	25	T T TRESTLE	SMOKE CR	E	G	G		E	G		G		G		G			E		G	G	E			G		
S251 0000 0498	25	T T TRESTLE	EAGLE CR	G	G	G		G	G		F		G		G			F	P	G		F		P	G		
S252 0000 0015	100	T T TRESTLE	HORSE CR	G	G	G	G	G	G	G	G	N	F	N	G	N	N	G	P	G	G	G	N	P	G		
S252 0000 0070	38	T T TRESTLE	DENWOODY CR	G	G	G	G	G	G	N	G	N	F	N	G	N	N	G	P	G	G	G	N	P	G		
S252 0000 0080	75	T T TRESTLE	HORSE CR	G	G	G	G	G	G	G	G	N	F	N	G	N	N	F	N	G	G	G	N	P	G		
S252 0000 0130	57	T T TRESTLE	HORSE CR	G	G	G	G	G	G	G	G	N	F	N	G	N	N	G	N	G	G	G	N	P	G		
S252 0000 0141	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	N	G	G	G	N	P	G		
S253 0000 0009	825	RIV PL GIRDERS	YELLOWSTONE R	G	N	G	G	N	G	G	G	G	G	E	N	N	G	G	P	G	N	G	G	G	E		
S253 0000 0046	363	STEEL I BEAM	CHERRY CR	G	G	G	G	G	G	G	G	F	G	G	N	N	G	F	G	F	G	F	F	P	F		
S253 0000 0080	95	T T TRESTLE	BRACKETT CR	G	G	G	G	N	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	P	G		
S253 0000 0094	133	T T TRESTLE	CEDAR CR	G	G	G	G	N	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	P	G		
S253 0000 0147	76	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	F	P	G	G	P	N	P	F		
S253 0000 0174	76	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G		
S253 0000 0188	95	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G		
S253 0000 0224	75	T T TRESTLE	CEDAR CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
S253 0000 0269	38	T T TRESTLE	CEDAR CR	G	G	G	G	G	G	N	G	F	F	N	G	N	N	F	P	G	G	F	N	P	G
S253 0000 0371	75	T T TRESTLE	EAST DUCK CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	F	P	G	G	F	N	P	G
S253 0000 0462	150	T T TRESTLE	REDWATER R	F	G	G	G	G	G	G	G	N	G	N	G	N	N	P	P	G	G	P	N	P	F
S254 0000 0175	25	T T TRESTLE	LOWER 7 MILE CR	G	G	G	N	G	G	N	G	N	F	N	G	N	N	G	N	G	G	G	N	G	G
S254 0000 0229	25	T T TRESTLE	S FK 13 MILE CR	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	N	G	G	G	N	G	G
S254 0000 0288	25	T T TRESTLE	MID FK BURNS CR	G	G	G	N	G	G	N	G	G	F	N	G	N	N	G	N	G	G	G	N	G	G
S254 0000 0532	74	PRE CONC BEAM	REDWATER R	G	N	G	G	G	G	N	G	N	G	G	N	N	N	G	N	G	N	G	N	G	G
S257 0000 0001		UNDERPASS	CMSTP&P RR	G	F	F		G	G					G	G		G			G	F	P		P	F
S257 0000 0002	459	ST PRATT TRUSS	CLARK FORK	G		G	F	G	G	G	G		G		F	G	G	F		F	F	F	F	P	F
S257 0000 0003		UNDERPASS	SUPERIOR INT I90	G		E		E	E					E			E	E	G	E		E	E	G	E
S257 0000 0004		UNDERPASS	SUPERIOR INT I90	G		E		E	E					E			E	E	G	E		E	E	G	E
S257 0000 0012	110	CONT CONC T BM	CEDAR CR	G		G	G		G		G	F	G	G		G	G	G		G		G		P	G
S257 0000 0037	188	CONT CONC T BM	NP RY	P		G	G		G					G			G	G		G		G		P	G
S258 0000 0002	150	T T TRESTLE	BIG MUDDY CR	F	G	P			G	G	F		G		G			F	P	F	G	F		P	F
S258 0000 0008	113	T T TRESTLE	DRAINAGE	F	G	P			G	F			G		G			F	P	F		F		P	F

S261 0000 0000	163	PRE CONC BEAM	INT I94 W WIBAUX	G	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	E	N	E	G	G	E	
S261 0000 0004	56	CONC T BEAM	DRY CR	G	N	F	N	N	F	N	G	N	G	F	N	N	N	F	G	F	N	F	N	N	F	
S261 0000 0435	40	STEEL TRESTLE	OBRIEN CR	P	P	P	N	P	P	N	G	N	G	F	N	N	N	N	N	G	N	N	N	P	P	
S267 0000 0001		UNDERPASS	NP RR	E		E		E	E					E			E	E		E		E	E	G	E	
S267 0000 0001A		UNDERPASS	NP RR	E		E		E	E					E			E	E		E		E	E	G	E	
S267 0000 0002		UNDERPASS*	VAN BUREN ST INT	E		E		E	E					E			E	E		E		E	E	G	E	
S267 0000 0002A		UNDERPASS*	VAN BUREN ST INT	E		E		E	E					E			E	E		E		E	E	G	E	
S267 0000 0044	50	UNT T & CONC	RATTLESNAKE CR																							
S269 0000 0034	22	CONCRETE T BEAM	IRRIGATION DITCH	G		G		F	G		G		G	G						G	G	G			G	
S269 0000 0053	25	T T TRESTLE	IRRIGATION DITCH	G		G		G	G		G		G	G				G		G	G	G		F	G	
S269 0000 0208	75	T T TRESTLE	BITTERROOT R OF	G	G	G	G	G	G	F	G	G	G		G			F		F		P		C	F	
S269 0000 0210	324	CONT ST GIRDER	BITTERROOT R	G		G	G	G	G	G	G	G	G	G			G	G		G		G	C	P	G	
S270 0000 0036	35	STEEL I BEAM	HORSE CR	G	N	F	N	G	G	N	G	G	G	F	N	N	N	P	N	F	N	P	N	P	F	
S270 0000 0066	142	PRATT ST TRUSS	LIT MISSOURI R	P	F	C	P	P	C	F	P	F	P	F	F	P	N	P	N	P	P	P	N	P	C	X
S270 0000 0189	60	ST PONY TRUSS	COTTONWOOD CR	F	F	P	P	P	P	N	G	N	P	N	F	F	N	P	N	F	P	P	N	P	P	X
S270 0000 0198	23	STEEL I BEAM	HACKBERRY CR	F	F	F	N	F	F	N	G	N	G	F	N	N	N	P	N	F	F	P	N	P	F	

[illegible] BRIDGE CONDITION REPORT

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y		7	Z
S271 0000 0000		UNDERPASS*	SEP I 90	G		E		E	E				E				E	E		E		E		G	E		
S271 0000 0000P		UNDERPASS*	SEP I 90	G		E		E	E				E				E	E		E		E		G	E		
S271 0000 0202	38	T T TRESTLE	NEVADA CR	G	G	G	G		G		G		G		G			F		G		P		P	F		
S271 0000 0257	179	ST PONY TRUSS	BIG BLACKFOOT R	F		G	G		G	G	G	G	G	G	G	E	E	E		G	G	E	G	G	E		
S272 0000 0117	38	T T TRESTLE	THE RHINE CR	G	G	G		G	G		G	G	G		G			G	P	F	F	P		P	F		X
S272 0000 0133	57	T T TRESTLE	NEVADA CR	G	G	G		G	G		F	F	G		G			F	P	G	G	F		P	F		
S272 0000 0284	38	T T TRESTLE	NEVADA CR	G	G	G	G		G		G		G		G			F		G		P		P	F		
S272 0000 0354	189	ST PONY TRUSS	BIG BLACKFOOT R	E		G	G		G	G	G	G	G	G	G	E	E	E		G	G	E	G	G	E		
S272 0000 0419	152	ST PRATT TRUSS	N FK BLACKFOOT R	F				F	F		G		G	F		G	F			P	F	F		C	F		X
S273 0000 0007	42	STEEL I BEAM	WARM SPRINGS CR	G		F	F	F	G		G		G	F					P	F	P	P		P	P		X
S274 0000 0016	25	T T TRESTLE	MILL CR	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		
S274 0000 0122	57	T T TRESTLE	BIG CALIF CR	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		
S274 0000 0164	57	T T TRESTLE	FRENCH GULCH	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		
S274 0000 0198	57	T T TRESTLE	FRENCH GULCH	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		
S275 0000 0018	30	T T TRESTLE	WILLOW CR																								R

S275 0000 0021	37	T TRUSS SPAN	CLARK FORK																							N
S275 0000 0023	246	PRE CONC BEAM	SEP-I90	G		E		E	E					E			E	E	E	E	E	E	E	E	E	
S277 0000 0209	23	TIMBER TRESTLE	WHITETAIL CR	G	N	F	N	P	F	N	G	N	G	N	G	N	N	G	N	G	G	G	N	F	F	
S277 0000 0253	62	T T TRESTLE	MUSKRAT CR	F	G	F	G	F	F	N	G	N	F	N	P	N	N	P	N	F	F	P	N	P	F	
S277 0000 0290	51	T T TRUSS	CORRAL CR	P	F	P	F	P	C	N	G	N	G	N	C	C	N	C	N	C	P	C	N	N	C	X
S277 0000 0315	104	ST I BM PILES	BOX ELDER CR	F	G	G	G	F	F	N	G	N	F	F	F	N	N	P	N	P	F	P	N	P	F	
S278 0000 0186	50	T T TRESTLE	GRASSHOPPER CR	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G	
S278 0000 0432	35	UNT LOG TRESTLE	WARM SPRINGS CR	G	F	F		F	F		G		G		F				P	F	P	P			F	
S278 0000 0433	37	CONC & STEEL	DRAINAGE	G		F		G	G		G		G	G					P	G	G	G		P	G	
S279 0000 0178	57	T T TRESTLE	LT PRICKLY PEAR	G	G	G		G	G		G		G		G			G	F	G	G	G		F	G	
S279 0000 0199	57	T T TRESTLE	CANYON CR	G	G	G		G	G		P		G		G			G	F	G	G	F		F	G	
S279 0000 0211	57	T T TRESTLE	CANYON CR	G	G	G		P	P		G	F	F		G			G	F	F	F	F		F	F	
S279 0000 0216	63	T T TRESTLE	CANYON CR	G	G	G		F	F		G	G	G		G			G	F	G	F	F		F	G	
S280 0000 0004	215	PRE CONC BEAM	SEP-I15 YORK RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E	
S280 0000 0013	34	T T TRESTLE	HELENA VALLEY CA	G	G		G	G	G		G		G		G			G	F	G	G	F		P	G	

PLANNING SURVEY BRIDGE CONDITION REPORT

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	
S280 0000 0026	31	STEEL I BEAM	PRICKLY PEAR CR	G		F	F		F	P	G		G	G						G	G	F		F	F		
S280 0000 0146	545	ST THRU TRUSS	MISSOURI R	G		F	F	G	F	G	G		G		F	F	F			F	G	F		F	F		
S281 0000 0027	57	T T TRESTLE	LITTLE BOULDER R	G	G	G		G	G	G	G	G	G		F			G	P	G	G	F		P	G		X
S284 0000 0047	72	T T TRESTLE	HELENA VALLEY CA	G	G	G	G		G		G		G		G			G	F	G	G	G		P	G		
S284 0000 0089	1000	CONCRETE DAM	MISSOURI R	G			G	G	G	G	G		G	G			G	G	G	G	G	G	F	G	G		
S285 0000 0064	25	T T TRESTLE	CROW CR	G	G	G		G	G		G	G	G		G			G	P	G	G	F		P	G		
S286 0000 0030	154	ST PRATT TRUSS	GALLATIN R	F		F	F	G	G	G	G	F	G		G	G	P	F	P	G	G	F	G	P	F		X
S287 0000 0079	25	T T TRESTLE	WILLOW CR	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		
S288 0000 0000	235	PRE CONC BEAM	MANHATTAN INT 90	E		G		E	E					E			E	E		E		E	E	E	E		
S288 0000 0050	25	T T TRESTLE	CAMP CR	G	G	G		F	G	G	G		G		F		F	F	F	G	G	F		P	F		
S290 0000 0045	50	T T TRESTLE	E GALLATIN R	G	E	E	E	E	E	G	E	G	G		E			G		E	E	E		G	E		
S290 0000 0047	50	T T TRESTLE	E GALLATIN R	E	E	E	E	E	E	G	E	G	G		E			G		E	E	E		G	E		

S290 0000 0053	38	T T TRESTLE	SMITH CR	E	G	E	E	E	E	G	E	G	G		E			G		E	E	E		G	E
S290 0000 0108	26	STEEL I BEAM	DRY CR	G		E		E	E		E	F	E		E			P		G		F		P	G
S292 0000 0207	225	PRE CONC BEAM	BOX ELDER CR	G	N	E	E	E	E	G	F	G	F	E	N	N	E	E	P	G	N	E	G	G	G
S293 0000 0016	57	T T TRESTLE	E GALLATIN R	G	F	F	F	F	F		P	F	G		F		F	F	P	F	F	F		F	F
S293 0000 0032	38	T T TRESTLE	BRIDGER CR	G	F	F	F	F	F		P	F	G		F		F	F	P	F	F	F		F	F
S293 0000 0108	25	T T TRESTLE	BRIDGER CR	F	G	G		G	F		G	G	G		G		F	F	P	G	G	F		F	G
S294 0000 0125	50	T T TRESTLE	SAWMILL CR	G	G	G		G	G		G		G		G			G	G	G	F	G		P	G
S294 0000 0225	75	CONT STEEL GIR	COTTONWOOD CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G		G	G
S294 0000 0272	31	T T TRESTLE	OF MUSSELSHELL R	G	G	G		G	G						G			G	G	G	G	G		P	G
S294 0000 0273	100	T T TRESTLE	S FK MUSSELSHELL	G	G	G		G	G	G	P	G	G		G			G	G	G	G	G		P	G
S295 0000 0003		UNDERPASS	SEP I90	G		G		G	G					G			E	G	G	G	G	G		F	G
S295 0000 0004		UNDERPASS	SEP I90	G		G		G	G					G			E	G	G	G	G	G		F	G
S296 0000 0003	112	PRE CONC BEAM	MUSSELSHELL R	G		G	G	G	G	G	P	G	G	G			G	G	G	G		G		G	G
S296 0000 0094	30	UNT T TRESTLE	BIG ELK CR	F	F	F		F	G		G		G		G				F	F	P	P		P	F

PLANNING SURVEY BRIDGE CONDITION REPORT

A	B	C	D	E	F	G	H		J	K	L	M	N	O	P		R	S		U	V	W			Z	Z	
S297 0000 0009	57	T T TRESTLE	DEADMANS BASIN	G	G	G		G	G		G		G		G			G		G	G	G		G	G		
S298 0000 0085	120	ST THRU TRUSS	BOULDER R	F		P		P	F		G	P	G		P	P	P	P	F	P	P	P		P	P		
S298 0000 0130	150	CONT ST GIRDER	BOULDER R	G		G	G	G	G	G	P	F	G	G			G	G	P	G	G	F	F	F	G		
S298 0000 0162	60	ST PONY TRUSS	W BOULDER R	F		F		F	F		G	P	F		F	F	P	P	P	G	P	F		P	F		
S299 0000 0044	102	PRE CONC BEAM	CARELESS CR	G		G	G	G	G		G	G	G	G				G	G	G	G	G		G	G		
S300 0000 0002	142	PRE CONC BEAMS	MUSSELSHELL R	G		G	G	G	G	G	P	G	G	G			G	G	G	G	G	G		G	G		
S300 0000 0012	63	T T TRESTLE	FISH CR	F	G	G		G	G		P	F	F		G			G	G	G	G	G		G	G		
S300 0000 0081	49	UNT T TRESTLE	BIG COULEE	G	F	F		F	F		G		G		G			F		F	F				F		
S300 0000 0089	40	ST QUEEN TRUSS	BIG COULEE	F	G	F		P	P		G		G			F				F	F	F		P	P		X
S302 0000 0090		UNDERPASS	GN RY	G		G								G			G							P	G		
S303 0000 0072	24	STEEL I BEAM	ARROW CR	F	C	P		P	F		G		G		P			P		G		P		P	P		X
S303 0000 0082	36	STEEL I BEAM	CANAL	G		G	G	G	G		G		G		G			F		F		G		G	G		
S303 0000 0104		UNDERPASS	I 90 SEP																							N	
S303 0000 0105		UNDERPASS	I 90 SEP																							N	

				E	F		H			K		M	N	O			R	S	T			W		Y		ZZ
S303 0000 0150	23	ST I BM PILE	CANAL	G	G	G		F	F		G		G		G			P		F		P		G	G	
S303 0000 0159	25	T T TRESTLE	CANAL	G	G	G			G		P		G		G					G	F	F		F	G	
S305 0000 0036	120	CONT CONC T BM	CANYON CR	G		G			G		F	G	G	G			G	G	F	G		F		F	G	
S305 0000 0049	25	T T TRESTLE	BIG DITCH BBWA	G	G	G		G	G		G		G		G			G		G	G	G		G	G	
S305 0000 0101	29	T T TRESTLE	BBWA CANAL	F	G	G		G	G		G		G		G			G		G	G	G		G	G	
S305 0000 0112	190	PRE CONC BEAM	NP RY	G		E			E					E			E	E		E		E	E	G	E	
S305 0000 0112P	190	PRE CONC BEAM	NP RY	G		E			E					E			E	E		E		E	E	G	E	
S305 0000 0118	175	PRE CONC BEAMS	SEP US 10	G		E			E					E			E	E		E		E	E	G	E	
S305 0000 0118P	175	PRE CONC BEAMS	SEP US 10	G		E			E					E			E	E		E		E	E	G	E	
S306 0000 0036	30	STEEL I BEAM	KEYSER CR	G		G		G			G	F		G											F	
S306 0000 0058	95	T T TRESTLE	KEYSER CR	F	G	G	G	G	G	G	G	G			G			F	P	F	G	G		P	G	
S307 0000 0129	25	T T TRESTLE	W RED LODGE C	P	G	G		G	G		G		G		G			G	P	G	G	G		P	G	
S307 0000 0198	110	CONT CONCT BEAM	E ROSEBUD CR	P		G			G		G	G	G	G			G	G	G	G		G		G	G	
S307 0000 0262	153	PRE CONC BEAMS	E ROSEBUD CR	F		G	G		G		G	G	G	G			G	G	G	G		G	G	G	G	
S307 0000 0301	30	STEEL I BEAM	BUTCHER CR	G		G		G	G		G		G		G			G		G		G		F	G	
S307 0000 0349	50	T T TRESTLE	BEAVER CR	G	G	G		G	G		G	G	G		F			G	P	G	F	F		P	G	X

S307 0000 0435	63	T T TRESTLE	SHAYNE CR	G	G	G	G	G	G		G	G	G		C		G	P	G	G	G		P	G	X
S307 0000 0461	576	RIV PL GIROERS	YELLOWSTONE R	P		G	G	G	G	G	G	G	G	G	G	G	G		G	G	G	G	F	G	
S309 0000 0040	38	T T TRESTLE	ORAINAGE	G	G	G		G	G		G	G	G		G		G		G	G	G		P	G	X
S310 0000 0008	562	RIV PL GIRO	YELLOWSTONE R	P		E	E		G	E	E	G	G	E		E	E	G	E	E	E	G	G	G	
S310 0000 0427	193	PRE CONC BEAMS	MUSSELSHELL R	G		G	G	G	G	G	G	G	G	G		G	G	G	G		G	G	G	G	
S311 0000 0130	62	UNT T TRESTLE	DRAINAGE	G	P	F			F		P		G		F		P		F	F	P		P	P	X
S311 0000 0169	704	WELOED PL GIRO	YELLOWSTONE R	E		E	E	E		E	G	E		E		E	E	E	E		E	E	E	E	X
S311 0000 0202	88	T T TRESTLE	BUCKINGHAM COU	G	G	G			G		G	P	G		P		F	P	G	G	P		P	G	X
S311 0000 0237	95	T T TRESTLE	BOX ELOER CR	G	G	P			F		G		G		P		F	G	G	G	P		P	F	X
S313 0000 0018	25	T T TRESTLE	WILLIAMS CR	G	G	G		G	G		G	F	G		C		F		G	G	G		F	G	X
S313 0000 0055	45	T T TRESTLE	TWO LEGGIN CANAL	G	G	G		G	G		G		G		F		F		G	G	G		P	G	
S313 0000 0070	50	T T TRESTLE	TWO LEGGIN CANAL	G	G	G		G	G		G		G		F		F		G	G	F		P	G	
S313 0000 0072	57	T T TRESTLE	OVERFLOW OITCH	P	G	G		G	P		P				C		F		F	G	F		P	F	X
S313 0000 0075	576	RIV PL GIROERS	BIG HORN R	G		G	G		G	G	G	G	G	G		G	G	G	G	G	G	G	G	G	
S313 0000 0230	64	T T TRESTLE	ROTTEN GRASS CR	F	G	G			G		G		G		P		G		G	G	P		P	F	X

PLANNING SURVEY BRIDGE CONDITION REPORT

CONTROL NUMBER A	TOTAL LENGTH FEET B	TYPE C	NAME OF FEATURE CROSSED D	END E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	Q	SHOES R	CURBS S	MARKERS T	DECK U	BR V	RAIL W	X	Y	Z	Z1	Z2
S313 0000 0317	102	PRE CONC BEAM	SOAP CR	F		E		E	E		G	G	G	E			E	E	E	E		E		G	E		
S313 0000 0341	65	PRE CONC BEAM	INDIAN SERVICE C	F		E		E	E		G	G	G	E			E	E		E		E		G	E		
S315 0000 0136	113	T T TRESTLE	ROSEBUD CR	G	G	G	G		G	G	G		G		G			G	G	G	G	G		P	G		
S315 0000 0154	100	T T TRESTLE	MILLER COULEE	G	G	G			G		G	G	G		G			G	P	G	G	G		P	G		
S315 0000 0263	57	T T TRESTLE	STOCKER CR	G	G	G		G	G		F		G		G			G	P	G	G	G		G	G		
S315 0000 0292	38	T T TRESTLE	CORRAL CR	G	G	G			G		G	G	G		G			G	F	G	G	G		G	G		
S315 0000 0306	38	T T TRESTLE	MCGILVREY CR	G	G	G		G	G		G	G	G		G			G	F	G	G	G		G	G		
S315 0000 0339	57	T T TRESTLE	SEVEN MILE CR	G	G	G			G		G	P	G		G			G	F	G	G	G		G	G		
S315 0000 0364	76	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
S315 0000 0383	125	T T TRESTLE	E FK ARMELLS CR	G	G	G			G		F	G	G		F			G	G	G	G	G		G	G		X
S315 0000 0386	57	T T TRESTLE	SHEEP CR	G	G	G			G		G		G		G			G		G	G	G		G	G		
S315 0000 0438	92	PRE CONC BEAM	ARMELLS CR	P		E	E		E	E	G	G	G	E			E	E		E		E		E	E		
S315 0000 0512	143	PRE CONC BEAM	COLSTRIP INT 194	F		E			E					E			E	E		E		E		E	E		
S320 0000 0022	95	T T TRESTLE	COTTONWOOD CR	C	G	G			G		G	F	G		C			F			G	F		P	F		X
S320 0000 0051	36	STEEL I BEAM	STATION CR	G		F		F	F		G		G		F			F		F		P		P	F		
S320 0000 0053	202	ST PONY TRUSS	OFALLON CR	F		F	F	P	F	G	G		G		G	F	F	G		G	G	P		P	F		

S321	0000	0060	100	T T TRESTLE	PENNEL CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G		
S322	0000	0111	133	STEEL GIRDER	LITTLE BEAVER CR	G	G	G	G	F	G	F	F	F	P	G	G	N	G	F	P	G	G	G	G	G	F		
S323	0000	0177	183	CONCRETE T BM	BOX ELDER CR	F	N	G	G	G	G	G	G	G	G	G	N	N	G	G	N	G	N	G	G	P	G		
S323	0000	0565	172	ST PRATT TRUSS	LIT MISSOURI R	F	F	F	C	N	G	N	G	F	F	G	G	F	G	P	N	F	F	P	N	P	F		
S324	0000	0001	133	PRE CONC BEAM	INT-I 15	G		E		E	E					E			P	E	E	E	E	E	G	G	G		X
S324	0000	0045	92	PRE CONC BEAM	HORSE PRAIRIE CR	G		E		E	E		G	G	G	E			E	E	E	E	E	E			E	E	
S324	0000	0051	71	PRE CONC BEAM	HORSE PRAIRE CR	G		E		E	E		G	G	G	E			E	E	E	E	E	E		E	E		
S324	0000	0069	71	PRE CONC BEAM	MEDICINELODGE CR	G		E		E	E		G	G	G	E			E	E	E	E	E	E		E	E		
S325	0000	0003	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	P	G	G	G		P	G		
S325	0000	0004	76	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G	P	G	G	G		P	G		
S325	0000	0005	38	T T TRESTLE	CANAL	G	G	G	G		G	G	G		G		G			G	P	G	G	G		P	G		
S327	0000	0039	100	T T TRESTLE	LITTLE MUDDY CR	F	G	G			G		G		G		G			G		G		G		P	G		
S327	0000	0123		UNDERPASS	GN RY	G		G								G			G								G		

	TOTAL LENGTH FEET			END F	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS			CURBS									
A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S329 0000 0017	537	STEEL TRUSS	YELLOWSTONE R	F		F	F	F		G	G	F	F	G	F	G	F	G		F	F	F	P	P	F		X
S329 0000 0022	59	STEEL TRESTLE	OUCK CR	G	G	G				G	G		G	G				G		G		P		P	G		
S329 0000 0024	40	STEEL I BEAM	DUCK CR	E		E		E			F				E					E		E		G	E		X
S330 0000 0003	559	ST HOWE TRUSS	MISSOURI R	G		P	F	P	P	G	G		G	G	G	G	P			F	F	F	P	F	F		X
S330 0000 0050	130	STEEL GIRDER	SMITH R	G		G	G	G	G	G	F	G	G	G	G		F	G	F	G		G	P	F	G		
S330 0000 0152	142	PRE CONC GIROER	SMITH R	G		G	G	G	G	G	P	G	G	G			G	G	G	G		G	G	G	G		
S330 0000 0366	648	ST PLATE GIROER	MISSOURI R	G		G	G	G	G	G	G		G	X	G		G	G	G	F		G	G	F	G		X
S331 0000 0011		UNOERPASS	GN RY	G		G		G	G						G		G	F		G				F	G		
S332 0000 0009	138	PRE CONC BEAMS	PUMPKIN CR	F		E			E		G	G	F	E			E	E	G	G		E		G	E		
S332 0000 0105	38	T T TRESTLE	ASH CR	G	G	G			G		F		G		G			G	G	G	G	G		G	G		X
S332 0000 0106	38	T T TRESTLE	ASH CR OVERFLOW	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		X
S332 0000 0109	38	T T TRESTLE	ASH CR OVERFLOW	G	G	G		G	G		F		G		G			G	G	G	G	G		G	G		
S332 0000 0138	25	T T TRESTLE	JACK CR	G	G	G		G	G		G		G		F			G	G	G	G	G		G	G		X
S332 0000 0157	25	T T TRESTLE	BROWN CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S332 0000 0173	38	T T TRESTLE	HAOOOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S332 0000 0198	38	T T TRESTLE	FOSTER CR	G	G	G		G	G		P		F		G			F	G	G	G	G		G	G		

				E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
S332 0000 0396	214	PRE CONC BEAMS	TONGUE R	G		E	E		E		F	G	G	E		E	E	E	E	E		G		G	E
S333 0000 0081	23	STEEL I BEAM	DRAINAGE	G	F	F			P		G		G		G					P		P		P	P
S333 0000 0142	39	STEEL I BEAM	STREVELL CR	G	G	G		G	G		G		G		G			F		F		F		F	F
S333 0000 0160	138	ST THRU TRUSS	MIZPAH CR			F										G								P	
S335 0000 0017	50	T T TRESTLE	DRAINAGE	P	G	G	N	G	G	N	G	P	F	N	G	N	N	G	N	G	G	G	N	F	F
S335 0000 0038	52	T T TRESTLE	DRAINAGE	F	F	F	N	G	G	N	F	N	G	N	F	N	N	P	P	F	F	P	N	P	P
S335 0000 0053	102	PRE CONC BEAM	SAND CR	P	N	G	G	G	G	N	F	P	F	E	N	N	E	G	P	G	N	G	N	G	F
S335 0000 0144	200	T T TRESTLE	CEDAR CR	G	G	G	N	G	G	N	P	F	P	N	P	N	N	F	P	P	P	F	N	P	P
S336 0000 0053	50	T T TRESTLE	FK OF BEAVER CR	G	G	G	G	G	G	G	G	N	F	N	G	N	N	G	P	G	G	G	N	G	G
S336 0000 0070	75	T T TRESTLE	BEAVER CR	G	G	G	G	G	G	G	G	N	G	N	G	N	N	G	P	G	G	G	N	G	G
S339 0000 0002	50	T T TRESTLE	FLATHEAD CR	G	G	G	G	F	F	G	F	P	G		G		G	F	P	F	G	G		P	F
S339 0000 0037	71	CONCRETE T BEAM	SHIELDS R	G		G	G	G	G		G	G	G	F			F	G	P	F	G	P		F	G
S339 0000 0141	25	T T TRESTLE	SHIELDS R	F	G	G		G	F		G	F	G		G		G	F	P	G	G	F		F	G
S340 0000 0019	63	T T TRESTLE	PLUM CR	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	P	G	G	G	N	F	G

A	B FEET	C	D	E FND	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TRUSSES	R SHOES	S CURBS	T	U DECK	V	W	X	Y	Z	Z	Z2 REMARKS
S344 0000 0007	50	T T TRESTLE	SHEEP CR	F	G	G		G	G		G		G		G			G		G	G	G		P	G		
S344 0000 0040	110	CONT CONC T BM	BIG MUDDY CR	F		G			G		G	G	G	G			G	G	P	G		G		F	G		
S344 0000 0121	110	CONT CONC T BM	SMOKE CR	F		G			G		G	G	G	G			G	G	F	G		G		F	G		
S345 0000 0044	21	CONC SL-ST I BM	MIDDLE CR	G		G		E	E		G		G		G		G	P	P	G	G			P	G		
S346 0000 0000	235	PRE CONC BEAM	MANHATTAN INT 90	E		G		E	E					E			E	E		E		E	E	E	E		
S346 0000 0018	102	PRE CONC BEAM	BAKER CR	E		E	E	E	E	E	E	E	G	E			E	E	E	E		E		E	E		
S346 0000 0021	192	PRE CONC BEAM	W GALLATIN R	E		E	E	E	E	E	F	E	G	E			E	E	E	E		E	E	G	E		
S346 0000 0056	132	PRE CONC BEAM	EAST GALLATIN R	E		E	E	E	E	E	F	E	G	E			E	E		E		E		E	E		
S347 0000 0027	94	STEEL GIRDER	BAKER CR	G		G	G	G	F	F	F	F	G	G			F	G		G	G	F	F	F	G		
S347 0000 0034	178	STEEL GIRDER	GALLATIN R	G		G	G	G	F	F	P	G	G	G			F	G		G	G	F	F	F	G		
S348 0000 0004	38	T T TRESTLE	FLINT CR	G	G	G	G	G	G		G		G		G			G		G		G		C	G		
S348 0000 0139	102	PRE CONC BEAMS	ROCK CR	E		E	E	E	E	E	E	E	E	E			E	E		E		E		G	E		
S350 0000 0030	110	CONT CONC T BM	BIG MUDDY CR	F		G	G		G		G	G	G	G			G	G	F	G		F		G	G		

A	B				F	G	H		J	K		M	N	O			R								Z		
S353 0000 0001		UNDERPASS	NP RY	G	G	G									G						G				G		
S354 0000 0066	69	UNT T TRESTLE	IRRIGATION CA	G	F	F		F	F		G		G		G			F		F	F	P		P	F		
S356 0000 0001	65	ST PONY TRUSS	TENMILE CR	G		G		G	G		G		G		G	F	P		P	G	F	G		P	F		X
S356 0000 0035	28	STEEL I BEAM	SEVENMILE CR	G		G		G	G		G		G	G					P	G	F	F		G	G		
S358 0000 0074	285	PRE CONC BEAM	BIRCH CR	E		E	E	E	E	E	G	E	G	E			E	E		E	E	E	E	E	E		
S358 0000 0174	316	PRE CONC BEAM	TWO MEDICINE CR	E		E	E	E	E	E	G	E	G	E			E	E		E	E	E	E	E	E		
S358 0000 0278	92	PRE CONC BEAM	SPRING CR	G		E	E	E	E		G	E	G	E			E	E		E	E	E		E	E		
S359 0000 0003	112	PRE CONC BEAM	JEFFERSON R SL																							N	
S359 0000 0012	289	PRE CONC BM	JEFFERSON R	E		E	E	E	E	E	E	E	E	E			G	E	G	G	E	E	E		E		
S359 0000 0017	38	T T TRESTLE	SLOUGH	G	G	G		F	G		G		G		G			P	P	G	G	F		P	G		X
S359 0000 0050	50	T T TRESTLE	SOUTH BOULDER R	G	G	G		F	G		P		G		G			P	P	G	G	F		F	G		X
S360 0000 0004	29	T T TRESTLE	N FK SMITH R	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S360 0000 0163	61	PRATT ST TRUSS	SMITH R	G		P		P	P		G		G		G	P	P	F		G	P	P		P	P		X

[illegible]

NUMBER	TOTAL LENGTH FEET	MATERIAL & TYPE MAX MAIN SPAN	FEATURE CROSSED	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MAR	DECK	BRACING	RA	ON	F NT	GENERAL CONDIT	NOT INSPE	REMARKS
A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S362 0000 0008	300	STEEL GIRDER	YELLOWSTONE R	F		G	F	G	G	P	P	G	G	G			F	F	P	F	G	G	F	F	G		
S362 0000 0011	25	T T TRESTLE	ARMSTRONG IRR CA	F	F	F		F	F		G		G		G		G	P	P	G	G	F		P	F		
S363 0000 0007	29	STEEL I BEAM	CANAL	F	F	F			P		G		G		F			P		F					F		X
S363 0000 0013	219	ST THRU TRUSS	MILK R	C		F	F		P		G		G		P	F	F	F		F		F		P	P		X
S363 0000 0088	112	PRE CONC BEAM	ALKALI CR	G		E	E	E	E	G	G	G	F	E			G	E	G	E		E		E	G		
S363 0000 0113	75	PRE CONC BEAM	IRRIGATION CANAL	G		G		E	E		G		F	E			G	E	G	E		E		G	G		
S365 0000 0005	183	PRE CONC BEAM	BRADY INT I 15	G		G	G	G	G					G			G	G		G		G	G	G	G		
S366 0000 0023	25	T T TRESTLE	COU & CANAL OF	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S366 0000 0059	106	CONT ST GIRDER	DRY FK MARIAS R	F		G	G	G	G	G	G	P	P	E			G	G		G	G	G	G	P	G		X
S367 0000 0005	33	STEEL & TIMBER	IRRIGATION CANAL	F	P	F		P	P		G		G	G						F	F	C		C	F		
S369 0000 0003	38	T T TRESTLE	PONDERA COULEE	F	G	G		F	F		G	G	G		G				G	G	F	F			G		
S370 0000 0007	351	ST HOWE TRUSS	BITTERROOT R																								X
S370 0000 0010	80	UNT T TRESTLE	DRAINAGE																								X

A	B				F		H		J	K		M	N				R								Z	
S370 0000 0011	41	UNT T TRESTLE	DRAINAGE																							X
S370 0000 0013	40	UNT T TRESTLE	DRAINAGE																							X
S370 0000 0020	42	ST I BEAM	BITTERROOT R																							X
S371 0000 0012	120	CONT CONC T BM	SWEET GRASS CR	F		G		G	G		G	E	G	G			G	G	F	F		G		F	G	
S371 0000 0109	45	T QUEEN TRUSS	SWEET GRASS CR	F		G		P	F		G	F	F		F	F				F	P	P		P	F	
S373 0000 0004	324	STEEL GIRDER	BITTERROOT R	F		G	G	G	G	G	F	G	G	G			G	G		G	G	G	G	F	G	
S374 0000 0037	38	T T TRESTLE	PLENTYWOOD CR	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G	
S375 0000 0055	266	PRE CONC BEAMS	9 MI SEP-I15	E		E		E	E					E			E	E	E	E	E	E	G	F	E	
S375 0000 0081		UNDERPASS	NP RY	G		G	G	G	G					G			G			G	G	G		G	G	
S375 0000 0083	215	PRE CONC BEAMS	NP RY	G		G		G	G					G			G	G	P	G	G	G		F	G	
S378 0000 0058	39	STEEL I BEAM	MUDDY CR	G	F	F		F	F					F						F	F			F	F	
S378 0000 0063	39	UNT T TRESTLE	DRAINAGE	G	F	F		F	F		F				F					F	F	F		F	F	
S381 0000 0004	150	STEEL GIRDER	MUSSELSHELL R	G		G	G	G	G	G	P	G	G	G			G	G		G	G	G	G	G	G	

A	FEET B	C	D	END F E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	Q	R	CURBS S	T	DECK U	BRACING V	W	X	Y	Z	Z1	Z2
S381 0000 0044	38	T T TRESTLE	HARPER COULEE	G	G	G		G	G	G	G		G		G			G		G	G	G		P	G		
S382 0000 0000	128	PRE CONC BEAM	NP RY	P		G		G	G								G	G	G	G		G	G	G	G		X
S382 0000 0001	650	WELDED PL GIR	FLATHEAD R	P		G	G	G	G	G	G	G	G	G	G		G	G	G	G	G	G	G	G	G		X
S382 0000 0027	50	T T TRESTLE	CAMAS CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
S382 0000 0032	50	T T TRESTLE	CAMAS CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
S382 0000 0036	50	T T TRESTLE	CAMAS CR	P	G	G		G	G		P	F	G		G			G	G	G	F	P		P	G		X
S384 0000 0005	183	PRE CONC BEAM	LIT BIG HORN R	G		E	E		E	E	P	G	G	E			E	E	F	E		E	E	F	E		
S384 0000 0139	92	PRE CONC BEAM	TULLOCK R																							N	
S386 0000 0005		UNDERPASS	GN RY	G		G		G	G						G		G	G	G	G				F	G		
S388 0000 0033	32	STEEL I BEAM	SKALKAHO CR	G		F		G	F	F	G	F	G	G						G	G			P	F		
S390 0000 0038		UNDERPASS	DAKOTA ST	E		E		E	E					G	G		E	E		E	E	G		G	E		
S390 0000 0039		UNDERPASS	CMSTP&P RR	E		E		E	E					G	G		E	E		E	E	G		G	E		
S390 0000 0043	420	STEEL GIRDER	CLARK FORK	G		G	G	G	G	G	G	G	G	G	G		G	G	F	G	G	F	G	F	G		

A	B	C																									
391 0000 0037	45	T T TRESTLE	SAND CR	F	G	G			G		G	E	G		G			G		G	G	G		P	G		
391 0000 0078	60	ST PONY TRUSS	ROUGH CR	F	G	F			F		G		G		C	G	G	P		F	F	F		P	F		
391 0000 0359		FORD	POWDER R																							N	
391 0000 0393	31	STEEL I BEAM	HORSE CR																							X	X
394 0000 0005	130	STEEL GIRDER	MUSSELSHELL R	G		G	G	G	G	G	F	F	G	G			G	G		G	G	G		G	G		
396 0000 0014	100	STEEL I BEAM	THIRTY MILE CR	G	G	G		G	G		G		G		G			G		G		G		P	G		
396 0000 0087	48	STEEL I BEAM	WAYNE CR	F		F	F		F		F		F		F			P		C		P		P	F		X
396 0000 0121	24	UNT T TRESTLE	DRAINAGE	F		F		P	P		F		G		F			F		F		F		P	F		
396 0000 0141	74	ST PONY TRUSS	SAVOY CR	F		G			G		G		G		F	F	F	F		G		P		P	F		
399 0000 0004	121	STEEL GIRDER	BOULDER R	F		G	G		G	G	G	G	G	G			G	G	F	G	G	G	G	F	G		
399 0000 0236	32	STEEL I BEAM	WHITETAIL CR	G		G		G	G		G	G	G					F	P	F	F	F		P	F		
399 0000 0259		UNDERPASS*	WHITEHALL INT 90	G		E		E	E					E			E	E		E	E	E	E	G	E		
399 0000 0260		UNDERPASS*	WHITEHALL INT 90	G		E		E	E					E			E	E		E	E	E	E	G	E		
402 0000 0045	251	STEEL TRUSS	LITTLE POWDER R	G	G	G	G		G	G	F	G	F		G	G	G	G	P	G	G	G	F	P	G		

NUMBER	FEET			END F	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MAR	DECK	BRA	RA	EXP	PAINT	GENERAL	NOT INSP	REMARKS
A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S403 0000 0008	76	T T TRESTLE	BA & P RY	G		G		F	G						P			F	F	F	G	F		P	F		
S403 0000 0011		UNDERPASS	CROSSWALK			F								G				F		F	F	F		F	F		
S404 0000 0198	110	CONT CONC T BM	SMOKE CR	G		G			G		G	G	G	G			G	G	G	G		G		F	G		
S407 0000 0002	54	ST HOWE TRUSS	LIT BLACKFOOT R	F				F	P		G		G		G	G	G			G	G	F		P	P		X
S408 0000 0013	38	T T TRESTLE	USRS LAT DITCH	G	G	G		G	G		G		G		G			G	P	G	G	G		G	G		
S408 0000 0040	75	T T TRESTLE	USRS MAIN CA	G	G	G		G	G		G			G				G	G	G	G	G		G	G		
S410 0000 0000		UNDERPASS	KEVIN INT-I15	G		E		E	E					E			E	E	G	E	E	E		E	E		
S410 0000 0112	70	PRE CONC BM	W FK WILLOW CR	G		E		E	E		G		G	E			E	E		E	E	E	E	E	E		
S410 0000 0162	35	STEEL I BEAM	WILLOW CR	F		F		F	F		G		G	F				P		F	F	C		C	P		X
S410 0000 0166	23	STEEL I BEAM	E FK WILLOW CR	F		P		C	F		G	G	G	F				P		F	F	C		C	P		X
S410 0000 0217	31	STEEL I BEAM	TRAIL CR	F		G		G	F		G		F	G				P		F	F	C		P	F		X
S411 0000 0003	50	ST PONY TRUSS	E GALLATIN R	F	F	C		F	F		P	F	F		F	F	P	C	P	F	F	P		P	F		X
S413 0000 0004	150	T T TRESTLE	BEAVER CR	G	G	G	G	N	G	G	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G		

A	B		D		F	G	H		J	K		M	N	O		Q	R		T		V	W			Z	Z	
413 0000 0038	25	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	P	G		
413 0000 0246	100	T T TRESTLE	BEAVER CR	G	G	G	G	G	G	G	G	F	G	N	G	N	N	G	G	G	G	G	N	P	G		
415 0000 0020	142	PRE CONC BM	SARPY INT I94	E		E			E					E				E	E	E		E		E	E		
415 0000 0037	25	T T TRESTLE	SARPY CR	G	G	G		P	F		G		G		G			P		F	G	P		P	G		
415 0000 0093	25	UNT T TRESTLE	SARPY CR	P	P	P		P	F		G		G		F			P		F	G	P		P	P		
415 0000 0184	36	UNT T & CONC	SARPY CR	G		G	G			G	P		G		P			P		F	P	P		P	F		
416 0000 0010	215	PRE CONC BEAM	BILLINGS BLV SEP	G		E			E					E			E	E		E		E	E	E	E		
416 0000 0023	766	STEEL TRUSS	YELLOWSTONE R	G		G	G		G	G	F		G		G	G	G	F	F	F	G	F	F	P	G		
416 0000 0029	38	T T TRESTLE	BLUE CR	F	G	G		G	G		P		G		G			F	F	G	G	P		P	G		
417 0000 0071	450	STEEL GIRDER	MARIAS R	F		G	G	G	G	G	P	G	F	G	G		G	G	P	F	G	G	G	P	G		X
418 0000 0005	64	T T TRESTLE	PASS CR	G	C	P			G		F		G		G					G	F	G		P	P		X
418 0000 0096	90	STEEL TRUSS	LIT BIGHORN R	G		G			G		G	G	G		G	G	G	G		G	G	G	G	G	G		
419 0000 0001	26	STEEL I BEAM	OF E ROSEBUD CR	G		P		G	G		G		G		G					G		P		F	G		X
419 0000 0002	56	ST PONY TRUSS	EAST ROSEBUD CR	G		P		F	F		G		G		G	G		G		G	G	F		F	G		X

A	B FEET	C DESC	D	E	F	G BENTS	H PIERS	I WINGWA	J	K ICE BREAKERS	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S419 0000 0036	60	ST PONY TRUSS	WEST ROSEBUD CR	G		G					G	P	G		P	P		P		G	G	P		P	F		X
S419 0000 0199	176	REINF CONC GIR	STILLWATER R	P		G	G				G		G	G			G	G	G	G		G	G		G		X
S419 0000 0213	31	UNT T PONY TRUS	DRAINAGE	F		F		F	F		G		G		P	P				F		P		P	F		
S419 0000 0214	42	STEEL I BEAM	W FK STILLWATER	G		G		G	G		G		G	G	P					F		P		P	F		
S420 0000 0002	24	STEEL I BEAM	DRAINAGE	F		G		G	G		G		G		G					G		P		P	G		
S420 0000 0003	95	STEEL TRUSS	ROSEBUD CR	G		P		G	G		G	P	G		G	G	G	F		G	G	P	F	P	G		X
S422 0000 0001	285	ST THRU TRUSS	JEFFERSON R	F		F	F		F	F	G	F	F		G	F	F	F	P	F	F	G		P	F		
S422 0000 0015	60	UNT T TRESTLE	JEFFERSON R OF	F	P	F		P	F		G		F		F				P	P	P	P		P	P		
S422 0000 0086	245	PRE CONC BEAMS	JEFFERSON R	G		E	E	E	E	E	F	G	G	G			E	E	F	E	E	E	G	G	G		
S423 0000 0001	210	PRE CONC BEAMS	VICTOR INT-I15	E		E		E	E					E			E	E	E	E	E	E	E	F	E		
S423 0000 0003	231	STEEL GIRDER	UPRR	G		G		G	G					G			G	G	G	G	G	G	G	G	G		
S424 0000 0234	200	UNT T TRESTLE	STILLWATER R	G	G	G		F	G		P		G		G					G	G	G			G		X
S427 0000 0122	38	T T TRESTLE	OTTER CR	G	G	G		G	G		F		G		G			G	G	G	G	G		G	G		

A	FEET	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z		
S429 0000 0002	457	PRE CONC BEAMS	SEP-I90	G		G			G					E			G	G		G		G	G	F	G		
S429 0000 0012	133	PRE CONC BEAMS	CANYON CR	G		G			G		G	G	G	G			G	G	G	G		F	G	P	G		
S429 0000 0017	29	T T TRESTLE	BBWA CANAL	G	G	G		G	G		G		G		G			G		G	G	G		P	G		
S430 0000 0056		UNDERPASS	RESERVE ST INT I	E		E	E	E	E			E	E		E		E	E		E		E		E	E		
S430 0000 0057		UNDERPASS	RESERVE ST INT I	E		E	E	E	E			E	E		E		E	E		E		E		E	E		
S431 0000 0001	57	T T TRESTLE	MAIN IRR CANAL	G	G	G		G	G		G		G		G			G	P	G	G	G		G	G		
S431 0000 0048	57	T T TRESTLE	MAIN IRR CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S431 0000 0163	50	CONCRETE SLAB	BIG MUDDY CR	G	G	G		G	G		F		G					G		G					G		
S432 0000 0291	23	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G		G	G	G		P	G		
S433 0000 0005	32	CONCRETE SLAB	PRICKLY PEAR CR	G		G		G	G		G		G					G	P	G	G	G		F	G		
S433 0000 0018	42	CONC & TIMBER	HELENA VALLEY CA	G		G		G	G		G		G		G			G	G	G	G	G		F	G		
S434 0000 0000		UNDERPASS	WOLF CR INT I15	G		G		G	G					G			G	G		G					G		
S434 0000 0187	75	PRE CONC SLAB	MID FK DEARBORN	G	G	G		G	G		F	G						G	P	G					G		
S434 0000 0267	231	ST PRATT TRUSS	N FK DEARBORN R	G		G	P		F		G		G		G	F	F			F	F	F		G	F		X

NUMBER CONTROL JUNCTION MILE A	TOTAL LENGTH FEET B	MAX MUM SPAN C	D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	J	ICE BREAKERS K	L	M	N	O	STRINGERS P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S434 0000 0407	38	T T TRESTLE	S FK SUN R	G	G	G		G	G		P		G		G			F	G	G	G	G		F	G		
S434 0000 0424	75	T T TRESTLE	SMITH CR	G	G	G		G	G		P	G	G		G			G	G	G	G	G		G	G		
S436 0000 0006	25	T T TRESTLE	IRRIGATION CA	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
S436 0000 0013	75	T T TRESTLE	FIFTEEN MILE CR	G	G	G	G	G	G	G	G		G		G			G	G	G	G	G		F	G		
S438 0000 0252	78	STEEL I BEAM	E FK PORCUPINE	G	G	C			G		G		G		G			F		G	G	F		P	G		
S438 0000 0355	23	UNT T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			F		G	G	F		P	G		
S441 0000 0022	32	CONCRETE T BEAM	CLARK FORK	G		F		F	P		G		G	F						F	F	F			F		
S441 0000 0042	265	PRE CONC BEAM	GREGSON INT I90	G		E		E	E					E			E	E	E	E	E	E	E	E	E		
S444 0000 0035	50	T T TRESTLE	WILLOW CR	G	G	G		P	F	G	G		G		G			G	F	F	F	F		P	G		
S444 0000 0037	100	T T TRESTLE	CUT BANK CR	G	G	G		F	F	G	G		G		F			G	G	G	G	F		P	G		
S444 0000 0057	38	T T TRESTLE	COBELLE CR	G	G	G		G	G	G	G		G		G			G	G	G	G	G		G	G		
S445 0000 0091	163	PRE CONC BEAMS	CUT BANK CR	G		E	E	E	E	E	G	E	G	E			E	E		E	E	E		F	E		
S446 0000 0004	867	STEEL TRUSS	YELLOWSTONE R	F	P	P	F	P	P	F	G		G		P	F	F	P		P	F	P		P	P		

A	B	C		E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	ZZ
S446 0000 0061	38	T T TRESTLE	SAND CR	G	E	E		E	E		G		F		E			G		G	E	G		F	G		
S447 0000 0051	75	ST PRATT TRUSS	ROSEBUD CR	G		G		G	G		G		G		G	G				F	F	P		P	G		
S447 0000 0094	58	UNT T TRESTLE	DRAINAGE	F	P	P		P	F		G		G		P			P		P		P		P	P		
S447 0000 0172	96	STEEL I BEAM	DRAINAGE	G		F	F	F	F		F		G		G			P		F		P		P	F		
S447 0000 0224	31	STEEL I BEAM	DRAINAGE	G		F		F	F		G		G		G			P		F		P		P	F		
S447 0000 0427	31	STEEL I BEAM	LAY CR	F		F		F	F		G		G		G			P		F		F		P	F		
S448 0000 0021	75	T T TRESTLE	BIG SANDY CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		X
S449 0000 0002	102	PRE CONC BEAM	SAGE CR	E		E	E	E	E	E	G	E	G		E			E	E	E	E	E		E	E		
S452 0000 0012	96	ST PONY TRUSS	BULLHOOK CR	F	F	F	G	P	C		G		G		F	F				G	G	F		P	F		X
S456 0000 0007	127	UNT T HOWE TRUS	STILLWATER R	G	F	F		F	F		F		G		G	F				G	F	F			F		X
S457 0000 0082	110	CONCRETE T BEAM	UNTIBER DAM	G		G	G	G	G	G	G		G	G			F	F		G		G	G	P	F		X
S460 0000 0000		UNDERPASS	I90 GOLD CR INT	G		E		E										E		E					E		

G BRIDGE REPORT

RATING

CONTROL BRIDGE NUMBER A	TOTAL LENGTH FEET B	DESCRIPTIVE FEATURES MATERIAL & TYPE C	NAME D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	T	U	BRAC V	RAILING W	EXPANS X	PAINT Y	G Z	Z1	Z2
S460 0000 0001		UNDERPASS	I90 GOLD CR INT	G		E		E										E		E					E		
S460 0000 0003	120	ST HOWE TRUSS	CLARK FORK	F		P		F	P			C			F	F	F			F	F	P		P	F		X
S461 0000 0129	445	REINF CONC GIR	CLARK FORK	G		G	G		G		G	F					G	G		G		G	G		E		
S461 0000 0138		UNDERPASS	NP RY				G	G	G	G				G		G	G			G	E			P	F		
S462 0000 0103	23	UNT T TRESTLE	FROZEN DOG COU	F	F	F	N	P	F	N	G	N	G	N	F	N	N	F	N	P	N	N	N	N	F		
S462 0000 0125	23	UNT T TRESTLE	DRAINAGE	P	P	P	N	P	P	N	G	N	G	N	P	N	N	N	N	F	P	N	N	N	P		
S462 0000 0192	225	PRE CONC BEAMS	LITTLE DRY CR	F	N	G	G	G	G	G	G	G	G	G	N	N	G	G	N	G	N	G	G	G	E		
S463 0000 0157	101	PRE CONC BEAM	ROTTEN GRASS CR	G		E			E		E	E		E			E	E		E		E		E	E		
S463 0000 0411	58	T T TRESTLE	BIG HORN CANAL	G	G	G			G		P		G		P					G	G	G		P	G		X
S464 0000 0046	173	PRE CONC BEAMS	CUT BANK CR	G		E	E	E	E	E	G	E	G	E			E	E		E	E	E		E	E		
S464 0000 0169	43	STEEL GIR	S FK MILK R	F		F			F		G		G	F	G					F				P	F		
S464 0000 0239	27	UNT T TRESTLE	DRY FK MILK R	F	P	P		P	P		G		P	F				P		F					P		X
S465 0000 0007	411	PRE CONC BEAMS	BIG DRY CR	P	N	G	G	G	G	N	G	G	G	G	N	N	G	G	N	G	N	G	G	G	E		

			FEET			E	F	C			J	K		M	N	O			R	S			V	W			Z	Z	ZZ
S466	0000	0002	75	PRE CONC BEAM	E FK SPRING CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G		G	G		
S466	0000	0014	32	UNTR T TRESTLE	SPRING CR	F	F	F		F	F		G		F		G					F	F	F		P	F		X
S467	0000	0005	193	PRE CONC BEAM	REDWATER R	G	N	E	E	E	E	G	G	G	G	G	N	N	E	E	N	G	N	E	E	G	E		
S467	0000	0010	38	T T TRESTLE	HELL CR	G	G	G	G	G	G	N	G	G	G	N	G	N	G	G	N	G	G	G	N	F	G		
S467	0000	0034	38	T T TRESTLE	MCCUNE CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	N	G	G	G	N	G	G		
S467	0000	0335	36	UNT T TRESTLE	UPPER 7 MILE CR	G	G	G	G	G	G	N	G	N	G	N	E	N	N	F	P	G	G	F	N	P	G		
S469	0000	0019	1159	STEEL GIRDER	MISSOURI R	G		G	G		G	G	G		G	G		G	G	G		F	G	G		F	G		
S470	0000	0130	79	UNT T TRESTLE	N FK DEER CR	G	P	F	F	G	G	N	G	N	G	N	P	N	N	P	P	P	P	N	N	P	P		
S470	0000	0235	25	TIMBER TRESTLE	DRAINAGE	F	F	F	N	F	F	N	G	N	G	N	P	N	N	P	P	P	P	P	N	P	P		
S471	0000	0112	48	UNT T TRESTLE	PROSPECT CR	F				F	F		G		F		F					F					F		
S473	0000	0063	56	CONT CONC GIR	TRAPPER CR	P		G	G	G			G	C	G	G				G		G		G			G		X
S473	0000	0143	170	ST PONY TRUSS	W FK BITTERROOT	G		G			G		G	P	G	G	G	G	G	F		G	G	F		P	G		
S474	0000	0011	180	STEEL GIRDER	NP RY																								

A	B FEET	C	D	END FILL E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	K	DRIFT L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
S476 0000 0008	360	RIV PL GIRDER	YELLOWSTONE R	F		G	F	G	G	P	F	G	G	G			F	G	P	F	G	F	F	F	G		
S476 0000 0039	33	T LAMINATED BM	MILL CR	G		G		G	G		P	F	G		F		G	P	P	F	G	G		P	F		
S476 0000 0065	43	T LAMINATED BM	MILL CR	F		G		G	G		F	F	G		F		F	P	P	F	G	C		P	F		X
S476 0000 0098	25	T T TRESTLE	E FK MILL CR	F	G	G		G	G		G	F	G		G		G	F	P	G	G	G		F	G		
S478 0000 0008	336	STEEL TRUSS	YELLOWSTONE R	F		P	P	P	F	P	G	F	G		P	F	P	P	P	P	F	P	P	P	P		
S478 0000 0080	50	LMA STRINGERS	SWEET GRASS CR	G	G	G		F	G		G	P	G		E		E	P	P	E	G	G		F	G		
S478 0000 0113	70	T & ST TRUSS	SWEET GRASS CR	G		G		G	G		G	P	G		F	F	F	P	P	F	F	F		P	F		
S478 0000 0122	30	T KING TRUSS	E FK SWT GRASS C	F	F	P		P	F		G	P	G		F	F	F	P	P	F	F	F		P	F		
S479 0000 0063	30	UNT T KING TRUS	TENMILE CR	G	F	F		G	G		G	P	G		F	F			P	F	F	P		P	F		
S479 0000 0159	93	STEEL TRUSS	SWEET GRASS CR	G		F		F	F		G	F	G		E	F	F			E	F	E		F	G		
S480 0000 0030	1056	CONT PL GIRDER	MISSOURI R	E		E	E		E	E	E	E	E	E			E	E		E	E	E	E	E	E		
S480 0000 0138	29	STEEL I BEAM	LONGGRASS CR	P	C	P		P	F		G		G		F			P		F					P		X
S481 0000 0000	285	PRE CONC BEAM	SEP I-15																							N	
S482 0000 0026	122	PRE CONC BEAMS	LIBBY CR	G		G	G	G	G	G	F	G	G	G			G	G	P	G	G	G	G	G			

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z
S483 0000 0030	52	STEEL I BEAM	ROCKY COULEE	F		G		F	F		G		P		F			F		P	F	P		P	F		
S483 0000 0278	150	T T TRESTLE	S FK MILK R	F	F	P		F	G	C	P	F	F		G			F		G	P	P		P	P		X
S484 0000 0034	102	PRE CONC BEAM	OTTER CR	G		E			E		G	G	G	E			E	E	G	E		E		G	E		
S484 0000 0236	90	STEEL TRUSS	OTTER CR	F	G	P			F		G		G		F	G	G		G	P	F	P		P	P		
S484 0000 0254	45	ST PONY TRUSS	OTTER CR	F	F	F					G		G		F	G	G	P		F	F	F		P	F		
S484 0000 0258	35	STEEL TRUSS	BEAR CR	F	G	F			F		G		G		G	G		F		P	F	F		P	F		
S486 0000 0043	22	UNT PILE TRES	CEDAR CR	G		G		G	G		G		G		G			F		F					G		
S486 0000 0068	22	UNT T TRESTLE	CEDAR CR	G		G		G	G		G		G		G			F		F					G		X
S486 0000 0208	95	ST PONY TRUSS	BIG CR	F		G		G	G		G		G		G	G	G	F		G	G	F	F	P	F		
S486 0000 0291	60	ST PONY TRUSS	COAL CR	G		P		F	F		G		G		G	P	P	F		F	F	F		P	F		X
S486 0000 0338	30	T T TRESTLE	MORAN CR	F		G		G	G		G		G		G			F		F	F	F		P	G		
S486 0000 0354	45	STEEL I BEAM	HAY CR	G		F		P	P		G		G		G			F		G		P		P	F		X
S486 0000 0410	43	STEEL GIRDER	RED MEADOW CR	F		G		G	G		G		G	G			G	F		F	F	F		F	G		
S486 0000 0448	75	ST PONY TRUSS	WHALE CR	G		F		F	F		G		F		G	F	F	F		F	F	P		P	F		X
S486 0000 0506	39	T T TRESTLE	TRAIL CR	G		G		G	G		G		G		G			G		G	G	G		F	G		
S486 0000 0574	22	T T TRESTLE	COLTS CR	G	G	G		G	G		G		G		G			F		F	G	F		P	G		

BRIDGE NUMBER	TOTAL LENGTH FEET	MATERIAL AND TYPE / MAXIMUM SPAN	NAME OF FEATURE	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	[illegible]	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	[illegible]	PAINT	GENERAL	[illegible]	[illegible]
A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S487 0000 0002	633	ST WARREN TRUSS	GN RY	G		G		G	F						G	G	G	F		G	G	F	P	F	G		X
S489 0000 0037	198	PRE CONC BEAM	SUNDAY CR	F		G	G		G	G	F	G	G	G			G	G	X	G	G	G	G	G	G		
S490 0000 0002	198	PRE CONC BEAMS	E FK BITTERROOT	G		E	E	E	E	E	G	G	G	E		E	E	E	G	E		E	E	E	E		
S490 0000 0007	173	PRE CONC BEAMS	W FK BITTERROOT	G		E	E	E	E	E	G	G	G	E		E	E	E	G	E		E	E	G	E		
S494 0000 0003	132	PRE CONC BEAM	SANDSTONE CR	G	N	E	E	E	E	N	G	G	G	E	N	N	G	E	P	G	N	G	N	G	E		
S494 0000 0011	132	PRE CONC BEAM	S FK SANDSTONE	G	N	E	E	E	E	N	G	G	G	E	N	N	G	E	P	G	N	G	N	G	E		
S495 0000 0040		UNDERPASS	GN RY	G		G		G	G			G		G			G			G		G			G		
S496 0000 0103	27	STEEL I BEAM	W FK SHOTGUN CR	P	P	P		P	P		G		G		F					F					P		X
S496 0000 0122	25	STEEL I BEAM	E FK SHOTGUN CR	F	G	G		G	G		G		G		G					G					G		
S496 0000 0140	26	STEEL I BEAM	DRAINAGE	G	G	G		G	G		G		G		G			P		F					G		
S496 0000 0172	22	CONCRETE BEAM	SHOTGUN CREEK	G	G	G		G	G		G		G					G		G					G		N
S498 0000 0001	100	STEEL GIRDER	GN RY	P		G		P	G					G				P		F		P		P	P		X

S500 0000 0123	28	UNT T TRESTLE	DRAINAGE	P	F	F		P	F		G		G		F					P	P				P		X
S500 0000 0300	132	PRE CONC BEAM	FLATWILLOW CR	G		G	G	G	G	G	P	G	G	G			G	G		G		G	G	G	G		
S502 0000 0001		UNDERPASS	BEETDUMP SEP-I90	G		E			E					E			E								E		
S502 0000 0002		UNDERPASS	BEETDUMP SEP-I90	G		E			E					E			E								E		
S502 0000 0004	24	STEEL I BEAM	BBWA CANAL	G		G		G	G		G		G		G			G		G		G		G	G		
S502 0000 0005	30	STEEL I BEAM	BBWA CANAL	G		G		G	F		G		P		G			G		G		P		P	G		X
S504 0000 0130	67	STEEL I BEAM	CABIN CR	G	N	P	P	N	P	N	F	N	F		F	N	N	P	P	F	N	P	N	P	P		
S505 0000 0064	163	PRE CONC BEAM	BIG SPRING CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G		G	G		
S505 0000 0123	75	ST PONY TRUSS	JUDITH R	G		F		F	F		G		G			F	P			F	F	F		G	F		X
S506 0000 0034	64	UNT T TRESTLE	PIPE CR	F	F	F		F	F		G	F	G		F					F	F	F			F		
S507 0000 0017		UNDERPASS	SEP-I90	E		E	E	E	E					E			E		E	E	E	E	E	P	E		
S507 0000 001B	457	WELDED PL GIRD	CLARK FORK	E		E	E	E	E	E	E	E	E	E		E	E	E		E	E	E	E	E	E		
S507 0000 00BB	34	T T TRESTLE	PETTY CR	G		G	G	G	G		G		G		G			G	F	G		G		P	G		

CONDI RA
SUBSTRUCTURE

A	B TOTAL LENGTH FEET	C MAX M M SPAN	D	E END F S	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STR N S	Q SS	R SHOES	S CURBS	T MARKERS	U DECK	V BRA	W RAIL	X EXPAN	Y PAINT	Z GENERAL	Z1 NOT INSP TE	Z2 REM
S508 0000 0121	22	CONC T TRES	FOURTH JULY CR	G		G		G	G		G		G		G			G		G	G	P		P	G		X
S508 0000 0188	36	CONC T TRES	MEADOW CR	G		G		G	G		G		G		G			G		G	G				G		
S508 0000 0191	35	CONC T TRES	HELLROARING CR	G		G		G	G		G		G		G			G		G	G				G		
S508 0000 0237	111	STEEL GIRDER	SPREAD CR	G		G		G	G		P		G		G		G	G		G	G	G		P	G		
S508 0000 0282	34	CONC T TRES	PETE CR	G		G		G	G		G		G		G			G		G	G				G		
S508 0000 0383	112	WARREN ST TRUSS	YAK RIVER	P		F		G	G		G		G		G	F	F	G		G	F	P		G	G		
S508 0000 0426	34	ST I BEAM	E FK YAK R	G		G		G	G		G		G	G				G		G				F	G		
S508 0000 0484	22	T T TRESTLE	CARIBOU CR	G	G	G		G	G		G		G		G			G		G	F	G		P	G		
S508 0000 0672	24	T T TRESTLE	SULLIVAN CR	G	G	G		G	G		G		G		G			G		G	G				G		X
S509 0000 0001		UNDERPASS	MONIDA INT I15	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
S510 0000 0050	119	UNT T TRESTLE	TUSLER CR	P	P	P	P	P	F	F	G	N	F	N	F	N	N	P	P	P	P	P	N	P	P		
S512 0000 0007	102	PRE CONC BEAM	FLINT CR	E		E	E	E	E	E	E	F	E	E			E	E		E	E			G	E		
S514 0000 0003	176	CONT STEEL GIR	POPLAR R	F		G	G	G	G	G	G		G	G			G	G		G	G	G	F	F	G		
S514 0000 0191	245	PRE CONC BEAM	POPLAR R	F		E	E		E	E	G	G	G	E			E	E	E	E		E	E	G	E		

	FEET			E	F	G	H	I	J	K		M	N	O			R	S	T			W			Z	Z1	
S515 0000 0088	92	PRE CONC BEAM	LAKE CR	G		G		E	E		G	G	G	E			G	E	G	E		G		G	G		
S518 0000 0000	297	PRE CONC BEAM	MONT CITY INT																							N	
S520 0000 0000S		UNDERPASS	CYR INT I90	E		E	E	E	E	E	E	E	E	E	E		E	E		E		E	E	E	E		
S520 0000 0001	516	CONT ST TRUSS	CLARK FORK	G		G	G		G		G	G	G	G	G	G	G	G	F	F	G	F	P	G			
S520 0000 0040	198	PRE CONC BEAM	FISH CR INT I 90	E		E	E	E	E						E		E	E	E	E		E	E	E	E		
S522 0000 0019	70	PRE CONC BEAM	HUNTLEY CANAL	E		E		E	E			E		E				E		E		E		E	E		
S522 0000 0021	92	PRE CONC BEAM	PRYOR CR.	E		E		E	E			E		E				E		E		E		E	E		
S522 0000 0023		UNDERPASS	HUNTLEY INT I-94	E		E			E					E										E	E		
S522 0000 0024		UNDERPASS	HUNTLEY INT I-94	E		E			E					E										E	E		
S523 0000 0007	25	T T TRESTLE	DRAINAGE	F	F	C		P	F		G		G		F			F		C		P			P		X
S526 0000 0002	190	PRE CONC BEAM	GALLATIN R	G		E	E	E	E	E	G	E	G	G			E	E	G	E	E	E		G	E		
S527 0000 0007	278	PRE CONC BEAM	MADISON R	E		E	E	E	E	G	G	E	E	E			E	E		G	E	E	E	E	E		

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S528 0000 0108	75	ST PONY TRUSS	SAND CR	G	G	G		G	G		G		G		G	G	G	G		G	G			P	G		
S528 0000 0191	230	UNT T TRESTLE	PRAIRIE ELK CR	F	P	P	P	G	G	P	F		G		P			G		G	P				P		X
S529 0000 0000	84	CONT CONC SLAB	RED ROCK CR	E	E	E			E		G	E	G					E	G	E		E		E	E		
S529 0000 0010	213	PRE CONC BEAM	MILK R	F		E	E		E	E	G	E	G		E			E		E		E		E	E		
S529 0000 0055	30	UNT T TRESTLE	DRAINAGE	F	P	P		P			G		G		F			P		P		F		P	P		X
S530 0000 0018	26	CONC & TIMBER	N CROW CR	G		G		G	G		G		G					P	P	G	G			P	G		
S531 0000 0035	48	UNT T TRESTLE	SAWTOOTH CR	G		F		G	P		G		G		F					P	F	F		P	F		
S531 0000 0054	300	PRE CONC BEAM	BITTERROOT R	E		E		E	E		E	E	E	E		E	E	E	E	E	E	E	E	E	E		
S532 0000 0009	35	STEEL&CONCRETE	BIG DITCH	E		E		E			E		E	E				E		E		E		E	E		
S532 0000 0078	152	PRE CONC BEAM	CANYON CR	E		E		E			E		E	E				E		E		E		E	E		
S533 0000 0100		UNDERPASS	SEP I 90	E		E	E	E	E					E			E			E		E		E	E		
S533 0000 0101		UNDERPASS	SEP I 90	E		E	E	E	E					E			E			E		E		E	E		
S534 0000 0078	24	T T TRESTLE	DRAINAGE	G	G	G		F	G		G		G		G					G	F	P		P	G		

S534	0000	0098	94	ST GIRDER	DRY FK MARIAS R	G		E	E	E	E	E	G		G	G				E		E	E	E		E	E		
S534	0000	0185	24	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			F		G	G	P		P	G		
S535	0000	0018	32	STEEL I BEAM	BBWA CANAL	F		G		C	G		G		G		G			F		G		C		P	F		
S537	0000	0023	272	ST HOWE TRUSS	MILK R	G	G	G		G	G		G		G	G	G	F	G	P	P	F	G	P		P	F		
S537	0000	0057	32	T TRESTLE	CASH CR	F	P	P		C	F		F		F		P					P	P	F		P	C		X
S540	0000	0068	57	T T TRESTLE	HAY WAGON PASS	F	F	F		F	F		G	G	G		G		F	F	G	F	F	F		F	F		
S540	0000	0078	31	STEEL I BEAM	SIX MILE CR	F		G		P	G		G	G	G		G		F	P	G	F	G	P		P	G		
S540	0000	0089	31	STEEL I BEAM	EMIGRANT CR	F		F		P	F		F	F	F		G		F	P	G	F	G	P		F	F		
S540	0000	0170	67	STEEL I BEAM	MILL CR	F		F	P	F	P	P	G	P	G		F		P	F	G	F	G	F		P	P		
S540	0000	0250	21	STEEL I BEAM	PINE CR	G		G		F	F		G	F	G		G		F	F	G	G	G	P		F	F		
S540	0000	0318	285	REIN CONC RIB	YELLOWSTONE R	F		F	P		P	P	F		F	F				G	G	F	P	G		F	F		
S543	0000	0027	48	UNTR TIMBER	VAIL CR	G	P	P		P	P		G		G		P					F	P				P		X
S544	0000	0003	107	ST HOWE TRUSS	POWDER R	P		F		F	F		G		G		P	G	G	P		F		P		P	P		X
S544	0000	0342	34	STEEL I BEAM	E FK SCOTT CR	F	F	C		P	P		G		G		G			P		P		P		P	C		X

MISSOULA CONSTRUCTION DIVISION

A	B	C	D	E	F		H	I	J	K		M	N	O			R	S	T	U	V	W			Z
I 90 0000 0024	42	STEEL GIRDER	ST REGIS R	G		G		G	G		G	G	G	G	G		G	G	F	G		G	G		G
I 90 0000 0068	23	STEEL I BEAM	RANDOLPH CR	G		G		G	G		G	G	G	G	G			G	F	G		P	G		G
I 90 0000 0082	100	CANT ST GIRDER	ST REGIS R	G		G	G		G		G	G	G	G			G	P	G	G		F		P	F
I 90 0000 0109	100	CANT ST GIRDER	ST REGIS R	G		G	G		G		G	F	G	G			G	P	P	G		G		P	G
I 90 0000 0224	42	CONCRETE T BEAM	TWELVE MILE CR	G		G		G	G		G	G	G	G				G	G	G	G	G		F	G
I 90 0000 0343	190	CONT ST GIRDER	ST REGIS R	G		G	G		N		G	P	G	G			G	P	F	G		F	F	F	F
I 90 0000 0346	787	STEEL TRUSS	CLARK FK & NP RY	G		G	G		G	G	G		G	G	G	G	G	G	G	G		G	P	P	G
I 90 0000 0391	482	ST PLATE GIRDER	CMSTP&P RR	G		G			G				G	G			G	G	G	G		F	F	P	G
I 90 0000 0456	621	RIV PL GIRDER	CLARK FK	G		G	G		G		G		G	G	G		G	G	G	G	G	G	G	F	E
I 90 0000 0466	17	CONCRETE SLAB	JR GR SEP-CO RD	G		G		G	G									G		G		G		G	E
I 90 0000 0479	153	PRE CONC BEAM	SUPERIOR INT	G		G		G	G					G			E	E	G	E	E	E	G	P	E
I 90 0000 0479P	153	PRE CONC BEAM	SUPERIOR INT	G		G		G	G					G			E	E	G	E	E	E	G	P	E
I 90 0000 0495	168	PRE CONC BEAM	CEDAR CR	G		E		E	E		E	E	E	E			E	E		E	E	E	E	G	E
I 90 0000 0495P	168	PRE CONC BEAM	CEDAR CR	G		E		E	E		E	E	E	E			E		E	E	E	E	E	G	E
I 90 0000 0498	801	WELDED PL GIR	CLARK FK	G		E	E	E	E	E	E	E	E	E	E		E	E	E	E	E	E	G	F	E
I 90 0000 0498P	801	RIV PL GIRDER	CLARK FK	G		E	E	E	E	E	E	P	E	E	E		E	E	E	E	E	E	E	G	E
I 90 0000 0542	757	WELDED PL GIR	CLARK FORK	G		E	E	E	E	E	E	E	E	E	E		E	E	E	E	E	E	E	E	E
I 90 0000 0542P	757	WELDED PL GIR	CLARK FORK	G		E	E	E	E	E	E	E	E	E	E		E	E	E	E	E	E	E	E	E
I 90 0000 0545		UNDERPASS	NP RY	E		E	E	E	E						E		E	E	P	E	E	E		E	E

A	TOTAL LENGTH FEET B	MAX SPAN C	D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	Q	R	CURBS S	T	U	V	W	X	Y	Z	Z1	Z2
I 90 0000 0545A		UNDERPASS	NP RY	E		E	E	E	E						E		E	E	P	E	E	E		E	E		
I 90 0000 0559	128	PRE CONC BM	LOZEAU INT-CO RD	G		E		E						E			E	E		E		E	E	G	E		
I 90 0000 0559P	128	PRE CONC BM	LOZEAU INT-CO RD	G		E		E						E			E	E		E		E	E	G	E		
I 90 0000 0579	296	PRE CONC BM	NP RY	F		E	E	E	E					E			E	E		E		E	E	G	E		
I 90 0000 0579P	296	PRE CONC BM	NP RY	F		E	E	E	E					E			E	E		E		E	E	G	E		
I 90 0000 0590	826	WELDED PL GIR	CLARK FORK	E		E	E	E	E	E	E	E	E		E		E	E	E	E	E	E	E	E	E		
I 90 0000 0590P	826	WELDED PL GIR	CLARK FORK	E		E	E	E	E	E	E	E	E		E		E	E	E	E	E	E	E	E	E		
I 90 0000 0592		UNDERPASS	CMSTP&P RR	E		E	E	E	E						E		E		P	E	E		G	E	E		
I 90 0000 0592A		UNDERPASS	CMST P&P RR	E		E	E	E	E						E		E		P	E	E		G	E	E		
I 90 0000 0603	17	CONCRETE SLAB	JRGR SEP-CO RD	E		E		E	F									E		E		E		G	E		
I 90 0000 0603S	17	CONCRETE SLAB	JR GR SEP-CO RD	E		E		E	F									E		E		E		P	E		
I 90 0000 0620	128	PRE CONC BEAM	TARKIO INT-CO RD	E		E		E	E						E		E	E	E	E		E	G	P	E		
I 90 0000 0620P	128	PRE CONC BEAM	TARKIO INT-CO RD	E		E		E	E						E		E	E	E	E		E	G	P	E		
I 90 0000 0663	445	STEEL GIRDER	CMST P&P RR-CO R	E		E		E	E						E		E	E		E		E	G	F	E		
I 90 0000 0669	807	WELDED PL GIR	CLARK FORK	E		E	E	E	E	E	E	E	E	E	E		E	E		E		E	E	G	E		
I 90 0000 0671	338	STEEL GIRDER	NP RY	E		E	E	E	E					E	E		E	E		E		E	E	G	E		
I 90 0000 0675		UNDERPASS	FISH INT-OR 520	E		E	E	E	E						E		E	E	E	E		E	E	E	E		
I 90 0000 0708	190	PRE CONC BEAM	NP RY	F		E	E	E	E						E		E	E		E		E	E	E	E		X
I 90 0000 0710	762	CONT PL GIRDER	CYR INT & CLARK	E		E	E	E	E	E	E	E	E	E	E		E	E		E		E	E	E	E		

	FEET		D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
I 90 0000 0760		UNDERPASS	ALBERTON INT	E		E	E	E	E					E			E	E		E		E	E	E	E
I 90 0000 0760A		UNDERPASS	ALBERTON INT	E		E	E	E	E					E			E	E		E		E	E	E	E
I 90 0000 0784	128	PRE CONC BEAM	SEP-OR507	E		E	E	E	E					E			E		E	E	E	E	E	P	E
I 90 0000 0802	17	CONCRETE SLAB	JR GR SEP-CO RD	E		E		F	E									E		E		E		F	E
I 90 0000 0812	879	WELDED PL GIR	CLARK FORK	E		E	E	E	E	E	E	E	E	E	E		E	E	G	E	E	E	G	G	E
I 90 0000 0827	982	WELDED PL GIR	CLARK FK & RR	E		E	E	E	E	E	E	E	E	E	E		E	E	G	E	E	E	E	G	E
I 90 0000 0827	982	WELDED PL GIR	CLARK FK & RR	E		E	E	E	E	E	E	E	E	E	E		E	E	G	E	E	E	E	G	E
I 90 0000 0835	123	PRE CONC BEAM	9 MILE INT-CO RD	E		E	E	E	E						E		E	E		E		E		F	E
I 90 0000 0835P	123	PRE CONC BEAM	9 MILE INT-CO RD	E		E	E	E	E						E		E	E		E		E		F	E
I 90 0000 0970		UNDERPASS*	DESMET INT-10A	E		E	E	E	E						E		E	E	E	E		E	E	E	E
I 90 0000 0970A		UNDERPASS*	DESMET INT-10A	E		E	E	E	E						E		E	E	E	E		E	E	E	E
I 90 0970 0987	163	PRE CONC BEAM	NPRY	E		E	E	E	E						E		E	E		E		E		E	E
I 90 0970 0987P	163	PRE CONC BEAM	NPRY	E		E	E	E	E						E		E	E		E		E		E	E
I 90 0970 0991	138	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E						E		E	E		E		E		E	E
I 90 0970 0991P	138	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E						E		E	E		E		E		E	E
I 90 0970 1023	195	PRE CONC BEAM	RESERVE ST-INT	E		E	E	E	E			E	E		E		E	E		E		E		E	E
I 90 0970 1023P	195	PRE CONC BEAM	RESERVE ST-INT	E		E	E	E	E			E	E		E		E	E		E		E		E	E
I 90 0970 1037	138	PRE CONC BEAM	SEP-CO RD	G		E	E	E	E					E			E	E		E		E		G	E
I 90 0970 1037P	138	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E			E	E		E		E		G	E

A	TOTAL LENGTH FEET B	C	D	END E	PILES F	BENTS G	PIERS H	WINGWA I	J	ICE BREAKERS K	L	RIP RAP M	SCOUR N	GIRDER O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I 90 0970 1054	179	PRE CONC BEAM	ORANGE ST INT	E		E	E	E	E					E			E	E		E		E		E	E		
I 90 0970 1054T	179	PRE CONC BEAM	ORANGE ST INT	E		E	E	E	E					E			E	E		E		E		E	E		
I 90 1054 1061	245	PRE CONC BEAM	RATTLESNAKE CR	E		E	E	E	E		E	E	E	E			E	E		E		E	E	E	E		
I 90 1054 1061T	245	PRE CONC BEAM	RATTLESNAKE CR	E		E	E	E	E		E	E	E	E			E	E		E		E	E	E	E		
I 90 1054 1063	165	PRE CONC BEAM	VAN BUREN ST INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I 90 1054 1063T	165	PRE CONC BEAM	VAN BUREN ST INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I 90 1054 1079	194	PRE CONC BEAM	E MISSOULA INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I 90 1054 1079T	194	PRE CONC BEAM	E MISSOULA INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
I 90 1079 1089	455	ST PLATE GIRDER	CLARK FORK	E		E	E	E	E	G	E	E	E	E			E	E		E	E	E	G	E	E		
I 90 1079 1089P	455	ST PLATE GIRDER	CLARK FORK	E		E	E	E	E	E	E	E	E	E			E	E		E	E	E	E	E	E		
I 90 1079 1099	143	PRE CONC BEAM	SEP-OR 533	E		E	E	E	E					E			E			E		E		E	E		
I 90 1079 1099P	143	PRE CONC BEAM	SEP-OR 533	E		E	E	E	E					E			E			E		E		E	E		
I 90 1079 1100	409	ST PLATE GIRDER	CLARK FORK-SEP	G		E	E	E	E	E	E	G	E	E			E	E		E	E	E	E	E	E		
I 90 1079 1100P	399	ST PLATE GIRDER	CLARK FORK-SEP	G		E	E	E	E	E	E	G	E	E			E	E		E	E	E	G		E		
I 90 1079 1108		UNDERPASS	BONNER INT-APPR	E		E	E	E	E					E			E	E		E		E	E	E	E		
I 90 1079 1108A		UNDERPASS	BONNER INT-APPR	E		E	E	E	E					E			E	E		E		E	E	E	E		
I 90 1079 1111	342	STEEL GIRDER	NP RY	E		E	E	E	E					E			E	E		E		E	E	F	E		
I 90 1079 1111P	342	STEEL GIRDER	NP RY	E		E	E	E	E					E			E	E		E		E	P	F	E		
I 90 1079 1113	343	WELDED PL GIR	BLACKFOOT R	E		E	E	E	E	E	E	E	E	E			E	E		G	E	E	E	G	E		

I	90	1079	1113P	343	WELDED PL GIR	BLACKFOOT R	E		E	E	E	E	E	E	E	E	E	E	E		G	E	E	E	G	E
I	90	1079	1120	153	PRE CONC BEAM	CMSTP&P RR	E		E	E	E	E					E		E		G		E		E	E
I	90	1079	1120P	153	PRE CONC BEAM	CMSTP&P RR	E		E	E	E	E					E		E		G		E		E	E
I	90	1079	1127	118	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E		E		E		E		G	E
I	90	1079	1127P	118	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E		E		E		E		G	E
I	90	1079	1150	118	PRE CONC BEAM	TURAH INT	E		E	E	E	E					E		E		E		E		G	E
I	90	1079	1150P	118	PRE CONC BEAM	TURAH INT-US 10	E		E	E	E	E					E		E		E		E		G	E
I	90	1150	1181	128	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E		E		E		E		G	E
I	90	1150	1181P	128	PRE CONC BEAM	SEP-CO RD	E		E	E	E	E					E		E		E		E		G	E
I	90	1150	1197	351	STEEL GIRDER	NP RY	E	E	E	E	E	E					E		E		E		E		E	E
I	90	1150	1197P	355	STEEL GIRDER	NP RY	E		E	E	E	E					E		E		E		E		E	E
I	90	1150	1555	123	PRE CONC BEAM	W DRUMMOND INT	E		E	E	E	E					E		E	E	G	E	E	E	G	G
I	90	1150	1555T	123	PRE CONC BEAM	W DRUMMOND INT	E		E	E	E	E					E		E	E	G	E	E		G	G
I	90	1555	1559	128	PRE CONC BEAM	MAIN ST SEP	E		E	E	E	E				E	E	E	E	E	E	E	E		G	E
I	90	1555	1559T	128	PRE CONC BEAM	MAIN ST SEP	E		E	E	E	E				E	E	E	E	E	E	E	E		G	E
I	90	1555	1564	133	PRE CONC BEAM	E DRUMMOND INT	F		E	E	G	E				E	E	E	E	E	E	E	E		G	E
I	90	1555	1564P	133	PRE CONC BEAM	E DRUMMOND INT	F		E	E	G	E				E	E	E	E	E	E	E	E		G	E
I	90	1564	1579	128	PRE CONC BEAM	SEP-OR 271	F		E	E	G	E								E	E	E	E		G	E
I	90	1564	1579P	128	PRE CONC BEAM	SEP-OR 271	F		E	E	G	E								E	E	E	E		G	E

A	B TOTAL LENGTH FEET	C	D	E END FILLS	F PILES	G BENTS	H PIERS	I WINGWALLS	J	K ICE BREAKERS	L	M RIP RAP	N	O GIRDERS	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I 90 1564 1591	17	CONCRETE SLAB	JR GR SEP-CO RO	E		E	E	E	E									E		E	E	E		G	E		
I 90 1564 1591P	17	CONCRETE SLAB	JR GR SEP-CO RO	E		E	E	E	E									E		E	E	E		G	E		
I 90 1564 1609	17	CONCRETE SLAB	JR GR SEP-CO RO	E		E	E	E	E									E		E	E	E		G	E		
I 90 1564 1609P	17	CONCRETE SLAB	JR GR SEP-CO RD	E		E	E	E	E									E		E	E	E		G	E		
I 90 1564 1625	17	CONCRETE SLAB	JR GR SEP-CO RO	G		E		E	G									E		E		E		G	E		
I 90 1564 1625P	17	CONCRETE SLAB	JR GR SEP-CO RO	G		E		E	G									E		E		E		G	E		
I 90 1564 1631	17	CONCRETE SLAB	JR GR SEP-CO RO	G		E		E										E		E		E		G	E		
I 90 1564 1631P	17	CONCRETE SLAB	JR GR SEP-CO RO	G		E		E										E		E		E		G	E		
I 90 1564 1639	113	PRE CONC BEAM	JENS INT-CO RO	G		E		E	E					E			E	E		E		E	G	G	E		
I 90 1564 1639P	113	PRE CONC BEAM	JENS INT-CO RO	G		E		E	E					E			E	E		E		E	G	G	E		
I 90 1564 1671	17	CONCRETE SLAB	JR GR SEP	G		E		E										E		E		E		G	E		
I 90 1564 1671P	17	CONCRETE SLAB	JR GR SEP	G		E		E										E		E		E		G	E		
I 90 1564 1679	153	PRE CONC BEAM	GOLO C INT-OR460	G		E		E	E					E			E	E	G	E		E	G	G	E		
I 90 1564 1679P	153	PRE CONC BEAM	GOLO C INT-OR460	G		E		E	E					E			E	E	G	E		E	G	G	E		

P	2	0970	0970	321	PRE CONC BEAM	OE SMET INT	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	2	0970	0977		UNDERPASS	NP RY	G	F	F		F	F					G	G		G			G	F			P	F		
P	2	0970	1026		UNOERPASS	INT OR 430																							N	
P	2	1060	1061	65	PRE CONC BEAM	RATTLESNAKE CR	G	G			G	G		G	G	G	G		G	G			G	G	G		G	G		
P	2	1060	1079		UNDERPASS	NP RY																								
P	2	1060	1081		UNDERPASS*	E MISSOULA INT	E		E	E	E	E					E			E	E		E		E	E	E	E		
P	2	1081	1126	354	CONT ST GIROER	BIG BLACKFOOT R	G		G	G	G	G		G		G	G			G	G	F	G	G	G	G	F	G		
P	2	1126	1139	88	CONCRETE T BEAM	CMSTP&P RR																								
P	2	1126	1161		UNOERPASS*	TURAH INT-I 90	E		E	E	E	E					E			E	E	E	E		E	E	G	E		
P	2	1126	1162		UNOERPASS*	TURAH INT-I 90	E		E	E	E	E					E			E	E	E	E		E	E	G	E		
P	2	1574	1574S		UNDERPASS*	W DRUMMOND INT	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	2	1575	1587S		UNOERPASS*	E DRUMMOND INT	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	2	1575	1588S		UNOERPASS*	E DRUMMOND INT	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	5	0000	0000	321	PRE CONC BEAM	DE SMET INT I90	E		E	E	E	E					E			E	E	E	E		E	E	E	E		
P	5	0000	0096	173	PRE CONC BEAM	NP RY	G		G	E	E	E					E			E	E	F	E		G		C	G		
P	5	0000	0189	104	CONCRETE T BEAM	JOCKO R	F		G			G		G		G	F				G	G	F		G		F	G		X
P	6	0000	0109	162	STEEL GIRDER	BULL R	E		E			E	E	E	E	E	E			E	E	G	E	E	E	E	P	E		

[illegible] CONDI[illegible] REPORT

	NUMBER CONTROL UNIT ON MILE	TOTAL LENGTH FEET	DESCRIPTIVE FEATURES MATERIAL & TYPE MAXIMUM SPAN All structures not carrying [illegible] by type of facility, Underpass, Tunnel, Ferry	NAME OF FEATURE CROSSED River, Creek, [illegible] Irrigation, Drainage, Railroad, Highway, Interchanges and Separation, Etc.	END FILLS	P[illegible]	BENTS	PIERS	WINGWALLS	BACKW[illegible]	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TR[illegible]	SHOES	CURBS	MARKER	DECK	BR[illegible]	RAILING	E[illegible]	PAINT	GENERAL	[illegible]	[illegible]
	A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	6 0000 0127	346	STEEL GIRDER	NPRY	E		E		E	E					E			E	E		E	E	E	E	P	E		
P	6 0000 0170	315	CONT D PL GIR	NP RY	E		E	E	E	E					E			E	E	C	E	E	E	E	P	E		
P	6 0000 0281	1061	CONT D PL GIR	CLARK FORK	G		E	E	E	E	E	E		E	E	E	E	E	E		E	E	E	E	P	E		
P	6 0000 0313		UNDERPASS	NP RY	G		G	G		G					E			E		G	G		E		P	E		
P	6 0000 0335	230	STEEL BEAM	BEAVER CR	F		G	G	F	G		G		G	G			G	C	G	F		P		G	F		X
P	6 0000 0492	949	RIV PL GIRDER	CLARK FORK	G		E	E		E	E	E		E	E	E		E	E	G	F		E	F	P	E		
P	6 0000 0533	156	STEEL GIRDER	NP RY	G	G	F	G	F	G						F			P	G	F	G	F	F	P	F		
P	6 0000 0562	427	STEEL TRUSS	THOMPSON R	G		G	G	G	G				G	G	G	G	G	F	G	G	G	F	G	P	G		
P	6 0000 0730	83	CONCRETE T BEAM	LYNCH CR	G		G	G	F	G	G	G	G	G	G					F	F		P			F		
P	6 0766 0767	51	CONCRETE T BEAM	BOYER CR	G		G	G	F	G		G	G	G	G				G	G	G		G			G		
P	6 0766 0827	970	STEEL TRUSS	CLARK FORK	G		G	G		G	G	G	P	G	G	G	G	G	G	F	G	G	F	F	C	F		X
P	6 0766 0848	455	STEEL TRUSS	CLARK FORK	F		E	E	G	E	E	E	P	E		E	E	E	E	G	G	E	E	E	G	E		
P	6 0766 0923	31	STEEL I BEAM	SEEPAY CR	G		G		G	G		G		F	G	G			E	G		E		G		G		
P	6 0766 1012	39	STEEL I BEAM	MAGPIE CR	G		G		G	G		G		F	G				E	G	G		E		G	E		
P	6 0766 1059	19	CONCRETE SLAB	REVALS CR	G		P		F	P		G	G	G	G				G	G	G	G		F	F			X
P	7 0001 0106	7	TT TRESTLE	ANDREWS CR STK	G		G		F	G		G		G						C	G		F		C	G		
P	7 0001 0129	140	STEEL BEAM	E FK BITTERROOT	G		G	G		G		G		G		G		G	G	F	G	G	G	G	C	G		
P	7 0001 0155	130	CONT STEEL BEAM	E FK BITTERROOT	G		G	G		G		G		G		G		G	F	F	F	G	G	G	P	G		

	A		C		E	F	G	H		J	K	L	M	N	O	P	Q	R	S				W		Z		
P	7 0001 0181	130	CONT ST GIRDER	E FK BITTERROOT	G		G	G		G		G		G		G		G	P	F	G	G	G	G	C	G	
P	7 0001 0259	76	T T TRESTLE	RYE CR	G	G	G	G		G		G	F	F		G			G	F	P		F		C	F		X
P	7 0001 0264	182	PONY TRUSS	BITTERROOT R	G		G	F	G	G	F	G		G		G	G	G	G	F	G	G	P	G	C	G	
P	7 0001 0270	19	T T TRESTLE	DRAINAGE	G	G	G			G						G			F	F	G		P		C	G	
P	7 0001 0292	209	T T TRESTLE	FERN CR	G	G	G	G		G		G	F	G		G			F	P	G		F		C	G	
P	7 0001 0298	57	T T TRESTLE	TINCUP CR	F	G	G	G		G		G	P	G		G			P	P	F		F		C	F	
P	7 0001 0337	19	T T TRESTLE	DRAINAGE	G	G	G			G			F	G		G			F	P	G		P		C	G	
P	7 0001 0349	95	CONCRETE T BEAM	ROCK CR	P		G	G		G		F		F	G			G	G	F	G		G	F		G	
P	7 0001 0369	76	T T TRESTLE	LICK CR	G	G	G	G		G		G	G	G		G			F	F	G	G	F		C	G	
P	7 0001 0377	137	CONCRETE T BEAM	LOST HORSE CR	F		G	G	G	G		G	P	F		G		G	G	F	G		G	G		G	
P	7 0001 0388	19	T T TRESTLE	DRAINAGE	G	G				G		G		G		G			F	P	G		F		C	G	
P	7 0001 0399	38	T T TRESTLE	CAMAS CR	G	G	G	G		G		G	G	G		G			G	P	G		F		C	F	
P	7 0001 0418	100	T T TRESTLE	GOLD CR	P	G	G	G		P			P	G		G			F	F	G	G	C		G	P	
P	7 0001 0436	300	STEEL GIRDER	BITTERROOT R	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G		G	
P	7 0445 0450	57	T T TRESTLE	SKALKAHO CR	F	G	G	G		P	G	F	P	F		G			F	G	G		F		F	F	
P	7 0445 0486	36	CONCRETE T BEAM	CORVALLIS CR	G		G			G		G		G	G				G	G	G		G			G	
P	7 0445 0495	392	CONT ST TRUSS	BITTERROOT R	G		G	G		G	G	G	G	G		G	G	G	G	G	G	G	G	G	G	P	G
P	7 0445 0499	25	T T TRESTLE	IRRIGATION CA	G	G	G			G		G	G	G		G			G	F	G		G		P	G	
P	7 0445 0503	49	T T TRESTLE	BLOODGETT CR	G	G	G	G		G		F	G	G		G			F	F	F		G		P	G	

F A SYSTEM	F A ROUTE	NUMBER CONTROL-JUNCTION MILE	BRIDGE MILE TO TENTH	TOTAL LENGTH FEET B	MATERIAL & TYPE MAXIMUM SPAN Also structures not carrying road by type of facility Underpass, Tunnel, Ferry C	NAME OF FEATURE CROSSED (River, Creek, Canal, Irrigation or Ditch, Drainage, Railroad, Highways, Interchange Separations) D	END FILL E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILING W	EXPANSION JT. X	PAINT Y	GENERAL Z	NOT INSPECTED Z1	REMARKS Z2
P	7	0445	0504	11	T T TRESTLE	STOCKPASS	G	G	G			G						G			G	F	F		G		P	G		
P	7	0445	0508	25	T T TRESTLE	MILL CR	G	G	G			G		G	G	G		G			G	F	F		G		P	G		
P	7	0445	0545	88	T T TRESTLE	SHEAFMAN CR	G	G	G	G		G		G	G	G		G			G	G	F		G		P	G		
P	7	0445	0570	100	T T TRESTLE	S FK BEAR CR	G	G	G	G		G		F	F	G		G			G	G	G	G	G		P	G		
P	7	0445	0583	38	T T TRESTLE	N FK BEAR CR	G	G	G	G		G		P	G	G		G			G	G	G	G	G		P	G		
P	7	0445	0597	81	T T TRESTLE	SWEATHOUSE CR	G	G	G	G		F		G	F	G		G			G	G	G	G	G		P	G		
P	7	0445	0616	114	T T TRESTLE	BIG CR	G	G	G	G		F		G	F	G		G			G	G	G		G		P	G		
P	7	0445	0650	38	T T TRESTLE	MCCALLA CR	G	G	G	G		G		G	G	G		G			G	G	G		G		P	G		
P	7	0445	0660	57	T T TRESTLE	MCCALLA CR	G	G	G	G		G		G	G	G		G			G	G	G		G		P	G		
P	7	0445	0662	75	T T TRESTLE	KOOTENAI CR	E	G	G	G		G		G	G			G			G	G	G	G	G		P	G		
P	7	0445	0829	122	PRE CONC BEAM	LOLO CR																								X
P	7	0835	0903	346	PRE CONC BM	BITTERROOT R																							N	
P	7	0835	0903P	346	PRE CONC BM	BITTERROOT R																							N	
P	7	0940	0942	972	RIV PL GIRDER	CLARK FORK & RR	G		E	E	E	E	E	G	E	G	E	E		E	E		E	E	G	E	G	E		
P	7	0940	0942T	972	RIV PL GIRDER	CLARK FORK & RR	G		E	E	E	E	E	G	E	G	E	E		E	E		E	E	G	E	G	E		
P	7	0946	0958	209	CONCRETE T BEAM	CMSTP&P RR	F		G	G		G					G			G	F		P		G	G	F	F		
P	7	0946	0959	503	DECK TRUSS	CLARK FORK	F		G	G		G	G	G	G	G		G	G	G	G		F	G	G	G	F	G		
P	7	0960	0965		UNDERPASS	NP RY	G		G		G	G					F			G	G		G	G	G	G	F	G		X
P	7	0960	0968		UNDERPASS	ORANGE ST INT-90	E		E		E	E					E			E	E		E	E	E		E	E		

				FEET B	C	D	E	F		H		J	K		M	N	O	P		R	S									
P	7	0965	0971	552	ST PLATE GIRDER	CLARK FORK & RR	G		G	G	G	G	G	G	G	G	G	G		G	G		G	G	G	G	G	G		
P	19	0316	0353	63	CONCRETE T BEAM	FRED BURR CR	G	G		G		G		G	F	G	G				G	F	G	G	G			G		
P	19	0316	0490	71	CONCRETE T BEAM	BOULDER CR	F	F		P		G		F	P	F	G				F	G	G	G	F	G		F		X
P	19	0316	0533	114	CONCRETE T BEAM	FLINT CR	G			F		F		G	F	G	G			G	G	G	G	G	G	G		G		X
P	19	0316	0597	39	STEEL I BEAM	WILLOW CR	G		G		G	G		G		G	G				G	G	G	G	F		F	G		
P	19	0316	0631	301	PRE CONC BEAM	CLARK FORK	E		E	E	E	E	E	G	G	G	E			E	E	G	E	E	E	E	G	E		
P	19	0316	0633	163	PRE CONC BEAM	CMSTP& P RR	G		E	E	F	E					E		E		E	G	E	E	E	E	G	E		
P	19	0316	0637	188	PRE CONC BEAM	NP RR	G		E	E	F	E					E		E	E		G	E	E	E	E	G	E		
P	24	0000	0055	361	CONT ST GIRDER	BLACKFOOT R	G		G	G	G	G	G	G	E	E	E			E	E	G	G		E	E	G	E		
P	24	0000	0090	75	T T TRESTLE	WEST TWIN CR	G		G	G		G		G		G		G			F	F	G		C		C	F		
P	24	0000	0093	75	T T TRESTLE	EAST TWIN CR	G		G	G		G		G		G		G			F	F	G		C		C	F		
P	24	0000	0112	446	CONT D ST TRUSS	BLACKFOOT R	G		G	G		G	G	G		F		G	G	G		F	P	G	F	G	C	G		
P	24	0000	0229	11	T T TRESTLE	STOCKPASS	G	G	G			G						G			C	G	G		C		C	F		
P	24	0000	0245	11	T T TRESTLE	STOCKPASS	G	G	G			G						G			C	G	G		C		C	F		
P	24	0000	0253	55	T T TRESTLE	ELK CR	G	G	G	G		G		G	F	G		G			P	G	G	F	P		C	G		
P	24	0000	0267	244	PLATE GIRDER	BIG BLACKFOOT R	G		G	G	G	G	G	G	G	G		G	G		G	F	G	F	G	C	G	G		
P	24	0000	0271	11	T T TRESTLE	STOCKPASS	E	E	E		E	E						E			F	E	G		G		G	E		

DESCRIPTIVE FEATURES

CONDITION RATING

BRIDGE NUMBER	TOTAL LENGTH FEET	MATERIAL & TYPE	NAME OF FEATURE	END FILL	PILES	BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TRUSS	R SHOES	S CURBS	T MARKERS	U DECK	V BRACING	W RAILING	X PAINT	Y	Z	Z1	Z2
P 24 0000 0280	11	T T TRESTLE	STOCKPASS	E	E	E		E	E						E			F	E	G		G		G	E		
P 24 0000 0302	11	T T TRESTLE	STOCKPASS	E	E	E		E	E						E			F	E	F		F		P	G		
P 24 0000 0313	113	CONT STEEL BEAM	CLEARWATER R	G		G	G		G	E	E	E	E	E			E	G	G	G		G	F	G	G		
P 24 0000 0314	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			F	G	G		G		G	G		
P 24 0000 0415	100	T T TRESTLE	MONTURE CR	G	G	G	G		G	E	F	F	G		G			F	G	F	F	G		C	G		
P 24 0000 0496	182	CONT CONC T BM	N FK BLACKFOOT R	G		E	E		E	E	E	E		E			E	E	E	G		G		P	E		
P 24 0000 0579	57	T T TRESTLE	ARRASTRA CR	G	G	G	G	G	G		P		G		G			F	G	G		G		G	G		
P 35 0000 0010	25	T T TRESTLE	REPUBLICAN DT	G	G	G		G	G		G		G		G			G		F	G	G		P	G		
P 35 0000 0017	25	T T TRESTLE	HEDGES CANAL	F	G	G		G	G		G		G		G			G		F	G	G		P	G		
P 35 0000 0029	76	T T TRESTLE	SKALKAHO CR	G	G	G		G	G	G	F		G		G			G		F	G	G		P	G		
P 35 0000 0036	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G		P	G	G		F	G		
P 35 0000 0043	19	T T TRESTLE	WARD CANAL	G	G	G		G	G		G		G		G			G		G	G	G		P	G		
P 35 0000 0046	50	T T TRESTLE	BRI CANAL	G	G	G		F	F	G	G		G		G			G		P	G	G		P	G		
P 35 0000 0052	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G												
P 35 0000 0364	45	ST PONY TRUSS	W FK ROCK CR	G		F		P	P		G		G	F	F	F	F	F		F	F	F		C	F		
P 35 0000 0397	45	ST PONY TRUSS	W FK ROCK CR	P		P		C	C				P		G	G	F	P		P	F	F		C	P		
P 35 0000 0423	140	CONCRETE T BEAM	ROCK CR	G		G	P		G		G	G	G	G	G		G	P	F	G	G	F	G		F		

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Column ... 7
P = Poor
... be Removed
... Unable to Inspect

CONTROL BRIDGE NUMBER (A)	TOTAL LENGTH FEET (B)	MAIN FRAME TYPE MAXIMUM SPAN (C)	NAME OF FEATURE (D)	FND FILLS (E)	PILES (F)	BENTS (G)	PIERS (H)	WINGWALLS (I)	BACKWALLS (J)	ICE BREAKERS (K)	DRIFT (L)	RIP RAP (M)	SCOUR (N)	GIRDERS (O)	STRINGERS (P)	TR (Q)	SHOES (R)	CURBS (S)	MA (T)	DECK (U)	BRAC (V)	RAILING (W)	(X)	PAINT (Y)	GENERAL CONDITION (Z)	NEXT INSP (Z)	REMARKS (Z)
P 46 0000 0041	19	REINF CONC SLAB	JOSEPH CR	G	E	G		G	G									G		G		G			G		
P 46 0000 0049	19	REINF CONC SLAB	JOSEPH CR	G	G	G		G	G									G		G		G			G		
P 46 0000 0070	19	REINF CONC SLAB	JOSEPH CR	G	G	G		G	G									G		G		G			G		
P 46 0000 0075	38	REINF CONC SLAB	TRAIL CR	G	G	G		G	G									G		G		G			G		

A	B	C	D	E	F PILES	G BENTS	H PIERS	I WINGWALLS	J	K ICE BREAKERS	L	M RIP RAP	N SCOUR	O GIRDERS	P	Q	R SHOES	S CURBS	T	U	V	W	X	Y	Z	Z1	Z2
M209 0000 0122	75	T T TRESTLE	MORRELL CR	G	G	G	G	G	G		G		G		G			G	G	G		G		G	G		
M412 0000 0247	84	T T TRESTLE	LOLO CR	G	G	G	G	G	G		G		G		G			G	G	G	G	G		G	G		
M412 0000 0250	63	T T TRESTLE	LOLO CR	G	G	G	G	G	G		G		G		G			G	F	G		G		G	G		
M412 0000 0265	28	T T TRESTLE	LOLO CR	G	G	G		G	G		G		G		G			G	F	G		G		G	G		
M412 0000 0267	28	T T TRESTLE	LOLO CR	G	G	G		G	G		G		G		G			G	F	G		G		G	G		

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	ZZ
S202 0000 0218	79	CONCRETE SLAB	BULL R	G		G	G	G	G		G	F	G					G		G		G			G		
S202 0000 0264	83	T T TRESTLE	BULL R	P	G	G	G	G	G		P		F		G			G		G	G	G		C	G		
S203 0000 0052	374	CONCRETE T BEAM	BITTERROOT R	G		E	E	E	E	E	F	G	G	E			E	G		E	E	G	G	F	E		
S203 0000 0055	38	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	F	G		G		G			G		G		G		G	G		
S257 0000 0001		UNDERPASS	CMSTP&P RR	G	F	F		G	G					G	G		G			G	F	P		P	F		
S257 0000 0002	459	ST PRATT TRUSS	CLARK FORK	G		G	F	G	G	G	G		G		F	G	G	F		F	F	F	F	P	F		
S257 0000 0003		UNDERPASS	SUPERIOR INT I90	G		E		E	E					E			E	E	G	E		E	E	G	E		
S257 0000 0004		UNDERPASS	SUPERIOR INT I90	G		E		E	E					E			E	E	G	E		E	E	G	E		
S257 0000 0012	110	CONT CONC T BM	CEDAR CR	G		G	G		G		G	F	G	G		G	G	G		G		G		P	G		
S257 0000 0037	188	CONT CONC T BM	NP RY	P		G	G		G					G			G	G		G		G		P	G		
S267 0000 0001		UNDERPASS	NP RR	E		E		E	E					E			E	E		E		E	E	G	E		
S267 0000 0001A		UNDERPASS	NP RR	E		E		E	E					E			E	E		E		E	E	G	E		
S267 0000 0002		UNDERPASS*	VAN BUREN ST INT	E		E		E	E					E			E	E		E		E	E	G	E		
S267 0000 0002A		UNDERPASS*	VAN BUREN ST INT	E		E		E	E					E			E	E		E		E	E	G	E		
S267 0000 0044	50	UNT T & CONC	RATTLESNAKE CR																								

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
	FEET																										
S269 0000 0034	22	CONCRETE T BEAM	IRRIGATION DITCH	G		G		F	G		G		G	G						G	G	G			G		
S269 0000 0053	25	T T TRESTLE	IRRIGATION DITCH	G		G		G	G		G		G	G				G		G	G	G		F	G		
S269 0000 0208	75	T T TRESTLE	BITTERROOT R OF	G	G	G	G	G	G	F	G	G	G		G			F		F		P		C	F		
S269 0000 0210	324	CONT ST GIRDER	BITTERROOT R	G		G	G	G	G	G	G	G	G	G			G	G		G		G	C	P	G		
S271 0000 0000		UNDERPASS*	SEP I 90	G		E		E	E				E				E	E		E		E		G	E		
S271 0000 0000P		UNDERPASS*	SEP I 90	G		E		E	E				E				E	E		E		E		G	E		
S271 0000 0202	38	T T TRESTLE	NEVADA CR	G	G	G	G		G		G		G		G			F		G		P		P	F		
S271 0000 0257	179	ST PONY TRUSS	BIG BLACKFOOT R	F		G	G		G	G	G	G	G	G	G	E	E	E		G	G	E	G	G	E		
S272 0000 0284	38	T T TRESTLE	NEVADA CR	G	G	G	G		G		G		G		G			F		G		P		P	F		
S272 0000 0354	189	ST PONY TRUSS	BIG BLACKFOOT R	E		G	G		G	G	G	G	G	G	G	E	E	E		G	G	E	G	G	E		
S272 0000 0419	152	ST PRATT TRUSS	N FK BLACKFOOT R	F				F	F		G		G	F		G	F			P	F	F		C	F		X
S348 0000 0004	38	T T TRESTLE	FLINT CR	G	G	G	G	G	G		G		G		G			G		G		G		C	G		
S348 0000 0139	102	PRE CONC BEAMS	ROCK CR	E		E	E	E	E	E	E	E	E	E			E	E		E		E		G	E		
S367 0000 0005	33	STEEL & TIMBER	IRRIGATION CANAL	F	P	F		P	P		G		G	G						F	F	C		C	F		

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z
S370 0000 0007	351	ST HOWE TRUSS	BITTERROOT R																								X
S370 0000 0010	80	UNT T TRESTLE	DRAINAGE																								X
S370 0000 0011	41	UNT T TRESTLE	DRAINAGE																								X
S370 0000 0013	40	UNT T TRESTLE	DRAINAGE																								X
S370 0000 0020	42	ST I BEAM	BITTERROOT R																								X
S373 0000 0004	324	STEEL GIRDER	BITTERROOT R	F		G	G	G	G	G	F	G	G	G			G	G		G	G	G	G	F	G		
S388 0000 0033	32	STEEL I BEAM	SKALKAHO CR	G		F		G	F	F	G	F	G	G						G	G			P	F		
S390 0000 0038		UNDERPASS	DAKOTA ST	E		E		E	E					G	G		E	E		E	E	G		G	E		
S390 0000 0039		UNDERPASS	CMSTP&P RR	E		E		E	E					G	G		E	E		E	E	G		G	E		
S390 0000 0043	420	STEEL GIRDER	CLARK FORK	G		G	G	G	G	G	G	G	G	G	G		G	G	F	G	G	F	G	F	G		
S430 0000 0056		UNDERPASS	RESERVE ST INT I	E		E	E	E	E			E	E		E		E	E		E		E		E	E		
S430 0000 0057		UNDERPASS	RESERVE ST INT I	E		E	E	E	E			E	E		E		E	E		E		E		E	E		
S460 0000 0000		UNDERPASS	I90 GOLD CR INT	G		E		E										E		E					E		
S460 0000 0001		UNDERPASS	I90 GOLD CR INT	G		E		E										E		E					E		

DE ... T VE F A ... R ...

CON ... RA ...

SU ... STR ... RE

NUMBER A	FEET B	MATERIAL ... MAXIMUM SPAN ... C	... (River, Creek or ..., Irrigation ..., Railroad, Highways, Interchange ..., Separation, etc.) D	END E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWA... J	ICE BREAKERS K	DRIF... L	RIP RAP M	SCOUR N	GIRDERS O	STR... P	TRUSS Q	SHOES R	CURBS S	MARKER T	DE... U	BR... V	RA... W	EX... X	PA... Y	G... Z	NOT... Z1	REMAR... Z2
S460 0000 0003	120	ST HOWE TRUSS	CLARK FORK	F		P		F	P			C			F	F	F			F	F	P		P	F		X
S461 0000 0129	445	REINF CONC GIR	CLARK FORK	G		G	G		G		G	F					G	G		G		G	G		E		
S461 0000 013B		UNDERPASS	NP RY				G	G	G	G				G		G	G			G	E			P	F		
S471 0000 0112	48	UNT T TRESTLE	PROSPECT CR	F				F	F		G		F		F					F					F		
S473 0000 0063	56	CONT CONC GIR	TRAPPER CR	P		G	G	G			G	C	G	G				G		G		G			G		X
S473 0000 0143	170	ST PONY TRUSS	W FK BITTERROOT	G		G			G		G	P	G	G	G	G	G	F		G	G	F		P	G		
S474 0000 0011	180	STEEL GIRDER	NP RY																								
S490 0000 0002	198	PRE CONC BEAMS	E FK BITTERROOT	G		E	E	E	E	E	G	G	G	E		E	E	E	G	E		E	E	E	E		
S490 0000 0007	173	PRE CONC BEAMS	W FK BITTERROOT	G		E	E	E	E	E	G	G	G	E		E	E	E	G	E		E	E	G	E		
S507 0000 0017		UNDERPASS	SEP-I90	E		E	E	E	E					E			E		E	E	E	E	E	P	E		
S507 0000 0018	457	WELDED PL GIRD	CLARK FORK	E		E	E	E	E	E	E	E	E	E		E	E	E		E	E	E	E	E	E		
S507 0000 0088	34	T T TRESTLE	PETTY CR	G		G	G	G	G		G		G		G			G	F	G		G		P	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

S512 0000 0007	102	PRE CONC BEAM	FLINT CR	E	E	E	E	E	E	E	F	E	E			E	E		E	E			G	E
S520 0000 0000S		UNDERPASS	CYR INT I90	E	E	E	E	E	E	E	E	E	E	E		E	E		E		E	E	E	E
S520 0000 0001	516	CONT ST TRUSS	CLARK FORK	G	G	G		G		G	G	G	G	G	G	G	G	F	F	G	F	P	G	
S520 0000 0040	198	PRE CONC 8EAM	FISH CR INT-I 90	E	E	E	E	E						E		E	E	E	E		E	E	E	E
S531 0000 0035	48	UNT T TRESTLE	SAWTOOTH CR	G	F		G	P		G		G		F					P	F	F		P	F
S531 0000 0054	300	PRE CONC BEAM	BITTERROOT R	E	E		E	E		E	E	E	E		E	E	E	E	E	E	E	E	E	E
S533 0000 0100		UNDERPASS	SEP I 90	E	E	E	E	E					E			E			E		E		E	E
S533 0000 0101		UNDERPASS	SEP I 90	E	E	E	E	E					E			E			E		E		E	E

MISSOULA DIVISION

I 90-0000-0708 190' Pre Conc. Beam N.P.R.R.
Remarks: End bents appear to be settling

P 5-0000-0189 104 ft Conc T Beam Jocko River
The upstream arch has two small cracks full depth. Three of the diaphragms are cracked.

P 6-0000-0335 230 ft Steel Beam Beaver Creek
East end fill is moving. Old highway signs used to stop fill. Outside of curb breaking away. See photos.

P 6-0766-0827 970' Steel Truss Paradise Br.
End ramps shifted. End ramp low. South right pier cracked. See photos.

P 6-0766-1059 19 ft Concrete Slab Revals Creek
Water washing under back wall. Back wall deteriorating.

P 7-0001-0259 76 ft T.T. Trestle Rye Creek
Two broken stringers. Deck appears to be loose.

P 7-0445-0829 122 ft Pre Conc Beam Lolo Creek
Not inspected

P 7-0960-0965 N.P.R.R. Underpass
End girder hit by high loads of logs. Back side shattered out. See photo.

P 19-0316-0490 Boulder Creek
Concrete piers deteriorating. See photo.

P 19-0316-0533 Flint Creek
Concrete pier deteriorating. See photo.

S 272-0000-0419 152 ft Stl Pratt Truss North Fork Blackfoot River
Shoes are in expanded position instead of contracted position for temperatures below 60 degrees.

S 370-0000-0007 351 ft St Howe Truss Bitterroot River
Not inspected. Change in FAS alignment after bridge inspection completed.

S 370-0000-0010 80 ft Unt. T. Trestle Drainage
Not inspected. Change in FAS alignment after bridge inspection completed.

MISSOULA DIVISION

S 370-0000-0011 41 ft Unt T Trestle Drainage
Not inspected. Change in FAS alignment after bridge inspection completed.

S 370-0000-0013 40 ft Unt T. Trestle Drainage
Not inspected. Change in FAS alignment after bridge inspection completed.

S 370-0000-0020 42 ft St I Beam Bitterroot River
Not inspected. Change in FAS alignment after bridge inspection completed.

S 460-0000-0003 120 ft St Howe Truss Clark Fork River
The river has changed courses and the flow is hitting the center of bent No. 2 (or north one) it is 6 foot from the top of the footing to the river bottom which is sand and gravel. Bent needs rip rap on down stream side and center line of road way. Footing does not appear to be under mined. See photos

S 473-0000-0063 56 ft Conc Arch Trapper Creek
West bridge beam completely washed out. (County notified) See photo

P-6-0000-0335

P-6-0000-0335

P-6-0766-0827

P-6-0766-0827

P-6-0766-0827

P-7-0960-0965

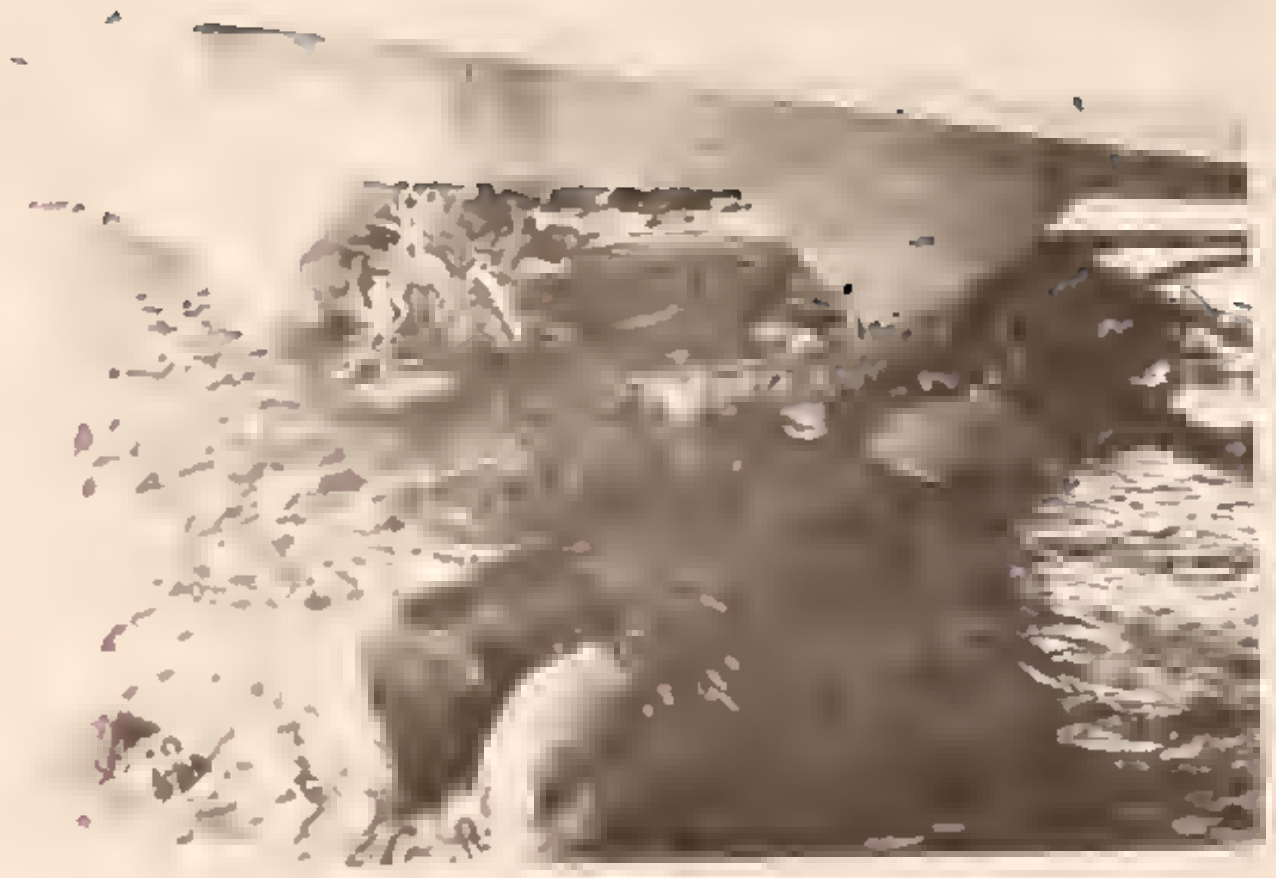
P-19-0316-0490

P-19-0316-0533

S-460-0000-0003

S-460-0000-0003

S-460-0000-0003

S-473-0000-0063

KALISPELL CONSTRUCTION DIVISION

P	1	0000	0063	210	STEEL GIRDER	YAAK R	G		G	G	G	G		G		G	G			G	G	G	F	G	G	G	G	G	X
P	1	0000	0116	939	STEEL TRUSS	KOOTENAIR-GN RY	F		G	G	G	G	G	G	G	G		G	G	G	G	G	G	G	G	G	P	G	X
P	1	0000	0145	187	ST PONY TRUSS	CALLAHAN CR	G		F	F	G	G		P	P	G		G	G	G	G	G	G	G	G	G	G	G	X
P	1	0000	0153	175	CONT STEEL 8EAM	LAKE CR	G		G		F	F		G		G	G			G	G	G	G	G	P	G	P	G	X
P	1	0000	0278	39	CONCRETE T 8EAM	CEDAR CR	G		G		G	G		G		F	G					P	G		G		G	G	
P	1	0000	0311	22	CONCRETE SLA8	PARMENTER CR	G		G		G	G		G		G						G	G		F		G	G	
P	1	0000	0322	22	CONCRETE SLA8	FLOWER CR	G		G		G	G		G		G						G	G		G		G	G	
P	1	0323	0353	179	STEEL 8EAM	GRANITE CR	P		F		G	G		P		G	G	G		G	F	P	P	G	F	P	P	F	X
P	1	0323	0412	38	T T TRESTLE	GETNER CR	F	G	G		G	G		P		G		G			G	G	G	G	G		P	G	
P	1	0323	0447	140	STEEL TRUSS	LI88Y CR	F		G		G	G		G	G	G			G	G	G	G	G	G	G	G	G	G	
P	1	0323	0461	30	T T & CONC	SWAMP CR	G	G	G		G	G		G		G		G			G	G	G	G	G			G	
P	1	0323	0467	30	T T & CONC	SWAMP CR	G	G	G		G	G		G		G		G			G	G	G	G	G			G	
P	1	0323	0483	45	T T & CONC	SWAMP CR	G	G	G		G	G		G		G		G			G	G	G	G	G			G	
P	1	0323	0487	19	T T TRESTLE	SWAMP CR	F	G	G		G	G		G		F		G			G	G	G	G	P			G	
P	1	0323	0567	23	T T & CONC	MILLER CR	G	G	G		G	G		G		G		G			G	G	G	G	G			G	
P	1	0323	0571	180	THRU ST TRUSS	FISHER R	G		G		G	G		G	G	G			G		G	G	G	G	G		G	G	
P	1	0323	0689	75	T T TRESTLE	PRIVATE RD	G	G	G		G	G						G			G	G	G	G	G		G	G	
P	1	0323	0711	38	T T TRESTLE	FISHER R	F	G	G		G	G	G	G	F	G		G			G	G	G	G	F		F	G	
P	1	0323	0804	38	T T TRESTLE	LANG CR	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G	

P	1	0323	0962	19	T T TRESTLE	LIT BITTEROOT R	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	1	0323	1052	75	T T TRESTLE	ASHLEY CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P	1	0323	1139	41	CONCRETE T BEAM	ASHLEY CR	F		G		G	G		G	G	G	G				G	G	G		G			G	
P	1	0323	1146	41	CONCRETE T BEAM	ASHLEY CR	G		G		G	G		G	G	G	G				F	F	G		F			G	
P	1	1209	1216		UNDERPASS	GN RY	G		G		G	G					G			G	G		G				G	G	
P	1	1209	1216A		UNDERPASS	GN RY	G		G		G	G					G			G	G		G				G	G	
P	1	1209	1224	182	PRE CONC BEAM	STILLWATER R	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G	
P	1	1209	1224P	182	PRE CONC BEAM	STILLWATER R	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G	
P	1	1209	1235	92	PRE CONC BEAM	SPRING CR	G		G		G	G		G	G	G	G			G	G	G	G		G		G	G	
P	1	1209	1248	898	STEEL TRUSS	FLATHEAD R	G		G	G	G	G	G	F		F			F	F	P	G	F	G	F	G	F	F	X
P	1	1383	1400	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G	
P	1	1383	1422	590	STEEL GIRDER	S FK FLATHEAD R	G		G		G	G	G	G	G	G	G			G	G	G	G	G	G	G	G	G	
P	1	1383	1444	22	CONCRETE SLAB	MARTIN CR	G		G		G	G		G		G					G	G	G		G			G	
P	1	1532	1610	115	T T TRESTLE	DEER LICK CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G			G	
P	1	1532	1647	363	STEEL GIRDER	GN RY	G		G		G	G					G			G	G	G	G	G	G		P	G	
P	1	1532	1675	209	CONCRETE T BEAM	GN RY	G		G		G	G					G			G	G	G	G	G	G		F	G	
P	1	1532	1805	744	PRE CONC GIRDER	MID FK FLATHEAD																							N
P	1	1532	1825	144	ST PONY TRUSS	SNOWSLIDE GULCH	G		F		F	F		G		G			G	G	P	G	F	G	F	G	P	G	
P	1	1532	1841		UNDERPASS	GN RY	G		G		G	G					G						G				F	G	

							E	F					K	L	M	N	O	P		R	S	T			W					
P	1	1532	1863	122	PRE CONC BEAM	BEAR CR	F		G		G	G		F	G	G	G				G	P	G		G			G		
P	1	1532	1895	26	CONCRETE SLAB	DEVIL CR	G		G		F	G		G		G					G	P	G		G			G		
P	1	1532	1922	112	PRE CONC BEAM	BEAR CR	G		G	G	G	G		G	G	G	G				G		G	G	G			G		
P	1	6671	6672		UNDERPASS	GN RY	G		G		G	G					G				G		G		G		G	G		
P	1	6671	6673	433	WELDED PL GIR	MID FK FLATHEAD	G		G	G	G	G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
P	5	0275	0377	51	CONCRETE T BEAM	POST CR	G		G		G	G		F	F	G	G				G	G	G		G		G	G		
P	5	0275	0407	76	T T TRESTLE	NINE PIPES RES	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
P	5	0275	0510	20	CONCRETE SLAB	DRAINAGE	G		G		G	G		G		G						G	G		F			G		
P	5	0275	0570	82	CONT CONC T BM	PABLO FEEDER CA	G	G	G		G	G		G	G	G	G			G	G	G	G		G		P	G		
P	5	0590	0611	1536	PRE CONC BEAM	FLATHEAD R	G	G	G		G	G		G	G	G	G			G	G		G		G	G	G	G		
P	5	0775	0823	61	CONCRETE T BEAM	DAYTON CR	F		F		G	G		G	F	G	G				F	G	F		F			F		
P	5	1126	1161	155	CONCRETE T 8EAM	STILLWATER R	F		G	G	G	G	G	G		G	G			G	G	F	G		G	G	F	G		
P	5	1254	12B1	215	STEEL BEAM	WHITEFISH R	G		P		G	G		G		G	G			P	G		G	G	P	P	F	F		X
P	5	1254	1447		UNDERPASS	GN RY	G		G		G	G					G			G			G				F	G		
P	5	1254	15B0	60	CONCRETE T BEAM	STILLWATER R	F		G	G	G	G		G		G	G				G	P	G		G		F	G		
P	5	1254	1702	57	CONCRETE T BEAM	GRAVES CR	F		G	G	G	G	G	G		G	G			G	G	G	G		G			G		
P	5	1254	1705	43	CONCRETE T BEAM	DRAINAGE	F		F		G	G		F		G	G				G	G	G		G			G		
P	5	1B09	1B22	11	T T TRESTLE	DRAINAGE	G	G	G		G	G						G			G	G	G	G	G		G	G		

P	5	1809	1843	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G	
P	5	1809	1870	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G	
P	6	0766	1159	332	CONCRETE T BEAM	NP RY & JOCK R	G		G	G	G	G	G	G		G	G			G	G	G	G	G	G	G		G	
P	33	0000	0005	271	CONT STEEL BEAM	GN RY	G		G		G	G					G	G		G	G		F	G	G	G	F	G	
P	33	0000	0008	698	RIV PL GIRDER	KOOTENAI R	G		G	G	G	G	G	G	G	G	G	G		G	G	P	G	G	G	G	G	G	
P	33	0000	0300	17	ENCASED GIRDER	BRISTOW CR	G		G		G	G		G		G						G	G		G			G	
P	33	0000	0366	12	CONCRETE SLAB	ROSEY CR	G		G		G	G		G		G						G	G		P			G	
P	33	0000	0388	12	CONC SLAB	GRIBLER CR	G		G		G	G		G		G						G	G		G			G	
P	33	0000	0422	24	ENCASED GIR	PARSNIP CR	G		G		G	G		G		G						F	G		G			G	
P	33	0000	0423	12	CONC SLAB	N FK RAINY CR	G		G		G	G		G		G						G	G		F			G	
P	33	0000	0471	60	STEEL GIRDER	BIG CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G		P	G	
P	33	0000	0586	483	STEEL TRUSS	KOOTENAI R	F	P	F	P	F	F	P	G	F	G			F	F	F	G	F	F	P	F	P	F	X
P	33	0000	0622	130	ST PONY TRUSS	TABACCO R	F		G		G	G		G	F	G			G	G	G	G	G	G	G	G	F	G	
P	36	0000	0012	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G	
P	36	0000	0030	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G	
P	36	0000	0140	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G	

				E			H					M	N	O				R	S								
P 36 0189 0198	50	PRE CONC BEAM	HOT SPRINGS CR	G		G		G	G		G	G	G	G				G	G	G	G	G	G		G	G		
P 36 0189 0267	57	T T TRESTLE	LIT BITTERROOT R	G	G	G		G	G		G	G	G		G				G	G	G	G	G		G	G		
P 36 0189 0290	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G	G		G	G		
P 36 0189 0307	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G	G		G	G		
P 36 0189 0311	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G	G		G	G		
P 36 0189 0312	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G	G		G	G		
P 36 0189 0325	38	T T TRESTLE	SULLIVAN CR	G	G	G		G	G		G	G	G		G				G	G	G	G	G		G	G		
P 36 0189 0328	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G	G		G	G		
P 36 0189 0339	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G	G		G	G		
P 36 0189 0351	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G	G		G	G		
P 36 0189 0359	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G	G		G	G		
P 38 0000 0016	138	STEEL BEAM	WHITEFISH R	G	G	G	G	G	G	G	G	F	G	G	G				G	F	G	G	P	G	G	G		X
P 38 0000 0079	496	STEEL TRUSS	FLATHEAD R	P		G	G	G	G	G	G		G		G	G	G	G	G	F	G	G	G	G	G	G		X
P 38 0000 0080	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G					G	G	G	F		F	G		
P 38 0000 0085	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G					G	G	G	F		F	G		
P 52 0000 0310	220	CONT ST GIRDER	SWAN R	G		F	G	G	G	G	G		G	G	G			P	G	G	G	G	G		G	G		X
P 52 0000 0354	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G				G	G	G	G	F		G	G		

P 52 0000 0408	95 T T TRESTLE MILL CR	F F F G G G G G G G G G F G G

A	B	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
M208 0000 0058	686 STEEL GIRDER	FLATHEAD R	G		G	G	G	G	G	G	G	G	G	G		G	G	G	G	G	G	G	G	G
M209 0000 0355	57 T T TRESTLE	HOLLAND CR	G		G		G	G		G		G		G		G	G	G	G	G	G		P	G
M209 0000 0524	69 T T TRESTLE	LION CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G
M209 0000 0570	57 T T TRESTLE	GOAT CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G
M209 0000 0656	57 T T TRESTLE	LOST CR	G	G	G		G	G		G		G		G			G	G	G	F	G		P	G
M209 0000 0830	225 PRE CONC BEAM	SWAN R	G		G	G	G	G	G	G	G	G	G			G	G		G		G	G	G	G

A	B	C		E	F	G	H		J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
S212 0000 0124	75	T T TRESTLE	POST CR-RD PLANS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S353 0000 0001		UNDERPASS	NP RY	G	G	G									G						G				G		
S354 0000 0066	69	UNT T TRESTLE	IRRIGATION CA	G	F	F		F	F		G		G		G			F		F	F	P		P	F		
S382 0000 0000	128	PRE CONC BEAM	NP RY	P		G		G	G								G	G	G	G		G	G	G	G		X
S382 0000 0001	650	WELDED PL GIR	FLATHEAD R	P		G	G	G	G	G	G	G	G	G	G		G	G	G	G	G	G	G	G	G		X
S382 0000 0027	50	T T TRESTLE	CAMAS CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
S382 0000 0032	50	T T TRESTLE	CAMAS CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
S382 0000 0036	50	T T TRESTLE	CAMAS CR	P	G	G		G	G		P	F	G		G			G	G	G	F	P		P	G		X
S424 0000 0234	200	UNT T TRESTLE	STILLWATER R	G	G	G		F	G		P		G		G					G	G	G			G		X
S456 0000 0007	127	UNT T HOWE TRUS	STILLWATER R	G	F	F		F	F		F		G		G	F				G	F	F			F		X
S482 0000 0026	122	PRE CONC BEAMS	LIBBY CR	G		G	G	G	G	G	F	G	G	G			G	G	P	G	G	G	G	G			
S486 0000 0043	22	UNT PILE TRES	CEDAR CR	G		G		G	G		G		G		G			F		F					G		

					F		H		J	K		M	N	O			R				W				
S486 0000 0068	22	UNT T TRESTLE	CEDAR CR	G		G		G	G		G		G		G			F	F					G	X
S486 0000 0208	95	ST PONY TRUSS	BIG CR	F		G		G	G		G		G		G	G	G	F	G	G	F	F	P	F	
S486 0000 0291	60	ST PONY TRUSS	COAL CR	G		P		F	F		G		G		G	P	P	F	F	F	F		P	F	X
S486 0000 0338	30	T T TRESTLE	MORAN CR	F		G		G	G		G		G		G			F	F	F	F		P	G	
S486 0000 0354	45	STEEL I BEAM	HAY CR	G		F		P	P		G		G		G			F	G		P		P	F	X
S486 0000 0410	43	STEEL GIRDER	RED MEADOW CR	F		G		G	G		G		G	G			G	F	F	F	F		F	G	
S486 0000 0448	75	ST PONY TRUSS	WHALE CR	G		F		F	F		G		F		G	F	F	F	F	F	P		P	F	X
S486 0000 0506	39	T T TRESTLE	TRAIL CR	G		G		G	G		G		G		G			G	G	G	G		F	G	
S486 0000 0574	22	T T TRESTLE	COLTS CR	G	G	G		G	G		G		G		G			F	F	G	F		P	G	
S487 0000 0002	633	ST WARREN TRUSS	GN RY	G		G		G	F						G	G	G	F	G	G	F	P	F	G	X
S506 0000 0034	64	UNT T TRESTLE	PIPE CR	F	F	F		F	F		G	F	G		F				F	F	F			F	
S508 0000 0121	22	CONC T TRES	FOURTH JULY CR	G		G		G	G		G		G		G			G	G	G	P		P	G	X
S508 0000 0188	36	CONC T TRES	MEADOW CR	G		G		G	G		G		G		G			G	G	G				G	
S508 0000 0191	35	CONC T TRES	HELLROARING CR	G		G		G	G		G		G		G			G	G	G				G	
S508 0000 0237	111	STEEL GIRDER	SPREAD CR	G		G		G	G		P		G		G		G	G	G	G	G		P	G	
S508 0000 0282	34	CONC T TRES	PETE CR	G		G		G	G		G		G		G			G	G	G				G	

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
S508 0000 0383	112	WARREN ST TRUSS	YAK RIVER	P		F		G	G		G		G		G	F	F	G		G	F	P		G	G		
S508 0000 0426	34	ST I BEAM	E FK YAK R	G		G		G	G		G		G	G				G		G				F	G		
S508 0000 0484	22	T T TRESTLE	CARIBOU CR	G	G	G		G	G		G		G		G			G		G	F	G		P	G		
S508 0000 0672	24	T T TRESTLE	SULLIVAN CR	G	G	G		G	G		G		G		G			G		G	G				G		X
S530 0000 0018	26	CONC & TIMBER	N CROW CR	G		G		G	G		G		G					P	P	G	G			P	G		

KALISPELL DIVISION

P 1-0000-0063 210 ft St Girder Yaak River
Deck shows wear and spalling in spots. Some concrete chipped away at joints in deck.

P 1-0000-0116 210 ft Steel Truss Kootenai River
Rail shows settlement of west end bent. Spalling of concrete at outside edges of curb. One rail post has been knocked out of line. Undercoat of paint is showing through in spots on rail and steel truss.

P 1-0000-0145 187 ft St Pony Truss Callahan Creek
Spalling on cap edges and around some bearing concrete. Spalling on outside edges of curb and posts. See photo.

P 1-0000-0153 175 Cont St Beam Lake Creek
Rail quite badly deteriorated. Spalling concrete on curb edges.

P 1-0323-0353 179 ft St Beam Granite Creek
Asphalt on deck has chuck holes. Edges of bents are spalling. Rail needs paint. Drift collected near bents. No dirt berm under east end bent.

P 1-1209-1248 898 ft Steel Truss Flathead River
Some rail bolts sheared off. 2 shoe pin nuts gone on Bent 1. 2 rocker pin nuts gone over connection to cantelever truss in span 3 and 5. 1 nut loose in slip joint to cantelever section span 3. Some rail posts shattered. Concrete end posts have concrete knocked away. Curbs spalling away in places. We were up under the truss when some large trucks went over and there is considerable movement of the truss section. The concrete deck is rough and gets the loads bouncing.

P 5-1254-1281 215 ft Steel Beam Whitefish River
Three shoes bent 1 have concrete gone away from under the bearing plates. No room for expansion. Rail spalled badly. See photo.

P 33-0000-0586 483 ft St Truss Kootenai River
Some portals bent. Ice breaker steel hanging loose. Rail sections broken or gone. Concrete spalling at pier. See photos.

P 38-0000-0016 138 ft St Beam Whitefish River
Rail and corner posts badly spalled.

P 38-0000-0079 496 ft Steel Truss Flathead River
Cavity under roadway at east end bent, no berm on west end bent. Repair work not painted. Couple gouges in diagonal top chord over east pier. See photo.

KALISPELL DIVISION

P 52-0000-0310 220 ft Cont St Girder Swan River
The two end bents must be drifting together as rockers on both are in full expansion position, to the point where they are starting to bend the anchor bolts. See photo.

S 382-0000-0000 128 ft Pre-Conc Beam N. P. Ry
End fill has hole washed out around end bent.

S 382-0000-0001 650 ft Weld Plate Girder Flathead River
End fill shows movement. Cracks opening up and end bent exposed. One crack in concrete cap of middle pier from anchor bolt out to edge. Rail shows a drop at bent 1.

S 382-0000-0036 50 ft T. T. Trestle Camas Creek
No dirt berm on one end and fill is falling out under backing plank. One stringer cracked. End rail section knocked off and some rotten rail posts. Poor rail paint.

S 486-0000-0291 60 ft St Pony Truss Coal Creek
Drift or ice has come down and bent the up-stream bottom chord of truss. Concrete under one bearing plate is 50% gone leaving half of bearing plate with nothing under it.

S 486-0000-0354 45 ft St I Beam Hay Creek
Vertical crack in wingwall. Several broken places under bearing shoes. Rail has a section missing and left rail in leaning.

S 486-0000-0448 75 ft St Pony Truss Whale Creek
Upstream bottom chord bent from ice or drift. Rail pretty well beat up. One concrete footing badly spalled at water line.

S 487-0000-0002 633 ft St. Warren Truss Great Northern Ry
Cracked stringer span 7 and north end span. Scattered spalling on rail. No expansion room at bent 9.

S 508-0000-0121 22 ft Conc. T. Trestle 4th of July Creek
Broken rail.

S 508-0000-0672 24 ft T T Trestle Sullivan Creek
No rail No markers

P-1-0000-0145

P-5-1254-1281

P-33-0000-0586

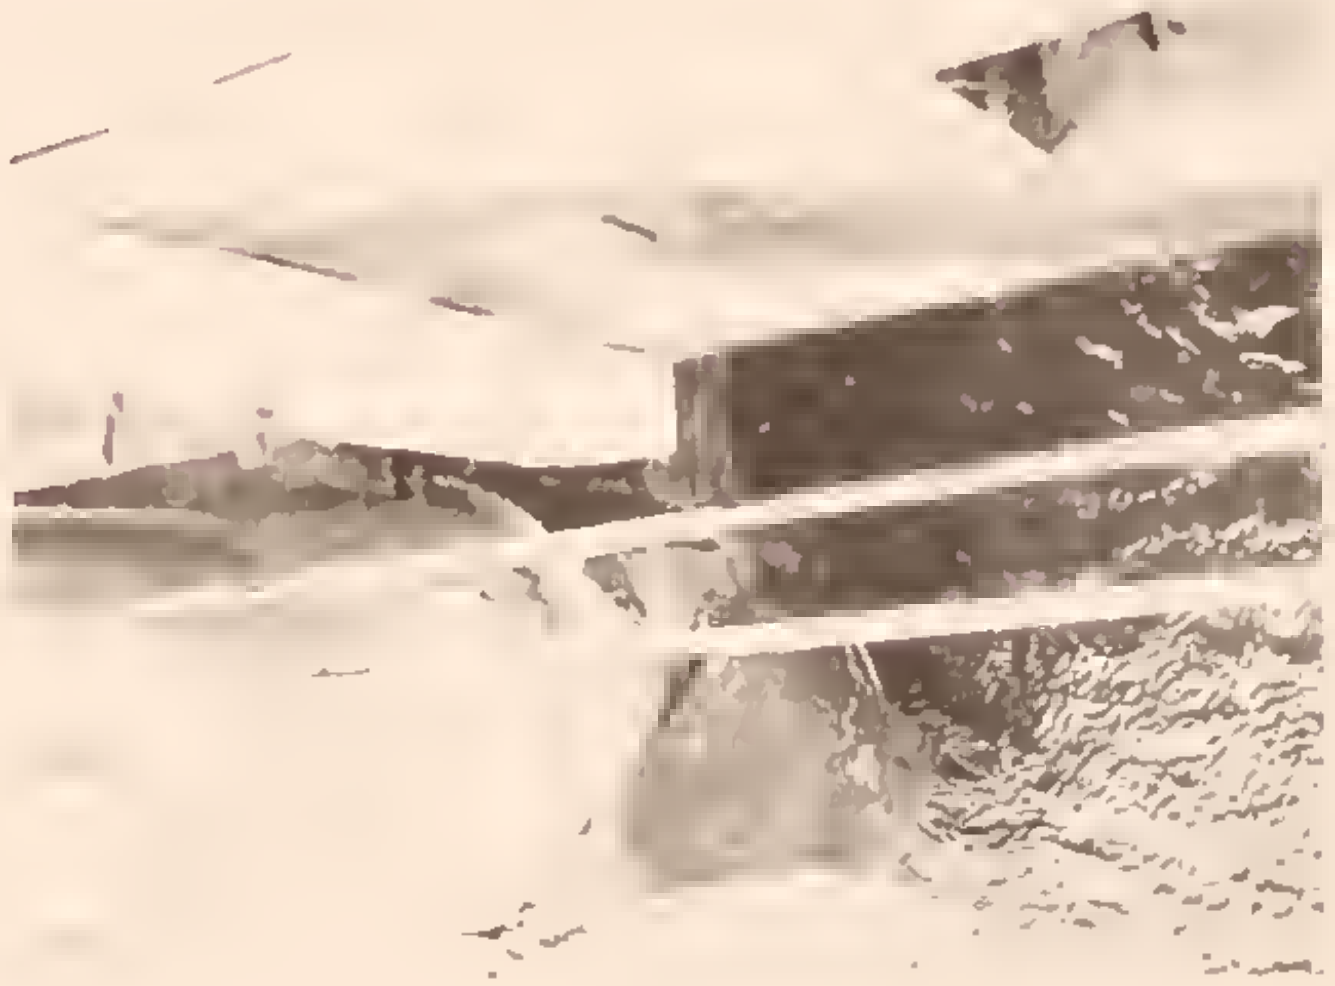

P-33-0000-0586

P-38-0000-0079

P-52-0000-0310

BUTTE CONSTRUCTION DIVISION

I 15 0000 0005	118	PRE CONC BEAM	MONIDA INT-DR509	G	E		E	E					E		E	E	E	E	E	E	E	G	E	
I 15 0000 0015	281	PRE CONC BEAM	UP RR	G	E		E	E					E		P	E	E	E	E	E	F	F	G	X
I 15 0000 0095	17	SPPAC CULVERT	JR INT CD RD	G			G																G	
I 15 0000 0147	450	ST PLATE GIRDER	UP RR	G	G		E	E					E		P	E	E	E	E	E	G	F	G	X
I 15 0000 0151	118	PRE CONC BEAM	LIMA INT-CD RD	G	E		E	E					E		G	E	E	E	E	E	E	G	E	
I 15 0000 0198	108	PRE CONC BEAM	GOSMAN LANE-SEP	E	E		E	E					E		E	E	E	E	E	E	E	E	E	
I 15 0000 0232	22	CONCRETE SLAB	BIG SHEEP CR	G	G		G	G		G	G	G				F	G	G		P		G	G	X
I 15 0000 0310	22	CONCRETE SLAB	DRAINAGE	G	G		F	F				G					G	G	G	G			G	
I 15 0000 0383	143	PRE CONC BEAM	RED ROCK RIVER	G	E	E	E	E	E	E	E	G	E		E	E	E	E	E	E	G	G	E	
I 15 0000 0386	107	PRE CONC BEAM	SEP-CD RD	E	E		E	E					E		E	E	E	E	E	E		G	E	
I 15 0000 0443		UNDERPASS	INT-DR 324	G	E		E	E					E		P	E	E	E	E	E	G	G	E	X
I 15 0000 0448	173	PRE CONC BEAM	BEAVERHEAD RIVER	G	E	E	E	E	E	E	E	G	E		E	E	E	E	E	E	G	E	E	
I 15 0000 0458	401	WELDED PL GIR	BEAVERHEAD RIVER	G	P	E	E	E		E	G	E	G	G		G	E	E	E	E	G	E	E	X
I 15 0000 0499	163	PRE CONC BEAM	BEAVERHEAD RIVER	G	E	E	E	E	E	G	E	G	E		E	E	E	E	E	E	G	E	E	
I 15 0000 0526	188	PRE CONC BEAMS	BEAVERHEAD R	G	E	E	E	E	E	E	E	G	E		E	E	E	E	E	E		E	E	
I 15 0000 0529	163	PRE CONC BEAMS	BEAVERHEAD R	G	E	E	E	E	E	E	E	G	E		E	E	E	G	E	E		E	E	X
I 15 0000 0559	123	PRE CONC BEAMS	BARRATT INT-CD R	E	E		E	E					E		E	E	E	E	E	E		E	E	
I 15 0000 0605	140	CONT ST I BEAM	BEAVERHEAD RIVER	G	G	G		G	G	G	G	G	G		G	G	G	G	G	G	G	G	G	
I 15 0000 0610	143	CONCRETE T BEAM	UP RR	G	F			G					F		F	G	G	G	G	G	G		G	X

A	TOTAL LENGTH FEET B	C	D	E	PILES F	G	H	I	J	K	L	RIP RAP M	SCOUR N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I 15 0000 0611	77	CONCRETE T BEAM	POINDEXTER SL	F		G			G		G		G	G			G	G	G	G	G	G			G		
I 15 0644 0655	150	CONT ST I BEAM	BEAVERHEAD R	G		G	G		G	G	G	G	F	G			G	G	G	G	G	G	G	G	G		
I 15 0644 0691	29	CONCRETE T BEAM	IRR CA	G		G		G	G		G		G	G			G	G	G	G	G	F			G		
I 15 0644 0700	66	CONCRETE T BEAM	FRY PAN CR	G		G		G	F		G	F	F	G				F	F	G	F	F			F		X
I 15 0644 0873	238	STEEL TRUSS	BIG HOLE R	F		P	P		F	G	G	G	G		G	G	F	P	G	F	G	G	F	E	P		X
I 15 1042 1223		UNDERPASS	VICTOR INT-DR423	E		E		E	E					E			E	E	E	E	E	E	E	F	E		
I 15 1042 1223A		UNDERPASS	VICTOR INT-DR423	E		E		E	E					E			E	E		E	E	E	E	E	E		
I 15 1042 1231	614	STEEL GIRDER	BRY-CLARK FORK	G		E		E	E		G		G	E			E	E	E	E	E	E	G	G	G		
I 15 1042 1231P	599	STEEL GIRDER	BRY-CLARK FORK	G		E		E	E		G		G	E			E	E	E	E	E	E	G	G	E		
I 15 1042 1237			UNDERPASS																							N	
I 15 1042 1237A			UNDERPASS																							N	
I 15 1237 1237			UNDERPASS																							N	
I 15 1237 1237A			UNDERPASS																							N	
I 15 1237 1249	118	PRE CONC BEAM	ROCKER INT-CO-RD																							N	
I 15 1237 1249P	118	PRE CONC BEAM	ROCKER INT-CO-RD																							N	
I 15 1237 1264	133	CONCRETE T BEAM	BA&P RY	G		G			G					G			G	G	G	G			F		G		
I 15 1237 1264P	133	CONCRETE T BEAM	BA&P RY	G		G			G					G			G	G	G	G			F		G		
I 15 1266 1268S		UNDERPASS	W BUTTE INT-I115	G		E		E	E				E			E	P	E	E	E	E	E	G	E	E		X
I 15 1266 1270	301	PRE CONC BEAM	BA&P-CMSTP&P RR	G		E		E	E					E			E	E	E	E	E	E	G	G	E		

A				B	C	D	E	F	G	H		J	K	L	M	N	O	P	Q	R	S	T		V	W	X	Y	Z	Z	ZZ
I	15	1266	1270P	321	PRE CONC BEAM	BA&P-CMSTP&P RR	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
I	15	1266	1272	442	RIVETED ST GIR	NP RY	G		E		E	E		G	G	G	E			E	E	E	E	E	E	G	G	E		
I	15	1266	1272P	489	RIVETED ST GIR	NP RY	G		E		E	E		G	G	G	E			E	E	E	E	E	E	G	G	E		
I	15	1266	1281	472	STEEL GIRDER	CMSTP&P RR-NP RY	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
I	15	1266	1281P	472	STEEL GIRDER	CMSTP&P RR-NP RY	G		E		E	E					E			E	E	E	E	E	E	G	E	E		
I	15	1266	1287	168	STEEL GIRDER	MONT S INT-US 10	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
I	15	1266	1287P	168	STEEL GIRDER	MONT S INT-US 10	G		E		E	E					E			E	E	E	E	E	E	G	G	E		
I	15	1287	1291		UNDERPASS	LEXINGTON ST SEP	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1287	1291A		UNDERPASS	LEXINGTON ST SEP	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1287	1296		UNDERPASS	OREGON ST SEP	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1287	1296A		UNDERPASS	OREGON ST SEP																								
I	15	1287	1303	210	PRE CONC BEAM	HARRISON AVE INT	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1287	1303P	210	PRE CONC BEAM	HARRISON AVE INT	G		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1303	1311		UNDERPASS	SHERIDAN ST-SEP	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1303	1311A		UNDERPASS	SHERIDAN ST-SEP	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1303	1314		UNDERPASS	9MILE SEP-OR 375	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1303	1314A		UNDERPASS	9MILE SEP-OR 375	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1314	1318		UNDERPASS*	E BUTTE INT-I90	E		E		E	E					E			E	E		E	E	E	G	F	E		
I	15	1314	1319		UNDERPASS*	E BUTTE INT-I90	E		E		E	E					E			E	E		E	E	E	G	E	E		

				FEET A		C		E	F	G	H		J	K	L	M	N		P	Q	R	S	T	U	V	W			Z	Z	Z2
I	15	1314	1323	230	STEEL GIRDER		NPRY	E		E		E	E					E			E	E		E	E	E	G	E	E		
I	15	1359	1447	31	STEEL I BEAM		BISON CREEK	G		F		P	G		G		G	G				P	G	G	G	F		F	F		
I	15	1359	1482	81	CONCRETE T BEAM		BISON CREEK	F		G	F	G	G		G	P	G	F			F	F	G	G	G	G			F		
I	15	1359	1484	99	CONCRETE T BEAM		BISON CREEK	G		G		F	G		G		G	G				P	G	G	G	F			G		
I	15	1359	1503	31	CONCRETE T BEAM		BISON CREEK	G		G		F	G		G		G	G				P	G	G	G	F			G		
I	15	1359	1527		UNDERPASS		GN RY	G		G	G		G					G			G		G	G	G				G		
I	15	1359	1538	43	CONCRETE T BEAM		BOULDER R	G		F		F	G		G	F	G	G				P	G	F	G	F			F		
I	15	1359	1547	22	CONCRETE SLAB		RED ROCK CR	G		G		F	G		G		G					F	G	G	G	F			G		
I	15	1359	1580	23	CONCRETE SLAB		BASIN CR	G		G		G	G		G	G	G					G	G	G	G	G		F	G		
I	15	1359	1590	79	CONCRETE T BEAM		CATARACT CR	G		F		G	G		G	G	G	G				P	G	G	F	F			F		
I	15	1359	1606		UNDERPASS		GN RY	G	F	F	G		G					G			G			G	G				G		
I	15	1359	1607	149	CONCRETE T BEAM		BOULDER R	G		F	G	F	G	G	G	G	G	G			G	P	G	F	F	F	G		F		
I	15	1359	1625	138	CONCRETE T BEAM		BOULDER R	G		G	F	F	G	G	G	G	G	G			G	P	G	F	G	F	G		F		
I	15	1359	1680	7	T T TRESTLE		STOCKPASS	G	G	G		F	G		G				G			P	F	G	G				G		
I	15	1359	1693	7	T T TRESTLE		STOCKPASS	G	G	G		F	G		G				G			P	F	G	G				G		
I	15	1359	1702	7	T T TRESTLE		STOCKPASS	G	G	G		F	G		G				G			P	F	G	G				G		
I	15	1359	1708	7	T T TRESTLE		STOCKPASS	G	G	G		F	G		G				F			P	F	G	G				G		X
I	15	1359	1717	7	T T TRESTLE		STOCKPASS	G	G	G		F	G		G				G			P	F	G	G				G		
I	15	1359	1730	7	T T TRESTLE		STOCKPASS	G	G	G		F	G		G				F			F	P	G	G				G		X

		A					E	F	G	H		J	K		M	N	O	P	Q	R	S	T		V	W		Y	Z	Z	Z
I	15	1359	1830	31	CONCRETE T 8EAM	PRICKLY PEAR CR	G		G		G	G		G		G	G				G	G	G	G	F			G		
I	15	1359	1887	133	PRE CONC 8EAM	SEP FRONT RD																							N	
I	15	1359	1887P	133	PRE CONC 8EAM	SEP FRONT RD																							N	
I	15	1359	1902	231	PRE CONC BEAM	GN RY																							N	
I	15	1359	1902P	231	PRE CONC 8EAM	GN RY																							N	
I	15	1359	1909		UNDERPASS	MONT CITY INT																							N	
I	15	1359	1909A		UNDERPASS	MONT CITY INT																							N	
I	15	1359	1926		UNDERPASS	SEP OR 481																							N	
I	15	1359	1926A		UNDERPASS	SEP OR 481																							N	
I	15	1359	1953		UNDERPASS*	CAPITOL INT-US12	G		E		E	E					E			F	E		E	E	E	G	G	E		
I	15	1359	1953A		UNDERPASS	CAPITOL INT-US12	G		E		E	E					E			E	E		E	E	E	E	G	G	E	
I	15	1953	1953		UNDERPASS*	CAPITOL INT-US12	G		E		E	F					E			E	E		E	E	E	E	E	G	E	
I	15	1953	1953A		UNDERPASS	CAPITOL INT-US12	G		E		E	E					E			E	E		E	E	E	E	E	G	E	
I	15	1953	1961	798	RIV PL GIRDER	GN&NP RY-AVENUE	G		E		E	E					E			E	E	G	E	E	E	E	E	G	E	
I	15	1953	1961P	810	RIV PL GIRDER	GN&NP RY-AVENUE	G		E		E	E					E			E	E	E	E	E	E	E	E	G	E	
I	15	1953	1965		UNDERPASS	CEDAR ST INT	G		E		E	E					E			P	E		E	E	E	E	E	G	E	X
I	15	1953	1965A		UNDERPASS	CEDAR ST INT	G		E		E	E					E			P	E		E	E	E	E	E	G	E	X
I	15	1953	1971		UNDERPASS	YORK SEP-OR 280	G		E		E	E					E			E	E		E	E	E	E	E	G	E	
I	15	1953	1971A		UNDERPASS	YORK SEP-OR 280	G		E		E	E					E			E	E		E	E	E	E	E	G	E	

			FEET			E	F	G	H		J	K	L	M	N	O	P	Q	R		T	U	V	W	X	Y	Z	7	Z2
I 15	1953	1992	50	PRE CONC BEAM	TEN MILE CREEK	G		E		E	E		G		G	E			E	E		E	E	E		G	E	E	
I 15	1953	1992T	50	PRE CONC BEAM	TEN MILE CREEK	G		E		E	E		G		G	E			E	E		E	E	E		G	E		
I 15	1953	2001	118	PRE CONC BEAM	SEP-CO RD	G		E		E	E					E			E	E		E	E	E	E	G	E		
I 15	1953	2001P	118	PRE CONC BEAM	SEP-CO RD	E		E		E	E					E			E	E		E	E	E	F	G	E		
I 15	1953	2032		UNDERPASS*	LINCOLN INT-US 9	G		E		E	E					E			E	E		E	E	E	G	G	E		
I 15	1953	2032A		UNDERPASS	LINCOLN INT-US 9	G		E		E	E					E			E	E		E	E	E	G	G	E		
I 15	2032	2122	118	PRE CONC BEAM	INT-CO RD	G		E		E	E					E			E	E		E	E	E	G	G	E		
I 15	2032	2122P	118	PRE CONC BEAM	INT-CO RD	G		E		E	E					E			E	E		E	E	G	G	G	E		
I115	4038	4040R	244	STEEL GIRDER	W BUTTE INT-I 90	G		E		E	E				E			E	P	E	E	E	E	E	G	E	E		X
I115	4038	4047	12	CONCRETE BOX	JR GR SEP-TR RD	G		G		G	E		G		G					G	G	G	G				G		
I115	4038	4047P	12	CONCRETE BOX	JR GR SEP-TR RD	G		G		G	G		G		G					G	G	G	G				G		
I115	4038	4050	156	CONCRETE T BEAM	EXCELSIOR ST SEP	G		G			G					G				G	G	G	G	G		F	G		
I115	4038	4050T	156	CONCRETE T BEAM	EXCELSIOR ST SEP	G		G			G					G				G	G	G	G	G		F	G		
I 90	1765	1767	204	CONT ROLL BM	NP RY	F		G		G	G					G			G	G	G	G	G	G	F	F	G		X
I 90	1765	1771	141	CONT T BEAM	LIT BLACKFOOT R	G		G	G		G	G	G	F	G	G			G	G	G	G	G	G	G	F	G		
I 90	1765	1821	20	CONCRETE SLAB	JR GR SEP-CO RD	G		G		G	E									E		E	G	E		G	E		X
I 90	1765	1850	20	CONCRETE SLAB	JR GR SEP-CO RD	G		E		E	E									E		E	E	E		G	E		

I	90	1765	1865	123	PRE CONC BEAM	N D-L INT-US 10	G		E	E	E					E	E	E		E	E	E	G	G	E	
I	90	1865	1876	118	PRE CONC BEAM	SEP-MILWAUKEE AV	G		E	E	E					E	E	E		E	E	E	P	F	G	X
I	90	1865	1886	168	PRE CONC BEAM	SEP-CO RD	G		E	E	E					E	E	E	F	E	E	G	F	G	G	
I	90	1865	1893	153	PRE CONC BEAM	CLARK FORK	G		E	E	E	E	G	G	G	E	E	E	G	E	E	E	G	G	G	
I	90	1865	1893P	153	PRE CONC BEAM	CLARK FORK	G		E	E	E	E	G	G	G	E	E	E	G	E	E	E	G	G	G	
I	90	1865	1895		UNDERPASS*	S D-L INT-US 10	G		E	E	E					E	E	E		E	E	E	E	G	G	
I	90	1865	1895A		UNDERPASS	S D-L INT-US 10	G		E	E	E					E	E	E		E	E	E	E	G	G	
I	90	1895	1905	35	CONCRETE T BEAM	POWELL CR	G		G	G	G		G		F	G		G	G	F	G	G			G	
I	90	1895	1937	62	CONCRETE SLAB	DEMPSEY CR	G	F	G	G	G		G	P	G			G	G	G	G	G			F	
I	90	1895	1956	35	CONCRETE T BEAM	RACE TRACK CR	G		G	G	G		G	F	G	G		G	G	G	G	G			G	
I	90	1895	1967	182	CONCRETE T BEAM	CMSTP&P RR	F		F		G					G		G	F	G	F	G	G		F	
I	90	1895	2004	35	CONCRETE T BEAM	LOST CR	G		G	G	G		G		G	G		G	G	G	G	G			G	
I	90	1895	2031	27	CONCRETE T BEAM	WARM SPRINGS CR	G		G	G	G		G		G	G		G	G	G	G	G			G	
I	90	2039	2059	31	CONCRETE T BEAM	DR	G		G	G	G		G	F	G	G		G	G	G	G	G			G	
I	90	2039	2064	35	CONCRETE T BEAM	DR	G		G	G	G		G	F	G	G		G	G	G	G	G			G	
I	90	2039	2070	35	CONCRETE T BEAM	WILLOW CR	G		G	G	G		G	F	G	G		G	G	G	G	G			G	
I	90	2039	2073	75	CONCRETE T BEAM	CLARK FORK	G		G	G	G	G	G	F	G	G		G	G	G	G	G			G	
I	90	2039	2083		UNDERPASS	SEP-OR 275	G		E	E	E					E	E	E		E	E	E	E	E	E	
I	90	2039	2083A		UNDERPASS	SEP-OR 275	G		E	E	E					E	E	E		E	E	E	E	E	E	

I	90	2039	2092		UNDERPASS*	INT-US 10A	G	E	E	E	E	E	E		E	E	E	G	E	E	
I	90	2039	2092A		UNDERPASS	INT-US 10A	G	E	E	E	E	E	E		E	E	E	G	E	E	
I	90	2092	2115	211	PRE CONC BEAM	CMSTP&P RR	G	E	E	E	E	E	E		E	E	E	G	E	E	
I	90	2092	2115P	211	PRE CONC BEAM	CMSTP&P RR	G	E	E	E	E	E	E		E	E	E	G	E	E	
I	90	2092	2126		UNDERPASS	GREGSON INT-441	G	E	E	E	E	E	E	E	E	E	E	E	E	E	
I	90	2092	2126A		UNDERPASS	GREGSON INT-441	G	E	E	E	E	E	E	E	E	E	E	E	E	E	
I	90	2092	2171P	158	PRE CONC BM	BA & P RY	G	E	E	E	E	E	E	E	E	E	E	E	E	E	
I	90	2092	2171A	158	PRE CONC BM	BA & P RY	G	E	E	E	E	E	E	E	E	E	E	E	E	E	
I	90	2092	2177		UNDERPASS	RAMSEY INT-CO RD	G	E	E	E	E	E	E	E	E	E	E	E	E	E	
I	90	2092	2177A		UNDERPASS	RAMSEY INT-CO RD	G	E	E	E	E	E	E	E	E	E	E	E	E	E	
I	90	2092	2201	303	PRE CONC BEAM	INT I15 NISSLER															N
I	90	2092	2201P	293	PRE CONC BEAM	INT I15 NISSLER															N
I	90	2278	2279		UNDERPASS	9MILE SEP-OR375	G	E	E	E	E	E	E	E	E	E	E	E	G	E	
I	90	2278	2279A		UNDERPASS	9MILE SEP-OR375	G	E	E	E	E	E	E	E	E	E	E	E	G	E	
I	90	2278	2284	193	STEEL GIRDER	E BUTTE INT-I 15	G	E	E	E	E	E	E	E	E	E	E	E	G	E	
I	90	2278	2284P	193	STEEL GIRDER	E BUTTE INT-I 15	G	E	E	E	E	E	E	E	E	E	E	E	G	E	
I	90	2278	2288		UNDERPASS	SEP-CO RD	G	E	E	E	E	E	E	E	E	E	E	E	G	E	
I	90	2278	2288A		UNDERPASS	SEP-CO RD	G	E	E	E	E	E	E	E	E	E	E	E	G	E	
I	90	2278	2346		UNDERPASS	HOMESTAKE INT-CO	G	E	E	E	E	E	E	E	E	E	E	E	G	E	

I 90 2278 2346A		UNDERPASS	HOMESTAKE INT-CD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2434	123	PRE CONC BEAM	PIPESTONE INT-CD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2434P	123	PRE CONC BEAM	PIPESTONE INT-CD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2447	315	STEEL GIRDER	NPRY	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2447P	315	STEEL GIRDER	NPRY	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2465	108	PRE CONC BEAM	SEP-CD RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2465P	108	PRE CONC BEAM	SEP-CD RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2504	128	PRE CONC BEAM	WHITEHALL INT	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2504P	128	PRE CONC BEAM	WHITEHALL INT	G		E		E	E					E			E	E	E	F	E	E	E	G	E		
I 90 2278 2511		UNDERPASS	SEP CD RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2511A		UNDERPASS	SEP CD RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
I 90 2278 2546	214	PRE CONC BEAM	SEP-FRTG RD																							N	
I 90 2278 2546P	199	PRE CONC BEAM	SEP-FRTG RD																							N	
I 90 2278 2576	138	PRE CONC BEAM	CARDWELL INT																							N	
I 90 2278 2576P	138	PRE CONC BEAM	CARDWELL INT																							N	
I 90 2278 2581	112	PRE CONC BEAM	BOULDER R																							N	
I 90 2278 2581P	112	PRE CONC BEAM	BOULDER R																							N	
I 90 2702 2758	102	PRE CONC BEAM	MILLIGAN CR																							N	
I 90 2702 2772	7	TT TRESTLE	STOCKPASS	G	F	F		G	G						F			P	G	F	F				F		X

A	B TOTAL LENGTH FEET	C MAX [illegible] SPAN	D	E END FILLS	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q	R SHOES	S CURBS	T MARKERS	U DECK	V BRA[illegible]	W	X	Y	Z GENERAL	Z1 NOT INSPECTED	Z2 REMARKS
I 90 2702 2779	7	TT TRESTLE	STOCKPASS	F	F	F		P	G						F			P	G	F	F				F		X
I 90 2702 2790	7	T T TRESTLE	STOCKPASS	F	F	F		F	G						F			F	G	F	F				F		
I 90 2702 2793	7	T T TRESTLE	STOCKPASS	F	F	F		F	G						F			F	G	F	F				F		
I 90 2801 2801	247	CONT ST GIRDER	JEFFERSON R	G		G	G	G	G	G	G	G	G	G			G	G	G	F	G	G	G	G	G		
I 90 2801 2818	208	STEEL GIROER	CMSTP&P RR	F		F			G					G			G	G	G	G	G	F	F	G	G		
I 90 2838 2842	735	PRE CONC 8EAM	2 RR-MAOISON R	G		E	E	E	E	E	G	E	G	E			E	E	G	E	E	E	F	E	E		
I 90 2838 2842P	624	PRE CONC 8EAM	2 RR-MAOISON R	G		E	E	E	E	E	G	E	G	E			E	E	G	E	E	E	F	E	E		
I 90 2838 2849	144	PRE CONC 8EAM	MIO FK MAOISON R	G		E	E	E	E	E	E	E	G	E			E	E		E	E	E		E	E		
I 90 2838 2849P	144	PRE CONC 8EAM	MID FK MAOISON R	G		E	E	E	E	E	E	E	G	E			E	E		E	E	E		E	E		
I 90 2838 2855	92	PRE CONC 8EAM	E FK MAOISON R	G		E	E	E	E	E	E	E	G	E			E	E		E	E	E		E	E		
I 90 2838 2855P	92	PRE CONC 8EAM	E FK MAOISON R	G		E	E	E	E	E	E	E	G	E			E	E		E	E	E		E	E		
I 90 2838 2857	128	PRE CONC 8EAM	SEP-CO RD	G		E		E	E				E			E	E		E	E	E		E	E	E		
I 90 2838 2857P	128	PRE CONC 8EAM	SEP-CO RO	G		E		E	E				E			E	E		E	E	E		E	E	E		

P	2	1B91	1B91		UNDERPASS	N D-L INT-I 90	G		E		E	E					E			E	E		E	E	E	G	G	E	
P	2	1B91	1901	23	CONCRETE SLAB	COTTONWOOD CR	G		G		F	G		G		G					G	F	G	G	G			G	
P	2	1B91	1920	130	CONT ST GIRDER	CLARK FORK	G		G	G		G	G	G	F	G	G			G	G	G	G	G	F	G	G	G	
P	2	1B91	1926S	256	PRE CONC BEAM	S D-L INT-I 90	G		E		E	E					E			E	E		E	E	E	E	G	G	
P	2	2254	2258	36	CONCRETE SLAB	CLARK FORK	F		F	P	P	P		G		G					P		F	F	P			P	
P	2	2254	2259		UNDERPASS	NP RY	G		G		F	G					G			G		F	F	G			F	F	
P	2	2254	2260		UNDERPASS*	MONT S INT-I 15	G		E		E	E					E			E	E	E	E	E	E	G	G	E	
P	2	2258	2258		UNDERPASS*	MONT S INT-I 15	G		E		E	E					E			E	E	E	E	E	E	G	G	E	
P	2	2258	2280	33	CONCRETE SLAB	DRAINAGE	G		G	F	G	G		G		G					G	G	G	F	G			G	
P	2	22BD	2441	6	T T TRESTLE	STOCKPASS	G	G	G		F		G		G		G	G			F	G	G	G				G	
P	2	22BD	2449	6	T T TRESTLE	STOCKPASS	G	G	G		F		G		G		G	G			F	G	G	G				G	
P	2	22BD	2467	7	T T TRESTLE	STOCKPASS	G	G	G		F		G		G		G	G			F	G	G	G	F		F	G	
P	2	22BD	2469	95	T T TRESTLE	RADER CR	G	G	F		F	G		G	G	G		G			F	G	G	G	F		P	F	
P	2	22B0	2472	7	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			F	G	G	F	F		P	G	
P	2	24B1	1610		UNDERPASS	I90 SEP																							N
P	2	24B1	1611		UNDERPASS	I90 SEP																							N
P	2	24B1	1642		UNDERPASS	CARDWELL INT I90																							N
P	2	2481	1643		UNDERPASS	CARDWELL INT I90																							N
P	2	24B1	2492	38	T T TRESTLE	COLBERT CR	G	G	G		G	G		G		G		G			F	G	G	F	F		P	G	

		A		FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	2	2481	2517	7	T T TRESTLE	STOCKPASS	F	G	G		G	G		G	G	G		G			F	G	G	G	F		P	G		
P	2	2481	2526	76	T T TRESTLE	BIG PIPESTONE CR	F	G	G		G	G		G	G	G		G			F	G	G	G	F		P	G		
P	2	2481	2529	7	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	F		P	G		
P	2	2481	2530	113	CONCRETE T BEAM	NP RY	F		G		G	G					G				G	G	G	G	P			G		
P	2	2481	2580	64	CONC T BEAM	WHITETAIL CR																							N	
P	2	2909	2909	235	PRE CONC BEAM	INT I-90	G		E		E	E					E			E	E		E	E	E	G	E	E		X
P	2	2909	2915	220	CONT ST GIRDER	MADISON R	G		G	G		G	G	G	F	G	G			G	G	G	G	G	G	G	G	G		
P	2	2909	2922	100	CONCRETE SLAB	MID FK MADISON R	G		P		F	G		G	F	G					P	G	F	F	P		P	P		
P	2	2909	2928	80	CONCRETE SLAB	E FK MADISON R	G		P		P	G		G	F	G					P	G	F	F	P		P	P		
P	2	2909	2936	80	CONCRETE SLAB	REY CR	G		P		F	F		G		G					P	G	F	F	P		P	P		
P	2	2909	2959	77	CONCRETE T BEAM	SEP-CO RD	G		G		G	G					G				G	G	G	G	F			G		
P	2	2909	2960	343	CONCRETE T BEAM	NP RY	G		G			G					G			P	F	F	G	G	F	G	F	F		X
P	2	7060	7062	162	STEEL GIRDER	BA&P CMSTP&P RR	G		G			G					G			G	G	G	G	G	G	G	F	G		
P	2	7060	7068		UNDERPASS	CMSTP&P RR	G		G		G	G					G			G		G	G	G	G		F	G		
P	2	7081	7083		UNDERPASS	NP RY	G		G		G	G					G			G		G	G	G	G		F	G		
P	2	7081	7096		UNDERPASS*	HARRISON AVE INT	E		E		E	E					E			E	E		E	E	E	G	F	E		
P	2	7081	7096A		UNDERPASS	HARRISON AVE INT	E		E		E	E					E			E	E		E	E	E	G	F	E		
P	2	7096	7096		UNDERPASS*	HARRISON AVE INT	E		E		E	E					E			E	E		E	E	E	G	F	E		
P	2	7096	7096A		UNDERPASS	HARRISON AVE INT	E		E		E	E					E			E	E		E	E	E	G	F	E		

	3	1276	1290	157	STEEL BEAM	NP RY	F		G			G					G		P	P		G	G	F	G	G	F	X
	3	1276	1291	158	T T TRESTLE	CLARK FORK	G	G	G			G		G		G		P		P		G	G	G			G	X
	3	1276	1292	145	CONT STEEL BEAM	NP RY	G		F			G					G		P	P		G	G	G	G	G	G	X
	3	1276	1299	126	STEEL GIRDER	GN RY	G		G			G					G		G	G	G	G	G	G	G	F	G	
	3	1276	1300	25	CONCRETE T BEAM	DRY WASH	G		G		G	G		F	G	G	G			G	G	G	G	G			G	
	3	1935	1935	261	STEEL GIRDER	CAPITOL INT-I 15	G		E		E	E					E		F	E		E	E	E	G	G	G	X
	3	1935	1935P	261	STEEL GIRDER	CAPITOL INT-I 15	G		E		E	E					E		F	E		E	E	E	G	G	G	X
	3	1958	1960	83	CONCRETE T BEAM	GN RY	G		G		G	F					F			G	G	G	G	G			G	
	3	1958	1961	119	CONCRETE T BEAM	NP RY	G		F		P	P					G		G	G	G	G	F	G			F	X
P	3	1966	1972	23	STEEL & CONC	HELENA VALLEY CA	G		G		G	G		G		G				G	G	G	G	G		G	G	
P	3	1966	1978	67	CONCRETE T BEAM	TEN MILE CR	G		G		F	G		G		G	F		G	G	G	G	G	G			G	
P	3	1966	2036	205	PRE CONC BEAM	LINCOLN INT-I 15	G		E		E	E					E		E	E	E	E	E	E	G	G	E	
P	8	0000	0062	462	STEEL GIRDER	LIT BLFT R-NP RY	G		G	G		G	G	G		G	G		P	G	G	G	G	G	G	F	G	X
P	8	0000	0118	107	CONCRETE T BEAM	LIT BLACKFOOT R	F		P		G	F		G	F	G	F			P	G	G	F	P			P	X
P	8	0000	0132	95	CONCRETE T BEAM	LIT BLACKFOOT R	F		P		G	F		G	F	G	F			P	G	G	F	P			P	
P	8	0000	0222	59	CONCRETE T BEAM	LIT BLACKFOOT R	F		P		G	F		G	F	G	F			P	G	G	F	P			P	X
P	8	0000	0369	102	CONCRETE T BEAM	TENMILE CR	G		G		F	G		G	G	G	G		G	G	G	G	G	G			G	
P	8	0454	0478	149	CONCRETE T BEAM	GN RY	G		G			G					G		G	G	G	G	G	G	G		G	

				FEET B	C	D	E	F	BENTS G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	8	0454	0479	212	CONCRETE T BEAM	NP RY	G		G			G					G			G	F	G	G	G	G	G		G		
P	8	0454	0492	65	CONCRETE T BEAM	PRICKLY PEAR CR	G		G		G	G		G		G	G				G	G	G	G	G			G		
P	8	0454	0592	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	F		G	G		
P	8	0454	0607	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	F		G	G		
P	8	0454	0763	500	CONT PL GIRDER	MISSOURI R	G		G	G		G	G	G		G	G	G		G	G	G	G	G	G	G	F	G		
P	8	0775	0788	22	CONCRETE SLAB	IRRIGATION CA	F		G		G	G		G		G					G	P	G	G	G			G		
P	8	0775	0800	66	CONCRETE T BEAM	DEEP CR	G		F		G	G		G		G	G				G	P	F	G	G			F		
P	8	0775	0806	22	CONCRETE SLAB	DEEP CR OF	G		G		F	G		G		G					G	F	G	G	G			G		
P	8	0775	0872	22	CONCRETE SLAB	SIX MILE CR	G		G		G	G		G		G					G	F	G	G	G			G		
P	8	0775	0880	386	CONCRETE T BEAM	NP RY	F		G			G					G			G	G	F	G	G	G	G	G	G		
P	8	0775	0882	690	STEEL GIRDER	MISSOURI R	G		G	G		G	G	G	G	G	G			G	G	F	G	G	G	G	F	G		
P	8	0775	1079	295	CONT CON GIRD	INT I90 FUTURE																							N	
P	8	1093	1095	206	PRE CONC BEAM	GN RY	G		G		G	G					G			G	G		G	G	G		F	G		
P	8	1093	1095P	206	CONCRETE T BEAM	GN RY	G		F			G					G			G	G		G	F	G	G		G		
P	14	0000	0065	7	T T TRESTLE	STOCKPASS	G	F	F		G	G						P			F	G	G	F	F		F	P		X
P	14	0000	0073	7	T T TRESTLE	STOCKPASS	G	G	G		F	G						P			G	G	G	P	G		F	P		X
P	14	0000	0090	7	T T TRESTLE	STOCKPASS	G	F	P		F	G						F			F	G	F	F	F		F	P		X
P	14	0000	0111	57	T T TRESTLE	DEEP CR	G	G	F		G	G	G	G		G		G			G	G	G	P	F		G	F		

	FEET					BENTS	PIERS		BA		DR									MA							
A	B			E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S		U	V	W			Z	Z	ZZ
P 19 0000 0000	276	PRE CONC 8EAM	ANACONDA INT-I90	G		E		E	E					E			E	E	E	E	E	E	G	E	E		
P 19 0000 0000T	276	PRE CONC 8EAM	ANACONDA INT-I90	G		E		E	E					E			E	E	E	E	E	E	G	E	E		
P 19 0000 0003	148	PRE CONC 8EAM	NP RY	G		E		E	E					E			E	E	E	E	E	E		E	E		
P 19 0000 0003P	148	PRE CONC 8EAM	NP RY	G		E		E	E					E			E	E	E	E	E	E		E	E		
P 19 0000 0005	70	PRE CONC BEAM	CLARK FORK	G		E		E	E		G	E	G	E			E	E	E	E	E	E		E	E		
P 19 0000 0005P	70	PRE CONC 8EAM	CLARK FORK	G		E		E	E		G	E	G	E			E	E	E	E	E	E		E	E		
P 19 0055 0105	41	CONCRETE T 8EAM	WARM SPRINGS CR	G		G		G	G		G		G	G				G	G	G	G	G			G		
P 19 0055 0169	41	CONCRETE T 8EAM	WARM SPRINGS CR	G		G		G	G		G		G	G				G	G	G	G	G			G		
P 29 0000 0178	38	T T TRESTLE	GRANITE CR	G	G	G		G	G		G	F	G		G			P	G	G	G	F		F	G		
P 29 0000 0182	38	T T TRESTLE	MCNEAL GULCH	G	G	G		G	G		G	F	G		G			P	G	G	G	F		F	G		
P 29 0000 0187	57	T T TRESTLE	WATER GULCH	G	G	G		G	G		G	P	F		F			G	G	G	F	F		F	F		
P 29 0000 0258	38	T T TRESTLE	ALDER CR	G	G	G		G	G		G		G		G			G	G	G	G	F		F	G		
P 29 0000 0267	19	T T TRESTLE	CALIFORNIA CR	G	G	G		G	G		G		G		G			G	G	G	G	F		F	G		
P 29 0000 0284	38	T T TRESTLE	RAMSHORN CR	G	G	G		G	G		G	F	G		G			G	G	G	G	F		F	G		
P 29 0000 0303	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	F	F		F	G		
P 29 0000 0341	19	T T TRESTLE	INDIAN CR	G	G	G		F	G		G	G	G		G			G	G	G	G	F		F	G		
P 29 0000 0343	19	T T TRESTLE	INDIAN CR	G	G	G		F	G		G	G	G		G			G	G	G	G	F		F	G		
P 29 0000 0372	57	T T TRESTLE	WISCONSIN CR	G	G	G		F	G		G	G	G		G			G	G	G	G	F		F	G		

P 29 0428 0498	358	ST PONY TRUSS	JEFFERSON R	G		G	F		G	G	G		G		G	G	G	G	G	G	G	G	G	G	G		
P 29 0428 0499	25	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G		G		F			F	G	G	G	F		P	G		
P 29 0428 0503	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		F			G	G	F	F	G		P	F		X
P 29 0428 0507	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		F			F	G	G	F	F		P	F		
P 29 0428 0509	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		F			P	G	G	F	F		P	F		
P 29 0428 0513	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	F	F		P	G		
P 29 0428 0516	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	P	F	F		P	F		
P 29 0428 0519	25	T T TRESTLE	DRY WASH	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
P 29 0428 0521	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 29 0428 0522	25	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 29 0428 0531	19	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 29 0428 0533	25	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 29 0428 0536	25	T T TRESTLE	CHERRY CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 29 0428 0549	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
P 29 0428 0550	19	T T TRESTLE	CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 29 0428 0553	19	T T TRESTLE	CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 29 0428 0557	19	T T TRESTLE	CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 29 0428 0564	19	T T TRESTLE	CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 29 0428 0571	57	T T TRESTLE	LITTLE CHERRY CR	G	G	G		G	G		G	F	G		G			G	G	G	G	F		P	G		

P	29	0428	0573	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G
P	29	0428	0598	57	T T TRESTLE	FISH CR	G	G	G		G	G		G	F	F		G			G	G	G	G	G		P	G
P	29	0428	0632	136	STEEL BEAM	CMSTP&P RY	G		G			G				G				G	G	G	G	G	G	G		G
P	29	0428	0655	76	T T TRESTLE	LIT PIPESTONE CR	G	G	G		G	G		G		G		G			G	G	G	G	F		P	G
P	46	0000	0090	60	REINF CONC SLAB	TRAIL CR	G		E		E	E		G	E	G					E	G	E	E	E			E
P	46	0000	0098	60	REINF CONC SLAB	TRAIL CR	G		E		E			G	E	G					E	G	E	E	E			E
P	46	0000	0141	60	REINF CONC SLAB	TRAIL CR	G		E		E			G	E	G					E	G	E	E	E			E
P	46	0000	0158	60	REINF CONC SLAB	RUBY CR	G		E		E			G	E	G					E	G	E	E	E			E
P	46	0000	0258	215	PRE CONC BEAM	BIG HOLE R	G		E	E	E	E	E	E		G	E			E	E	E	E	E	E	G	G	E
P	46	0000	0276	38	T T TRESTLE	STEEL CR	G	G	G		G	G	G	G		G		G			G	G	G	G	G		G	G
P	46	0000	0419	235	PRE CONC BEAM	BIG HOLE R	G		E	E	E	E	E	G	G	G	E			E	E	E	E	E	E	G	E	E
P	46	0000	0485	57	T T TRESTLE	FISHTRAP CR	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		G	G
P	46	0000	0502	81	T T TRESTLE	LAMARCHE CR	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		G	G
P	46	0000	0531	38	T T TRESTLE	SEYMOUR CR	G	G	G		G	G	G	G		G		G			G	G	G	G	G		G	G
P	46	0000	0543	75	T T TRESTLE	DEEP CR	G	G	G		G	G	G	G		G		G			G	G	G	G	G		G	G
P	46	0000	0580	325	RIV ST PL GIR	BIG HOLE R	G		G	G	E	E	E	G	E	G	E			E	E	E	E	E	G	E	G	E
P	46	0000	0649	29	STEEL I BEAM	BRANCH OF WISE R	G		G		G	G		G		G	G					F	G	G	F		F	G
P	46	0000	0651	44	STEEL I BEAM	BRANCH OF WISE R	F		G		G	G		G		G	G					F	G	G	F		F	G

A	B	C	D	E	F	G	H		J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P 46 0000 0652	43	STEEL I BEAM	BRANCH OF WISE R	G		G		G	G		G		G	G					F	G	G	F		F	G		
P 46 0000 0749	304	PRE CONC BEAM	BIG HOLE R																								N
P 46 0000 0769	38	T T TRESTLE	DIVIDE CR	G	E	G		E	G		G		G		G			G	G	G	G	G		F	G		
P 49 0000 0033	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			F	G	G	G	F		G	G		
P 49 0000 0069	25	T T TRESTLE	IRRIGATION DITCH	G	G	G		G	G		G	G	G		G			F	F	F	F	F		G	G		
P 49 0000 0090	38	T T TRESTLE	STONE CR	G	G	G		G	G		G	G	G		G			F	F	F	G	F		G	G		
P 49 0000 0147	150	STEEL GIRDER	BEAVERHEAD R	G		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
P 49 0000 0273	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			F	G	G	G	G		G	G		
P 49 0000 0275	181	STEEL GIRDER	BEAVERHEAD R	G		G	G		G	G	G		G	G			G	G	G	G	G	G	G	F	G		

M401 0000 0002	76	T	T	TRESTLE	PIPESTONE CR	G	G	G	G	G	G	G	G	G	G	G	G	G	P	G
M401 0000 0084	38	T	T	TRESTLE	FISH CR	G	G	G	G	G	G	G	G	G	G	G	G	G	P	G

BRIDGE CONDITION REPORT

				E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S272 0000 0117	38	T T TRESTLE	THE RHINE CR	G	G	G		G	G		G	G	G		G			G	P	F	F	P		P	F		X
S272 0000 0133	57	T T TRESTLE	NEVADA CR	G	G	G		G	G		F	F	G		G			F	P	G	G	F		P	F		
S273 0000 0007	42	STEEL I BEAM	WARM SPRINGS CR	G		F	F	F	G		G		G	F					P	F	P	P		P	P		X
S274 0000 0016	25	T T TRESTLE	MILL CR	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		
S274 0000 0122	57	T T TRESTLE	BIG CALIF CR	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		
S274 0000 0164	57	T T TRESTLE	FRENCH GULCH	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		
S274 0000 0198	57	T T TRESTLE	FRENCH GULCH	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		
S275 0000 0018	30	T T TRESTLE	WILLOW CR																								R
S275 0000 0021	37	T TRUSS SPAN	CLARK FORK																								N
S275 0000 0023	246	PRE CONC BEAM	SEP-I90	G		E		E	E					E			E	E	E	E	E	E	E	E	E		
S278 0000 0186	50	T T TRESTLE	GRASSHOPPER CR	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
S278 0000 0432	35	UNT LOG TRESTLE	WARM SPRINGS CR	G	F	F		F	F		G		G		F				P	F	P	P			F		
S278 0000 0433	37	CONC & STEEL	DRAINAGE	G		F		G	G		G		G	G					P	G	G	G		P	G		
S279 0000 0178	57	T T TRESTLE	LT PRICKLY PEAR	G	G	G		G	G		G		G		G			G	F	G	G	G		F	G		

A			D	E	F	G	H		J		L	M	N	O	P	Q	R	S		U	V	W			Z		
S279 0000 0199	57	T T TRESTLE	CANYON CR	G	G	G		G	G		P		G		G			G	F	G	G	F		F	G		
S279 0000 0211	57	T T TRESTLE	CANYON CR	G	G	G		P	P		G	F	F		G			G	F	F	F	F		F	F		
S279 0000 0216	63	T T TRESTLE	CANYON CR	G	G	G		F	F		G	G	G		G			G	F	G	F	F		F	G		
S280 0000 0004	215	PRE CONC BEAM	SEP-I15 YORK RD	G		E		E	E					E			E	E	E	E	E	E	E	G	E		
S280 0000 0013	34	T T TRESTLE	HELENA VALLEY CA	G	G		G	G	G		G		G		G			G	F	G	G	F		P	G		
S280 0000 0026	31	STEEL I BEAM	PRICKLY PEAR CR	G		F	F		F	P	G		G	G						G	G	F		F	F		
S280 0000 0146	545	ST THRU TRUSS	MISSOURI R	G		F	F	G	F	G	G		G		F	F	F			F	G	F		F	F		
S281 0000 0027	57	T T TRESTLE	LITTLE BOULDER R	G	G	G		G	G	G	G	G	G		F			G	P	G	G	F		P	G		X
S284 0000 0047	72	T T TRESTLE	HELENA VALLEY CA	G	G	G	G		G		G		G		G			G	F	G	G	G		P	G		
S284 0000 0089	1000	CONCRETE DAM	MISSOURI R	G			G	G	G	G	G		G	G			G	G	G	G	G	G	F	G	G		
S285 0000 0064	25	T T TRESTLE	CROW CR	G	G	G		G	G		G	G	G		G			G	P	G	G	F		P	G		
S286 0000 0030	154	ST PRATT TRUSS	GALLATIN R	F		F	F	G	G	G	G	F	G		G	G	P	F	P	G	G	F	G	P	F		X
S287 0000 0079	25	T T TRESTLE	WILLOW CR	G	G	G		G	G		G		G		G			G	P	G	G	F		P	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

A	B			F	F	G	H			K		M	N				R	S		U		W					
S324 0000 0001	133	PRE CONC BEAM	INT-I 15	G		E		E	E					E			P	E	E	E	E	E	G	G	G		X
S324 0000 0045	92	PRE CONC BEAM	HORSE PRAIRIE CR	G		E		E	E		G	G	G	E			E	E	E	E	E	E			E	E	
S324 0000 0051	71	PRE CONC BEAM	HORSE PRAIRE CR	G		E		E	E		G	G	G	E			E	E	E	E	E	E		E	E		
S324 0000 0069	71	PRE CONC BEAM	MEDICINELODGE CR	G		E		E	E		G	G	G	E			E	E	E	E	E	E		E	E		
S356 0000 0001	65	ST PONY TRUSS	TENMILE CR	G		G		G	G		G		G		G	F	P		P	G	F	G		P	F		X
S356 0000 0035	28	STEEL I BEAM	SEVENMILE CR	G		G		G	G		G		G	G					P	G	F	F		G	G		
S359 0000 0003	112	PRE CONC BEAM	JEFFERSON R SL																							N	
S359 0000 0012	289	PRE CONC BM	JEFFERSON R	E		E	E	E	E	E	E	E	E	E			G	E	G	G	E	E	E		E		
S359 0000 0017	38	T T TRESTLE	SLOUGH	G	G	G		F	G		G		G		G			P	P	G	G	F		P	G		X
S359 0000 0050	50	T T TRESTLE	SOUTH BOULDER R	G	G	G		F	G		P		G		G			P	P	G	G	F		F	G		X
S375 0000 0055	266	PRE CONC BEAMS	9 MI SEP-I15	E		E		E	E					E			E	E	E	E	E	E	G	F	E		
S375 0000 0081		UNDERPASS	NP RY	G		G	G	G	G					G			G			G	G	G		G	G		
S375 0000 0083	215	PRE CONC BEAMS	NP RY	G		G		G	G					G			G	G	P	G	G	G		F	G		
S399 0000 0004	121	STEEL GIRDER	BOULDER R	F		G	G		G	G	G	G	G	G			G	G	F	G	G	G	G	F	G		
S399 0000 0236	32	STEEL I BEAM	WHITETAIL CR	G		G		G	G		G	G	G					F	P	F	F	F		P	F		

				E	F	G	H			K		M	N			O	R	S		U	V	W					
S399 0000 0259		UNDERPASS*	WHITEHALL INT 90	G		E		E	E					E			E	E		E	E	E	E	G	E		
S399 0000 0260		UNDERPASS*	WHITEHALL INT 90	G		E		E	E					E			E	E		E	E	E	E	G	E		
S403 0000 0008	76	T T TRESTLE	BA & P RY	G		G		F	G						P			F	F	F	G	F		P	F		
S403 0000 0011		UNDERPASS	CROSSWALK			F								G				F		F	F	F		F	F		
S407 0000 0002	54	ST HOWE TRUSS	LIT BLACKFOOT R	F				F	P		G		G		G	G	G			G	G	F		P	P		X
S422 0000 0001	285	ST THRU TRUSS	JEFFERSON R	F		F	F		F	F	G	F	F		G	F	F	F	P	F	F	G		P	F		
S422 0000 0015	60	UNT T TRESTLE	JEFFERSON R OF	F	P	F		P	F		G		F		F				P	P	P	P		P	P		
S422 0000 0086	245	PRE CONC BEAMS	JEFFERSON R	G		E	E	E	E	E	F	G	G	G			E	E	F	E	E	E	G	G	G		
S423 0000 0001	210	PRE CONC BEAMS	VICTOR INT-I15	E		E		E	E					E			E	E	E	E	E	E	E	F	E		
S423 0000 0003	231	STEEL GIRDER	UPRR	G		G		G	G					G			G	G	G	G	G	G	G	G	G		
S433 0000 0005	32	CONCRETE SLAB	PRICKLY PEAR CR	G		G		G	G		G		G					G	P	G	G	G		F	G		
S433 0000 0018	42	CONC & TIMBER	HELENA VALLEY CA	G		G		G	G		G		G		G			G	G	G	G	G		F	G		
S441 0000 0022	32	CONCRETE T BEAM	CLARK FORK	G		F		F	P		G		G	F						F	F	F			F		

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	AA
S441 0000 0042	265	PRE CONC BEAM	GREGSON INT I90	G		E		E	E					E			E	E	E	E	E	E	E	E	E	
S481 0000 0000	285	PRE CONC BEAM	SEP I-15																							N
S509 0000 0001		UNDERPASS	MONIDA INT I15	G		E		E	E					E			E	E	E	E	E	E	E	G	E	
S518 0000 0000	297	PRE CONC BEAM	MONT CITY INT																							N
S526 0000 0002	190	PRE CONC BEAM	GALLATIN R	G		E	E	E	E	E	G	E	G	G			E	E	G	E	E	E		G	E	

BUTTE DIVISION

I-15-0000-0015	281' Pre Conc Beam	UP R.R.	Rocker shoes are in expanded position instead of contracted position for temperature below 60 degrees. Lean of approximately 1½ inches.
I-15-0000-0147	450 Plate Girder	UP R.R.	Rocker shoes are in expanded position instead of contracted position for temperature below 60 degrees. Lean of approximately 1½ inches.
I-15-0000-0232	22' Concrete Slab	Big Sheep Creek	Minor spalling on wing and backwalls. Railing not uniform.
I-15-0000-0443	Underpass	Int. OR 324	Rocker shoes are in expanded position instead of contracted position for temperature below 60 degrees.
I-15-0000-0458	401' Welded Plate Girder	Beaverhead River	South edge of bridge deck needs to be raised approximately 7". This work scheduled for spring of 1969.
I-15-0000-0629	163' Pre. Conc. Beams	Beaverhead River	Numerous hair cracks in deck.
I-15-0000-0610	143' Conc. T. Beam	UP R.R.	First span on west end has shifted to the north approximately 1¼". Cap on west side has minor spalling. Rocker shoes are in expanded position instead of contracted position for temperature below 60 degrees.
I-15-0644-0700	66' Conc. T. Beam	Frying Pan Basin Creek	North end has settlement of approximately 3 inches.
I-15-0644-0873	238' Steel Truss	Big Hole River	Span on east end shifted downstream approximately 2" and is bearing away from diaphram on pier. Beams on north end span appears to be ruptured. Rocker shoes are locked to extent that they are not functioning. Wheel guard has crumbled to extent that reinforcing steel is exposed. Piers are spalling badly.
I-15-1266-1268S	Underpass	W. Butte Int. I-115	Rocker shoes are in expanded position instead of contracted position for temperature below 60 degrees.
I-15-1359-1708	7' T. T. Trestle	Stockpass	One broken stringer
I-15-1359-1730	7' T. T. Trestle	Stockpass	One broken stringer.

BUTTE DIVISION

I-90-1765-1767 204' Cont. Roll BM N.P. R.R.
Fillet under expansion joint badly deteriorated- unable to hold expansion joint. See photo.

I-90-1765-1821 20' Concrete Slab Jr. Grade Sep. - Co. Rd.
Wing walls pushing out from fill at joint with backwall.

I-90-1865-1876 118' Pre Conc. Beam Sep. Milwaukee Avenue
Expansion joints are very loose.

I-15-1953-1965 Underpass Cedar Street Int.
Rocker shoes are in expanded position instead of contracted position for temperature below 60 degrees.

I-15-1953-1965-A Underpass Ceder Street Int.
Rocker shoes are in expanded position instead of contracted position for temperature below 60 degrees.

I-90-2702-2772 7' T. T. Trestle Stockpass
Curbing in poor condition, leaning away from roadway.

I-90-2702-2779 7' T.T. Trestle Stockpass
Wing walls in poor condition, curbing leaning away from roadway.

I-115-4038-4040-R 244' Steel Girder West Butte Int. I-90
Rocker shoes are in expanded position instead of contracted position for temperature below 60 degrees.

P-2-2909-2909 235'Pre-Conc. Beam Int I-90
Bridge condition rating taken from 1966 inspection report.

P-2-2909-2960 343' Conc. T. Beam NP R.R.
Center span out of alignment. Shoes are in expanded position instead of contracted position for temperature below 60 degrees.

P-3-1276-1290 157' Steel Beam NP R.R.
Shoes are in expanded position instead of contracted position for temperature below 60 degrees.

P-3-1276-1291 158' T.T. Trestle Clark Fork River
One broken stringer.

BUTTE DIVISION

P-3-1276-1292 145' Conc Steel Beam N.P. R.R.
Shoes are in expanded position instead of contracted position for temperature below 60 degrees.

P-3-1935-1935 261' St Girder Capitol Int.
Shoes are in expanded position instead of contracted position for temperature below 60 degrees.

P-3-1935-1935P 261' St Girder Capitol Int.
Shoes are in expanded position for temperature below 60 degrees.

P-3-1958-1961 119' Conc T. Beam N.P. R.R.
Wingwall and backwall badly cracked and appear to be moving. See photos.

P-8-0000-0062 462' Steel Girder Little Blackfoot River & G.N. R.R.
Shoes are in expanded position instead of contracted position for temperature below 60 degrees.

P-8-0000-0118 107' Conc. T. Beam Little Blackfoot River
Bridge Department recommended early replacement in 1968. Concrete in structure poor and deteriorated condition throughout structure. Center span moved upstream approximately 3 inches. See photo.

P-8-0000-0222 59' Conc T. Beam Little Blackfoot River
Bridge department recommended early replacement in 1968. Concrete throughout entire structure poor and in deteriorated condition.

P-14-0000-0065 7' T.T. Trestle Stockpass
Seven broken stringers.

P-14-0000-0073 7' T. T. Trestle Stockpass
Four broken stringers.

P-14-0000-0090 7' T.T. Trestle Stockpass
One broken stringer. Piles appear to be pushing in at top causing cap to tip allowing deck to move under heavier loads.

P-29-0428-0503 19' T.T. Trestle Drainage
Bridge has been previously widened, deck separating on left edge. See photo

BUTTE DIVISION

S-272-0000-0117 38' T.T. Trestle Rhine Creek
One broken stringer. Railing on west end broken away from structure. See photo.

S-273-0000-0007 42' St I Beam Warm Springs Creek
Concrete deteriorated badly throughout entire structure. Railing in poor condition, broken, NW section missing completely. See photos.

S-281-0000-0027 57' T. T. Trestle Little Boulder River
One broken stringer.

S-286-0000-0030 154' St Pratt Truss Gallatin River
Shoes are in expanded position instead of contracted position for temperature below 60 degrees.

S-324-0000-0001 133' Pre Conc Beam Int I-15
Shoes are in expanded position instead of contracted position for temperature below 60 degrees.

S-356-0000-0001 65' St Pony Truss Ten Mile Creek
Shoes are in expanded position instead of contracted position for temperature below 60 degrees.

S-359-0000-0017 38' T. T. Trestle Slough
Bolts which fasten curbing to deck are missing, no markers.

S-359-0000-0050 50' T. T. Trestle South Boulder River
Bolts which fasten curbing to deck are missing, no markers.

S-407-0000-0002 54' St. Howe Truss Little Blackfoot River
Crack on backwalls both ends extending through entire wall. See photos.

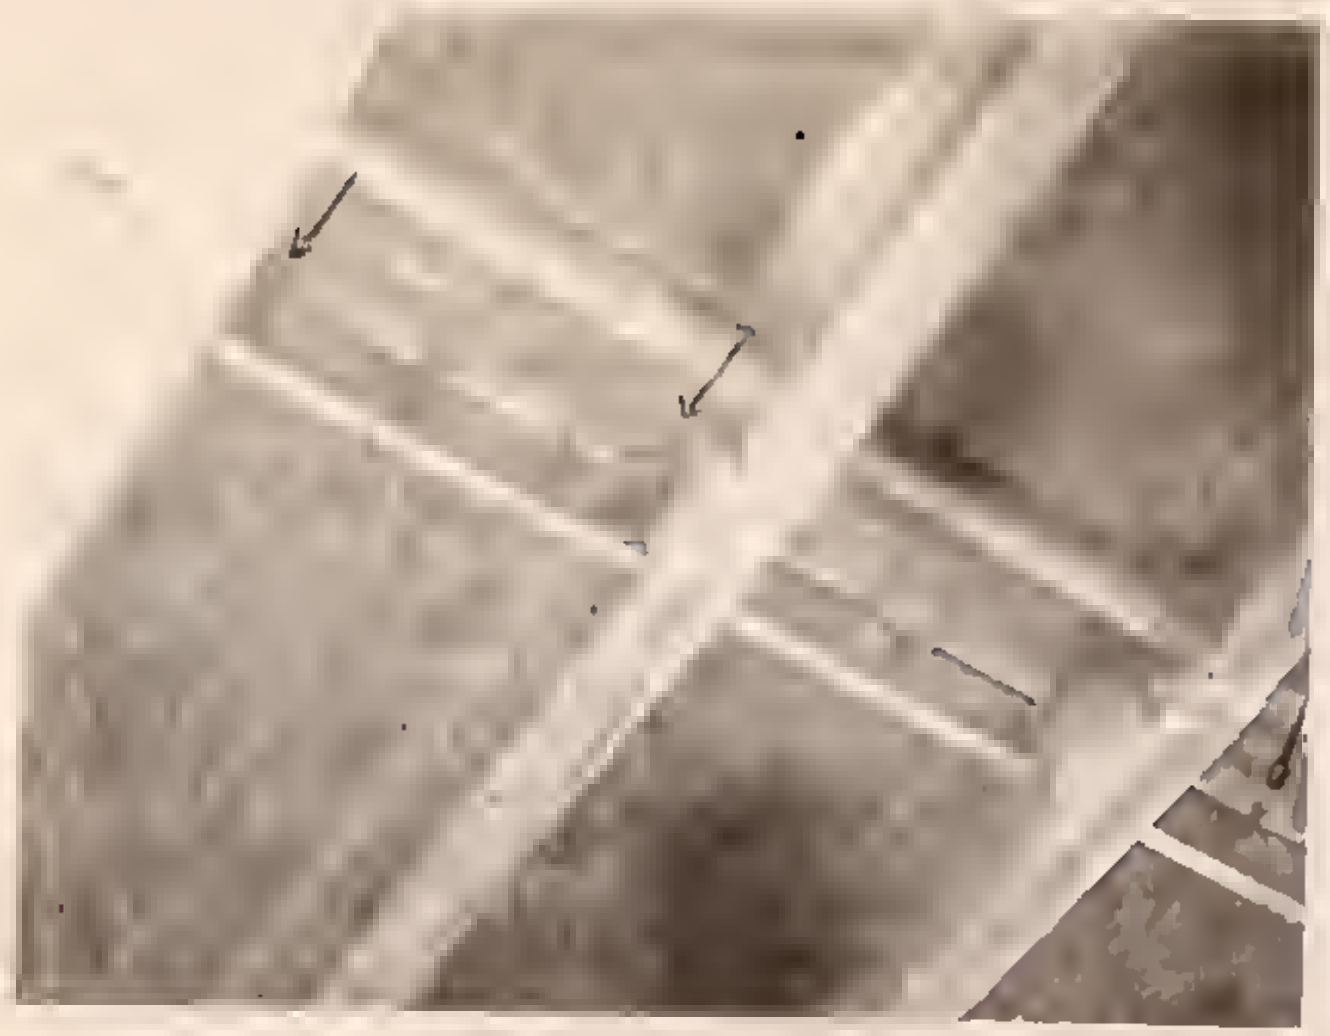

I-90-1765-1767

P-3-1958-1961

P-3-1958-1961

P-3-1958-1961

P-3-1958-1961

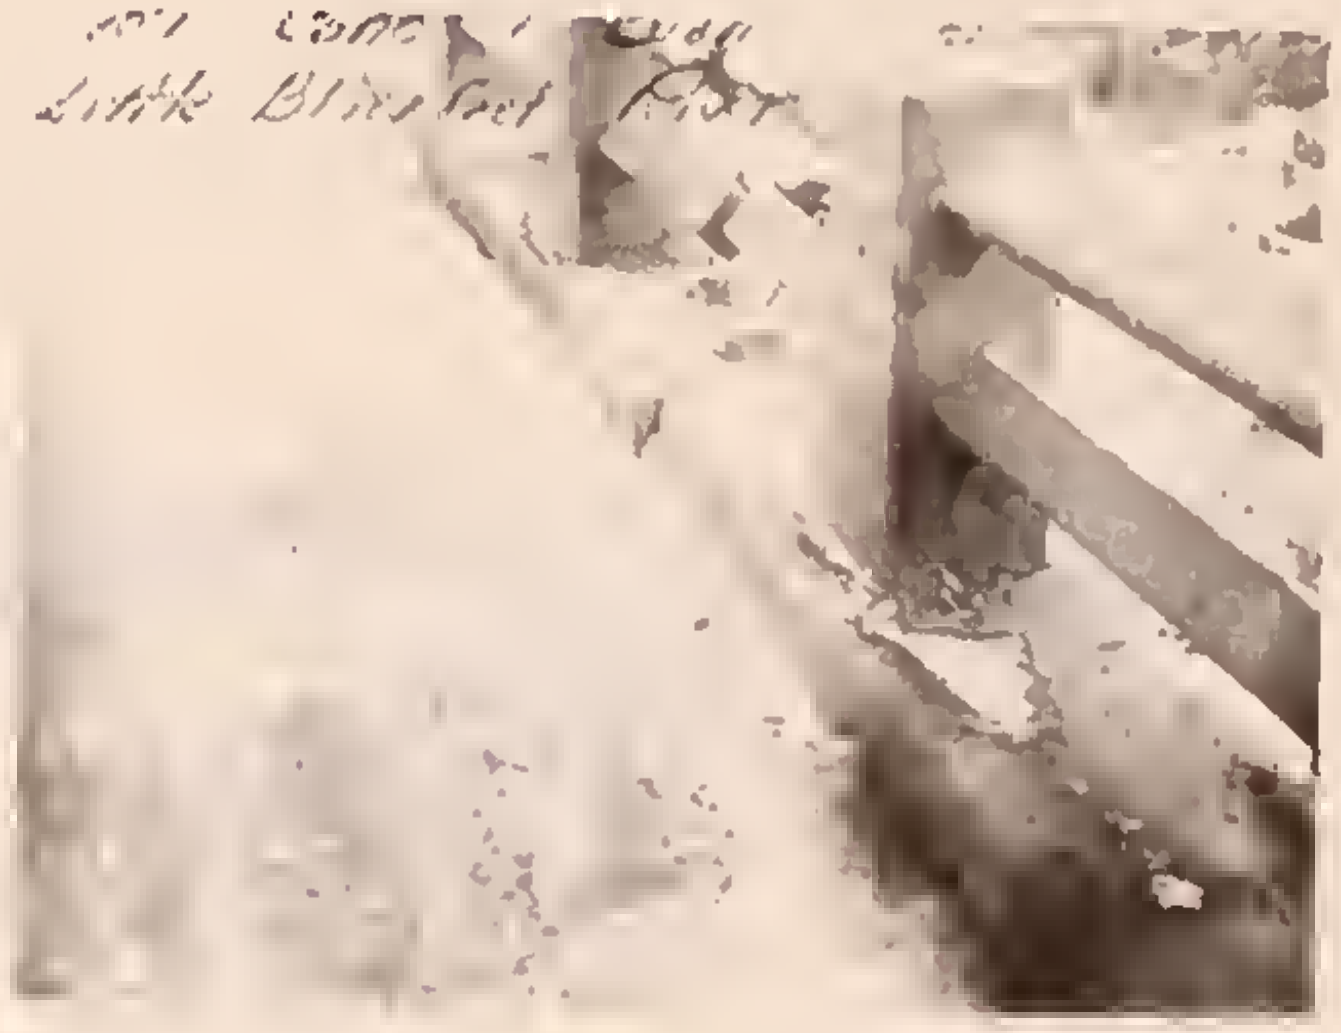

P-8-0000-0118

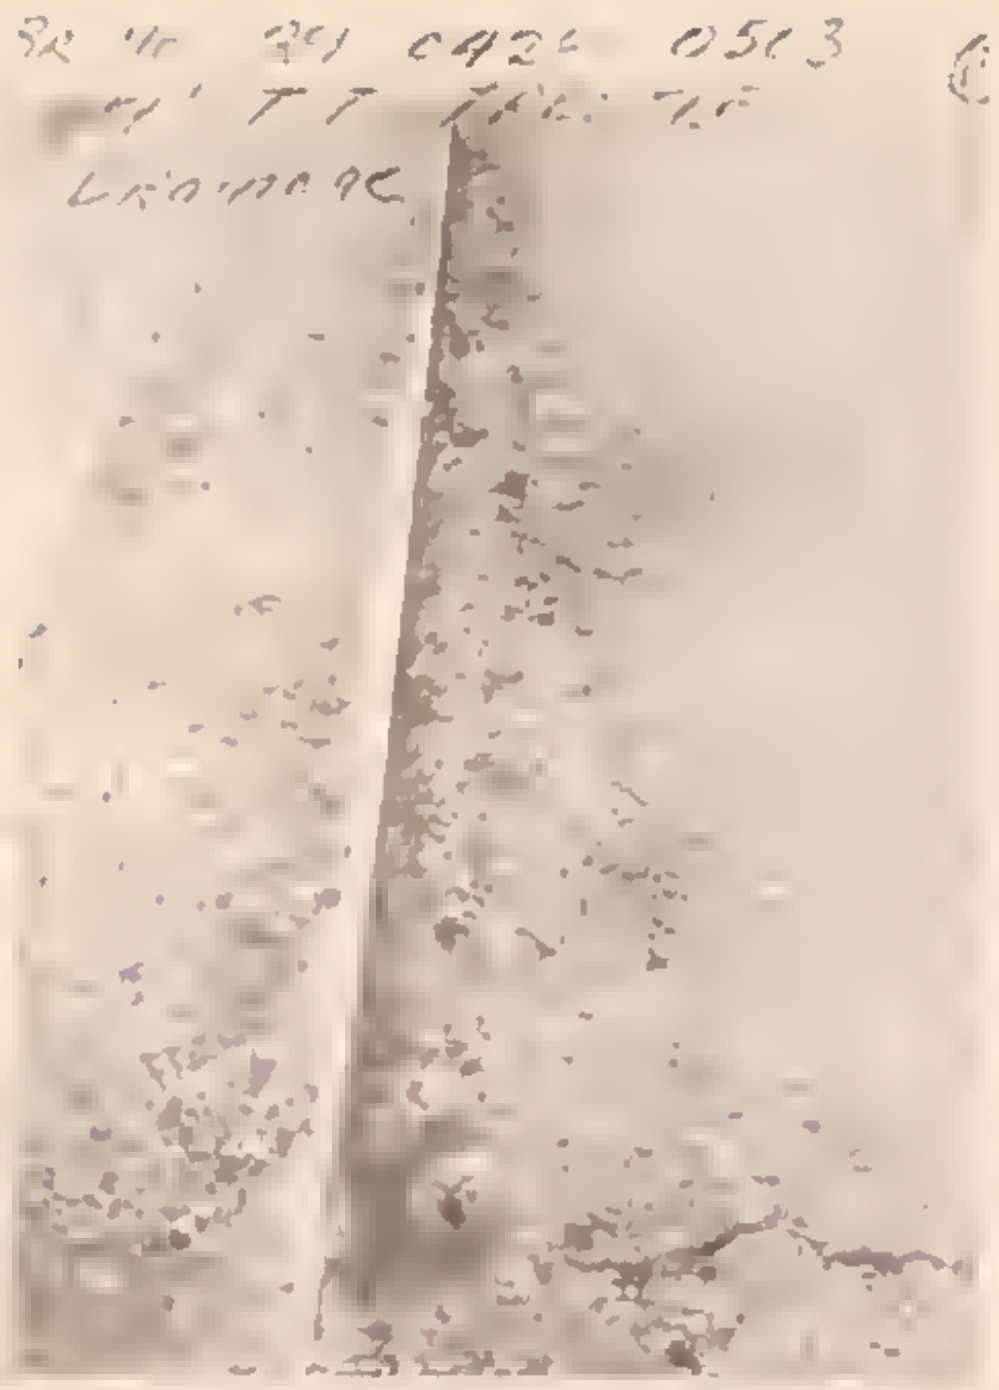

P-29-0428-0503

S-272-0000-0117

S-273-0000-0007

S-273-0000-0007

S-407-0000-0002

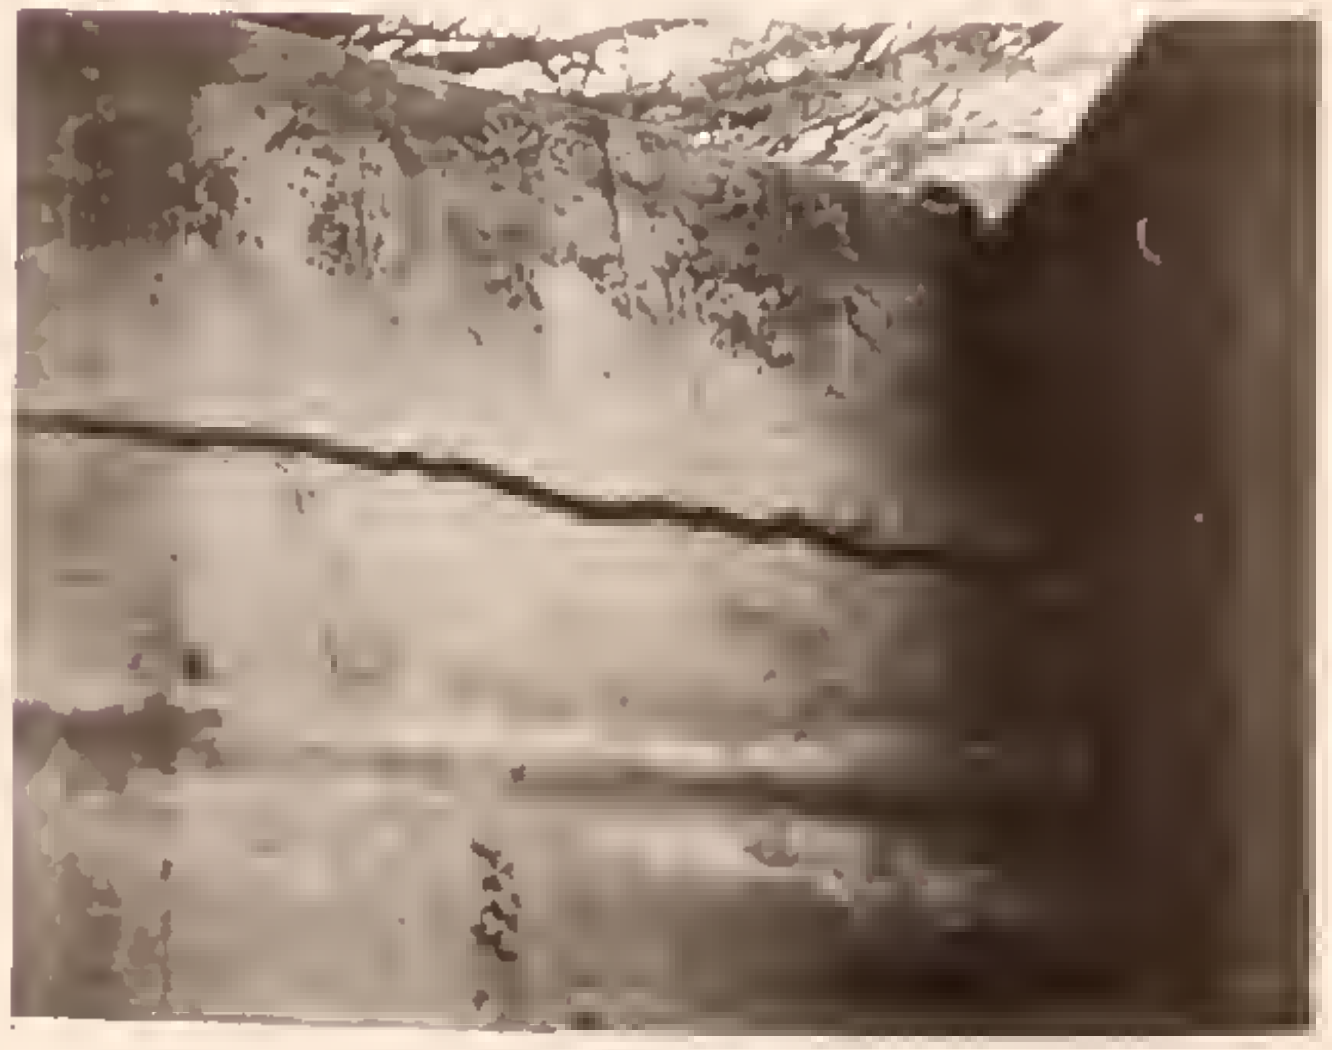

S-407-0000-0002

BOZEMAN CONSTRUCTION DIVISION

F A SYSTEM	F A ROUTE NUMBER	CONTROL-JUNCTION MILEPOST TO TENTHS	BRIDGE MILEPOST TO TENTH	DESCRIPTIVE	TOTAL LENGTH FEET	DESCRIPTION ... MAXIMUM ...	NAME OF FEATURE ...	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
A					B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I	90	2838	2888P		143	PRE CONC BEAM	LOGAN INT-CO RD	G		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2942			UNDERPASS	INT-OR 288	E		G		E	E					E			E	E		E		E	E	E	E		
I	90	2838	2942A			UNDERPASS	INT-OR 288																								
I	90	2838	2946		158	PRE CONC BEAM	CMSTP&P RR	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2946P		158	PRE CONC BEAM	CMSTP&P RR	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2948		163	PRE CONC BEAM	NP RY	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2948P		163	PRE CONC BEAM	NP RY	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2962		82	PRE CONC BEAM	CAMP CR	E		E	E	E	E	E	E	E	E	E			E	E		G		E		G	E		
I	90	2838	2962P		82	PRE CONC BEAM	CAMP CR	E		E	E	E	E	E	E	E	E	E			E	E		G		E		G	E		
I	90	2838	2963		92	PRE CONC BEAM	BAKER CR	E		E	E	E	E	E	E	E	E	E			E	E		G		E		G	E		
I	90	2838	2963P		92	PRE CONC BEAM	BAKER CR	E		E	E	E	E	E	E	E	E	E			E	E		G		E		G	E		
I	90	2838	2971		113	PRE CONC BEAM	HEEB LANE SEP-CO	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2971P		113	PRE CONC BEAM	HEEB LANE SEP-CO	E		E		E	E					E			E	E		G		E		G	E		
I	90	2838	2980		205	PRE CONC BEAM	W GALLATIN R	E		E	G	E	E	G	G	E	F	E			E	E		G		E		G	E		
I	90	2838	2980P		205	PRE CONC BEAM	W GALLATIN R	E		E	G	E	E	G	G	E	F	E			E	E		F		E		G	E		
I	90	2838	2990		113	PRE CONC BEAM	CENTRAL PARK SEP	E		E		E	E					E			E	E		E		E		G	E		
I	90	2838	2990P		113	PRE CONC BEAM	CENTRAL PARK SEP	E		E		E	E					E			E	E		E		E		G	E		
I	90	2838	3038			UNDERPASS	BELGRADE INT-291	E		E		E	E					E			E	E		E		E	G	G	E		
I	90	2838	3038A			UNDERPASS	BELGRADE INT-291																								

F.A.	NUMBER	CONTROL	BRIDGE	TOTAL LENGTH FEET	MAXIMUM SPAN	FEATURE	END FILL	PILE	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKER	DECK	BRAC	RA	EXP	P IN	GENERAL	NO SP	
	A			B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I	90	2838	3091	113	PRE CONC 8EAM	SEP CO RO	E		E		E	E					E			E	E		E		E		E	E		
I	90	2838	3091P	113	PRE CONC 8EAM	SEP CO RO	E		E		E	E					E			E	E		E		E		E	E		
I	90	2838	3125S	245	PRE CONC 8EAM	W 8OZEMAN INT	E		E		E	E					E			E	E		G		E	E	E	E		
I	90	2838	3132	351	WLD PL 136 GRO	NPRY & ROUSE ST																						E	N	
I	90	2838	3132P	351	WLD PL 136 GRD	NPRY & ROUSE ST																						E	N	
I	90	2838	3135	188	PRE CON 8M 70	MILW RY																						E	N	
I	90	2838	3135P	188	PRE CON 8M 70	MILW RY																						E	N	
I	90	2838	3136	143	PRE CON 8M 60	L ST																						E	N	
I	90	2838	3136P	143	PRE CON 8M 60	L ST																						E	N	
I	90	3137	3191	113	PRE CONC 8EAM	INT-CO RO	G		E		E	E					E			G	G	G	G	E	G	F	G	E		
I	90	3137	3191P	113	PRE CONC 8EAM	INT-CO RO	G		E		E	E					E			G	G	G	G	E	G	F	G	E		
I	90	3137	3197	338	ST GIROER	NP RY	G		G		E	E					G			G	G	G	G	E	G	F	F	G		
I	90	3137	3197P	328	ST GIRDER	NP RY	G		G		E	G					G			G	G	G	G	E	G	F	F	G		
I	90	3137	3225	128	PRE CONC 8EAM	INT-CO RO	G		G		E	E					G			G	G	G	G	G	F	F	F	G		
I	90	3137	3225P	128	PRE CONC 8EAM	INT-CO RD	G		G		E	E					G			G	G	G	G	G	F	F	F	G		
I	90	3137	3367	113	PRE CONC 8EAM	W INT-US 10	G		G		G	G					G			G	G	G	G		F	F	F	G		
I	90	3137	3367P	113	PRE CONC 8EAM	W INT-US 10	F		G		G	G					G			G	G	G	G	G	G	F	F	G		
I	90	3367	3386	251	PRE CONC 8EAM	S INT-US 89	G		G		G	G					G			E	G	G	G	G	G		F	G		
I	90	3367	3386P	251	PRE CONC 8EAM	S INT-US 89	G		G		G	G					G			E	G	G	G	G	G		F	G		

BRIDGE CONDITION REPORT

RATING

E - Excellent
G - Good
F - Fair
P - Poor

be removed
not inspected

FA SYSTEM	FA ROUTE NUMBER	CONTROL JUNCTION MILEPOST TO TENTH	BRIDGE MILEPOST TO TENTHS / DESCRIPTIVE	TOTAL LENGTH FEET	MATERIAL & TYPE	FEATURE	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION JOINTS	PAINT	GENERAL CONDITION	NO INSPECTION	REMARKS
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I	90	3386	3392	730	RIV PL GIRDER	YELLOWSTONE R	G		G	G	G	G	F	F		G	G			G	G	G	F	G	G	F	F	G		
I	90	3386	3392P	730	RIV PL GIRDER	YELLOWSTONE R	G		G	G	G	G	F	F		G	G			G	G	G	F	G	G	F	F	G		
I	90	3386	3415	15	CONCRETE SLAB	JR GR SEP	G		G		E	E									E		E		G		G	G		
I	90	3386	3415P	15	CONCRETE SLAB	JR GR SEP	G		G		E	E									E		E		G		G	G		
I	90	3386	3425	128	PRE CONC BEAM	SEP-OR 295	G		G		G	G					G			G	G	G	G	G	G	G	F	G		
I	90	3386	3425P	128	PRE CONC BEAM	SEP-OR 295	G		G		G	G					G			G	G	G	G	G	G	G	F	G		
I	90	3386	3436		UNDERPASS*	E INT-US 89	G		G		G	G					G			G	G	G	F	G	G	F	G	G		
I	90	3386	3436A		UNDERPASS	E INT-US 89																								
I	90	3436	3461		UNDERPASS*	INT-US 89	F		F		G	G					G			F	G	G	G	G	G	G	F	G		
I	90	3436	3461A		UNDERPASS	INT-US 89																								
I	90	3461	3472	118	PRE CONC BEAM	MISSION CR	G		G	G	G	E		G		G	G			G	G		G	G	G		F	G		
I	90	3746	3754	286	ST PLATE GIRDER	BOULDER R	G		G	F		F	F	P	G	G	F			F	G	G	F	F	G	F	F	F		
I	90	3746	3755	25	T T TRESTLE	BOULDER R DF	F	F	F		F	F		G	F	G		F		F	F	G	F	G	F		F	F		
I	90	3746	3796	57	T T TRESTLE	DRY CR	G	G	G	G	G	G		G	F	G		G		G	F	G	G	G	G		F	C		
I	90	3746	3801	11	T T TRESTLE	STOCKPASS	G	F	G		G	G			G	G		G		G	P	G	F	G	F		F	F		
I	90	3746	3803	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G		G	P	G	G	G	F		F	G		
I	90	3746	3810	19	T T TRESTLE	STOCKPASS	G	G	G		F	F						G		G	F	G	G	G	G		F	G		
I	90	3746	3817	39	CONCRETE I BEAM	UPPER DEER CR	F		P		P	C		P	F	P	G	F		P	P	G	F	F	P		G	P		X
I	90	3746	3833	39	STEEL I BEAM	LOWER DEER CR	F		G		F	G		F	F	G	G			G	G	G	G	G	G			G		

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I 90 3746 3836	25	T T TRESTLE	STK & SPRING CR	F	G	F		F	F		F	F	F		G			F	G	G	G	F		F	F		
I 90 3746 3907	95	CONCRETE T BEAM	BRIDGER CR	F		F	F		G		G	F	G	F				F	G	F		P			F		
I 90 3746 3942	67	CONCRETE T BEAM	WORK CR	F		G			F		F	P	G	F				P	G	F		F			F		
I 90 3746 3954	29	CONCRETE T BEAM	HUMPH CR	F		G		F	G		G	F	G	G				P	G	G		F			F		
I 90 3746 3970	102	PRE CONC BEAM	SEP-CO RD	P		G	G	G	G					G			G	G		G	G	G		F	G		

P	2	2909	2993	22	CONCRETE SLAB	DRAINAGE	E		G		G	E		E		E					G		E		G			E		
P	2	2909	3029	280	CONCRETE GIRDER	NP RY	F		F		P	G					E			G	F	G	G		P	G	G	G		
P	2	2909	303B	41	CONCRETE T BEAM	CAMP CR	E				G	E		E	G	G	E				G	E	G		G			E		
	2	2909	3040	52	CONCRETE T BEAM	BAKER CR	E		E	E	E	E	G	E	G	G	E				G	E	E		G			E		
	2	2909	3055	247	STEEL GIRDER	W GALLATIN R	G		E	E	E	E	E	G	E	G	E			E	E	E	G	E	E	E	G	E		
	2	2909	3175	19	T T TRESTLE	DRAINAGE	G	E	E		E	F		E		E		E			E	E	E	E	G		F	E		
	2	2909	3192	209	CONCRETE T BEAM	NP RY	G		G		G	E					G			N	P	G	G		F	G		G		
	2	2909	319B	245	PRE CONC BEAM	W BOZEMAN INT 90	E		E		E	E					E			E	E		E	E	E	E	E	E		
	2	2909	319BP	245	PRE CONC BEAM	W BOZEMAN INT 90	E		E		E	E					E			E	E		G	E	E	E	E	E		
	2	3466	3466		UNDERPASS*	W INT-I 90	G		G		G	G					G			G	G	G	G	G	F	F	F	G		
	2	3466	3467		UNDERPASS*	W INT-I 90	F		G		G	G					G			G	G	G	G	G	G	F	F	G		
	2	3490	3507	500	CONT ST GIRDER	YELLOWSTONE R	G		F	F	F	G	F	F		P	G			F	F	F	P	G	P	F	F	F		
	2	3490	352B	279	CONT ST GIRDER	E INT-I90	G		G		G	G					G			G	G	G	F	G	G	F	G	G		
	11	0000	0002	409	STEEL TRUSS	YELLOWSTONE R	P		C	F	F	F		G	G	G	F	G	G	F	F	P	F	G	F	F	F	F		X
	11	0000	0204	450	ST PLATE GIRDER	YELLOWSTONE R	F		G	F	G	G	F	G	G	G	G			G	G	G	G	G	G	F	F	G		
	11	0000	0240	90	CONT CONC T BM	BIG CR	F		G	G	F	G		F	G	G	G			G	F	G	G	G	F	G	F	G		
	11	0000	0530		UNDERPASS*	S INT-I 90	G		G		G	G					G			E	G	G	G	G	G		F	G		
	11	0000	0530A		UNDERPASS	S INT-I 90	G		G		G	G					G			E	G	G	G	G	G		F	G		

A				FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	11	0530	0530		UNDERPASS*	S INT-I 90	G		G		G	G					G			E	G	G	G	G	G		F	G		
P	11	0530	0530A		UNDERPASS	S INT-I 90	G		G		G	G					G			E	G	G	G	G	G		F	G		
P	11	0605	0605	210	PRE CONC BEAM	MISSION INT-I 90	F		F		G	G					G			F	G	G	G	G	G	G	F	G		
P	11	0605	0606	128	CONCRETE T BEAM	NP RY	G		G	G	G	G					G			F	G	G	F	F	G	F	F	G		
P	11	0605	0615	390	CONT STEEL GIR	YELLOWSTONE R	G		G	F	G	G	F	F	G	F	G			F	G	G	F	G	G	F	F	G		
P	11	0605	0632	60	CONCRETE SLAB	DRAINAGE	G		G	G	F	G		G	G	G					P	G	G		F			G		
P	11	0605	0650	11	T T TRESTLE	STOCKPASS	G	F	G		G	F						G		G	F	G	G	G	F		F	G		
P	11	0605	0655	19	T T TRESTLE	STOCKPASS	F	F	F		F	F						G		G	F	G	G	F	F		F	F		
P	11	0605	0673	19	T T TRESTLE	STOCKPASS	G	F	F		F	G						G		G	F	G	G	G	G		F	G		
P	11	0605	0677	38	T T TRESTLE	WILLOW CR	G	F	F	F	F	G		G	F	G		G		G	F	G	G	G	G		F	G		
P	11	0605	0686	19	T T TRESTLE	DRAINAGE	G	F	G		F	F		G	E	G		G		G	F	G	G	G	G		F	G		
P	11	0605	0697	11	T T TRESTLE	DRAINAGE-STK	G	F	F		F	F		G	F	G		F		F	F	G	F	G	G		F	G		
P	11	0605	0702	38	T T TRESTLE	DRAINAGE	G	G	G	G	F	F		G	F	G		G		G	F	G	G	G	F		F	G		
P	11	0605	0712	141	ST PONY TRUSS	SHIELDS R	G	G	F	F	F	F	G	G	F	F		G	G	F	P	G	F	G	G		P	F		
P	11	0605	0723	59	STEEL I BEAM	ROCK CR	G		F	F	F	F	F	G	P	G		F		P	P	G	F		P		P	F		
P	11	0605	0767	128	STEEL GIRDER	SHIELDS R	G	G	G	G	G	F	G	G	F	G		G		G	F	G	F	F	F		F	G		
P	11	0605	0810	19	T T TRESTLE	DRAINAGE	G	F	F		F	F		G	G	G		F		G	G	G	G	F	F		P	G		
P	11	0605	0845	55	STEEL I BEAM	FLATHEAD CR	F		F	F	F	F		G	P	F		F		P	P	P	F		F			F		

P 12 0000 0044	60	REIN CONC GIR	S FK MAOISON R	G		G	G		G	G	G	P	G	G				G	G	G	G	G			G		
P 13 0000 0081	260	PRE CONC GIROER	MAOISON R	G		G	G	F	G	F	G	P	G	F			F	G	G	F	G	G		F	G		
P 13 0000 0308	83	CONCRETE T 8EAM	INOIAN CR	F		G	G	G	G	G	G	G	F	G			G	F	G	G	G	G			G		
P 13 0000 0475	8	T T TRESTLE	STOCKPASS	G	G	G		G	G						G		G	G	G	G	F	G		G	G		
P 13 0000 0481	122	CONCRETE T 8EAM	OOELL CR	F		G	C	F	G	C	G	F	G	F			C	G	G	G	G	F			F		X
P 13 0000 0483	107	CONCRETE T 8EAM	MAOISON R OF	F		F	C	F	G	F	G	G	G	F			F	G	G	G	G	P			F		X
P 13 0000 0484	81	CONCRETE T 8EAM	MAOISON R OF	G		G	F	F	G	G	G	G	G	F			F	G	G	G	G	G			G		
P 13 0000 0485	107	CONCRETE T 8EAM	MAOISON R OF	F		F	G	G	G	G	G	G	G	F			F	F	G	G	G	F	F		G		
P 13 0000 0486	290	THRU ST TRUSS	MAOISON R	G		G	F	G	G	F	G	G	G		G	G	F	F	G	G	G	G	F	E	G		
P 13 0491 0564	19	T T TRESTLE	N MEAOOW CR	G	G	G		G	G		G	G	G		G			F	G	G	G	G		F	G		
P 13 0491 0567	7	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		F			G	G	G	G	G		F	G		
P 13 0491 0611	19	T T TRESTLE	STOCKPASS	G	F	G		G	G		G		F		G			F	G	G	F	F		F	G		
P 13 0491 0652	38	T T TRESTLE	WARM SPRINGS CR	G	F	G		F	F		G		G		G			F	G	G	F	F		F	F		
P 13 0491 0671	19	T T TRESTLE	STOCKPASS	G	F	G		G	G		G		G		G			F	G	G	G	F		F	G		
P 13 0491 0679	38	T T TRESTLE	ORAINAGE	G	F	G		F	F		G		G		G			F	G	G	G	F		F	G		
P 13 0491 0688	19	T T TRESTLE	STOCKPASS	G	F	G		F	F		G		G		G			F	G	G	G	F		F	G		
P 13 0491 0693	19	T T TRESTLE	STOCKPASS	F	F	G		F	G		G		G		G			F	G	G	F	F		G	G		
P 13 0491 0704	19	T T TRESTLE	STOCKPASS	G	F	G		F	G		G		G		G			F	G	G	F	G		F	G		

				E	F	G	H	I	J	K		M	N	O	P	Q	R	S	T	U	V	W		Y		Z2
P 13 0491 0713	19	T T TRESTLE	STOCKPASS	G	F	G		F	F		G		G		C			F	G	G	F	F		F	F	X
P 13 0491 0714	19	T T TRESTLE	NORWEGIAN CR	G	F	G		F	G		G		G		G			G	G	G	F	F		F	G	
P 13 0491 0735	76	T T TRESTLE	DRY HOLLOW CR	G	F	G		F	F		G		G		G			F	G	F	F	F		F	F	
P 13 0491 0751	38	T T TRESTLE	S WILLOW CR	G	F	G		G	G		G		G		G			F	G	G	G	F		F	G	
P 13 0491 0760	19	T T TRESTLE	N WILLOW CR	G	F	G		F	F		G	F	G		G			G	G	G	F	G		F	G	
P 13 0491 0824	370	STEEL GIRDER	NP RY-CMSTP&P RR	F		G		G	G					G			G	F	G	F	G	G		F	G	
P 13 0491 0830	395	THRU ST TRUSS	JEFFERSON R	F		G	F	G	G	G	G		G	G		G	F	F	G	G	P	F	G	E	G	
P 29 0000 0021	25	T T TRESTLE	WEBER IRRIGATION	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P 29 0000 0166	45	T T TRESTLE	HERMAN GULCH	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G	
P 45 0000 0008		UNDERPASS	NP RY	G		F		P	G					E			G			G	G	G		F	G	
P 45 0000 0009	11	T T TRESTLE	STOCKPASS	G	G	G		F	F						F			P	E	G	G	F		G	G	
P 45 0000 0010	380	CONT ST GIRDER	YELLOWSTONE R	G		G	G	G	G	G	F	F	G	G			F	G	G	F	G	F	G	F	G	
P 45 0000 0018	137	CONCRETE T BEAM	BIG TIMBER CR	G		F	G	F	G	G	F	F	G	P			F	F	E	G		F	F	P	F	
P 45 0000 0097	57	T T TRESTLE	DRAINAGE	G	F	G	G	F	G		G	G	G		G			F	E	G	G	G		G	G	
P 45 0000 0099	63	T T TRESTLE	SFK TENMILE CR	F	F	G	F	G	G		G	G	G		F			F	E	F	F	G		G	G	
P 45 0000 0114	57	T T TRESTLE	TENMILE CR	G	G	G	G	F	G		G	F	G		G			F	E	G	G	G		G	G	
P 45 0000 0140	63	T T TRESTLE	WHEELER CR	G	G	G	G	F	F		G	G	G		F			F	E	G	G	G		G	G	

							E	F		H		J	K		M	N	O	P	Q	R	S	T			W	X		Z
P	45	0000	0152	57	T T TRESTLE	DRAINAGE	G	F	G	F	G	F		G	G	G		G			F	E	G	G	G		G	G
P	45	0000	0163	88	T T TRESTLE	OTTER CR	G	G	G	G	F	F		G	G	G		G			F	E	G	G	G		G	G
P	45	0000	0181	57	T T TRESTLE	RYE CR	G	G	G		G	F		G	F	G		G			F	E	G	G	G		G	G
P	45	0000	0182	184	CONT ST GIRDER	SWEET GRASS CR	G		G	G	G	G	G	G	F	G	G			F	G	G	F	G	G	F	G	G
P	45	0000	0197	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			F	E	G	G	G		G	G
P	45	0000	0204	38	T T TRESTLE	CAYUSE CR	F	G	G		G	G						G			G	E	G	G	G		G	G
P	45	0000	0219	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			F	E	G	G	G		G	G
P	45	0000	0224	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	E	G	G	G		G	G
P	45	0000	0265	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	E	G	G	G		G	G
P	45	0000	0268	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	E	G	G	G		G	G
P	50	0000	0037	134	CONCRETE GIRDER	MADISON R	G	F	F	G	F	G		G	P	G	G			G	G	G	F	G	G	F	F	G
P	50	0000	0075	36	CONCRETE SLAB	COUGAR CR	G		G		G	G		G	E	G				G	G	G	E		F		F	G
P	50	0000	0099	105	REINF CONC GIR	GRAYLING CR	G		F	F	F	G	G	G	G	G	F			P	F	G	G	F	F		F	F
P	50	0000	0236	120	CONT CONC T BM	GALLATIN R	G		G	F	G	G	G	G	G	G	G				G	G	G	G	G		F	G
P	50	0000	0264	64	CONT CONC T BM	SPECIMEN CR	G		G	G	G	G	G	G	G	G	G				G	G	G	G	F		P	G
P	50	0000	0327	122	CONCRETE GIRDER	GALLATIN R	G		G	F	G	G	G	G	G	F	G				G	G	G	G	F		F	G
P	50	0000	0339	70	CANT CONC GIR	TAYLOR FORK	G		G	G	G	G	G	G	G	G	G				G	G	G	G	F		F	G
P	50	0000	0479	80	CANT CONC GIR	WEST FORK	G		G	G	G	G	G	G	E	G	G				G	G	G	F	F		F	G

				FEET B				F	G	PIERS H			K		M	N	O	P	Q	R	S	T	U	V	W	X		Z
P	50	0000	0498	160	CONCRETE T BEAM	GALLATIN R	G		G	G	G	G	G	G	G	G	G				G	G	G	G	F		F	G
P	50	0000	0572	54	REINF CONCRETE	SWAN CR	G		G	G	G	G		G	G	G	G				G	G	G		F		F	G
P	50	0000	0614	234	STEEL GIRDER	GALLATIN R	G		G	G	G	G	G	G	E	G	G			E	G	G	F	G	G	G	F	G
P	50	0000	0682	69	CONCRETE T BEAM	SPANISH CR	G		F	F	F	F	F	G	G	G	G			F	G	G	F		G		F	G
P	50	0000	0704	260	STEEL GIRDER	GALLATIN R	G		G	G	G	F	G	G	G	G	G			F	G	G	F	G	G	F	F	G
P	50	0000	0767	20	CONC SLAB	COTTONWOOD CR	G		G		G	G		G		G					E	G	E		G		F	G
P	50	0000	0776	20	CONC SLAB	FARMERS CANAL	G		G		G	G		G		G					E	G	E		G		F	G
P	50	0000	0814	20	CONC SLAB	FARMERS CANAL	G		G		G	G		G		G					E	G	E		G		F	G
P	50	0000	0827	30	CONCRETE GIRDER	MIDDLE CR	G		G		F	F		G	G	G	G			G	G	G	F	G	F		F	G

M289 0000 0079	250	STEEL TRUSS	MADISON R	G		G	G	G	G	G	G	F	G		G	G	G	F	G	G	G	G	G	F	G		
M289 0000 0096	38	T T TRESTLE	CHERRY CR	G	G	G	G	G	F	G	G	F	G		G		G	F	G	G	G	G		F	G		
M289 0000 0151	21	CONCRETE T BEAM	ELK CR	G		G		G	G	G	G		G		G		G	F	G	G		F		F	G		
M289 0000 0279	120	ST THRU TRUSS	GALLATIN R	F		G		F	G	G	F	G	G		F	F	F	F	G	F	C	P		P	F		X
M289 0000 0282	39	STEEL I BEAM	GALLATIN R	F		G		F	G	G	G	P	G	F			G	F	G	F	F	P		P	F		
M291 0000 0008	235	PRE CONC BEAM	BELGRADE INT I90	E		E		E	E					E			E	E		E		E	G	G	E		
M499 0000 0077	123	CONCRETE SLAB	BEAVER CR	F	G	G	F	G	G	P	G	F	G					G	G	G	G	G		E	G		
M499 0000 0091	83	CONCRETE T BEAM	CABIN CR	G		G	F	G	G	F	G	G	G	F			F	G	G	G	G	G			G		
M499 0000 0208	75	CONCRETE SLAB	GRAYLING CR	G	G	G	G	G	G	F	F	G	G					G	G	E	G	G			G		

A			B FEET	C	D	E END F	F PILE	G BENT	H PIERS	I WING	J BACK	K ICE	L DRIF	M RIP RAP	N SCOUR	O	P STR	Q	R SHOES	S CURBS	T MAR	U DE	V BE	W	X	Y	Z	Z	Z2
S288	0000	0000	235	PRE CONC 8EAM	MANHATTAN INT 90	E		G		E	E					E			E	E		E		E	E	E	E		
S288	0000	0050	25	T T TRESTLE	CAMP CR	G	G	G		F	G	G	G		G		F		F	F	F	G	G	F		P	F		
S290	0000	0045	50	T T TRESTLE	E GALLATIN R	G	E	E	E	E	E	G	E	G	G		E			G		E	E	E		G	E		
S290	0000	0047	50	T T TRESTLE	E GALLATIN R	E	E	E	E	E	E	G	E	G	G		E			G		E	E	E		G	E		
S290	0000	0053	38	T T TRESTLE	SMITH CR	E	G	E	E	E	E	G	E	G	G		E			G		E	E	E		G	E		
S290	0000	0108	26	STEEL I 8EAM	ORY CR	G		E		E	E		E	F	E		E			P		G		F		P	G		
S293	0000	0016	57	T T TRESTLE	E GALLATIN R	G	F	F	F	F	F		P	F	G		F		F	F	P	F	F	F		F	F		
S293	0000	0032	38	T T TRESTLE	8RIDGER CR	G	F	F	F	F	F		P	F	G		F		F	F	P	F	F	F		F	F		
S293	0000	0108	25	T T TRESTLE	8RIDGER CR	F	G	G		G	F		G	G	G		G		F	F	P	G	G	F		F	G		
S295	0000	0003		UNOERPASS	SEP I90	G		G		G	G					G			E	G	G	G	G	G		F	G		
S295	0000	0004		UNOERPASS	SEP I90	G		G		G	G					G			E	G	G	G	G	G		F	G		
S298	0000	0085	120	ST THRU TRUSS	8OULDER R	F		P		P	F		G	P	G		P	P	P	P	F	P	P	P		P	P		
S298	0000	0130	150	CONT ST GIRDER	8OULDER R	G		G	G	G	G	G	P	F	G	G			G	G	P	G	G	F	F	F	G		
S298	0000	0162	60	ST PONY TRUSS	W BOULOER R	F		F		F	F		G	P	F		F	F	P	P	P	G	P	F		P	F		

S339 0000 0002	50	T T TRESTLE	FLATHEAD CR	G	G	G	G	F	F	G	F	P	G		G		G	F	P	F	G	G		P	F
S339 0000 0037	71	CONCRETE T BEAM	SHIELDS R	G		G	G	G	G		G	G	G	F			F	G	P	F	G	P		F	G
S339 0000 0141	25	T T TRESTLE	SHIELDS R	F	G	G		G	F		G	F	G		G		G	F	P	G	G	F		F	G
S345 0000 0044	21	CONC SL-ST I BM	MIDDLE CR	G		G		E	E		G		G		G		G	P	P	G	G			P	G
S346 0000 0000	235	PRE CONC BEAM	MANHATTAN INT 90	E		G		E	E					E			E	E		E		E	E	E	E
S346 0000 0018	102	PRE CONC BEAM	BAKER CR	E		E	E	E	E	E	E	E	G	E			E	E	E	E		E		E	E
S346 0000 0021	192	PRE CONC BEAM	W GALLATIN R	E		E	E	E	E	E	F	E	G	E			E	E	E	E		E	E	G	E
S346 0000 0056	132	PRE CONC BEAM	EAST GALLATIN R	E		E	E	E	E	E	F	E	G	E			E	E		E		E		E	E
S347 0000 0027	94	STEEL GIRDER	BAKER CR	G		G	G	G	F	F	F	F	G	G			F	G		G	G	F	F	F	G
S347 0000 0034	178	STEEL GIRDER	GALLATIN R	G		G	G	G	F	F	P	G	G	G			F	G		G	G	F	F	F	G
S362 0000 0008	300	STEEL GIRDER	YELLOWSTONE R	F		G	F	G	G	P	P	G	G	G			F	F	P	F	G	G	F	F	G
S362 0000 0011	25	T T TRESTLE	ARMSTRONG IRR CA	F	F	F		F	F		G		G		G		G	P	P	G	G	F		P	F
S371 0000 0012	120	CONT CONC T BM	SWEET GRASS CR	F		G		G	G		G	E	G	G			G	G	F	F		G		F	G
S371 0000 0109	45	T QUEEN TRUSS	SWEET GRASS CR	F		G		P	F		G	F	F		F	F				F	P	P		P	F

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z2
S411 0000 0003	50	ST PONY TRUSS	E GALLATIN R	F	F	C		F	F		P	F	F		F	F	P	C	P	F	F	P		P	F		X
S476 0000 0008	360	RIV PL GIRDER	YELLOWSTONE R	F		G	F	G	G	P	F	G	G	G			F	G	P	F	G	F	F	F	G		
S476 0000 0039	33	T LAMINATED BM	MILL CR	G		G		G	G		P	F	G		F		G	P	P	F	G	G		P	F		
S476 0000 0065	43	T LAMINATED BM	MILL CR	F		G		G	G		F	F	G		F		F	P	P	F	G	C		P	F		X
S476 0000 0098	25	T T TRESTLE	E FK MILL CR	F	G	G		G	G		G	F	G		G		G	F	P	G	G	G		F	G		
S478 0000 0008	336	STEEL TRUSS	YELLOWSTONE R	F		P	P	P	F	P	G	F	G		P	F	P	P	P	P	F	P	P	P	P		
S478 0000 0080	50	LMA STRINGERS	SWEET GRASS CR	G	G	G		F	G		G	P	G		E		E	P	P	E	G	G		F	G		
S478 0000 0113	70	T & ST TRUSS	SWEET GRASS CR	G		G		G	G		G	P	G		F	F	F	P	P	F	F	F		P	F		
S478 0000 0122	30	T KING TRUSS	E FK SWT GRASS C	F	F	P		P	F		G	P	G		F	F	F	P	P	F	F	F		P	F		
S479 0000 0063	30	UNT T KING TRUS	TENMILE CR	G	F	F		G	G		G	P	G		F	F			P	F	F	P		P	F		
S479 0000 0159	93	STEEL TRUSS	SWEET GRASS CR	G		F		F	F		G	F	G		E	F	F			E	F	E		F	G		
S527 0000 0007	278	PRE CONC 8EAM	MADISON R	E		E	E	E	E	G	G	E	E	E			E	E		G	E	E	E	E	E		
S540 0000 0068	57	T T TRESTLE	HAY WAGON PASS	F	F	F		F	F		G	G	G		G		F	F	G	F	F	F		F	F		
S540 0000 0078	31	STEEL I 8EAM	SIX MILE CR	F		G		P	G		G	G	G		G		F	P	G	F	G	P		P	G		

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Columns E thru Z

P Poor

S540 0000 0089	31	STEEL I BEAM	EMIGRANT CR	F		F		P	F		F	F	F		G		F	P	G	F	G	P		F	F
S540 0000 0170	67	STEEL I BEAM	MILL CR	F		F	P	F	P	P	G	P	G		F		P	F	G	F	G	F		P	P
S540 0000 0250	21	STEEL I BEAM	PINE CR	G		G		F	F		G	F	G		G		F	F	G	G	G	P		F	F
S540 0000 0318	285	REIN CONC RIB	YELLOWSTONE R	F		F	P		P	P	F		F	F				G	G	F	P	G		F	F

BOZEMAN DIVISION

I-90-3746-3817 39' Conc I & WF Beams Upper Deer Creek

Original backwalls at both end bents appear to be settling. The I beams at the west end bent do not appear to have any bearing on the beam seats in the middle 2/3 of the width of the structure. The backwall at the east end bent is also settling but the I beams appear to have better bearing at this end. This bridge has been widened and the original portion of the backwalls are settling. The portion of the backwall under the left I beam at the east end bent is severely cracked. This condition has appeared just recently. This portion of the backwall was widened from the original and is taking the load from the original beams which have undergone settlement with the original backwall. See photos.

P-11-0000-0002 409' Stl Truss Cast in Pl Beams Yellowstone River

Columns of the north side of the river are spalling at the ground line. The left column seems to be of poor quality concrete and spalling has exposed a hoop which is badly rusted. Concrete is also spalling off further up on the left column. The strut is heavily spalled on the bottom face but no concrete has spalled off down to the reinforcing steel. See photos.

P-13-0000-0481 122' Concrete T Beam O'Dell Creek

The pier # 2 shaft is severly damaged by ice at both ends. Beam GR1 at the pier #2 end has sheared or failed behind the bearing shoe and the beam has settled 1"+ and now rests on the pier cap. See photos.

P-13-0000-0483 107' Concrete T Beam Madison River Overflow

Tops of piers 2 and 3 show excessive cracking under shoes of outside beams. Tops of piers are cracking at the 1/3 points of their width and the outside 1/3 portions are beginning to lean toward the adjacent spans. See photos.

P-13-0491-0713 19' T.T. Trestle Stockpass

The third stringer from the left or west side is cracked at mid span. See photo.

M-289-0000-0279 120' Steel Thru Truss Gallatin River

The bottom members of sway bracing at 5 of 6 panel points have been hit and bent. The bottom members of the portal bracing at each end bent have also been hit and bent. The truss on the downstream side appears to be leaning slightly toward the center of the roadway. See photos.

S-411-0000-0003 50' Steel Pony Truss East Gallatin River

The 12" x 12" pile cap on both end bents are rotting from the inside and collapsing on the upstream ends. The upstream truss is beginning to lean out as the pile cap continues to deteriorate. See photo.

BOZEMAN DIVISION

S-476-0000-0065 43' Lam. Timber Beam Mill Creek

Bridge rail on the right are completely broken away from the rail posts. The posts are loose and hanging. The end block on the right at bent #1 is broken off level with the top of the wingwall. This structure will no doubt be replaced in 1969. See photos.

I-90-3746-3817

I-90-3746-3817

I-90-3746-3817

I-90-3746-3817

P-11-0000-0002

P-11-0000-0002

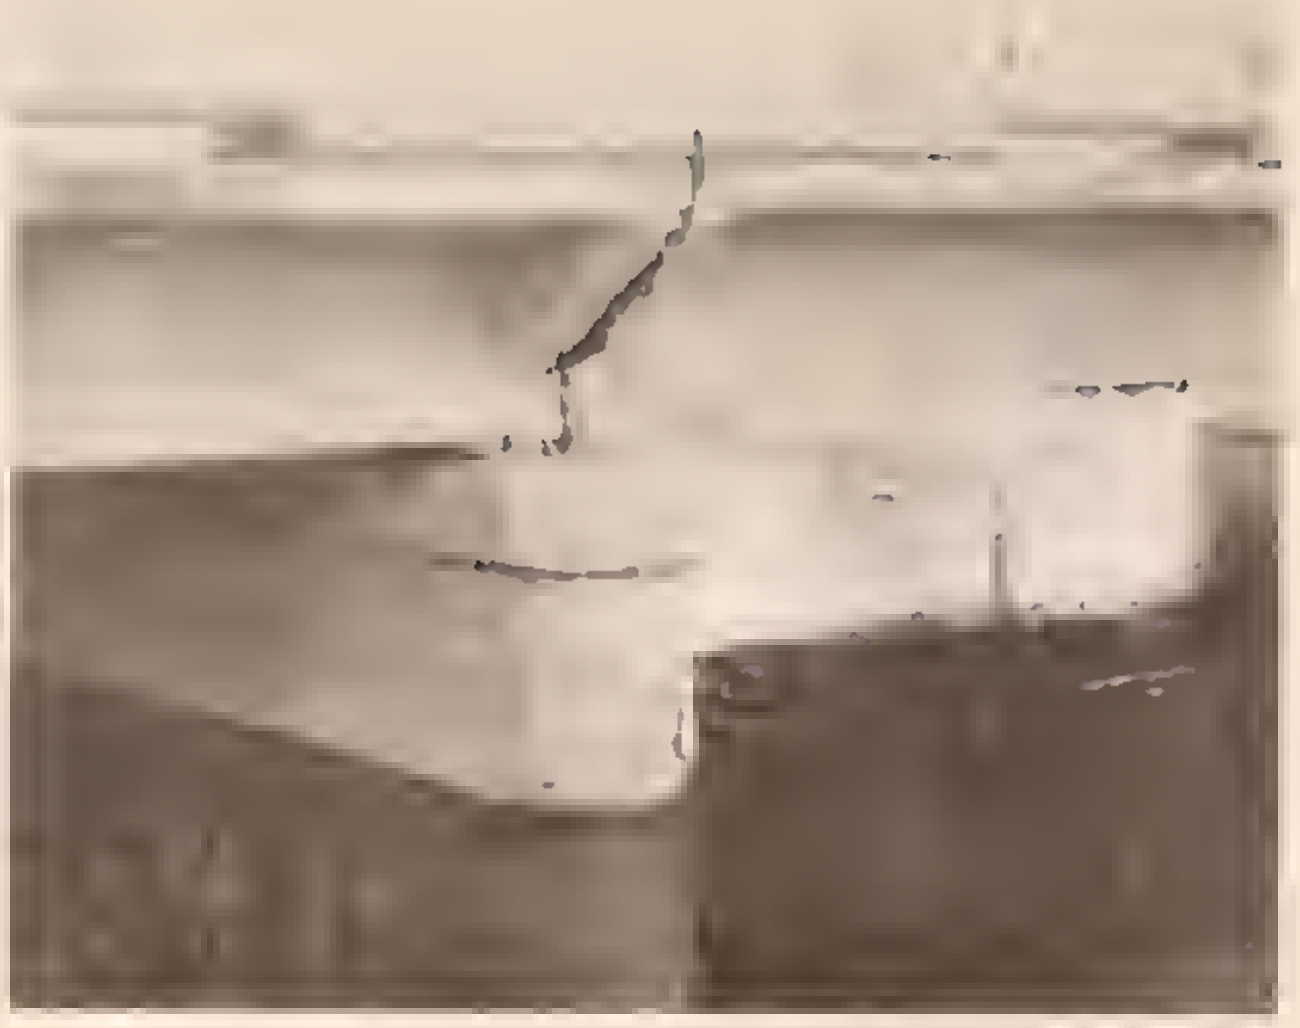

P-13-0000-0481

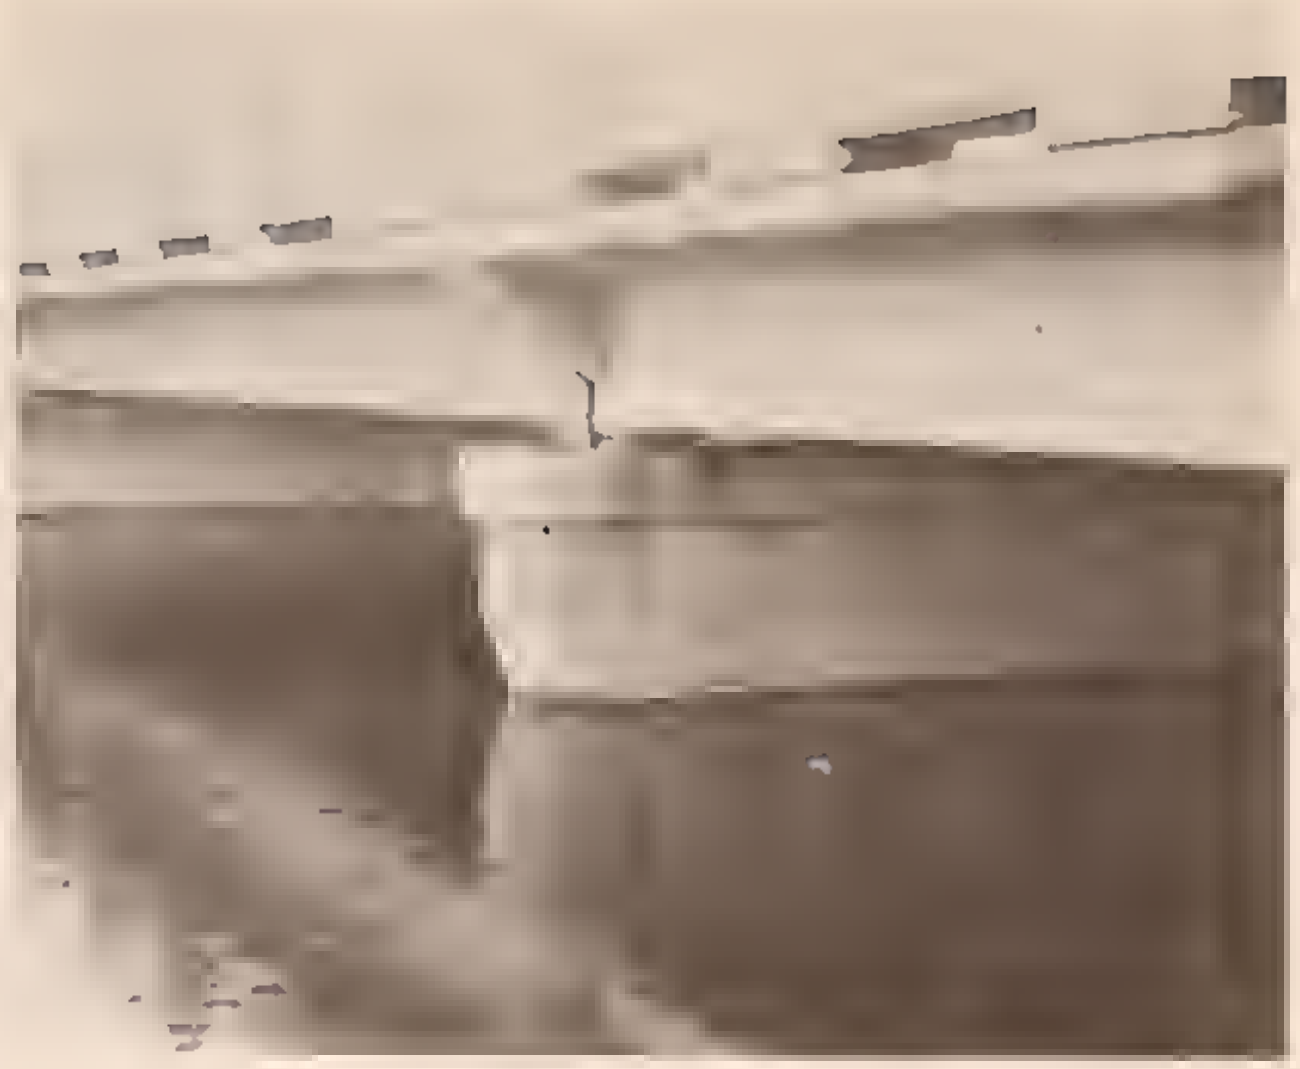

P-13-0000-0481

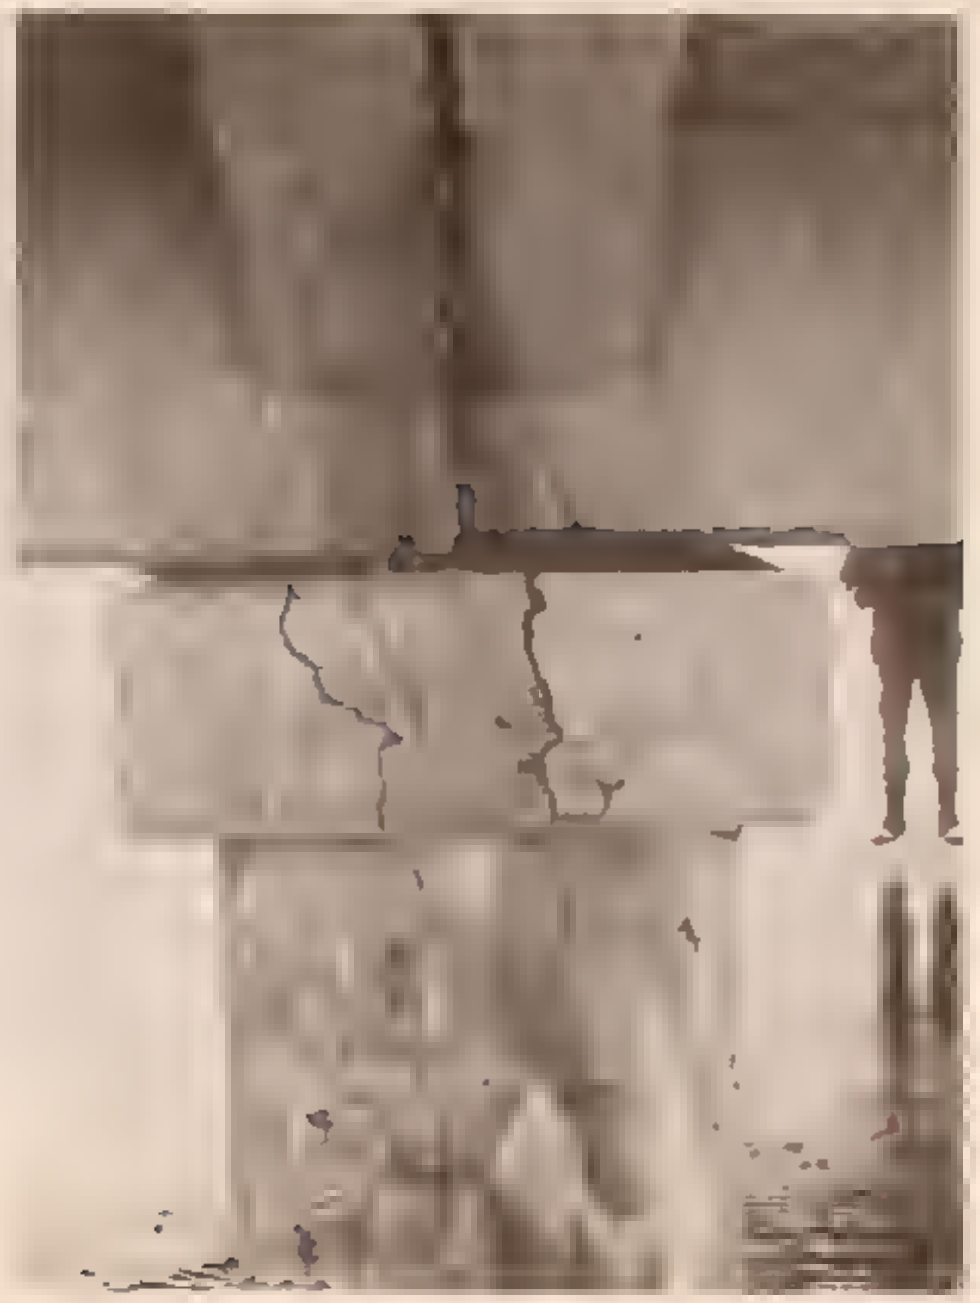

P-13-0000-0483

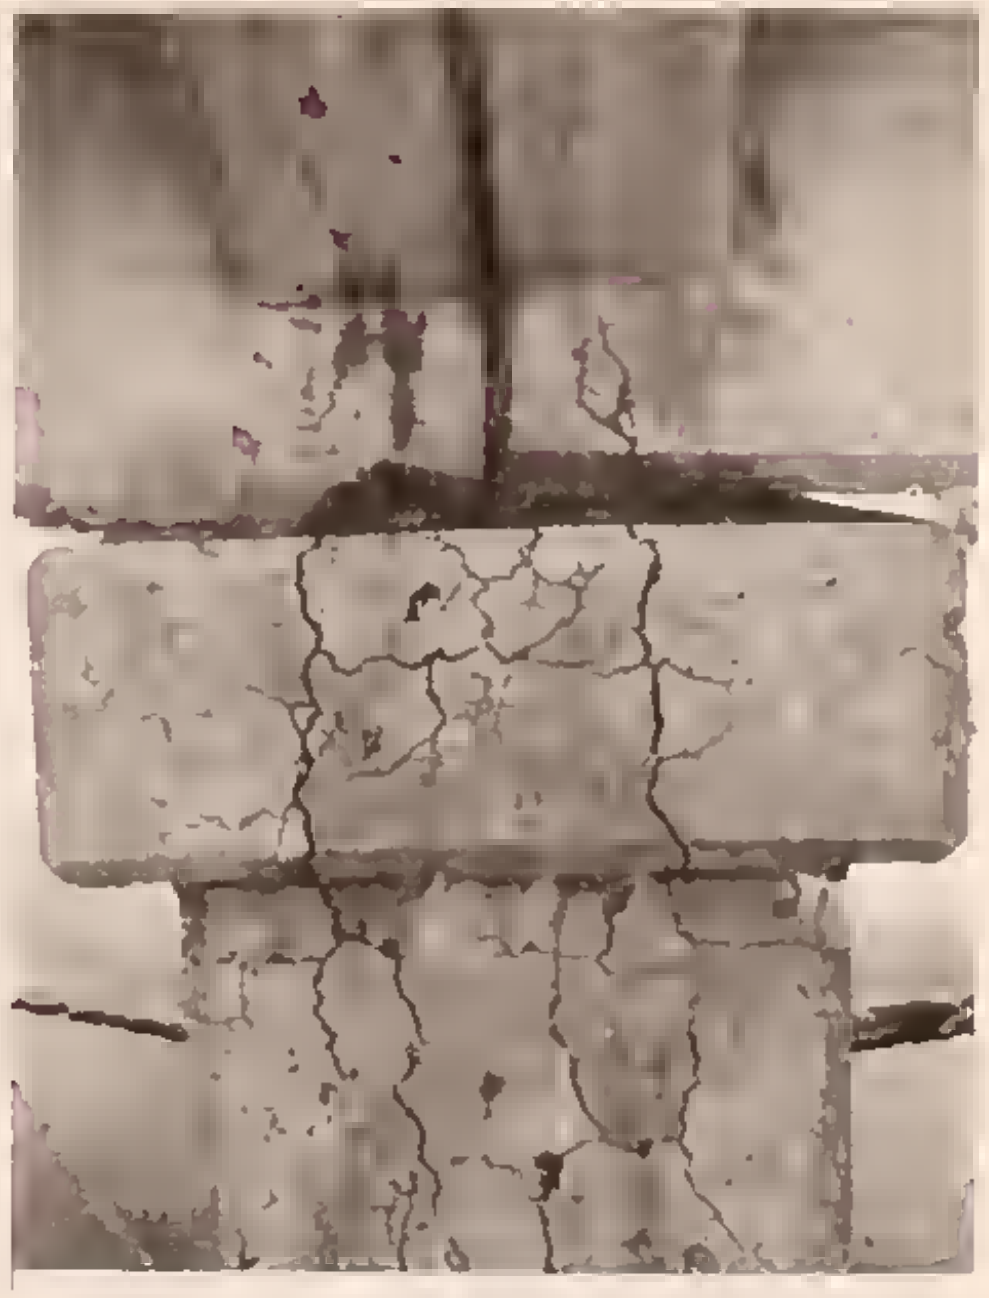

P-13-0000-0483

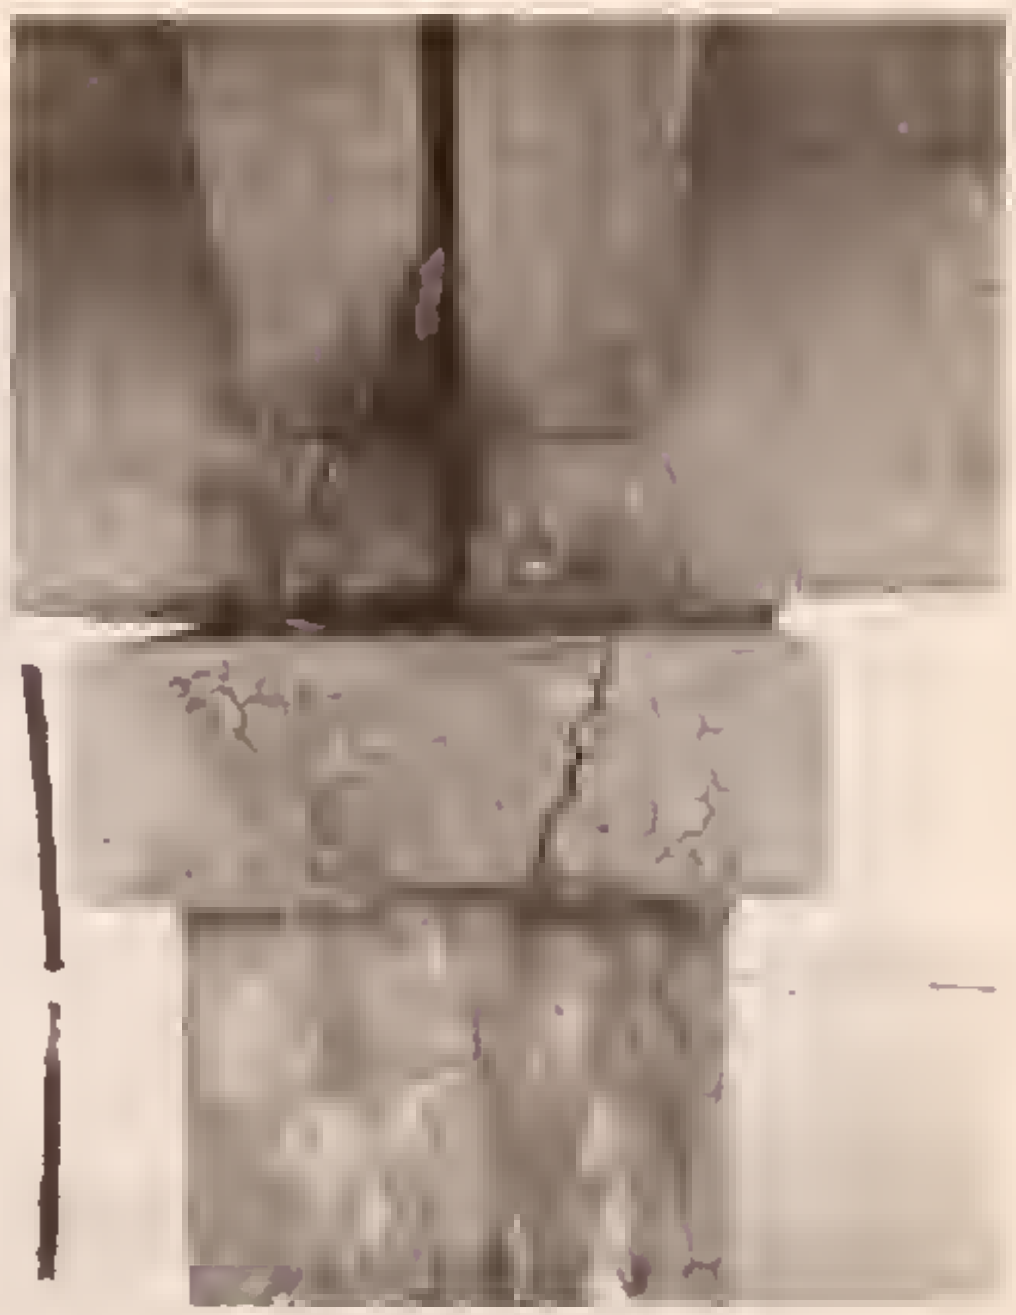

P-13-0000-0483

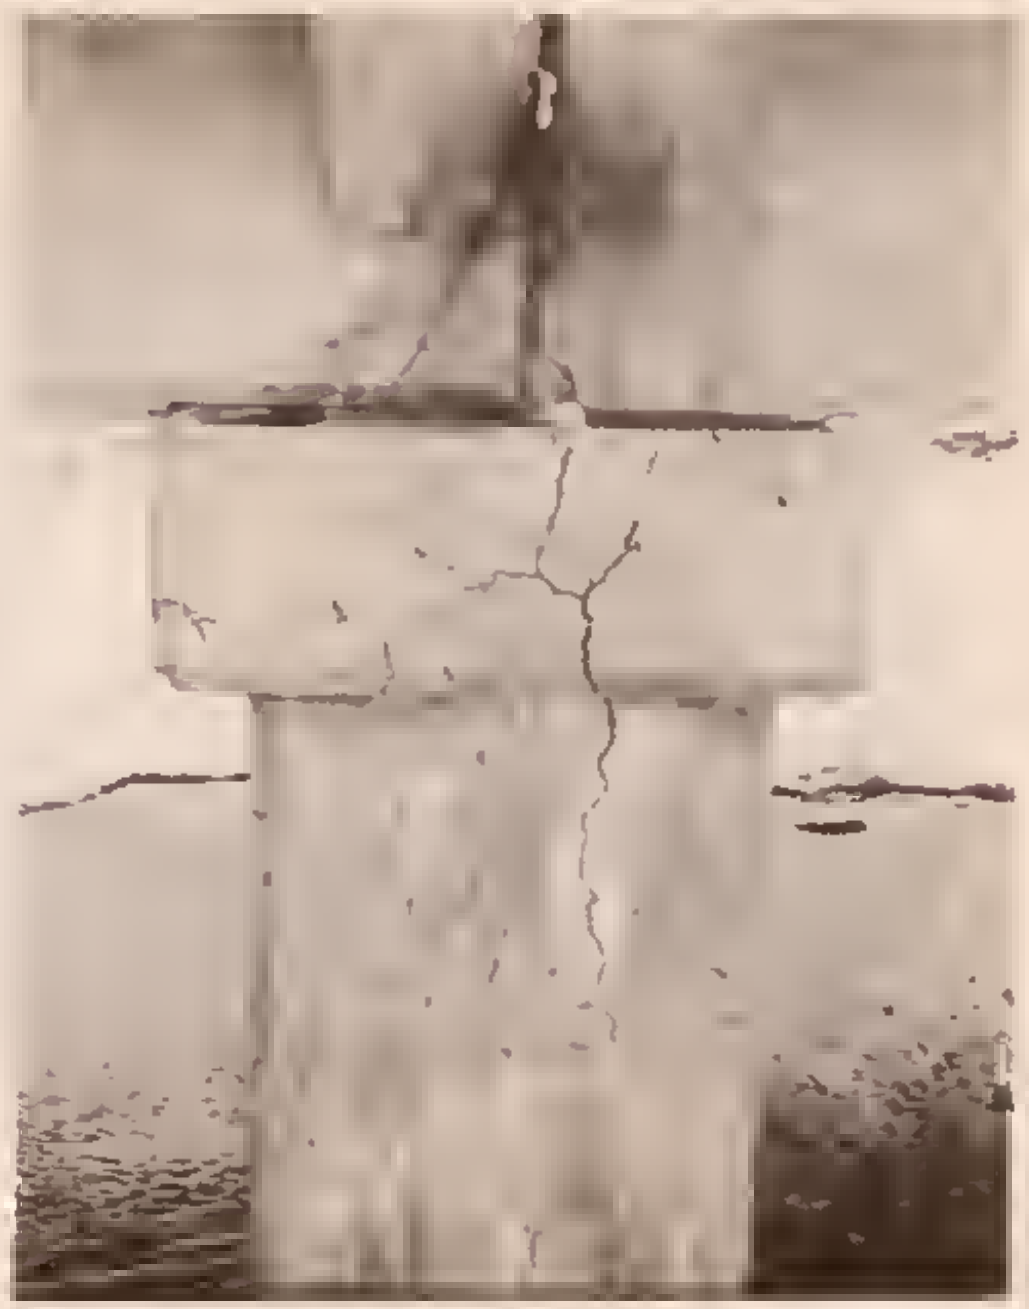

P-13-0000-0483

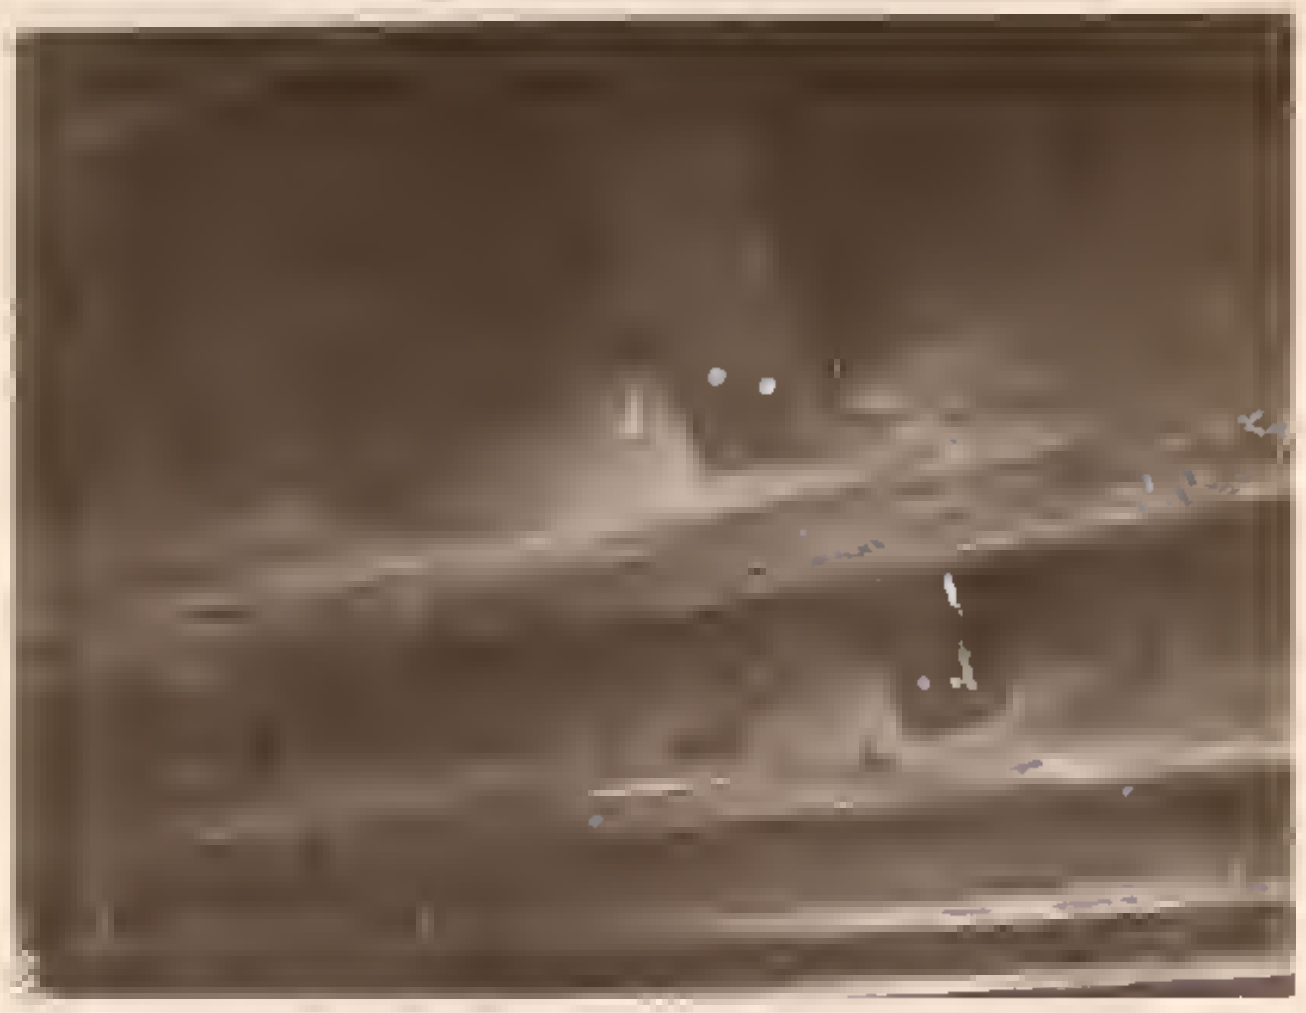

P-13-0491-0713

M-289-0000-0279

M-289-0000-0279

S-411-0000-0003

S-476-0000-0065

S-476-0000-0065

GREAT FALLS CONSTRUCTION DIVISION

I	15	2032	2196	133	PRE CONC BEAM	SIEBEN INT-CO RD	G	G	G	G					G		G	G	G	G		G	G		G	
I	15	2032	2196P	133	PRE CONC BEAM	SIEBEN INT-CO RD	G	G	G	G					G		G	G	G	G		G	G		G	
I	15	2032	2215	519	STEEL GIRDER	LIT PRICKLY CR C	G	G	G	G		G		G	G		G	G	G	G		G	F	G	G	
I	15	2032	2215P	519	STEEL GIRDER	LIT PRICKLY PR C	G	G	G	G		G		G	G		G	G	G	G		G	F	G	G	
I	15	2032	2223	539	PRE CONC BEAM	SPR CR INT-GN RY	G	G	G	G		G		G	G		G	G	G	G		G	F	G	G	
I	15	2032	2223P	539	PRE CONC BEAM	SPR CR INT-GN RY	G	G	G	G		G		G	G		G	G	G	G		G	F	G	G	
I	15	2032	2236	133	PRE CONC BEAM	LYONS CR SEP	G	G	G	G		G		G	G		G	G	G	G		G		G	G	
I	15	2032	2236P	133	PRE CONC BEAM	LYONS CR SEP	G	G	G	G		G		G	G		G	G	G	G		G		G	G	
I	15	2032	2298	113	PRE CONC BEAM	WOLF CR INT	G	G	G	G					G		G	G	G	G		G		G	G	
I	15	2032	2298T	113	PRE CONC BEAM	WOLF CR INT	G	G	G	G					G		G	G	G	G		G		G	G	
I	15	2032	2317		UNDERPASS*	AUGUSTA INT	G	G	G	G					G		G			G		G		G	G	
I	15	2032	2317A		UNDERPASS*	AUGUSTA INT	G	G	G	G					G		G			G		G		G	G	
I	15	2317	2374	123	PRE CONC BEAM	CRAIG INT-CO RD	G	G	G	G					G		G	G		G		G		G	G	
I	15	2317	2374P	123	PRE CONC BEAM	CRAIG INT-CO RD	G	G	G	G					G		G	G		G		G		G	G	
I	15	2317	2391	365	PRE CONC BEAM	GN RY	G	G	G	G					G		G	G	G	G		G	G	G	G	
I	15	2317	2391T	365	PRE CONC BEAM	GN RY	G	G	G	G					G		G	G	G	G		G	G	G	G	
I	15	2317	2394	770	WELDED PL GIR	MISSOURI R	G	G	G	G	G		G	G	G	G	G	G		G	G	G	G	G	G	
I	15	2317	2394T	770	WELDED PL GIR	MISSOURI R	G	G	G	G	G		G	G	G	G	G	G		G	G	G	G	G	G	
I	15	2317	2400	60	CAST CONC GIR	STICKNEY CR																				N

I	15	2317	2400T	60	CAST CONC GIR	STICKNEY CR															N	
I	15	2317	2484			UNDERPASS															N	
I	15	2317	2484T			UNDERPASS															N	
I	15	2317	2519	154	WELDED PL GIR	MISSOURI R															N	
I	15	2317	2519T	154	WELDED PL GIR	MISSOURI R															N	
I	15	2317	2527	62	PRE CONC BEAM	HARDY CR															N	
I	15	2317	2527T	62	PRE CONC BEAM	HARDY CR															N	
I	15	2317	2537	133	PRE CONC BEAM	INT-CO RD	P	G	G	G		G	G	G		G	G	F	F	G		X
I	15	2317	2554	82	PRE CONC BEAM	SEP-CO RD	G	G	E	E		E	G	G		G	G	G	G	G		
I	15	2317	2589	138	PRE CONC BEAM	S CASCADE INT	P	G	G	G		G	G	G		G	G	G	G	G		
I	15	2599	2614	123	PRE CONC BEAM	N CASCADE INT	F	G	G	G		G	G	G		G	G	G	G	G		
I	15	2614	2688	100	CONT CONC T BM	LITTLE MUDDY CR	P	G	G	G	F	G	G	G	G	G	G		P	G		X
I	15	2614	2688P	100	CONT CONC T BM	LITTLE MUDDY CR	P	G	G	G	F	G	G	G	G	G	G		P	G		
I	15	2614	2754	130	CONT CONC T BM	ULM INT	F	G	G	G		G	G	G		G	G		P	G		
I	15	2614	2827		UNDERPASS	GORE HILL INT	G	G	G	G		G	G	G	G	G	G			G		
I	15	2614	2827A		UNDERPASS	GORE HILL INT	G	G	G	G		G	G	G	G	G	G			G		
I	15	2614	2839		UNDERPASS*	SPUR INT-I 315	G	G	G	G		G	G			G	G	G	G	G		
I	15	2614	2839A		UNDERPASS*	SPUR INT-I 315	G	G	G	G		G	G			G	G	G	G	G		
I	15	2839	2842		UNDERPASS	CO RD SEP	G	G	G	G		G	G			G	G	G	G	G		

A	B			E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z		ZZ
I 15 2839 2842A		UNDERPASS	CO RD SEP	G		G		G	G					G			G			G		G	G	G	G		
I 15 2839 2849	483	PRE CONC BM	SUN R	G		G	G	G	G	G	G	G	G	G			G	G		G		G	G	G	G		
I 15 2839 2849P	483	PRE CONC BM	SUN R	G		G	G	G	G	G	G	G	G	G			G	G		G		G	G	G	G		
I 15 2839 2850	123	PRE CONC BM	5TH AVE SEP	G		G		G	G						G		G	G		G		G	G	G	G		
I 15 2839 2850P	123	PRE CONC BM	5TH AVE SEP	G		G		G	G						G		G	G		G		G	G	G	G		
I 15 2839 2855		UNDERPASS	CENTRAL AVE INT	G		G		G	G					G			G			G		G			G		
I 15 2839 2855A		UNDERPASS	CENTRAL AVE INT	G		G		G	G					G			G			G		G			G		
I 15 2839 2869		UNDERPASS	34TH ST SEP	G		G		G	G					G			G			G		G			G		
I 15 2839 2869A		UNDERPASS	34TH ST SEP	G		G		G	G					G			G			G		G			G		
I 15 2839 2874	354	PRE CONC BM	EMERSON INT-GNRY	G		G		G	G					G			G	G		G		G	G	G	G		
I 15 2839 2874P	359	PRE CONC BM	EMERSON INT-GNRY	G		G		G	G					G			G	G		G		G	G	G	G		
I 15 2874 2900	17	CONCRETE SLAB	JR GR SEP	G				G	G									G		G		G		G	G		
I 15 2874 2900P	17	CONCRETE SLAB	JR GR SEP	G				G	G									G		G		G		G	G		
I 15 2874 2913	108	PRE CONC BEAM	INT-CO RD	G		G		G	G					G			G	G		G		G	G	G	G		
I 15 2874 2913P	108	PRE CONC BEAM	INT-CO RD	G		G		G	G					G			G	G		G		G	G	G	G		
I 15 2874 2941	17	CONCRETE SLAB	JR GR SEP	G				F	G									G		G				G	G		X
I 15 2874 2941P	17	CONCRETE SLAB	JR GR SEP	G				F	G									G		G				G	G		
I 15 2874 2954		UNDERPASS*	VAUGHN INT-US 89	G		G		G	G						G		G			G				G	G		
I 15 2874 2954A		UNDERPASS	VAUGHN INT-US 89	G		G		G	G						G		G			G				G	G		

I 15	2954	3231	346	PRE CONC BEAM	TETON R	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G
I 15	2954	3326		UNDERPASS	BRADY INT-OR 365	G	G	G	G	G					G	G			G			G	G
I 15	2954	3339		UNDERPASS	SEP-CO RD	G	G		G	G					G	G			G			G	G
I 15	2954	3420	25	CONCRETE T BEAM	IRR CA	F	F			F					G				F	F			F
I315	4050	4050	296	PRE CONC BM	SPUR INT- I 15	G	G		G	G					G	G	G		G	G	G	G	G
I315	4050	4050T	296	PRE CONC BM	SPUR INT- I 15	G	G		G	G					G	G	G		G	G	G	G	G
I315	4050	4053	148	PRE CONC BM	BRIDGE ST SEP	G	G		G	G					G	G	G	G	G	G	G	G	G
I315	4050	4053P	148	PRE CONC BM	BRIDGE ST SEP	G	G		G	G					G	G	G	G	G	G	G	G	G
I315	4050	4055	174	CONT ST GIR	GN RY	G	G		G	G					G	G	G	G	G	G	G	G	G
I315	4050	4055P	206	STEEL BM	GN RY	G	G		G	G					G	G	G	G	G	G	G	G	G

								F	G	H		J	K		M	N	O	P		R	S				W					
P	3	2620	2620S		UNDERPASS*	S CASCADE INT	P		G		G	G					G			G	G		G		G		G	G		
P	3	2620	2637S		UNDERPASS*	N CASCADE INT	F		G		G	G					G			G	G		G		G		G	G		
P	3	2877	2878	396	STEEL TRUSS	SUN R	G		G	G	G	G		G		G		F	F	F	P	P	P	F	P	F	C	P		X
P	3	2877	2882		UNDERPASS	GN RY	G		G		G	G					G	G		F	G		G				P	G		
P	3	2889	2921		UNDERPASS*	EMERSON JCT INT	G		G		G	G					G	G		G			G		G					
P	3	2921	2921		UNDERPASS*	EMERSON JCT INT	G		G		G	G					G	G		G			G		G					
P	3	2996	2996	219	STEEL GIRDER	VAUGHN INT-I 15	G		G		G	G					G	G		G	G		G		G	G	G	G		
P	3	2996	2997	138	CONCRETE T BEAM	CMSTP&P RR-GN RY	F		G		G	G					G	G		G	G	G	G	G	G	F	G			
P	3	2996	2998	146	CONCRETE GIRDER	MUDDY CR	G		G	G	G	G	G	G	G	G	G	G		G	G	G	G		G	G	G	G		
P	3	3070	3074	19	T T TRESTLE	IRRIGATION CANAL	P	G	G		G	G						N			G	G	G	N	G		G	G		
P	3	3070	3079	76	T T TRESTLE	MILL COULEE CR	G	G	G		G	G		P	F	G		G			G	G	G	G	G		G	G		
P	3	3070	3100	76	T T TRESTLE	MILL COULEE CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	3	3070	3135	25	T T TRESTLE	ASHUELUT CANAL	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	3	3070	3144	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P	3	3070	3169	60	PRE CONC BEAM	GREENFIELD S CA	G		G		G	G		G	G	G	G			G	G	G	G		G		G	G		
P	3	3070	3199	57	T T TRESTLE	IRRIGATION CA	G		G		G	G		G		G	G				G	G	G	G	G		G	G		
P	3	3070	3335	11	T T TRESTLE	STOCKPASS	G	G	G		G	G					G				G	G	G	G	G		G	G		
P	3	3070	3342	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						F			G	G	G	G	G		G	G		X
P	3	3070	3348	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		

P	3	3070	3358	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	3	3070	3378	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	3	3070	3385	227	ST PONY TRUSS	TETON R	G		G	G	G	G	G	G	G	G		G	G	F	F	G	F	G	P		F	G		X
P	3	3402	3495	20	CONCRETE SLAB	DRAINAGE	G	G	G		G	G		G		G		S			G	G	G		G		G	G		
P	3	3402	3525	45	T T TRESTLE	FOSTER CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	3	3402	3546	285	T T TRESTLE	BIG MUDDY CR	G	G	G		G	G		P	F	G		G			G	G	G	G	F		G	G		
P	3	3402	3567	57	T T TRESTLE	JONES COU	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	3	3402	3582	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	3	3402	3588	57	T T TRESTLE	DRAINAGE	G	F	G		G	G		G		G		G			G	G	G	G	F		G	G		X
P	3	3402	3592	38	T T TRESTLE	BYNUM CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	3	3402	3622	57	T T TRESTLE	FARMERS COU	G	G	G		G	G		G		G		G			G	G	G	G	F		G	G		
P	3	3402	3643	38	T T TRESTLE	WALENSTEIN COU	G	P	P		P	P			F			G			P	G	F	G	P		P	P		
P	3	3402	3653	9	T T TRESTLE	STOCKPASS	G	P	P		P	P						F			P	P	F	P			F	P		X
P	3	3402	3675	114	T T TRESTLE	HINES COU	G	G	G		G	G						G			G	G	G	G	F		F	G		
P	3	3402	3697	57	T T TRESTLE	DRY FK MARIAS R	G	G	G		G	G			F	G		G			F	G	G	G	G		G	G		
P	3	3402	3699	75	T T TRESTLE	DRY FK MARIAS R	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	3	3402	3725	95	T T TRESTLE	MATCHETT COU	G	G	G		G	G				G		G			G	G	G	G	G		G	G		
P	3	4646	4655	2093	STEEL GIRDER	MISSOURI R-GN RY	F		G	G	G	G	G	G		G	G	G		G	G	G	F		G	G	P	G		X

		A					E	F	G	H	I	J	K		M	N	O			R				V	W			Z		
P	9	0000	0000	190	STEEL GIRDER	AUGUSTA RD INT	G		G		G	G					G			G	G	G	G		G	G	G	G		
P	9	0000	0130	294	RIV PL GIRDER	DEARBORN R	G		G	G	G	G	G	F	G	G	G			G	G	G	G		G	G	G	G		
P	9	0201	0236	57	T T TRESTLE	FLAT CR	F	G	G	G	G	G	G	G	F	G		G			G	G	G	G	G		G	G		
P	9	0201	0283	7	T T TRESTLE	STOCKPASS	G	G	F		G	G						G			G	C	G	G	C		G	F		X
P	9	0201	0287	7	T T TRESTLE	STOCKPASS	F	F	P		G	G						G			G	P	G		C			P		X
P	9	0201	0313	19	T T TRESTLE	STOCKPASS	P	G	G		G	P						G			G	G	G	G	G		G	G		
P	9	0201	0316	38	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	F	G		G	G		
P	9	0201	0321	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G				G			G	G	G	G	G		G	G		
P	9	0201	0326	38	T T TRESTLE	DRY CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	9	0201	0372	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	9	0201	0380	41	CONCRETE T BEAM	S FK SUN R	G		G		G	G		G		G		G			G	G	G		G			G		
P	9	0201	0381	57	T T TRESTLE	SLOUGH	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		X
P	9	0399	0401	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	9	0399	0431	315	STEEL GIRDER	N FK SUN R	P		G	G	G	G	G	P		G	G			G	G	G	G	G	G	G	F	G		
P	9	0399	0433	93	T T TRESTLE	FLOWEREE CANAL	G	G	G		G	G		G				G			G	G	G	G	G		G	G		
P	9	0399	0448	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	9	0399	0467	100	T T TRESTLE	USRS CANAL	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	9	0399	0586	57	T T TRESTLE	DRY WASH	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	9	0399	0596	19	T T TRESTLE	DRAINAGE	G	G	G		G	G						G			G	G	G	G	G		G	G		

P	9	0399	0616	183	PRE CONC BEAM	OEEP CR	G		G	G	G	G	G	F	G	G	G			G	G	G	G		G	G	G	G		
P	9	0399	0618	7	T T TRESTLE	ORAINAGE	G	G	G		G	G		G				G			G	G	G	G	G		G	G		
P	9	0399	0635	200	T T TRESTLE	TETON R	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		G	G		
P	10	0002	0004	965	CONCRETE ARCH	MISSOURI R	G		F	F	F	F		F		G	P				P	G	P		P			P		X
P	10	0002	0006		UNOERPASS	GN RY	G		G		G	G					G			G	G		G		G		G	G		X
P	10	0008	0014		UNOERPASS	GN RY	G		G		G	G					G			G			G				G	G		
P	10	0008	0015		UNOERPASS	CMSTP&P RR	G		G		G	G					G			G			G				G	G		
P	10	0015	0020	1130	CONCRETE ARCH	MISSOURI R	F		F	F	F	F		G		G	F	G			C	G	P		P			P		X
P	10	0032	0403	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P	10	0032	0458	126	CONCRETE T BEAM	GN RY	F		G		G	G					F			P	F	G	G		F	P		F		X
P	10	0032	0517	1151	CONT ST TRUSS	MARIAS R & GN RY	G		G	G	G	G	G	G		F	G	G	G	G	G	F	G	G	G	G	P	G		X
P	10	1120	1130	1126	RIV PL GIROER	MISSOURI R-GN RY	G		P	G	G	G	G	G		G	G	G		G	G	F	F		G	G	G	G		X
P	10	1120	1130T	1126	RIV PL GIROER	MISSOURI R-GN RY	G		P	G	G	G	G	G		G	G	G		G	G	F	P		G	G	G	G		X
P	10	1120	1131		UNOERPASS	GN RY	G		G		G	G					G	G		G	G	P	G		G		G	G		
P	10	1120	1131A		UNOERPASS	GN RY	G		G		G	G					G	G		G	G	P	G		G		G	G		
P	10	1120	1132		UNOERPASS	SMELTER AVE	G		G		G	G					G	G		G	G		G		G	G	G	G		
P	10	1120	1132A		UNOERPASS	SMELTER AVE	G		G		G	G					G	G		G	G		G		G	G	G	G		

		A		B			E	F		H		J	K		M	N	O			R	S				W			Z		
P	11	1291	1639	100	CONCRETE T BEAM	BELT CR	G		F		G	G		G	G	G	G				F	G	G		G			G		
P	11	1291	1693	100	CONCRETE T BEAM	BELT CR	G		G		G	G		G	G	G	G				G	G	G		G			G		
P	11	1291	1712	140	PRES CONC BEAM	BELT CR	G		G		G	G		G	G	G	G			G	G		G		G		G	G		
P	11	1291	1942	164	PRE CONC BEAM	BELT CR																							N	
P	11	1291	1956	158	PRE CONC BEAM	BELT CR																							N	
P	11	1291	1965	182	PRE CONC BEAM	BELT CR																							N	
P	11	1291	2003	163	PRE CONC BEAM	BELT CR																							N	
P	11	2008	2011	156	CONCRETE T BEAM	BELT CR	G		G	G	G	G	G	P	G	G	G			G	G	P	G		G		P	G		
P	11	2008	2123	40	CONCRETE T BEAM	BOX ELDER CR	G		G		G	G		G	G	G	G				P	F	G		P			G		X
P	11	2008	2129	11	T T TRESTLE	STOCKPASS	G		G		G	G						G			G	G	G		G		P	G		
P	11	2008	2157		UNDERPASS	GN RY	F		G								G			G		F	G				P	G		
P	15	0000	0002	123	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	F	G		P	G	G	G		X
P	15	0000	0005	118	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G		
P	15	0000	0008	118	PRE CONC BEAM	OTTER CR	F		G		X	G		G	G	G	G			G	G	G	G		G	G	G	G		X
P	15	0000	0015	102	PRE CONC BEAM	OTTER CR	F		G		G	G		G	G	G	G			G	G	P	G		G	G	G	G		X
P	15	0000	0019	102	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	P	G		P	G	G	G		X
P	15	0000	0022	92	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	G	G		G	G	G	G		
P	15	0000	0025	92	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	F	G		G	G	G	G		X

P 15 0000 0030	102	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	F	G		F	G	G	G		X
P 15 0000 0036	102	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	P	G		G	G	G	G		X
P 24 0000 0579	57	T T TRESTLE	ARRASTRA	G	G	G		G	G		F		G	G	G			G	P	G	G	G		G	G		
P 24 0000 0689	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G			G	G			G	G	G	G	G		G	G		
P 24 0000 0695	19	T T TRESTLE	BEAVER CR	G	G	G		G	G		G	F	G	G	G			G	P	G	G	G		G	G		
P 24 0000 0697	38	T T TRESTLE	KEEP COOL CR	G	G	G		G	G		G	G	G	G	G			G	F	G	G	G		G	G		
P 24 0000 0701	38	T T TRESTLE	SPRING CR	G	G	G		G	G		G	G	G	G	G			G	G	G	G	G		G	G		
P 24 0000 0710	25	T T TRESTLE	SPRING CR OF	G	G	G		G	G		G	G	G	G	G			G	G	G	G	F		G	G		
P 24 0000 0767	11	T T TRESTLE	STOCKPASS	G	G	G		G	G					G	G			G	G	G	G	G		G	G		
P 24 0000 0778	178	CONT ST I BEAM	LANDERS FORK	F		G	G	G	G	G	F		F	G	G		G	P	F	G	G	G	G	G	G		
P 24 0000 0784	30	T T TRESTLE	DRAINAGE	G	G	G		F	G		G	G	G	G	G			G	G	G	G	G		G	G		
P 24 0000 0794	30	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	F		G	G		
P 24 0000 0808	30	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	F		G	G		
P 24 0000 0820	30	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 24 0000 0829	75	T T TRESTLE	ALICE CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 24 0000 0855	38	T T TRESTLE	CADOTTE CR	G	G	G		G	G		G	G	G		G			G	G	G	F	G		G	G		
P 24 0000 0973	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 0000 0979	101	T T TRESTLE	MID FK DEARBORN	G	G	G		G	G	G		G		G			G	G	G	G	G			G	G		

				E	F	G	H		J	K		M	N	O			R	S				W					
P 24 0000 0984	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 24 0000 0990	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 24 0000 0995	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 24 0000 1002	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 24 0000 1025	185	CONT ST GIRDER	DEARBORN R	G		G	G	G	G	G	G		G	G			G	G	G	G	G	G	P	G	G		X
P 24 0000 1042	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	F	G	G	G		G	G		
P 24 0000 1078	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1096	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1112	75	T T TRESTLE	FLAT CR	G	G	F		G	G	G					G			G	F	G	G	G		G	G		
P 24 1090 1125	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1139	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1144	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1159	11	T T TRESTLE	STOCKPASS	P	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1179	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1194	63	T T TRESTLE	DRAINAGE	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1212	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1219	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1242	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 24 1090 1252	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		

P	24	1090	1259	25	T T TRESTLE	IRRIGATION CANAL	G	G	G		G	G						G			G	G	G	G	C		G	G		X
P	24	1274	1385	284	STEEL TRUSS	SUN R	G		G	F	G	G	G	G		G		G	G	G	G	G	F	G	G	G	P	G		X
P	24	1274	1390	57	T T TRESTLE	MILL COULEE	G	F	F		G	F		G	G	G		G			G	G	G	G	G		G	G		
P	24	1397	1407	150	T T TRESTLE	SIMMS CR	G	G	G		G	G	G	G	G	G		G			G	F	G	F	G		G	G		X
P	24	1397	1416	39	CONCRETE T BEAM	IRRIGATION CANAL	G		G		G	G		G	G	G	G				G	F	G		G			G		
P	24	1397	1426	57	T T TRESTLE	HEPPLER COULEE	G	G	G		G	G		G	F	G		G			F	G	G	G	G		G	G		
P	24	1397	1431	19	T T TRESTLE	STOCKPASS	G	G	G		G	G				G		G			G	G	G	G	G		G	G		
P	24	1397	1460	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	F	G	G	G		G	G		X
P	24	1397	1485	19	T T TRESTLE	STOCKPASS-OR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	24	1397	1513	76	T T TRESTLE	DRY CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	24	1397	1561	95	T T TRESTLE	SPRING COULEE CR	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		G	G		
P	24	1397	1597	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	24	1397	1602	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	24	1397	1604	79	CONCRETE T BEAM	S FK SUN R	G		G	G	G	G		G		G	G			G	G	G	G		P	G		G		X
P	24	1397	1605	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			P	G	G	G	G		G	G		
P	41	0040	0045	109	CONCRETE T BEAM	GN RY	P		P		G	G					P			G	G		G		F	G		P		X
P	41	0040	0046		UNDERPASS*	US BYP	G		G	G							G			G			G	G			G	G		
P	41	0040	0054		UNDERPASS	GN RY	G		G	G	G	G				G	G	G		G			P				F	G		

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	ZZ
P 41 0040 0057		UNDERPASS*	US 89	G		G		G	G		G		G	F						F					F		
P 41 0040 0058		UNDERPASS	CMSTP&P RR	G		G		G	G		G		G	G			G			F				F	G		

M230 0000 0002	128	CONCRETE T BEAM	GN RY	G		G		G	G					G		G	G	G	G		G	G	G	G	
M230 0000 0024	708	RIV PL GIRDER	MISSOURI R	F		G	G	G	G	G	G	G	G	G		G	G	G	G	G	G	G	F	G	
M230 0000 0040	125	T T TRESTLE	SHONKIN CR	P	G	G		G	G	G	F	P	F		G		G	P	G	G	G		F	G	
M230 0000 0086	75	T T TRESTLE	BOYLE COULEE	G	G	G		G	G		G	G	G		G		G	G	G	G	G		G	G	
M230 0000 0132	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G		G	G	G	G	G		G	G	
M230 0000 0322	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G		G	G	G	G	G		G	G	
M230 0000 0331	76	T T TRESTLE	FLAT CR	G	G	G		G	G		G		G		G		G	G	G	G	G		F	G	
M230 0000 0341	25	T T TRESTLE	TRIBUTARY FLAT C	G	G	G		G	G		G		G		G		G	G	G	G	G		G	G	
M230 0000 0416	75	T T TRESTLE	COWBOY STEELE CR	G	G	G		G	G		G		G		G		G	G	G	G	G		F	G	
M230 0000 0420	75	T T TRESTLE	BUTTE CR	G	G	G		G	G		G		G		G		G	G	G	G	G		G	G	
M230 0000 0467	250	T T TRESTLE	ARROW CR	G	G	G		G	G		G	P	P		G		G	G	G	F	G		G	G	

S219 0000 0031	57	T T TRESTLE	FARMERS COULEE	G	G	G		G	G						G			G	G	G	G	G		G	G		
S219 0000 0176	38	T T TRESTLE	DRAINAGE	G	G	G		G	G						G			G	G	G	G	G		P	G		
S221 0000 0049	268	STEEL I BEAM	TETON R	F		F	F	G	G	G	P	G	F	G	G		G	G		G	G	G	P	F	G		
S223 0000 0013	298	CONCRETE T BEAM	TETON R	G		G	G	G	G	G	F	G	G	G			G	G	F	G		G	G	F	G		
S225 0000 0316	408	PRE CONC BEAM	TETON R	G		G	G	G	G	G	G	G	G	G			G	G	F	G		G	G	G	G		X
S226 0000 0001		UNDERPASS	SPUR FAP 3	G		G	G							G			G			G	G			G	G		
S226 0000 0036	57	T T TRESTLE	SAND COULEE	G	G	G		G	G		G	G	G		G				G	G		G		F	G		
S228 0000 0105	57	T T TRESTLE	RED COULEE	G	G	G		G	G		G	G	G		G			G		G	G	G		G	G		
S228 0000 0164	186	STEEL I BEAM	BELT CR	G		G	F	G	G		G		F	G	G		G	G		G	G	F	G	P	G		
S228 0000 0223	75	T T TRESTLE	HIGHWOOD CR	F	G	G		F	G		G		G		F			G		G	P	G		F	G		
S330 0000 0003	559	ST HOWE TRUSS	MISSOURI R	G		P	F	P	P	G	G		G	G	G	G	P			F	F	F	P	F	F		X
S330 0000 0050	130	STEEL GIRDER	SMITH R	G		G	G	G	G	G	F	G	G	G	G		F	G	F	G		G	P	F	G		
S330 0000 0152	142	PRE CONC GIRDER	SMITH R	G		G	G	G	G	G	P	G	G	G			G	G	G	G		G	G	G	G		

S330 0000 0366	648	ST PLATE GIRDER	MISSOURI R	G		G	G	G	G	G	G	G	X	G	G	G	G	F		G	G	F	G	X
S331 0000 0011		UNDERPASS	GN RY	G		G		G	G					G	G	F		G				F	G	
S365 0000 0005	183	PRE CONC BEAM	BRADY INT I 15	G		G	G	G	G				G		G	G		G		G	G	G	G	
S378 0000 0058	39	STEEL I BEAM	MUDDY CR	G	F	F		F	F				F					F	F			F	F	
S378 0000 0063	39	UNT T TRESTLE	DRAINAGE	G	F	F		F	F		F			F				F	F	F		F	F	
S386 0000 0005		UNDERPASS	GN RY	G		G		G	G					G	G	G	G	G				F	G	
S408 0000 0013	38	T T TRESTLE	USRS LAT DITCH	G	G	G		G	G		G	G		G		G	P	G	G	G		G	G	
S408 0000 0040	75	T T TRESTLE	USRS MAIN CA	G	G	G		G	G		G		G			G	G	G	G	G		G	G	
S431 0000 0001	57	T T TRESTLE	MAIN IRR CANAL	G	G	G		G	G		G	G		G		G	P	G	G	G		G	G	
S431 0000 0048	57	T T TRESTLE	MAIN IRR CANAL	G	G	G		G	G		G	G		G		G	G	G	G	G		G	G	
S431 0000 0163	50	CONCRETE SLAB	BIG MUDDY CR	G	G	G		G	G		F	G				G		G					G	
S434 0000 0000		UNDERPASS	WOLF CR INT I15	G		G		G	G				G		G	G		G					G	

PLANNING SURVEY BRIDGE CONDITION REPORT

Columns E [illegible]
P - Poor

RATINGS

S434 0000 0187	75	PRE CONC SLAB	MID FK DEARBORN	G	G	G		G	G		F	G						G	P	G					G		
S434 0000 0267	231	ST PRATT TRUSS	N FK DEARBORN R	G		G	P		F		G		G		G	F	F			F	F	F		G	F		X
S434 0000 0407	38	T T TRESTLE	S FK SUN R	G	G	G		G	G		P		G		G			F	G	G	G	G		F	G		
S434 0000 0424	75	T T TRESTLE	SMITH CR	G	G	G		G	G		P	G	G		G			G	G	G	G	G		G	G		
S495 0000 0040		UNDERPASS	GN RY	G		G		G	G			G		G			G			G		G			G		
S498 0000 0001	100	STEEL GIRDER	GN RY	P		G		P	G					G				P		F		P		P	P		X

GREAT FALLS DIVISION

I-15-2317-2499 546 Steel Truss Missouri River
Left post gone and maintenance men repaired it with steel guard rail sections. High side portal bent from being hit and left side chord near portal bent and gouged from being hit.

I-15-2317-2507 79' Concrete T. Beam Pryetter Creek
One section rail has been knocked out.

I-15-2317-2546 133' Pre. Stress Beams Int. County Road
Some end fills washing around end wings. Expansion plate on deck is noisy when traffic hits it.

I-15-2614-2688 100' Concrete T Beam Little Muddy Creek
Water washes around wingwalls and erodes fill. The fill keeps settling under the ends and there is not much berm left. Bridge rail rusty and needs paint.

I-15-2874-2941 17' Concrete Slab Jr. Grade Separation
Wingwalls separating from backwall as much as 3 inches. Median retaining wall shows movement of 2½" from backwall.

P-3-2877-2878 396' Steel Truss Sun River
Cracked bearing haunch on both south and north approach span over piers. Slab looks bad underneath. Re-bar exposed and rusting. Poor anchorage of deck to stringers in places. Rail bent and broken in places. Entire bridge needs paint. Rusting spots throughout. Bridge markers broken and bent.

P-3-3070-3342 11' T. T. Trestle Stockpass
One cracked stringer.

P-3-3070-3385 227' St. Pony Truss Teton River
One anchor bolt gone. No room for expansion on pony truss. Expansion plate pushed up on its partner plate.

P-3-3402-3588 57' T. T. Trestle Drainage
One railpost rotted at bottom. One railpost split in two.

GREAT FALLS DIVISION

P-3-3402-3653 9' T. Trestle Stockpass
Cap is rotted and smashed from load. Backing plant and wing planks are rotten.

P-3-4646-4655 2093' Steel Girder Missouri River & G.N. R.R.
Paint critical on rail. Scattered rust spots throughout structure steel. One rail post support shattered downstream, 6th post back of pier 4. One broken spot in deck near bent 16, E.B. lane. Deck is showing moderate wear, many cracks transverse and exposed aggregate in driving lanes.

P-9-0201-0283 7' T.T. Trestle Stockpass
Bents are starting to push and rolling cap over slightly. No rail, no markers.

P-9-0201-0287 7' T. T. Trestle Stockpass
Caps have rolle part way from end pressure. No rail, no markers.

P-9-0201-0381 57' T. T. Trestle Slough
Bad condition on end fills. Washing out behind backing plank.

P-10-0002-0004 1130' Concrete Arch Missouri River
Concrete in some arches and rail in bad state of deterioration. Re-bar can be seen in may places. Some of the concrete does not look like it would have good strength. One spot on downstream arch and third arch from west side has an old honeycomb where rocks have fallen out and now all bottom layer of re-steel is exposed. This spot is about 10 ft from edge of pier. Many columns are cracked. Much drift collected on some piers. There is some spalling at joint where arch sets on pier, some places as much as 6".

P-10-0002-0006 Underpass G.N. R.R.
Medium curb spalling in about 5 spots. Roadway deck chipped at joints in 2 places.

P-10-0015-0020 1130' Concrete Arch Missouri River
The rail is deteriorated. The slab is deteriorated where you can see holes clear through and see rusted re-steel. The columns up from arch have many cracks and spall spots. The arches and webs between the upright columns are nearly all cracked and opened up sometimes as much as ½". The large span arches are o.k. Many of these sub-structure cracks look like they have been there since original construction. There are no curbs left now because of re-surfacing on deck and deterioration of concrete off the top of curb.

GREAT FALLS DIVISION

P-10-0032-0458 126' Concrete T. Beam G. N. R.R.
Rail has been hit, one post broken off. Center span slipped sideways about 1 inch. Piece of concrete broken off beam at bent 3.

P-10-0032-0517 1151" Cont. St. Truss Marias River & G.N. R.R.
Footing P-5 is exposed on river side. One portal bent. Seven concrete girders carcked on ends on ends over bents.

P-10-1120-1130 1126' Riv. Plate Girder Missouri R. & G. N. R.R.
North bound - end bent north end anchor bolts pulled from cap. This is already noticed by maintenance men and they have cut a pavement expansion section away from bridge. Slab has some places that have extensive spalling and deck re-bar is exposed.

P-10-1120-1130T 1126' Riv. Plate Girder Missouri R. & G. N. R.R.
South-bound end bent north end anchor bolts pulled from cap. This is already noticed by maintenance men and they have cut a pavement expansion section away from bridge. Slab has cracks but is not in bad condition. Bridge marker gone.

P-11-2008-2123 40' Conc. T. Beam Otter Creek
Post on left rail is shattered.

P-15-0000-0002 123' Pre. Conc. Beam Otter Creek
Two terminal sections gone and some rail not bolted up.

P-15-0000-0008 118' Pre. Conc. Beam Otter Creek
Construction work in progress on repair of wings on left side. Rail lapped wrong on left side.

P-15-0000-0015 102' Pre. Conc. Beam Otter Creek
One bridge marker gone.

P-15-0000-0019 102' Pre. Conc. Beam Otter Creek
One bridge marker gone, one rail section gone.

P-15-0000-0025 92' Pre. Conc. Beam Otter Creek
Left bridge marker gone.

P-15-0000-0030 102' Pre. Conc. Beam Otter Creek
One bridge marker gone. Left terminal end is gone, rail hit and bent.

Great Falls Division

P-15-0000-0036 102' Pre. Conc. Beam Otter Creek
One bridge marker gone.

P-24-0000-1025 185' Cont. St. Gir. Dearborn River
Girders touching end bent on east end. No room left for expansion.

P-24-1090-1259 25' T. Trestle Irr. Canal
Left rail has been recently knocked off.

P-24-1274-1385 284' Steel Truss Sun River
Left upstream end post cracked. Pier spalled at water line. Paint is badly deteriorated. Portals bent and some interior diaphrams.

P-24-1397-1407 150' T. T. Trestle Simms Creek
One cracked stringer, one plank fell of pile bent.

P-24-1397-1460 19' T. T. Trestle Stockpass
One stringer has horizontal check that is starting to open up.

P-24-1397-1604 79' Conc. T. Beam South Fork Sun River
Cavity behind both end bents. One rail broken.

P-41-0040-0045 109' Conc. T. Beam Great Northern Railway
Cap bent # 3 is cracked under bearing point. Girder haunch cracked over bent 2 and 3.

M-230-0000-0467 250' T. T. Trestle Arrow Creek
Cracked stringer span 4 and 7. Looks like scour has lowered channel leaving one ice breaker about 5 ft above flow line. Drift has collected at bents. One end bent has been recently worked on but still exposed and unprotected.

S-225-0000-0316 408' Pre Conc. Beam Teton River
One bridge marker missing.

S-330-0000-0003 559' Steel Howe Truss Missouri River
South end bent cracked and opened up about 1 inch. This eliminates all clearance for expansion. All expansion rollers not working and out of adjustment.

GREAT FALLS DIVISION

S-330-0000-0366 648' Plate Girder Missouri River
The city installed a water line under deck. This leaks at joints and drips water on structure steel. Paint is ruined in these spots and steel rusts.

S-434-0000-0267 231' St Pratt Truss North Fork Dearborn River
Rail broken three places. Steel casing of pier split away from concrete. One broken stringer and two cracked. North end bent looks like it is crumbling.

S-498-0000-0001 100' St Girder Great Northern Railway
Rail knocked off in places. End fills are short of material. Paint has weathered extensively.

P-10-0015-0020

P-10-0015-0020

HAVRE CONSTRUCTION DIVISION

P ANN NG [illegible] CONDITION REPORT

A	FEET B			E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I 15 2954 3469	113	CONCRETE T BEAM	DRY FK MARIAS R	F		G	F	F	F	F	G	F	F	G				F	G	G	G	F		P	F		X
I 15 2954 3524	64	CONCRETE T BEAM	IRR CA	F	F	G		G	G		G		G	G				G	G	G	G	F			G		
I 15 2954 3627	541	CONT ST PLATE	MARIAS R	F		G	F		G	F	F	F	G	G	G		G	G	F	F	G	F	G	F	F		X
I 15 2954 3690	360	STEEL BEAMS	INT US2 & GN RY	E		E		E	E					E			E	E		E	E	E	E	G	E		
I 15 2954 3690P	360	STEEL BEAMS	INT US2 & GN RY	E		E		E	E					E			E	E		E	E	E	E	G	E		
I 15 3690 3703		UNDERPASS*	N SHELBY INT	G		E		E	E					E			E	E	G	E	E	E	G	G	E		
I 15 3690 3703A		UNDERPASS	N SHELBY INT	G		E		E	E					E			E	E	G	E	E	E	G	G	E		
I 15 3703 3748		UNDERPASS	INT-CO RD	G		E		E	E					E			E	E	G	E	E	E		E	E		
I 15 3703 3858	11B	PRE CONC BEAM	KEVIN INT-OR 215	G		E		E	E					E			E	E	G	E	E	E		E	E		
I 15 3703 3954	16B	PRE CONC BEAM	SUNBURST INT	F		E		E	E					E			E	E	G	E	E	E	P	G	E		
I 15 3703 3957	313	STEEL GIRDER	GN RY	G		G		G	G					G	G		G	G	G	G		G	G	G	G		
I 15 3703 4035		UNDERPASS	SWEETGRASS INT	E		E		E	E					E			E	E	G	E	E	E	F	G	E		
I 15 3703 4035A		UNDERPASS	SWEETGRASS INT	E		E		E	E					E			E	E	G	E	E	E	F	G	E		

				A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	1	1532	2091		142	CONCRETE T BEAM	MIDVALE CR	G		G			G		G	G	G	G			G	P		F	G	P	F		F		X
P	1	2093	2102		760	CONT ST TRUSS	TWO MEDICINE CR	G		G	G	G	G		G		G		G	G	G	G	G	G	G	F	G	P	G		X
P	1	2093	2204		127	CONCRETE T BEAM	GN RY	G		G			G					G				G	G	G	G	F			G		
P	1	2093	2214		20	STL GIRDER	DRAINAGE	G		G		G	G		G		F	G				G	G	G				F	G		
P	1	2218	2232		144	CONCRETE T BEAM	GN RY	G		F		G	F					P				F	G	F	F	P			P		X
P	1	2240	2290		38	T T TRESTLE	WILLOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	U		
P	1	2240	2294		38	T T TRESTLE	WILLOW CR OF	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P	1	2240	2541		314	CONT ST GIRDER	CUT BANK CR	F		G			G	G	G	P	F	G	G		G	G	F	G	G	G	F		G		
P	1	2240	2784			UNDERPASS*	SHELBY INT-I 15	E		E		E	E					E			E	E		E	E	E	E	G	E		
P	1	2240	2784A			UNDERPASS	SHELBY INT-I 15	E		E		E	E					E			E	E		E	E	E	E	G	E		
P	1	2784	2784			UNDERPASS*	SHELBY INT-I 15	E		E		E	E					E			E	E		E	E	E	E	G	E		
P	1	2784	2784A			UNDERPASS	SHELBY INT-I 15	E		E		E	E					E			E	E		E	E	E	E	G	E		
P	1	2794	3001		57	T T TRESTLE	W FK WILLOW CR	G	G	G		G	G		G	G	G		G			G	F	G	G	G		F	G		
P	1	2794	3030		100	T T TRESTLE	N FK WILLOW CR	G	G	G		G	G		F	P	F		G			G	G	G	F	G		F	G		
P	1	2794	3224		57	T T TRESTLE	COTTONWOOD CR	G	G	G		G	G		G		G		G			G	G	G	F	G		G	G		
P	1	2794	3266		7	T T TRESTLE	STOCKPASS	F	F			G	G						G			F	G	G	F				G		
P	1	2794	3538		120	CONCRETE T BEAM	SAGE CR	G		E	E	E	E	G	G	G	G	E			E	E	G	G		G		G	E		
P	1	2794	3763		146	CONT CONC T BM	BIG SANDY CR	P		G	G	G	G	G	G	F	G	G			G	G	G	G	G	G		F	G		
P	1	2794	3780		312	STEEL BEAM	GN RY	F		G		G	G					G	G		G	G	G	G	G	G	P	F	G		X

A	B	C		E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z		
P 1 3791 3862	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G		G	G	G		G	G		
P 1 3791 3893	100	T T TRESTLE	BOX ELDER CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 1 3791 3897	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		G	G		
P 1 3791 3904	38	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			F		G	G	G		G	G		
P 1 3791 3924	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	P	G		P			G		X
P 1 3791 3927	38	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	G	G	F	G		G	G		
P 1 3791 3934	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 1 3791 3960	57	T T TRESTLE	CLEAR CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 1 3791 3971	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 1 3791 3977	242	ST PONY TRUSS	MILK R	G		G	G	G	G	G	F	G	G			G	G	G	G	G	G	G	G	G	G		
P 1 3791 4006	19	T T TRESTLE	CANAL	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 1 3791 4018	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 1 3791 4022	57	T T TRESTLE	RED ROCK CR	G	G	G		P	G		G	G	G		G			F	G	G	G	G		G	G		
P 1 3791 4027	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 1 3791 4041	57	T T TRESTLE	RED ROCK CR OF	G	G	G		G	G		G	F	G		G			F	G	G	G	G		G	G		
P 1 3791 4043	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 1 3791 4045	94	CONCRETE T BEAM	LODGE CREEK	G		G	G	G	G		P		F	G			G	G	G	G		G			G		X
P 1 3791 4053	57	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 1 3791 4056	152	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		

				FEET B	C		E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	1	3791	4060	11	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G			G	G		
P	1	3791	4068	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4070	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4079	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	1	3791	4084	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4099	196	THRU ST TRUSS	BATTLE CR	G		G	G	G	G		G	F	G		G	G	G	G	G	G	G	G	G	G	G		X
P	1	3791	4120	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4128	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	1	3791	4138	108	CONT ST GIRDER	FIFTEEN MILE CR	G		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
P	1	3791	4256	25	STL & CONC	MAIN IRR CA																							N	
P	1	3791	4279	213	PRE CONC BEAM	MILK R																							N	
P	1	3791	4324	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G	G	G		G		F	G		
P	1	3791	4428	119	CONCRETE SLAB	WHITE BEAR CR	F	G	G	G		G	G	G		G		G			G	G	G	G	F			G		
P	1	6674	6675		UNDERPASS	GN RY	G				G	G											G	G	G		P	G		
P	1	6674	6698	140	PRE CONC BEAM	TWO MEDICINE CR	E		E	E	E	E		G		G	E			E	E		E	E	E		E	E		
P	3	3402	3743	190	UNT T TRESTLE	DUPUYER CR	F	F	F		F	F		F		F		F			P	F	F	F	P		P	F		
P	3	3402	3746	122	PRE CONC BEAM	DUPUYER CR DF	E		E	E	E	E	E	G	E	G	E			E	E	G	E	E	E		E	E		
P	3	3402	3749	57	UNT T TRESTLE	SHEEP CR	G	P	P		P	F		G		G		F			P	G	F	P	P		P	P		

		A		FEET B			E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	
P	3	3402	3778	82	PRE CONC BEAM	VALIER CANAL	E		E	E	E	E	E	E		G	E			E	E	E	E	E	E		E	E	
P	3	3402	3823	18	UN TR TRESTLE	DRAINAGE	F	P	P		P	P			F	P		P			F	G	G	G	G		G	P	X
P	3	3402	3842	213	PRE CONC BEAM	BIRCH CR	E		E	E	E	E	E	G	E	G	E			E	E	G	E	E	E		E	E	
P	3	3402	3861	142	PRE CONC BEAM	BLACKTAIL CR	E		E	E	E	E	E	E	E	G	E			E	E	E	E	E	E		E	E	
P	3	3402	3952	70	PRE CONC BEAM	AGENCY CR	E		E		E	E		E	E	E	E			E	E		E	E	E		E	E	
P	3	3402	3955	306	PRE CONC BEAM	BADGER CR	E		E	E	E	E	E	G	E	G	E			E	E	G	E	E	E	E	E	E	
P	3	3402	4007	265	STEEL GIRDER	TWO MEDICINE CR	P		G	G	G	G	G	P		G	E			G	G	F	G	E	G	G	F	G	
P	3	3402	4014	50	T T TRESTLE	TWO MEDICINE CA	G	G	G		G	G	G	F		G		G			G	F	G	G	F		P	G	
P	3	4116	4160	16	ST GIR	DRAINAGE	G		G		G	G		G		G	G				G	G	G				P	G	
P	3	4250	4254	42	CONCRETE ARCH	DRAINAGE	G				F	G		F		G	G					G	G	G	P			G	
P	3	4250	4259	53	CONCRETE ARCH	S FK CUT BANK CR	G				F	G		G		G	G					G	G	G	F			G	
P	3	4250	4302	120	STEEL TRUSS	N FK CUT BANK CR	F		F		G	G		F		P		G	G	G	F	F	G	G	G	P	P	G	X
P	3	4250	4340	48	CONCRETE ARCH	DRAINAGE	F					G		G		G	G					G	G	G	P			G	X
P	3	4250	4516	312	CONT ST GIRDER	ST MARYS R	G		G	G		G	G	G	G	G	E			G	G	F	G	G	G	G	F	G	X
P	3	4250	4568	122	PRE CONC BEAM	KENNEDY CR	E		E	E	E	E	E	G	E	G	F			E	G	G	E	G	E	G	G	E	
P	10	0032	0619	19	T T TRESTLE	STOCKPASS	G	G	G		F	G						G			F	G	G	G	F		G	G	
P	10	0032	0639	114	T T TRESTLE	SPRING COULEE	F	F	G		F	G		G		G		G			G	G	G	G	F		G	G	
P	10	0032	0690	95	T T TRESTLE	DRY COURSE	G	G	G		F	G		G	G	G		G			G	G	G	G	G		G	G	

P 10 0032 0699	95	T T TRESTLE	ORY COURSE	G	G	G		F	G		G	P	P		G			G	G	G	G	G		G	G
P 10 0032 0727	95	CONCRETE T BEAM	GN RY	P		G		G	G					G				G	G	G		G	G		G
P 10 0032 0B29	95	T T TRESTLE	BIG SANOY CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G
P 10 0032 0849	57	T T TRESTLE	ORY COURSE	G	G	G		G	G		G	F	G		G			G	G	G	G	F		G	G
P 10 0032 0897	76	T T TRESTLE	BOX ELOER CR	G	G	G		G	F	G	F	F	F		G			G	G	G	G	G		G	G
P 10 0032 0996	95	T T TRESTLE	GRAVELLY COULEE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G
P 10 0032 1071	122	PRE CONC BEAM	BEAVER CR	E		E	E	E	E	E	E	E	E	E			E	E		E	E	E		E	E
P 21 0749 0752	3B2	STEEL BEAM	GN RY	F		G			G					G			G	F		G	G	F	F	F	G
P 21 0749 0768	276	STEEL GIRDER	N SHELBY INT	G		E		E	E					E			E	E	G	E	E	E	G	G	E

A	B			E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W			Z		
M232 0000 0001	826	STEEL I BEAM	GN RY	F	P	P		F	F					G	P		P	P		F	P	P	P	P	P		X
M232 0000 0002	287	STEEL TRUSS	MILK R	G	F	F	F		P	G	G		F		F	F		P		F	F	P	F	C	F		X
M376 0000 0166	25	T T TRESTLE	LIT PEOPLES CR	F	G	G		G	G		G		G		G			G	F	G	G	G		G	G		
M376 0000 0180	25	T T TRESTLE	LIT PEOPLES CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
M376 0000 0223	38	T T TRESTLE	LIT PEOPLES CR	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G		
M376 0000 0263	100	T T TRESTLE	S FK PEOPLES CR	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G		
M376 0000 0316	100	T T TRESTLE	PEOPLES CR	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G		
M376 0000 0409	75	T T TRESTLE	WHITE BEAR CR	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G		
M376 0000 0472	100	T T TRESTLE	THREE MILE COU	F	G	G	G	G	G	G	G		G		G			G	G	G	G	G		G	G		

S214	0000	0001		UNDERPASS	INT-I15 SUNBURST	F		E		E	E					E			E	E	G	E	E	E	P	G	E	
S214	0000	0243	256	PRE CONC BEAM	SW GRASS INT-I15	E		E		E	E					E			E	E	G	E	E	E	F	G	E	
S215	0000	0000		UNDERPASS	KEVIN INT-I15	G		E		E	E					E			E	E	G	E	E	E		E	E	
S216	0000	0053	57	T T TRESTLE	SOBERUP CR	F	F	G		F	F		F	P	C		G			F	G	G	G	F		F	F	X
S216	0000	0095	150	T T TRESTLE	DUPUYER CR	F		G		G	G		G	F	F		G			F		G	F	F		F	F	X
S216	0000	0117	38	T T TRESTLE	IRRIGATION CANAL	G	G	G		G	G		G		G		G			F		G	G	G		F	G	
S218	0000	0011	38	T T TRESTLE	PONDERA COULEE	G	G	G		F	F		G		G		G			F	G	G	G	G		P	G	
S218	0000	0107	60	T T TRESTLE	PONDERA COULEE	G	G	G	G	G	G	G			G		G			G	G	G	G	G		F	G	
S218	0000	0199	23	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G				G	G	G			F	G	
S218	0000	0299	50	T T TRUSS	PONDERA COULEE	F	G	G		P	F		F	P	F		G	F		F		F	G	F		P	F	
S223	0000	0378	346	PRE CONC BEAM	MARIAS R	E		E	E	E	E	E	E	E	G	E			E	E		E	E	E	E	E	E	
S223	0000	0435	57	T T TRESTLE	DRAINAGE	G	G	G		F	F		G	G	F		G			G		G	G	F		P	G	X
S231	0000	0090	38	T T TRESTLE	OBRIEN COULEE	G	G	G		F	G		G	G	G		G			F		G	G	G		P	G	
S231	0000	0138	38	T T TRESTLE	LITTLE SAGE CR	G	G	G		F	G		G		G		G			F	G	G	G	F		F	G	

[illegible] REPORT

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S231 0000 0186	57	T T TRESTLE	SAGE CR	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
S234 0000 0020	96	ST PONY TRUSS	SCOTT COULEE CA	G	G	G	G	G	G		G		G		G	G	G	F		F	G	P		P	G		X
S236 0000 0552	98	UNT T TRESTLE	CHIP COULEE	F	F	F		F	F		G		G		F			P		G	P	P		P	F		
S240 0000 0015	213	PRE CONC BEAM	MILK R	F		E	E	E	E	E	P	F	G	E			E	E	G	E		E		G	E		
S240 0000 0029	40	STEEL I BEAM	THREE MILE CR	F	G	G		G	G		G		G		G			G		G	G	F		P	G		
S240 0000 0124	38	T T TRESTLE	BEAN CR	G	G	G	G	G	G	G	G		G		G			G	F	G	F	G		P	G		
S240 0000 0166	38	T T TRESTLE	SNAKE CR	G	G	G	G	G	G	G	G		G		G			F	F	G	G	G		P	G		
S240 0000 0250	57	T T TRESTLE	PEOPLES CR	G	G	G	G	G	G	G	G		G		G			G	F	G	G	G		P	G		
S241 0000 0001	88	T T TRESTLE	THIRTY MILE CR	G	G	G			G		P		P		G			G	F	G	G	P		P	G		
S241 0000 0009	57	T T TRESTLE	BUCKLEY COULEE	F	G	G			G		F	F	G		G			G		G	G	P		P	G		
S241 0000 0075	76	T T TRESTLE	W FK WAYNE CR	F	G	G			G		G	F	F		G			F	P	F	G	F		P	F		
S241 0000 0091	76	T T TRESTLE	WAYNE CR	G	G	G			G		G	P	G		G			F	P	G	G	F		P	G		
S241 0000 0097	57	T T TRESTLE	E FK WAYNE CR	G	G	G			G		G	P	G		G			F	P	G	G	F		P	G		
S241 0000 0110	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G	P	G	G	F		P	G		
S241 0000 0122	57	T T TRESTLE	WEST SAVOY CR	G	G	G			G		G	G	G		G			G	P	G	G	F		P	G		

			FEET			E	F	G	H		J	K		M	N				R	S	T	U	V	W				
S241	0000	0375	117	STEEL I BEAM	WOODY ISLAND CR	G		G			G		F		G		G			F		F		P		P	G	
S325	0000	0003	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	P	G	G	G		P	G	
S325	0000	0004	76	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G	P	G	G	G		P	G	
S325	0000	0005	38	T T TRESTLE	CANAL	G	G	G	G		G	G	G		G		G			G	P	G	G	G		P	G	
S358	0000	0074	285	PRE CONC BEAM	BIRCH CR	E		E	E	E	E	E	G	E	G	E			E	E		E	E	E	E	E	E	
S358	0000	0174	316	PRE CONC 8EAM	TWO MEDICINE CR	E		E	E	E	E	E	G	E	G	E			E	E		E	E	E	E	E	E	
S358	0000	0278	92	PRE CONC BEAM	SPRING CR	G		E	E	E	E		G	E	G	E			E	E		E	E	E		E	E	
S366	0000	0023	25	T T TRESTLE	COU & CANAL OF	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
S366	0000	0059	106	CONT ST GIRDER	DRY FK MARIAS R	F		G	G	G	G	G	G	P	P	E			G	G		G	G	G	G	P	G	X
S369	0000	0003	38	T T TRESTLE	PONDERA COULEE	F	G	G		F	F		G	G	G		G				G	G	F	F			G	
S396	0000	0014	100	STEEL I BEAM	THIRTY MILE CR	G	G	G		G	G		G		G		G			G		G		G		P	G	
S396	0000	0087	48	STEEL I BEAM	WAYNE CR	F		F	F		F		F		F		F			P		C		P		P	F	X
S396	0000	0121	24	UNT T TRESTLE	DRAINAGE	F		F		P	P		F		G		F			F		F		F		P	F	
S396	0000	0141	74	ST PONY TRUSS	SAVOY CR	F		G			G		G		G		F	F	F	F		G		P		P	F	

A	FEET B		D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S410 0000 0000		UNDERPASS	KEVIN INT-I15	G		E		E	E					E			E	E	G	E	E	E		E	E		
S410 0000 0112	70	PRE CONC BM	W FK WILLOW CR	G		E		E	E		G		G	E			E	E		E	E	E	E	E	E		
S410 0000 0162	35	STEEL I BEAM	WILLOW CR	F		F		F	F		G		G	F				P		F	F	C		C	P		X
S410 0000 0166	23	STEEL I BEAM	E FK WILLOW CR	F		P		C	F		G	G	G	F				P		F	F	C		C	P		X
S410 0000 0217	31	STEEL I BEAM	TRAIL CR	F		G		G	F		G		F	G				P		F	F	C		P	F		X
S417 0000 0071	450	STEEL GIRDER	MARIAS R	F		G	G	G	G	G	P	G	F	G	G		G	G	P	F	G	G	G	P	G		X
S432 0000 0291	23	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G		G	G	G		P	G		
S436 0000 0006	25	T T TRESTLE	IRRIGATION CA	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
S436 0000 0013	75	T T TRESTLE	FIFTEEN MILE CR	G	G	G	G	G	G	G	G		G		G			G	G	G	G	G		F	G		
S444 0000 0035	50	T T TRESTLE	WILLOW CR	G	G	G		P	F	G	G		G		G			G	F	F	F	F		P	G		
S444 0000 0037	100	T T TRESTLE	CUT BANK CR	G	G	G		F	F	G	G		G		F			G	G	G	G	F		P	G		
S444 0000 0057	38	T T TRESTLE	COBELLE CR	G	G	G		G	G	G	G		G		G			G	G	G	G	G		G	G		
S445 0000 0091	163	PRE CONC BEAMS	CUT BANK CR	G		E	E	E	E	E	G	E	G	E			E	E		E	E	E		F	E		

			FEET			E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X			
S448	0000	0021	75	T T TRESTLE	BIG SANDY CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	X
S449	0000	0002	102	PRE CONC BEAM	SAGE CR	E		E	E	E	E	E	G	E	G		E			E	E	E	E	E		E	E	
S452	0000	0012	96	ST PONY TRUSS	BULLHOOK CR	F	F	F	G	P	C		G		G		F	F				G	G	F		P	F	X
S457	0000	0082	110	CONCRETE T BEAM	UNTIBER DAM	G		G	G	G	G	G	G		G	G			F	F		G		G	G	P	F	X
S464	0000	0046	173	PRE CONC BEAMS	CUT BANK CR	G		E	E	E	E	E	G	E	G	E			E	E		E	E	E		E	E	
S464	0000	0169	43	STEEL GIR	S FK MILK R	F		F			F		G		G	F	G					F				P	F	
S464	0000	0239	27	UNT T TRESTLE	DRY FK MILK R	F	P	P		P	P		G		P	F				P		F					P	X
S483	0000	0030	52	STEEL I BEAM	ROCKY COULEE	F		G		F	F		G		P		F			F		P	F	P		P	F	
S483	0000	0278	150	T T TRESTLE	S FK MILK R	F	F	P		F	G	C	P	F	F		G			F		G	P	P		P	P	X
S523	0000	0007	25	T T TRESTLE	DRAINAGE	F	F	C		P	F		G		G		F			F		C		P			P	X
S529	0000	0000	84	CONT CONC SLAB	RED ROCK CR	E	E	E			E		G	E	G					E	G	E		E		E	E	
S529	0000	0010	213	PRE CONC BEAM	MILK R	F		E	E		E	E	G	E	G		E			E		E		E		E	E	

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Columns E thru Z
E = Excellent
G = Good
F = Fair
P = Poor
C = Critical

Column Z1
N = New
R = To be Removed
- Unable to Inspect

Column Z2
X = Written Explanation

CONTROL	DESCRIPTIVE FEATURES			CONDITION RATING																							
A	B	C	D	E	F	G	H		J	K	L	M	N	O	P	Q	R	S		U		W			Z	Z1	Z2
S529 0000 0055	30	UNT T TRESTLE	DRAINAGE	F	P	P		P			G		G		F			P		P		F		P	P		X
S534 0000 0078	24	T T TRESTLE	DRAINAGE	G	G	G		F	G		G		G		G					G	F	P		P	G		
S534 0000 0098	94	ST GIRDER	DRY FK MARIAS R	G		E	E	E	E	E	G		G	G				E		E	E	E		E	E		
S534 0000 0185	24	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			F		G	G	P		P	G		

HAVRE DIVISION

I-15-2954-3469 113' Conc. T. Beam Dry Fork Marias
North end fill is sloughing out from backwall and leaves a cavity there.

I-15-2954-3627 541' St. Plate Marias River
Bad erosion and fill condition on north end. Fill is covering up some structural steel and has ruined paint. Some broken rails. Some bullet holes through steel web. Quite a bit of drift collected on one pier.

P-1-1532-2091 142' Conc. T. Beam Midvale Creek
Extensive spalling on rail, curb and edges of caps. Cracks show in diaphrams and bents.

P-1-2093-2102 760 St. Truss Two Medicine Creek
Extensive spalling on corners and edges of some bents. There is now a visual angle in rail and curb at 2nd bent back from east end bent. This east end bent fill has a history of sliding and it is possible that the end bent and first bent back is drifting off line. See photo.

P-1-2794-3780 312' Steel Girder Great Northern R.R.
Center exp. joint is opening up a little more than it was probably planned for. Exp. joint toward east end is loose and noisey when traffic goes over it. Maintenance has worked on it but it needs additional bolting.

P-1-3791-3924 11' T. T. Trestle Stockpass
Rail is gone.

P-1-3791-4045 94' Conc. T. Lodge Creek
One bearing haunch on concrete girder is cracked. Cavity under east end.

P-1-3791-4099 196' Thru St. Truss Battle Creek
Piece of concrete spalled off near shoe bent 2.

P-3-3402-3823 18' Unt. Timber Trestle Drainage
One cap is squashed from load. Stringers have rotted sections. Piling all look somewhat deteriorated and one is badly cracked at stream bed.

P-3-4250-4302 120' Steel Truss North Fork Cut Bank Creek
South end bent footing has been undercut. Expansion joint is tight, no room for movement. Extensive spalling on caps.

HAVRE DIVISION

P-3-4250-4340 48' Conc. Arch Drainage
Left rail partly gone.

P-3-4250-4516 312' Cont. St. Girder St Mary's River
Nut gone off rocker pin on south end bent and pin has slipped back.

M-232-0000-0001 826' St. I. Beam Great Northern R.R.
Photo shows fire damage of first 13 spans. This part of the structure is generally in poor condition. Fire occurred 15 years ago. One stringer broken in span. General deterioration of concrete super structure. Several sway bracing broken or unbolted. See photos.

M-232-0000-0002 287' Steel Truss Milk River
The truss part of this structure is in fair condition. The horizontal clearance is so narrow that one way traffic is necessary. The last span is an approach to the main structure. It has been damaged by flood waters to the extent of extreme settlement. This has been corrected by county force with a mud sill. The only poor part of this span is one only outside stringer is askew as seen in photo. The structural steel is rusting and badly in need of a paint job. See photo.

S-216-0000-0053 57' T. T. Trestle Soberup Creek
Scour at the west bent is quite bad. New backing planks have been added. Pile apparently settling as seen in photo. Shims betweel piling and cap. See photos.

S-216-0000-0095 150' T. T. Trestle Dupuyer Creek
One stringer in first span has a crack that is starting to open up.

S-223-0000-0435 57' T. T. Trestle Drainage
Piling in bents # 2 and # 3 are exposed approximately 5 feet due to hole washed out under bridge. West corner railing post split beyond repair. See photo.

S-234-0000-0020 96' Steel Pony Truss Scott Coulee Canal
Railing on both ends of structure are severly damaged. Some wing planks are rotten.

S-366-0000-0059 106' Cont. St. Girder Dry Fork Marias River
Some riprap has been added to the end fills which appears in poor condition. Scour on east end of structure very bad. Could wash under end bent.

HAVRE DIVISION

S-396-0000-0087 48' Steel I Beam Wayne Creek
Railing has been damaged and is very poor condition. Deck planks broke and loose. Won't last long. One plank splintered, shattered, deteriorated and dangerous. See photo.

S-410-0000-0162 35' St. I. Beam Willow Creek
One railing gone the other out of shape. Girders quite rust in need of paint. The only curb is 2 x 12 timber.

S-410-0000-0166 23' St. I. Beam East Fork Willow Creek
One railing gone the other badly bent. Curb cracked and loose. Far left wing wall gone replaced with riprap. Far right wing wall cracked. Paint is gone on all parts of structure. See photo.

S-410-0000-0217 31' St. I. Beam Trail Creek
Railing one on both sides. Paint gone on all parts of structure.

S-417-0000-0071 450' Steel Girder Marias River
Drift has collected up in the structural steel. Bullet holes in webs. End fills are settling and water is cutting around some wingwalls.

S-448-0000-0021 75' T. T. Trestle Big Sandy Creek
One broken stringer center span and loose bracing.

S-452-0000-0012 96' St. Pony Truss Bull Hook Creek
The top plank of the east backwall is pushing outward. It should be replaced.

S-457-0000-0082 110' Conc. T. Beam Tiber Dam
Posted load limit 15 ton. Deck on span three has shifted about 3 inches out of alignment, apparently by shome shifting in sub-structure.

S-464-0000-0239 27' Untr. Timber Trestle Dry Fork Milk River
Some piles are rotted on surface. Part of wing rail hanging loose. Water can flow under backing plank on south end.

HAVRE DIVISION

S-483-0000-0278 150' T. T. Trestle South Fork Milk River
Most of the icebreakers are gone. The ones that remain are in very poor condition. Drift seems to pile up easily as seen in photo. Many of the flashboards are gone or broken. The pile in bent # 4 leans towards the upstream railing and posts are cracked and broken. See photo.

S-523-0000-0007 25' Untreated Timber Trestle Drainage
End cap is rotten and deteriorated. Deck planks are broken and holes are left in deck. One end bent has sunk leaving bridge angled to the grade. Rail is gone on one side and broken on the other. See photo.

S-529-0000-0055 30' Untreated Timber Trestle Drainage
One broken stringer. One badly broken deck plank and several others in bad shape. Cap on south end is split. See photos.

P-1-2093-2102

M-232-0000-0001

M-232-0000-0001

M-232-0000-0002

S-216-0000-0053

S-216-0000-0053

S-223-0000-0435

S-396-0000-0087

S-410-0000-0166

S-483-0000-0278

S-529-0000-0055

S-529-0000-0055

GLENDIVE CONSTRUCTION DIVISION

I	94	1531	1668	95	T T TRESTLE	WILLIAMS COU	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
I	94	1531	1695	57	T T TRESTLE	CAMP CR	G	G	G	G	G	G	N	P	G	F	N	G	N	N	G	G	G	G	G	N	F	F
I	94	1531	1732	633	CONT ST TRUSS	POWDER R	F	N	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G
I	94	1531	1761	57	T T TRESTLE	CONNS COU	G	E	E	N	E	E	N	E	G	E	N	E	N	N	E	E	E	E	G	N	G	E
I	94	1531	1779	19	T T TRESTLE	STOCKPASS & DR	F	E	E	N	E	E	N	E	E	E	N	E	N	N	E	E	E	E	G	N	G	E
I	94	1531	1787	38	T T TRESTLE	DRAINAGE	F	E	E	N	E	E	N	E	E	E	N	E	N	N	E	E	E	E	G	N	G	E
I	94	1531	1799	38	T T TRESTLE	DRAINAGE	F	E	E	N	E	E	N	E	E	E	N	E	N	N	E	E	E	E	G	N	G	E
I	94	1531	1835		UNDERPASS	CMSTP&P RR	E	N	G	N	G	G	N	N	N	N	G	N	N	G	N	G	G	N	N	N	P	G
I	94	1531	1888	220	CONT ST GIRDER	O FALLON CR	F	N	P	G	G	P	G	G	G	G	G	N	N	P	G	G	F	N	G	P	G	F
I	94	1531	1891	146	CONCRETE T BEAM	NP RY	P	N	G	N	G	G	N	N	N	N	G	N	N	F	G	G	G	N	G	F	N	G
I	94	1531	1910	1142	STEEL TRUSS	YELLOWSTONE R	G	N	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	F	G	G	G	G
I	94	1531	1933	65	STEEL I BEAM	HATCHET CR	G	G	G	N	N	G	N	G	F	F	G	N	N	G	G	G	G	N	G	N	G	G
I	94	1531	1964	165	STEEL I BEAM	BAD ROUTE CR	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	G	G	G
I	94	1531	2011	165	STEEL I BEAM	CRACKER BOX CR	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	G	G	G
I	94	1531	2059	65	STEEL I BEAM	USRS CANAL	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	G	G	G
I	94	1531	2060	190	STEEL I BEAM	CLEAR CR	P	G	G	N	N	P	N	G	G	G	G	N	N	G	G	G	G	N	G	G	G	F
I	94	1531	2063	31	STEEL I BEAM	CANAL	G	N	G	N	N	G	N	G	N	G	G	N	N	G	G	G	G	N	G	N	G	G
I	94	1531	2086	65	STEEL I BEAM	WHOOPUP CR	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	N	G	G
I	94	1531	2109	40	STEEL I BEAM	USRS CANAL	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	N	G	G

A	FEET B	C	D	END E	PILE F	BENTS G	PIERS H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
I 94 1531 2110	90	STEEL I BEAM	SAND CR	G	G	G	N	N	G	N	G	G	G	G	N	N	G	G	G	G	N	G	N	G	G		
I 94 1531 2112	21	CONCRETE T BEAM	USRS CANAL	G	N	G	N	N	G	N	G	N	G	G	N	N	N	G	G	G	N	G	N	N	G		
I 94 1531 2138	21	CONCRETE T BEAM	USRS CANAL	F	N	G	N	N	G	N	F	N	F	G	N	N	N	G	G	G	N	G	N	N	G		
I 94 1531 2154	120	CONT CONC T BM	UPPER 7 MILE CR	E	N	E	E	E	E	N	E	E	G	E	N	N	E	E	G	G	N	E	N	G	G		
I 94 1531 2154P	120	CONT CONC T BM	UPPER 7 MILE CR	E	N	E	E	E	E	N	E	E	G	E	N	N	E	E	G	G	N	E	N	G	G		
I 94 2162 2163	120	CONT CONC T BM	DRY CR	G	N	E	N	E	E	N	E	E	E	E	N	N	E	E	G	G	N	E	N	G	G		
I 94 2162 2163P	120	CONT CONC T BM	DRY CR	G	N	E	N	E	E	N	E	E	E	E	N	N	E	E	G	G	N	E	N	G	G		
I 94 2169 2175	131B	CONCRETE GIRDER	YELLOWSTONE R	G	N	E	E	E	G	G	E	E	G	E	N	N	E	E	G	E	E	E	G	G	G		
I 94 2169 2265	106	CONT ST GIRDER	GRIFFITH CR	G	N	G	G	E	E	N	E	G	G	E	N	N	E	G	G	G	N	G	G	G	G		
I 94 2169 2355	123	PRE CONC BEAM	HODGES SEP-CO RD	P	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	E	N	E	N	E	E		
I 94 2169 2460		UNDERPASS*	W INT-SR 7	G	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	G	N	E	G	G	E		
I 94 2460 2463	2B6	PRE CONC BEAMS	BEAVER CR	G	N	E	E	E	E	G	G	E	G	E	N	N	E	E	G	G	N	E	G	G	E		
I 94 2460 2466		UNDERPASS*	E INT-SR 7	G	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	G	N	E	G	G	E		

P	2	6161	6779	140	STEEL GIRDER	SANDSTONE COU	G	N	G	F	F	F	G	G	G	F	G	N	N	G	F	G	G	N	F	F	F	F
P	2	6161	6807	133	STEEL GIRDER	SANDSTONE CR	F	N	G	F	G	G	G	G	G	F	G	N	N	G	F	G	G	N	F	F	F	F
P	2	6161	6823	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	F	G
P	2	6161	6829	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	F	G	G	N	G	N	N	G	G	G	G	F	N	F	G
P	2	6161	6847	50	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	P	G
P	2	6161	6859	19	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	P	G
P	2	6161	6863	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	F	N	G	G	G	N	G	N	N	G	G	G	G	G	N	P	G
P	2	6161	6874	76	T T TRESTLE	TIMBER CR	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	P	G
P	2	6161	6898	57	T T TRESTLE	RED BUTTE CR	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P	2	6161	6914	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	P	G
P	2	6161	6924	57	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	F	N	G	N	N	G	G	G	G	G	N	F	G
P	2	6930	6956	213	PRE CONC BEAM	CMSTP&P RR	E	N	E	N	E	E	N	N	N	N	E	N	N	E	E	N	E	N	E	N	G	E
P	15	2121	2310	57	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	G	F	D	G	G	N	G	G
P	15	2121	2325	25	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	F	D	G	G	N	G	G
P	15	2121	2327	76	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	F	D	G	G	N	G	G
P	15	2121	2345	101	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	G	G	G	G	N	G	G
P	15	2121	2356	93	T T TRESTLE	DRAINAGE	G	F	F	N	N	G	N	G	G	G	N	F	N	N	G	G	G	G	G	N	G	G
P	15	2121	2392	404	STEEL BEAM	LITTLE DRY CR	G	G	G	F	N	G	G	G	F	F	G	F	N	F	F	G	G	G	G	F	F	F

A	B FEET	C MAXIMUM SPAN	D	E FENC	F	G BENTS	H PIERS	I WINGWALLS	J	K ICE BREAKERS	L	M	N	O	P	Q	R SHOES	S CURBS	T	U	V	W	X	Y	Z	Z1	Z2
P 15 2121 2474	95	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2488	125	T T TRESTLE	TIMBER CR	G	G	G	G	G	G	G	G	F	F	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2497	123	T T TRESTLE	SKULL CR	G	G	G	G	G	G	G	G	P	F	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2530	57	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2533	85	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2547	85	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	F	N	N	G	G	G	G	G	N	G	G		
P 15 2486 2548	76	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 15 2486 2553	95	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2571	75	T T TRESTLE	COULEE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2579	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2588	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2601	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2615	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2618	38	T T TRESTLE	DIRTY CR	G	G	G		G	G	N	P	F	F	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2670	63	T T TRESTLE	COTTER CR	G	G	G		G	G	N	G	F	F	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2702	76	T T TRESTLE	STONEY BUTTE CR	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2716	76	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	F	F	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2733	57	T T TRESTLE	ANTELOPE CR	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	F	G	G	G	N	G	G		
P 15 2486 2756	95	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	F	G	G	G	N	G	G		

P	15	2486	2765	114	T T TRESTLE	OL CH REDWATER R	G	G	G	G	G	G	N	G	F	F	N	G	N	N	G	F	G	G	G	N	F	G
P	15	2486	2775	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	F	N	G	N	G	N	N	G	F	G	G	G	N	F	G
P	15	2795	2800	267	STEEL BEAM	REDWATER R	G		G	G		G	G	G		G	G			G	G	G	G	G	G	G	G	G
P	15	2807	2836	92	PRE CONC BEAM	BUFFALO SPR CR	P	N	E	E	E	E	N	G	E	G	E	N	N	E	E	G	E	N	E	N	G	G
P	15	2807	2981	57	T T TRESTLE	HAY CR	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	G	G	G	G	N	G	G
P	15	2807	2992	76	T T TRESTLE	HAY CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	F	G
P	15	2807	3004	57	T T TRESTLE	SAND CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	F	G
P	15	2807	3017	57	T T TRESTLE	DRAINAGE	G	G	G	G	F	F	N	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G
P	15	2807	3069	112	PRE CONC BEAM	N FK UPPER 7MI C	G	N	E	E	E	E	N	G	G	G	E	N	N	E	G	G	G	N	E	N	G	E
P	15	2807	3139	102	PRE CONC BEAM	UPPER 7 MI CR	G	N	E	E	E	E	N	G	G	G	E	N	N	E	G	G	G	N	E	N	G	E
P	15	3554	3554	163	PRE CONC BEAM	W INT-I 94	G	N	E	N	E	E	N	N	N	N	E	N	N	E	G	G	G	N	G	G	G	G
P	15	3558	3559	276	CONT ST GIRDER	BEAVER CR	G	N	G	G	G	G	G	G	G	G	G	N	N	G	G	G	F	N	G	G	F	G
P	15	3558	3563	173	PRE CONC BEAM	E INT I 94	G	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	G	N	G	G	G	G
P	18	0000	0434	95	T T TRESTLE	RED BUTTE CR	G	G	G	G	N	G	G	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G
P	18	0000	0439	57	T T TRESTLE	DRAINAGE	G	F	G	N	N	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G
P	18	0000	0450	76	T T TRESTLE	DRAINAGE	F	G	F	N	N	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G
P	18	0000	0463	57	T T TRESTLE	DRAINAGE	F	G	G	N	N	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G
P	18	0000	0478	95	T T TRESTLE	THOMPSON CR	G	G	G	N	N	G	G	G	G	G	N	G	N	N	F	G	G	G	G	N	G	G

A	B FEET	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P 18 0000 0490	38	T T TRESTLE	DRAINAGE	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	G	G	G	G	N	G	G		
P 18 0000 0518	57	T T TRESTLE	DRAINAGE	F	F	G	N	N	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 18 0000 0524	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	N	N	N	G		
P 18 0000 0527	57	T T TRESTLE	DRAINAGE	G	F	G	N	N	G	N	G	F	F	N	G	N	N	G	G	G	G	G	N	F	G		
P 18 0000 0540	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	N	N	N	N	G	N	N	G	G	G	G	N	N	N	G		
P 18 0000 0590	171	STEEL I BEAM	LITTLE DRY CR	F	G	G	G	N	G	G	G	F	F	G	F	N	N	F	G	G	G	G	N	F	G		
P 18 0000 0592	57	T T TRESTLE	WHITE HORSE CR	F	F	F	F	N	G	N	G	N	F	N	G	N	N	F	G	G	G	G	N	F	F		
P 18 0000 0614	57	T T TRESTLE	RED HORSE CR	F	G	G	G	N	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	F	G		
P 20 0000 0043	112	PRE CONC BEAM	DEER CR	F	N	E	E	E	E	N	E	E	E	E	N	N	E	E	G	E	N	E	N	E	F		
P 20 0000 0100	132	PRE CONC BM	LOWER 7 MILE CR	E	N	E	E	E	E	N	E	F	F	E	N	N	F	F	G	E	N	E	N	E	E		
P 20 0000 0124	122	PRE CONC BM	MORGAN CR	E	N	E	E	E	E	N	E	E	E	E	N	N	E	E	G	E	N	E	N	E	F		
P 20 0000 0156	190	T T TRESTLE	THIRTEEN MILE CR	G	G	G	G	G	G	N	G	N	G	G	G	N	N	G	G	G	G	G	N	G	G		
P 20 0000 0178	57	T T TRESTLE	LINDEN CR	G	G	G	G	G	G	N	G	N	G	G	C	N	N	G	G	G	G	G	N	G	G		
P 20 0000 0250	150	T T TRESTLE	BURNS CR	G	G	G	G	G	G	G	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 20 0000 0292	57	T T TRESTLE	BEEF SLOUGH	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 20 0000 0312	57	T T TRESTLE	GARDEN COULEE	G	G	G	G	G	G	N	G	G	F	N	G	N	N	G	G	G	G	G	N	F	G		
P 20 0000 0322	75	T T TRESTLE	USRS CANAL	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	F	G	G	P	N	F	G		
P 20 0000 0325	95	T T TRESTLE	DUNLAP CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G		

A	B			E	F		H			K		M	N				R	S	T						Z
P 20 0000 0328	63	T T TRESTLE	USRS CANAL	P	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P 20 0000 0375	75	T T TRESTLE	USRS CANAL	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P 20 0000 0378	57	T T TRESTLE	SEARS CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	F	G
P 20 0000 0466	76	UNT T TRESTLE	FOX CR	G	G	G	P	N	G	G	G	G	G	N	P	N	N	P	F	P	G	P	N	F	P
P 20 0000 0499	38	T T TRESTLE	DITCH	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	F	G
P 20 0500 0516	114	T T TRESTLE	LONE TREE CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	F	G	G	G	N	F	G
P 20 0525 0595	114	T T TRESTLE	FIRST HAY CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P 20 0525 0600	95	T T TRESTLE	SECOND HAY CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	G	G	G	G	N	F	G
P 20 0525 0608	76	T T TRESTLE	THIRD HAY CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P 22 0886 1126	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	N	N	G	N	N	G	G	G	G	G	N	G	G
P 22 0886 1153	95	T T TRESTLE	S FK 1ST HAY CR	G	G	G	G	G	G	N	G	F	G	N	G	N	N	G	P	G	G	G	N	G	G
P 22 0886 1156	38	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	P	G	N	G	N	N	G	G	G	G	G	N	G	G
P 22 0886 1229	11	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G
P 22 0886 1243	19	T T TRESTLE	STOCKPASS	F	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P 22 0886 1250	75	T T TRESTLE	USRS CANAL	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	G	G
P 25 0000 0002	114	T T TRESTLE	HORSE CR	P	F	F	F	P	P	G	F	F	P	N	G	N	N	G	G	G	F	G	N	G	F
P 25 0000 0009	7	T T TRESTLE	STOCKPASS	G	G	G	N	G	G	N	P	N	G	N	G	N	N	G	F	G	G	G	N	G	G

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P 25 0000 0017	38	T T TRESTLE	LONE TREE CR	G	G	G	G	G	G	N	G	F	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 25 0000 0024	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	F	F	N	G	N	N	G	F	G	G	G	N	F	G		
P 25 0000 0055	76	T T TRESTLE	LOST CR	F	G	G	G	N	G	N	G	F	F	N	G	N	N	G	F	G	G	F	N	F	F		
P 25 0000 0085	76	T T TRESTLE	S FK BUFFALO CR	G	G	G	G	N	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	F	G		
P 25 0000 0102	76	T T TRESTLE	N FK BUFFALO CR	G	G	G	G	N	G	N	G	F	G	N	G	N	N	G	G	G	F	F	N	P	G		
P 25 0000 0126	11	T T TRESTLE	STOCKPASS	G	G	G	N	N	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	F	G		
P 25 0000 0141	11	T T TRESTLE	STOCKPASS	G	G	G	N	N	G	N	G	G	G	N	G	N	N	F	F	G	G	F	N	P	G		
P 25 0000 0149	76	T T TRESTLE	DUCK CR	G	G	G	G	N	F	N	G	P	P	N	G	N	N	G	F	G	G	G	N	P	F		
P 25 0000 0185	57	T T TRESTLE	DRAINAGE	G	G	G	F	N	F	N	G	F	P	N	G	N	N	G	F	F	F	G	N	G	F		
P 25 0000 0202	114	T T TRESTLE	COW CR	G	G	G	G	N	G	F	G	G	G	N	G	N	N	G	F	G	F	G	N	F	G		
P 25 0000 0212	57	T T TRESTLE	DRAINAGE	F	G	G	N	N	G	N	G	G	G	N	G	N	N	F	F	G	G	G	N	G	G		
P 25 0000 0227	11	T T TRESTLE	STOCKPASS	G	G	G	N	N	G	N	G	G	G	N	G	N	N	G	F	G	G	G	N	G	G		
P 25 0000 0242	19	T T TRESTLE	STOCKPASS	G	G	G	N	N	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 26 0000 0003	57	T T TRESTLE	DITCH	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 26 0000 0012	1231	STEEL TRUSS	YELLOWSTONE R	G	N	G	G	F	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	F	G		
P 26 0000 0022	57	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P 26 0000 0061	113	CONCRETE T BEAM	BENNIE PEER CR	G	N	G	F	G	G	G	G	G	F	G	N	N	G	G	G	G	N	G	N	N	F		

P 27 0000 0013	38	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	N	G	N	P	N	N	G	G	G	G	G	N	G	F
P 27 0000 0023	38	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	P	G	N	G	N	N	G	G	G	G	G	N	G	F
P 27 0000 0050	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	F	G	F	G	G	N	G	G
P 27 0000 0060	95	T	T	TRESTLE	LITTLE BEAVER CR	P	G	G	G	G	G	G	G	F	P	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0064	57	T	T	TRESTLE	COLLINS CR	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0072	11	T	T	TRESTLE	STOCKPASS	G	G	G	N	G	G	N	N	N	N	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0080	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0095	11	T	T	TRESTLE	STOCKPASS	P	G	G	N	G	G	N	F	N	G	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0114	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	F	F	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0151	11	T	T	TRESTLE	STOCKPASS	P	G	G	N	G	F	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0173	11	T	T	TRESTLE	STOCKPASS	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0183	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0202	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0000 0214	57	T	T	TRESTLE	DRAINAGE	F	G	G	N	G	G	N	G	F	F	N	G	N	N	F	G	G	G	G	N	G	G
P 27 0000 0351	57	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	F	G	G	G	G	N	F	G
P 27 0354 0358	63	T	T	TRESTLE	SANDSTONE CR	G	G	G	N	G	G	N	G	G	F	N	G	N	N	G	G	G	G	G	N	F	G
P 27 0354 0550	75	T	T	TRESTLE	ASH CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	F	G	G	G	G	N	G	G
P 27 0354 0574	38	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G
P 27 0354 0608	45	T	T	TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Columns E thru Z
E = Excellent
G = Good
F = Fair
P = Poor
C = Critical

Column Z1
N = New
R = To be Removed
U = Unable to Inspect

Column Z2
X = Written Explanation

CONTROL BRIDGE NUMBER					DESCRIPTIVE FEATURES			CONDITION RATING SUBSTRUCTURE										SUPERSTRUCTURE													
F. A. SYSTEM	F. A. ROUTE NUMBER	CONTROL-JUNCTION MILEPOST TO TENTHS	BRIDGE LOCATION MILEPOST TO TENTHS	DESCRIPTIVE	TOTAL LENGTH FEET	MATERIAL & TYPE MAXIMUM SPAN - Also Structures not carrying road by type of facility, Underpass, Tunnel, Ferry	NAME OF FEATURE CROSSED (River, Creek, Canal, Irrigation Ditch, Drainage, Railroad, Highways, Interchanges and Separations, Etc.)	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION JOINTS	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
A					B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	27	0354	0620		57	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	F	G	F	G	G	N	G	G		
P	27	0354	0654		19	T T TRESTLE	DR & STOCKPASS	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	27	0354	0670		19	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	F	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	27	0354	0680		45	T T TRESTLE	DRAINAGE	G	F	F	N	G	G	N	G	G	G	N	G	N	N	G	G	F	G	G	N	G	F		
P	27	0354	0726		76	T T TRESTLE	DRAINAGE	G	F	G	F	G	G	N	G	F	F	N	G	N	N	G	G	F	G	G	N	G	F		
P	27	0354	0783		150	T T TRESTLE	BEAVER CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	27	0354	0796		150	STEEL GIRDER	BEAVER CR	G	N	G	G	G	G	G	G	G	G	G	N	N	G	G	G	G	N	G	G	F	G		
P	27	0354	0799			UNDERPASS	NP RY	G	N	G	N	N	G	N	N	N	N	G	N	N	G	G	F	N	N	G	N	P	G		
P	42	0000	0054		205	PRE CONC BEAM	TIMBER CR	G	N	G	G	G	E	G	G	G	G	G	N	N	E	E	G	G	N	E	G	E	E		
P	42	0000	0147		133	PRE CONC BEAM	NELSON CR	G	N	G	G	G	E	N	G	G	G	G	N	N	E	E	G	G	N	E	N	E	E		
P	51	0000	0004		88	T T TRESTLE	BUFFALO SPR CR	F	G	G	G	G	G	N	G	N	G	N	G	N	N	F	F	G	G	F	N	G	G		
P	51	0000	0072		88	T T TRESTLE	COTTONWOOD CR	F	G	G	G	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	51	0000	0105		88	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	N	P	N	G	N	N	G	G	G	G	G	N	G	G		
P	51	0000	0135		88	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	51	0000	0172		57	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	G	G		
P	51	0000	0699		75	T T TRESTLE	USBS CANAL	G	G	G	F	F	F	N	G	N	G	N	N	N	N	G	N	G	N	G	N	G	F		

S252	0000	0015	100	T T TRESTLE	HORSE CR	G	G	G	G	G	G	G	G	N	F	N	G	N	N	G	P	G	G	G	N	P	G
S252	0000	0070	38	T T TRESTLE	DENWOODY CR	G	G	G	G	G	G	N	G	N	F	N	G	N	N	G	P	G	G	G	N	P	G
S252	0000	0080	75	T T TRESTLE	HORSE CR	G	G	G	G	G	G	G	G	N	F	N	G	N	N	F	N	G	G	G	N	P	G
S252	0000	0130	57	T T TRESTLE	HORSE CR	G	G	G	G	G	G	G	G	N	F	N	G	N	N	G	N	G	G	G	N	P	G
S252	0000	0141	38	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	N	G	G	G	N	P	G
S253	0000	0009	825	RIV PL GIRDERS	YELLOWSTONE R	G	N	G	G	N	G	G	G	G	G	E	N	N	G	G	P	G	N	G	G	G	E
S253	0000	0046	363	STEEL I BEAM	CHERRY CR	G	G	G	G	G	G	G	G	F	G	G	N	N	G	F	G	F	G	F	F	P	F
S253	0000	0080	95	T T TRESTLE	BRACKETT CR	G	G	G	G	N	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	P	G
S253	0000	0094	133	T T TRESTLE	CEDAR CR	G	G	G	G	N	G	N	G	G	G	N	G	N	N	G	G	G	G	F	N	P	G
S253	0000	0147	76	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	F	P	G	G	P	N	P	F
S253	0000	0174	76	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G
S253	0000	0188	95	T T TRESTLE	DRAINAGE	G	G	G	N	G	G	N	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G
S253	0000	0224	75	T T TRESTLE	CEDAR CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G
S253	0000	0269	38	T T TRESTLE	CEDAR CR	G	G	G	G	G	G	N	G	F	F	N	G	N	N	F	P	G	G	F	N	P	G
S253	0000	0371	75	T T TRESTLE	EAST DUCK CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	F	P	G	G	F	N	P	G
S253	0000	0462	150	T T TRESTLE	REDWATER R	F	G	G	G	G	G	G	G	N	G	N	G	N	N	P	P	G	G	P	N	P	F
S254	0000	0175	25	T T TRESTLE	LOWER 7 MILE CR	G	G	G	N	G	G	N	G	N	F	N	G	N	N	G	N	G	G	G	N	G	G

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S254 0000 0229	25	T T TRESTLE	S FK 13 MILE CR	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	N	G	G	G	N	G	G		
S254 0000 02B8	25	T T TRESTLE	MID FK BURNS CR	G	G	G	N	G	G	N	G	G	F	N	G	N	N	G	N	G	G	G	N	G	G		
S254 0000 0532	74	PRE CONC BEAM	REDWATER R	G	N	G	G	G	G	N	G	N	G	G	N	N	N	G	N	G	N	G	N	G	G		
S261 0000 0000	163	PRE CONC BEAM	INT I94 W WIBAUX	G	N	E	N	E	E	N	N	N	N	E	N	N	E	E	G	E	N	E	G	G	E		
S261 0000 0004	56	CONC T BEAM	DRY CR	G	N	F	N	N	F	N	G	N	G	F	N	N	N	F	G	F	N	F	N	N	F		
S261 0000 0435	40	STEEL TRESTLE	OBRIEN CR	P	P	P	N	P	P	N	G	N	G	F	N	N	N	N	N	G	N	N	N	P	P		
S270 0000 0036	35	STEEL I BEAM	HORSE CR	G	N	F	N	G	G	N	G	G	G	F	N	N	N	P	N	F	N	P	N	P	F		
S270 0000 0066	142	PRATT ST TRUSS	LIT MISSOURI R	P	F	C	P	P	C	F	P	F	P	F	F	P	N	P	N	P	P	P	N	P	C		X
S270 0000 01B9	60	ST PONY TRUSS	COTTONWOOD CR	F	F	P	P	P	P	N	G	N	P	N	F	F	N	P	N	F	P	P	N	P	P		X
S270 0000 019B	23	STEEL I BEAM	HACKBERRY CR	F	F	F	N	F	F	N	G	N	G	F	N	N	N	P	N	F	F	P	N	P	F		
S277 0000 0209	23	TIMBER TRESTLE	WHITETAIL CR	G	N	F	N	P	F	N	G	N	G	N	G	N	N	G	N	G	G	G	N	F	F		
S277 0000 0253	62	T T TRESTLE	MUSKRAT CR	F	G	F	G	F	F	N	G	N	F	N	P	N	N	P	N	F	F	P	N	P	F		
S277 0000 0290	51	T T TRUSS	CORRAL CR	P	F	P	F	P	C	N	G	N	G	N	C	C	N	C	N	C	P	C	N	N	C		X
S277 0000 0315	104	ST I BM PILES	BOX ELDER CR	F	G	G	G	F	F	N	G	N	F	F	F	N	N	P	N	P	F	P	N	P	F		
S292 0000 0207	225	PRE CONC BEAM	BOX ELDER CR	G	N	E	E	E	E	G	F	G	F	E	N	N	E	E	P	G	N	E	G	G	G		

A	B FEET	C	D	E	F	G BENTS	H PIERS	I WINGWALLS	J	K ICE BR A ERS	L DRIFT	M R P RAP	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
S321 0000 0060	100	T T TRESTLE	PENNEL CR	G	G	G	G	G	G	G	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G		
S322 0000 0111	133	STEEL GIRDER	LITTLE BEAVER CR	G	G	G	G	F	G	F	F	F	P	G	G	N	G	F	P	G	G	G	G	G	F		
S323 0000 0177	183	CONCRETE T BM	BOX ELOER CR	F	N	G	G	G	G	G	G	G	G	G	N	N	G	G	N	G	N	G	G	P	G		
S323 0000 0565	172	ST PRATT TRUSS	LIT MISSOURI R	F	F	F	C	N	G	N	G	F	F	G	G	F	G	P	N	F	F	P	N	P	F		
S335 0000 0017	50	T T TRESTLE	ORAINAGE	P	G	G	N	G	G	N	G	P	F	N	G	N	N	G	N	G	G	G	N	F	F		
S335 0000 003B	52	T T TRESTLE	ORAINAGE	F	F	F	N	G	G	N	F	N	G	N	F	N	N	P	P	F	F	P	N	P	P		
S335 0000 0053	102	PRE CONC BEAM	SANO CR	P	N	G	G	G	G	N	F	P	F	E	N	N	E	G	P	G	N	G	N	G	F		
S335 0000 0144	200	T T TRESTLE	CEOAR CR	G	G	G	N	G	G	N	P	F	P	N	P	N	N	F	P	P	P	F	N	P	P		
S336 0000 0053	50	T T TRESTLE	FK OF BEAVER CR	G	G	G	G	G	G	G	G	N	F	N	G	N	N	G	P	G	G	G	N	G	G		
S336 0000 0070	75	T T TRESTLE	BEAVER CR	G	G	G	G	G	G	G	G	N	G	N	G	N	N	G	P	G	G	G	N	G	G		
S340 0000 0019	63	T T TRESTLE	PLUM CR	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	P	G	G	G	N	F	G		
S413 0000 0004	150	T T TRESTLE	BEAVER CR	G	G	G	G	N	G	G	G	G	G	N	G	N	N	G	P	G	G	G	N	P	G		
S413 0000 003B	25	T T TRESTLE	ORAINAGE	G	G	G	N	G	G	N	G	N	G	N	G	N	N	G	G	G	G	G	N	P	G		

S413 0000 0246	100	T T TRESTLE	BEAVER CR	G	G	G	G	G	G	G	G	F	G	N	G	N	N	G	G	G	G	G	N	P	G
S462 0000 0103	23	UNT T TRESTLE	FROZEN DOG COU	F	F	F	N	P	F	N	G	N	G	N	F	N	N	F	N	P	N	N	N	N	F
S462 0000 0125	23	UNT T TRESTLE	DRAINAGE	P	P	P	N	P	P	N	G	N	G	N	P	N	N	N	N	F	P	N	N	N	P
S462 0000 0192	225	PRE CONC BEAMS	LITTLE DRY CR	F	N	G	G	G	G	G	G	G	G	G	N	N	G	G	N	G	N	G	G	G	E
S465 0000 0007	411	PRE CONC BEAMS	BIG DRY CR	P	N	G	G	G	G	N	G	G	G	G	N	N	G	G	N	G	N	G	G	G	E
S467 0000 0005	193	PRE CONC BEAM	REDWATER R	G	N	E	E	E	E	G	G	G	G	G	N	N	E	E	N	G	N	E	E	G	E
S467 0000 0010	38	T T TRESTLE	HELL CR	G	G	G	G	G	G	N	G	G	G	N	G	N	G	G	N	G	G	G	N	F	G
S467 0000 0034	38	T T TRESTLE	MCCUNE CR	G	G	G	G	G	G	N	G	G	G	N	G	N	N	G	N	G	G	G	N	G	G
S467 0000 0335	36	UNT T TRESTLE	UPPER 7 MILE CR	G	G	G	G	G	G	N	G	N	G	N	E	N	N	F	P	G	G	F	N	P	G
S470 0000 0130	79	UNT T TRESTLE	N FK DEER CR	G	P	F	F	G	G	N	G	N	G	N	P	N	N	P	P	P	P	N	N	P	P
S470 0000 0235	25	TIMBER TRESTLE	DRAINAGE	F	F	F	N	F	F	N	G	N	G	N	P	N	N	P	P	P	P	P	N	P	P
S494 0000 0003	132	PRE CONC BEAM	SANDSTONE CR	G	N	E	E	E	E	N	G	G	G	E	N	N	G	E	P	G	N	G	N	G	E
S494 0000 0011	132	PRE CONC BEAM	S FK SANDSTONE	G	N	E	E	E	E	N	G	G	G	E	N	N	G	E	P	G	N	G	N	G	E

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Column E thru Z — Column Z

[illegible] Good — [illegible] Poor — [illegible] Critical — R [illegible] be Removed — [illegible]

			E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z
S504 0000 0130	67 STEEL I BEAM	CABIN CR	G	N	P	P	N	P	N	F	N	F		F	N	N	P	P	F	N	P	N	P	P
S510 0000 0050	119 UNT T TRESTLE	TUSLER CR	P	P	P	P	P	F	F	G	N	F	N	F	N	N	P	P	P	P	P	N	P	P

GLENDIVE DIVISION

S-270-0000-0066 142' Pratt Steel Truss Little Missouri River
End bent on north end is in critical condition and could very easily collapse. Railing is torn away in places. Untreated plank fastened to piling for abutment is in poor condition, also wing wall. Steel columns showing signs of rust in some areas. Concrete pier shows signs of severe scaling. Reinforced bars showing through. Underside of deck shows signs of cracking and deteriorating. Cross frames on top show signs of being buckled from being hit with high loads. See photos.

S-270-0000-0189 60' Pony Truss Cottonwood Creek
Timber pile and plank of north abutment show signs of severe scour causing displacement of piles. Paint worn off steel surfaces. Signs of rust. Wooden bridge rail in poor condition for need of paint. Brush and trees clogging channel. See photos.

S-277-0000-0290 51' Wood A Truss Corral Creek
Bridge is in citical condition. See photos.

S-270-0000-0066

S-270-0000-0066

S-270-0000-0066

S-270-0000-0066

S-270-0000-0066

S-270-0000-0066

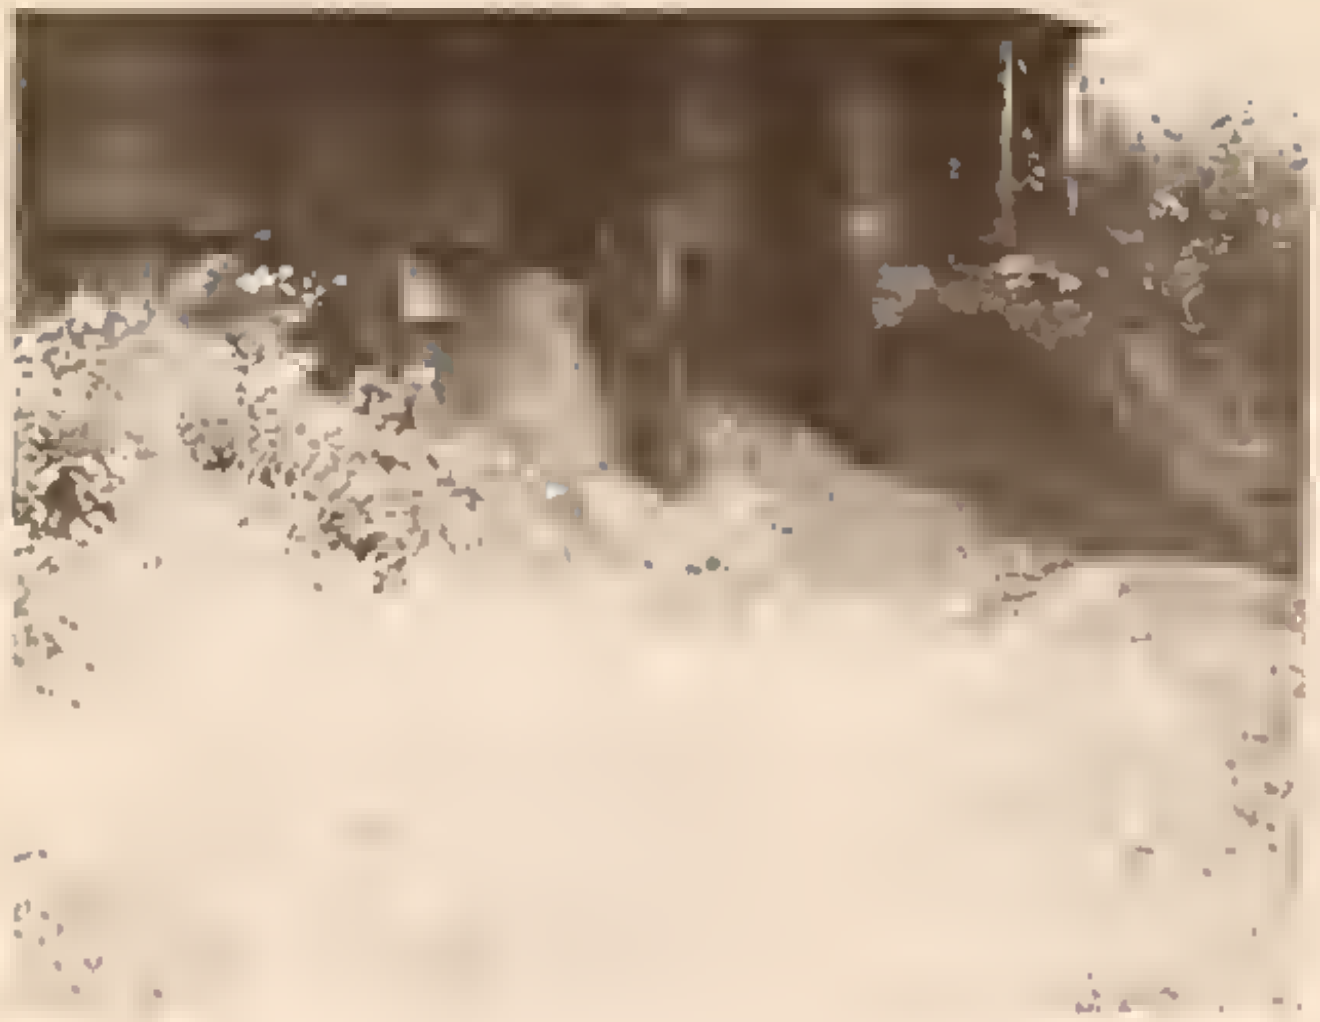

S-270-0000-0189

S-270-0000-0189

S-277-0000-0290

S-277-0000-0290

S-277-0000-0290

S-277-0000-0290

WOLF POINT CONSTRUCTION DIVISION

P	1	3791	4470	57	T T TRESTLE	PEOPLES CR OF	F	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4471	57	T T TRESTLE	PEOPLES CR OF	F	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4474	125	T T TRESTLE	PEOPLES CR	F	F	G	P		G	G	G		G		G			F	G	F	G	F		F	F		X
P	1	3791	4513	63	T T TRESTLE	DODSON CR CA	G	G	G		G	G		F		F		G			G	G	G	G	G		F	G		
P	1	3791	4517	240	STEEL TRUSS	MILK R	G	G	G	F		G	G	G		G		G	G	F	F	G	G	G	F		F	G		
P	1	3791	4535	75	T T TRESTLE	DODSON CR	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4540	57	T T TRESTLE	USRS CANAL	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4541	57	T T TRESTLE	DODSON CR OF	G	G	G			G		G		G		G			F	G	G	G	G		G	G		
P	1	3791	4560	57	T T TRESTLE	DODSON CR OF	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	1	3791	4576	57	T T TRESTLE	SPRING CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P	1	3791	4583	186	CONCRETE T 8EAM	GN RY	G		G			G					F			P	F		F		F	P		F		X
P	1	3791	4676	76	T T TRESTLE	EXETER CR	G	G	G			G		G	F	G		F			F	G	G	G	F		G	G		
P	1	3791	4716	240	STEEL GIRDER	MILK R	G		G	G		G	G	F	G	G	G			G	G	G	G		G	G	F	G		
P	1	4718	4857	102	PRE CONC 8M	NELSON CANAL	F	E	E		E	E		F		G	E			G	E	G	E		E		E	E		
P	1	4718	4905	90	CONT CONC SLA8	DRAINAGE	F		G		E	E		G	E	G					E		E		E		E	E		
P	1	4718	4918	90	CONT CONC SLA8	DRAINAGE	F		G		E	E		G	E	G					E		E		E		E	E		
P	1	4718	4927	163	CONC PRE 8EAM	8EAVER CREEK	G		E	E	G	E		F	E	G	E			G	G	G	G		G		G	G		
P	1	4718	4989	150	CONT ST 8EAM	8EAVER CR	G		G	F		G	G	F	F	G	G			F	F	F	G	G	G	F	F	G		
P	1	4718	5004	114	T T TRESTLE	8EAVER CR OF	G	G	G			G		G	F	G		P			G	F	G	G	G		F	G		X

DESCRIPTIVE FEATURES | CONDITION RATING

SUBSTRUCTURE

				TOTAL LENGTH FEET B	MATERIAL & TYPE C	NAME OF FEATURE D	END FLOORS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	W	X	Y	Z	Z1	REM Z2
P	1	4718	5009	190	T T TRESTLE	BEAVER CR OF	G	F	F			G		F	F	G		G			G	F	G	F	G		P	G		
P	1	4718	5013	133	T T TRESTLE	BEAVER CR OF	G	G	G			G		G	F	G		G			G	G	G	G	G		P	G		
P	1	4718	5019	38	T T TRESTLE	USRS CANAL	G	G	G		G	F		G	F	G		G			F	F	G	G	G		P	G		
P	1	4718	5066	38	T T TRESTLE	USRS CANAL	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	4718	5088	172	PRE CONC BEAM	BEAVER CR	F		G	G	G	G	G	G	G	G				G	G	G	G	G	G		G	G		
P	1	4718	5145	355	PRE CONC 8EAM	MILK R	G		E	E	E	E	E	G	G	G	E			E	E	E	E	E	E	G	G	E		
P	1	4718	5147	144	PRE CONC 8EAM	MILK R OF	G		E		E	E		G	G	G	E			E	E	E	E	E	E		G	E		
P	1	4718	5156	76	T T TRESTLE	MILK R OF	G	G	G			G		G		G		G			G	G	G	G	G		F	G		
P	1	4718	5157	38	T T TRESTLE	CANAL	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	1	4718	5178	95	T T TRESTLE	CANAL	G	G	G			G		G		G		G			G	G	F	G	G		F	G		
P	1	4718	5200	19	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		
P	1	4718	5223	95	T T TRESTLE	8EAR CR OF	G	G	G			G		G	G	G		P			G	G	G	G	G		G	G		X
P	1	4718	5225	114	T T TRESTLE	8EAR CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P	1	4718	5258	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	1	4718	5270	95	T T TRESTLE	UNGER CR	G	G	G			G		G	G	G		G			F	G	G	G	F		G	G		
P	1	4718	5281	152	T T TRESTLE	LIME CR	G	G	G			G		G	G	G		G			G	G	G	G	G		P	G		
P	1	4718	5333	95	T T TRESTLE	CHAPMAN COULEE	G	G	G			G		G	G	G		G			G	G	F	G	F		P	G		
P	1	4718	5342	95	T T TRESTLE	MOONEY COULEE	G	G	G			G		G	G	G		P			G	G	F	G	F		P	G		X
P	1	4718	5375	57	T T TRESTLE	RICHARDSON COU	G	G	G			G		G	G	G		G			F	G	G	G	F		P	G		

P	1	4718	5380	57	T T TRESTLE	ONEIL CR	G	G	G			G		G	G	G		G		G	G	F	G	F		P	G	
P	1	4718	5398	114	T T TRESTLE	CHERRY CR OF	G	G	G			G		G	G	G		F		F	G	G	G	F		P	G	
P	1	4718	5402	114	T T TRESTLE	CHERRY CR	G	G	G			G		G	G	G		G		F	G	F	G	F		F	G	
P	1	5416	5461	38	T T TRESTLE	GOUDGE COULEE	G	G	G		G	G		G		G		F		G	G	G	G	G		F	G	
P	1	5416	5484	50	T T TRESTLE	WHATLEY CR	G	G	G		G	G		G		G		G		G	G	G	G	F		P	G	
P	1	5416	5513	57	T T TRESTLE	ESPEIL COULEE	G	G	G		G	G		G		G		F		F	G	G	G	G		F	G	
P	1	5416	5518	95	T T TRESTLE	SPRING CR	G	G	G		G	G		G		G		G		G	G	G	G	F		P	G	
P	1	5416	5565	152	CONT CONC T 8M	PORCUPINE CR	F		G	G		G	G	F	G	G	G		G	G	F	G		G		P	G	
P	1	5416	5573	120	CONT CONC T 8M	PORCUPINE CR OF	F		G	G		G	G	G	G	G	G		G	G	F	G		G		P	G	
P	1	5416	5717	204	PRE CONC 8EAM	LIT PORCUPINE CR	F		G	G		G		G	G	G	G		G	G	G	G		G		P	G	
P	1	5416	5727	25	T T TRESTLE	INDIAN SERV CA	F	G	G		G	G		G		G		F		G	G	G	G	G		F	G	
P	1	5416	5795	63	T T TRESTLE	OSWEGO CR	G	G	G		G	G		G		G		G		G	G	G	G	G		P	G	
P	1	5416	5819	57	T T TRESTLE	FLYNN CR	G	G	G		G	G		G		G		G		F	G	G	G	G		P	G	
P	1	5416	5888	152	CONT CONC T 8M	WOLF CR	F		G	G		G	G	G	G	G	G		G	G	F	G		G		P	G	
P	1	5905	5916	63	T T TRESTLE	MOSQUITO CR	G	G	G		G	G		G	F	G		G		G	G	G	G	G		G	G	
P	1	5905	5926	100	T T TRESTLE	LITTLE WOLF CR	G	G	G		G	G		G	G	G		G		G	G	G	F	G		F	G	
P	1	5972	6013	120	CONCRETE T 8EAM	TULE CR	F		G	G		G	G	G	G	G			G	G	G	G		G		G	G	
P	1	5972	6110	294	STEEL GIRDER	POPLAR R	G		G	G		G	G	G	P	G	G		P	F	G	G		G	P	F	F	X
P	1	5972	6264	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	G		G		G	G	G	G	G		G	G	

[illegible] BRIDGE CONDITION REPORT

CONTROL NUMBER				DESCRIPTIVE DATA			CONDITION RATING																							
							SUBSTRUCTURE																							
	F.A.R. NUMBER	CONTROL JUNCTION	MILEPOST	TOTAL LENGTH FEET	MATERIAL & TYPE MAXIMUM SPAN	NAME OF FEATURE	END F	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKER	DECK	BRACING	RAILING	EXP.	PAINT		NOT	REMARKS
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	1	5972	6291	75	T T TRESTLE	BOX ELDER CR	F	G	F		G	G		G	G	G		P			G	G	G	G	F		F	G		X
P	1	5972	6312	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	5972	6323	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	5972	6391	163	CONT ST GIRDER	BIG MUDDY R	G		G	G	G	G	G	G	G	G	G			F	G	G	G	F		P	G	G		X
P	1	6445	6456	57	T T TRESTLE	SHEEP CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	1	6445	6483	90	CONT CONC SLAB	CLOVER CR	F		E			E		G	G	G					E	G	E		E		G	E		
P	1	6445	6590	76	T T TRESTLE	SHOTGUN CR	G	G	G			G		G		G		G			F	G	G	G	F		F	G		
P	16	2206	2731	57	T T TRESTLE	BEAVER CR	F	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	16	2206	2785	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	16	2206	2790	63	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	16	2206	2795	138	T T TRESTLE	LITTLE WARM CR	G	G	G			G	G	F	G	G		G			G	G	G	G	G		G	G		
P	16	2206	2839	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	16	2206	2874	100	T T TRESTLE	BIG WARM CR	F	G	G		G	G	G	G	F	F		G			G	G	F	G	G		G	G		
P	16	2206	2901	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	16	2206	2905	57	T T TRESTLE	WILD HORSE CR OF	G	G	G		G	G	G	G	F	G		P			G	G	G	G	G		G	F		X
P	16	2206	2907	100	T T TRESTLE	WILD HORSE CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	16	2206	2910	100	T T TRESTLE	WILD HORSE CR	F	G	G		G	G	G	G		F		F			G	G	G	G	G		G	G		
P	16	2206	2940	57	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		

P	16	2206	2943	57	T T TRESTLE	DRAINAGE	G	G	G	G	G	G	G	G	G		G		G	G	G	G	G		G	G	
P	16	2206	2973	100	T T TRESTLE	W ALKALI CR	F	G	G	G	G	G	F	G	F		P		G	G	G	G	G		G	F	X
P	16	2206	2979	75	T T TRESTLE	BLACK COU	F	G	G	G	G	G	F	G	F		G		G	G	G	G	G		G	G	
P	16	2206	3000	76	T T TRESTLE	HALFWAY COU	F	G	G	G	G		G	G	G		G		G	G	G	G	G		G	G	
P	16	2206	3033	157	ST PONY TRUSS	ALKALI CR	F	G	G		F	G	G	G	G	G	G	F	G	G	G	G	G	P	G	G	
P	16	2206	3039	57	T T TRESTLE	DESJARDIN COU	G	G	G	G	G		G	G	G		G		G	G	G	G	G		G	G	
P	16	2206	3082	75	T T TRESTLE	S FK TAYLOR CR	F	G	G	G	G		G	G	G		C		G	G	G	G	G		G	F	X
P	16	2206	3084	100	T T TRESTLE	N FK TAYLOR CR	F	G	G	G	G		G	F	G		G		G	G	G	G	G		F	G	
P	16	2206	3108	100	T T TRESTLE	DODSON SO CANAL	G	G	G		G		G	F	G		P		G	G	G	G	G		G	F	X
P	16	2206	3114		UNDERPASS	GN RY	G		G	G	G					G			G	G	G		G		F	G	
P	22	0000	0142	76	T T TRESTLE	N FK EAGLE CR	F	G	G		F		G	F	G		G		G	G	G	G	F		F	G	
P	22	0000	0153	19	T T TRESTLE	GAINES CR	G	G	G	F	G		G		G		G		G	G	G	G	F		F	G	
P	22	0000	0204	76	T T TRESTLE	N FK EAGLE CR	G	G	G		G		G	F	F		G		G	G	G	G	G		F	G	
P	22	0000	0215	95	T T TRESTLE	EAGLE CR	F	G	G		G	G	F	F	G		G		G	G	G	G	G		F	G	
P	22	0000	0238	76	T T TRESTLE	REDSTONE CR	G	G	G		G		G		G		G		G	G	G	F	G		G	G	
P	22	0000	0254	125	T T TRESTLE	BIG MUDDY CR	G	G	G		G	G	F	F	G		G		F	G	G	G	G		F	G	
P	22	0000	0262	38	T T TRESTLE	DRAINAGE	G	G	G		G		G	F	G		G		F	G	G	G	F		F	G	
P	22	0000	0278	19	T T TRESTLE	STOCKPASS	G	G	G	G	G						G		G	G	G		G		F	G	

DESCRIPTIVE FEATURE — CONDITION RATING — SUBSTRUCTURE

NUMBER	TOTAL LENGTH FEET	MATERIAL AND TYPE, MAXIMUM SPAN	NAME OF FEATURE CROSSED	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS								
A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P 22 0000 0288	19	T T TRESTLE	ARCHER COULEE	G	G	G		G	G		G		G		G			F	G	G	G	G		F	G		
P 22 0000 0300	19	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	P	G		G			F	G	G	G	F		F	G		
P 22 0000 0315	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 22 0000 0323	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P 22 0000 0366	114	T T TRESTLE	PLENTYWOOD CR	F	G	G			P	G	F	G	F		G			G	G	G	G	F		F	G		
P 22 0000 0384	114	T T TRESTLE	MCCOY CR	F	G	G			P	G	F	G	G		G			F	G	G	G	F		F	G		
P 22 0000 0426	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			F	G	G	G	F		P	G		
P 22 0000 0433	76	T T TRESTLE	MARRON CR	G	G	G		G	G		G	G	G		G			F	G	G	G	P		P	G		
P 22 0435 0446	38	T T TRESTLE	DRAINAGE	G	G	G			G		G	F	G		G			F	G	G	G	F		F	G		
P 22 0435 0456	19	T T TRESTLE	STOCKPASS	G	G	G			G			F			G			F	G	G	G	G		F	G		
P 22 0435 0463	95	T T TRESTLE	ATOR CR	G	G	F			P		F	G	G		G			F	G	F	G	F		F	F		
P 22 0435 0467	19	T T TRESTLE	STOCKPASS	F	G	P		G	G		G	F	G		G			G	G	G	G	G		G	F		X
P 22 0435 0470	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 22 0435 0481	19	T T TRESTLE	STOCKPASS	F	G	G		G	G		G	F	G		G			F	G	G		F		F	G		
P 22 0435 0513	114	T T TRESTLE	ANTELOPE CR	F	F	F			G	G	F	F	G		G			F	G	F	G	F		F	F		
P 22 0435 0655	95	T T TRESTLE	MEDICINE LAKE OF	F	G	F			G	G	G	G	G		G			F	G	G	G	P		F	F		
P 22 0435 0656	190	T T TRESTLE	MEDICINE LAKE	F	G	F			G	G	G	G	G		G			F	G	G	G	F		F	F		
P 22 0435 0698	7	T T TRESTLE	STOCKPASS	F	F	F		F	P			F	F		G			G	G	G		G		F	F		X
P 22 0435 0709	38	T T TRESTLE	HOMESTEAD CR	F	G	G			G				F		G			F	G	G	G	F		F	G		

P	22	0435	0719	38	T T TRESTLE	MCCABE CR	G	G	G			G		G	F	F		G			F	G	G	G	F		F	G		
P	22	0435	0728	57	T T TRESTLE	LOST CR	F	G	G			F		G	G	G		G			G	G	G	G	F		F	G		
P	22	0435	0758	106	PONY TRUSS	SHEEP CR	G		G			G		G		G	G			F	F	G	G	G	F	P	P	F		
P	22	0886	0895	264	STEEL GIRDER	SPRING CR-GN RY	G		G			G					G			G	G	F	G		G	G	G	G		
P	22	0886	0918	1169	THRU ST TRUSS	MISSOURI R	F		G	G		G	G	F		F	G	G	P	G	G	G	F	G	G	F	G	G		X
P	22	0886	0924	95	T T TRESTLE	MISSOURI R OF	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P	22	0886	0933	76	T T TRESTLE	DRY CR	F	G	G			G		G	F	G		G			G	G	G	G	F		F	G		
P	22	0886	0957	19	T T TRESTLE	WALLACE COULEE	G	G	G		G	G		G		G		G			F	G	G	G	F		F	G		
P	22	0886	1004	76	T T TRESTLE	CHERRY CR	F	G	G		G	G		G	F	G		G			F	G	G	G	F		F	G		
P	22	0886	1012	38	T T TRESTLE	MID FK CHERRY CR	G	G	G		G	G		G	G	G		G			F	G	G	G	F		F	G		
P	22	0886	1020	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P	22	0886	1022	38	T T TRESTLE	HACKLEY COULEE	F	G	G		G	G		G	G	G		G			F	G	G	G	F		F	G		
P	22	0886	1031	76	T T TRESTLE	S FK CHERRY CR	G	G	G		G	G		G	G	G		G				G	G	F	F		F	G		
P	22	0886	1044	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		G	G		
P	22	0886	1094	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		G	G		
P	22	0886	1120	76	T T TRESTLE	N FK 1ST HAY CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P	25	0000	0253	57	T T TRESTLE	E FK WOLF CR	F	G	G		G	G		G	G	G		G			F	G	G	G	G		F	G		
P	25	0000	0262	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G		G		G	G		

P 25 0000 0268	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			F	G	G		G		G	G
P 25 0000 0277	114	T T TRESTLE	WOLF CR		G	G		G	G	G	F	G	G		G			G	G	G	G	G		F	G
P 25 0000 0294	76	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G	G	G	G	F		F	G
P 25 0000 0315	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G
P 25 0000 0342	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			F	G	G	G	G		F	G
P 25 0000 0354	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	F		G			G	G	G	G	G		G	G
P 25 0000 0387	57	T T TRESTLE	SHEEP CR	F	G	G		G	G		G	G	G		G			F	G	G	F	G		G	G
P 25 0000 0397	19	T T TRESTLE	DRAINAGE	G	G	G		F	F		G	F	G		G			G	G	G	F	G		G	G
P 25 0000 0413	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G	G	G		G			G	G	G	G	F		F	G
P 25 0000 0418	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			F	G	G	G	F		F	G
P 25 0000 0420	38	T T TRESTLE	DRAINAGE	F	G	G		F	F		G	F	G		G			G	G	G	G	F		G	G
P 25 0000 0422	19	T T TRESTLE	STOCKPASS	G	G	G			F		G	F	G		G			F	G	G	G	F		G	G
P 25 0000 0450	7	T T TRESTLE	STOCKPASS	G	G	G			F						G					G					G
P 25 0000 0465	1074	ST THRU TRUSS	MISSOURI R	G		F	F		F	G	G		G		G	G	F	F	G	F	G	F	F	F	F
P 25 0469 0503	76	T T TRESTLE	LITTLE WOLF CR	G	G	G			G		G	P	G		F			F		G		F		F	G
P 25 0469 0513	57	T T TRESTLE	MOSQUITO CR	G	G	G			G		G	F	G		G			G	G	G	G	G		G	G
P 25 0469 0528		UNDERPASS	GN RY			F			F					G				F		P		G		F	F
P 30 0000 0113	57	T T TRESTLE	DAHL CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G

P 30 0000 0143	95	T T TRESTLE	MAIN CR	F	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P 30 0000 0153	25	T T TRESTLE	DRY CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 30 0000 0163	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		F	G		
P 30 0000 0170	76	T T TRESTLE	SHALLOW CR	G	G	G			G		G	G	G		G			G	G	G		G		P	G		
P 32 0037 0081	89	CONCRETE T BEAM	TULE CR	F		P			G		G	F	G	G			F	F	G	G		G			F		X
P 32 0037 0120	38	T T TRESTLE	BITTNER COULEE	G	G	G			F						G			G	G	G	G	G		F	G		
P 32 0037 0147	57	T T TRESTLE	S FK CHELSEA CR	G	G	G			G			F	G		G			G	G	G	G	G		F	G		
P 32 0037 0153	76	T T TRESTLE	CHELSEA CR	G	G	G			G			G	F		F			G	G	G	G	G		F	G		
P 32 0037 0203	95	T T TRESTLE	BOX ELDER CR	G	G	G			G	G	G	G	F		G			G	G	G	G	G		G	G		
P 32 0037 0217	38	T T TRESTLE	N FK BOX ELDER C	G	G	G			F		G	G	F		G			G	G	G	G	G		G	G		
P 32 0037 0275	76	T T TRESTLE	SPRAGUE COULEE	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P 32 0037 0300	57	T T TRESTLE	MIDWAY COULEE	F	G	G			G			P	G		G			G	G	G	G	F		G	G		
P 32 0037 0336	76	T T TRESTLE	W FK POPLAR R	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P 32 0037 0341	114	T T TRESTLE	W FK POPLAR R OF	F	G	G			G	G	G	F	F		G			G	G	G	G	G		F	G		
P 32 0037 0343	185	ST PONY TRUSS	W FK POPLAR R	F		G	G		G	G	G	G	G	G		G	P	G	G	G	G	G	P	P	G		X
P 32 0037 0381	38	T T TRESTLE	NELSON COULEE	F	G	G			G		G	G	G		G			G	G	G	G	F		F	G		
P 32 0037 0409	57	T T TRESTLE	BELKNAP CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P 32 0037 0439	38	T T TRESTLE	DICKINSON COULEE	G	G	G			G		G	G	G		G			F	G	G	G	F		G	G		

P	32	0037	0450	76	T T TRESTLE	BRICKER COULEE	G	G	G			G		G	G	G		G			G	G	G	G	F		F	G	
P	32	0037	0466	185	STEEL TRUSS	POPLAR R	F		G	G		G	G	G	G	G	G	G	G	G	G	G	F	G	G	F	P	G	X
P	32	0037	0472	19	T T TRESTLE	STOCKPASS	G	G	G			G						G			G	G	G	G	P		F	G	
P	32	0037	0481	57	T T TRESTLE	MANTERNACH COU	G	G	G			G		G	F	F		G			G	G	G	G	F		G	G	
P	32	0513	0555	143	CONC T BEAM	E FK POPLAR R	G		G	G		G	G	G	G	G	G			G	G	F	G		G		G	G	
P	32	0513	0595	143	CONC T BEAM	E FK POPLAR R	G		G	G		G	G	G	G	G	G			G	G	G	G		G		G	G	
P	32	0513	0626	50	T T TRESTLE	COW CR	F	G	G		G	G	G	G	P	G		G			G	G	G	G	G		P	G	
P	42	0000	0618	19	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	F		G			G	G	G	G	G		P	G	
P	42	0000	0626	57	T T TRESTLE	BARTON COULEE	F	G	G			G		G	G	G		G			G	G	G	G	G		P	G	
P	42	0000	0634	76	T T TRESTLE	GALPIN COULEE	F	F	P			G		G	G	G		G			G	G	G	G	G		P	F	X
P	42	0000	0651	57	T T TRESTLE	GALPIN COULEE	G	G	G			G		G	G	G		G			G	G	G	G	G		P	G	
P	42	0000	0662	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G				G	
P	42	0000	0692	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G	G	G		G			G	G	G	G	F		P	G	
P	42	0000	0704	38	T T TRESTLE	CANAL	G	G	G	F		G		P		G		G			P	G	G	G	F		P	G	X
P	42	0000	0714	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G	G	G	G	F		P	G	
P	42	0000	0725	152	T T TRESTLE	MILK R OF	F	G	G			F		G	G	G		G			G	G	G	G	F		P	G	
P	42	0000	0727	473	ST THRU TRUSS	MILK R	F	G	G	G		F		G	G	G		G	F	P	G	G	G	G	G	P	P	G	X
P	42	0000	0740	57	T T TRESTLE	SPRAGUE COULEE	G	G	G			G		G		F		G			G	G	G	G	F		P	G	

P 42 0000 0760	UNDERPASS	GN RY	G	G	F	G	G	G	P	G

M247	0000	0066	150	T T TRESTLE	E FK CHERRY CR	G	G	G			G		G		G		F			G	G	G	G	G		P	G		
M247	0000	0254	125	T T TRESTLE	DRY FK CR	G	G	G			G		G		G		G			G	G	G	G	G		P	G		
M247	0000	0281	114	T T TRESTLE	W FK PORCUPINE	G	G	G	F		G	G	G	G	F		G			G	G	G	G	F		G	G		
M247	0000	0351	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
M247	0000	0394	100	T T TRESTLE	M FK PORCUPINE	F	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
M247	0000	0400	76	T T TRESTLE	ALKALI CR	G	G	G			G		G	G	G		G			G	G	G	G	F		G	G		
M249	0000	0020	369	STEEL GIRDER	MILK R	G		G	G		G	G	G	G	G	G			G	G	F	G		F	F	F	G		
M249	0000	0072	57	T T TRESTLE	DRAINAGE	G	P	P			P		G		G		P			G	G	P	P	F		F	F		X
M249	0000	0098	286	STEEL I BEAM	OF MISSOURI R	G		G			G		G		G	G			G	G		G		G	G	F	G		
M511	0000	0037	76	T T TRESTLE	S FK WHITETAIL C	G	G	G			G		G	F	G		G			G	G	F	G	F		G	G		
M511	0000	0063	76	T T TRESTLE	WHITETAIL CR	F	G	G			P		F	G	G		G			G	G	G	G	F		F	G		
M511	0000	0070	38	T T TRESTLE	N FK WHITETAIL C	G	G	G			G		G	P	G		G			G	G	G	G	F		F	G		

A				E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	AA
S201 0000 0133	321	CONCRETE T BEAM	REDWATER R	G		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
S201 0000 0588	76	T T TRESTLE	FIRST HAY CR	G	G	G			G		G	G	G		G			G	P	G	G	F		P	G		
S201 0000 0640	57	T T TRESTLE	SECOND HAY CR	G	G	G			G		G	F	G		G			F	P	G	G	G		P	G		
S201 0000 0693	51	T T TRESTLE	MAIN CANAL	F	G	G			G		G		G		G			P		F	G	F		P	G		
S204 0000 0013	240	ST PLATE GIRDER	MILK R	F		G	G		G	G	G	G	G	G			F	G	P	G	G	G	G	P	G		
S204 0000 0014	63	T T TRESTLE	USRS CANAL	F	G	G		G	G		G		G		G			G	P	G	G	G		P	G		
S242 0000 0055	57	T T TRESTLE	CIRCLE DIAMOND	F	G	G			G		G	F	G		P			G	P	G	G	G		F	G		X
S242 0000 0060	114	T T TRESTLE	ASSINIBOINE CR	F	G	G			G		F	F	F		G			G	P	G	G	F		F	G		
S242 0000 0152	100	T T TRESTLE	COTTONWOOD CR	G	F	F			G	G	F	G	F		G			G	P	G	G	G		F	G		X
S242 0000 0174	76	T T TRESTLE	LIT COTTONWOOD C	G	G	G		G	G		F		F		G			G	P	G	G	G		F	G		
S242 0000 0470	100	T T TRESTLE	WHITEWATER CR	G	G	G		G	G	G	G	G	G		G			G	F	F	G	G		F	G		
S243 0000 0059	146	CONC SLAB FORD	MILK R	F																P					P		X
S243 0000 0117	117	STEEL I BEAM	WHITEWATER CR	F	P	F					G	F	G		F			P		F					P		X
S243 0000 0122	62	STEEL I BEAM	WHITE CR	F	G	G			G		G	G	G		F					F		P		P	F		
S243 0000 0160	250	ST PLATE GIRDER	MILK R	F		G	G		G	G	G	G	G	G			G	G	F	G	G	G	G	F	G		
S243 0000 0196	38	T T TRESTLE	DRAINAGE	F	G	G	G		G		G		G		G			F		G	G	F		F	G		

S243 0000 0200	114	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			F		G	G	F		F	G	
S243 0000 0202	38	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			F		G	G	F		F	G	
S243 0000 0204	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			F		G	G	F		F	G	
S243 0000 0205	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			F		G	G	F		F	G	
S243 0000 0206	95	T T TRESTLE	USRS DITCH	F	G	G			G		G	F	G		G			F		G	G	F		F	G	
S243 0000 0207	38	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			F		G	G	G		F	G	
S243 0000 0208	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			F		G	G	G		F	G	
S246 0000 0007	120	CDNT CDNC T BM	CHERRY CR	P		G	G		G	G	G	G	G	G			G	G	G	G		G		P	G	
S246 0000 0011	75	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			G		G	G	G		P	G	
S246 0000 0021	400	RIV ST PL GIR	MILK R	P		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	P	G	
S246 0000 0067	50	T T PILE	ANTELDPE CR	G	G	G		G	G		G		G		G			G		G	G	G		P	G	
S248 0000 0024	25	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G	
S248 0000 0029	278	ST PONY TRUSS	E FK POPLAR R	F	G	P			G	G	F	P	F	G	G	G	F	G		G	G	G	P	F	F	X
S248 0000 0031	76	T T TRESTLE	DRAINAGE	G	G	G		G	G	G	G	F	G		F			G	G	G	G	G		G	G	
S248 0000 0035	127	T T TRESTLE	BUTTE CR	G	G	F		G	G	G	F	G	F		G			G	G	G	F	F		F	G	
S248 0000 0092	25	T T TRESTLE	DRAINAGE	G	G	G		G	G	G	G	G	G		G			G	P	G	G	G		G	G	
S248 0000 0105	75	T T TRESTLE	SPRING CR	G	G	F		G	G		G	G	F		G			G	G	G	G	C		G	F	X

								E	F	G	H	I	J	K		M	N	O	P		R	S				W			Z	Z
S248	0000	0219	57	T	T	TRESTLE	DRAINAGE	G	G	F		G	G		G	G	G		F			G	G	G	G	G		P	G	X
S248	0000	0224	76	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			F	G	G	G	G		P	G	
S248	0000	0242	57	T	T	TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G	
S248	0000	0288	75	T	T	TRESTLE	DRAINAGE	G	G	G		G	G	G	G	G	G		G			G	G	G	G	G		P	G	
S248	0000	0289	50	T	T	TRESTLE	OLD OF CHANNEL	G	G	G		G	G		G	G	G		G			G	G	G	F	G		P	G	
S248	0000	0290	200	T	T	TRESTLE	W FK POPLAR R	G	G	G		G	G	G	F	G	F		C			G	G	F	F	G		P	G	X
S248	0000	0292	75	T	T	TRESTLE	OF W FK POPLAR R	G	G	G		G	G	G	G	G	G		G			G	F	G	G	G		P	G	
S248	0000	0293	19	T	T	TRESTLE	IRRIGATION CANAL	G	G	G		G	G						C			G	F	G	G	F		P	F	X
S248	0000	0315	50	T	T	TRESTLE	SPRING CR	G	G	G		G	F		G		G		G			G	P	G	G	F		P	G	
S251	0000	0118	25	T	T	TRESTLE	DRAINAGE	F	G	G			G		G		G		F			G		G	G	G		G	G	
S251	0000	0155	25	T	T	TRESTLE	DRAINAGE	F	G	G			G		G		G		G			G		G	G	F		G	G	
S251	0000	0178	25	T	T	TRESTLE	KIRN COULEE	G	G	G			G		G		G		G			G	P	G	G	G		F	G	
S251	0000	0207	25	T	T	TRESTLE	DRAINAGE	G	G	G			G		G		G		C			G		G	G	G		G	G	X
S251	0000	0217	38	T	T	TRESTLE	HAY CR	G	G	G			G		G		G		G			G	F	G	G	G		G	G	
S251	0000	0409	25	T	T	TRESTLE	SMOKE CR	E	G	G		E	G		G		G		G			E		G	G	E			G	
S251	0000	0498	25	T	T	TRESTLE	EAGLE CR	G	G	G		G	G		F		G		G			F	P	G		F		P	G	
S258	0000	0002	150	T	T	TRESTLE	BIG MUDDY CR	F	G	P			G	G	F		G		G			F	P	F	G	F		P	F	

S258 0000 0008	113	T T TRESTLE	DRAINAGE	F	G	P			G	F			G		G			F	P	F		F	P	F	
S327 0000 0039	100	T T TRESTLE	LITTLE MUDDY CR	F	G	G			G		G		G		G			G		G		G	P	G	
S327 0000 0123		UNDERPASS	GN RY	G		G								G			G							G	
S344 0000 0007	50	T T TRESTLE	SHEEP CR	F	G	G		G	G		G		G		G			G		G	G	G	P	G	
S344 0000 0040	110	CONT CONC T BM	BIG MUDDY CR	F		G			G		G	G	G	G			G	G	P	G		G	F	G	
S344 0000 0121	110	CONT CONC T BM	SMOKE CR	F		G			G		G	G	G	G			G	G	F	G		G	F	G	
S350 0000 0030	110	CONT CONC T BM	BIG MUDDY CR	F		G	G		G		G	G	G	G			G	G	F	G		F	G	G	
S363 0000 0007	29	STEEL I BEAM	CANAL	F	F	F			P		G		G		F			P		F				F	X
S363 0000 0013	219	ST THRU TRUSS	MILK R	C		F	F		P		G		G		P	F	F	F		F		F	P	P	X
S363 0000 0088	112	PRE CONC BEAM	ALKALI CR	G		E	E	E	E	G	G	G	F	E			G	E	G	E		E	E	G	
S363 0000 0113	75	PRE CONC BEAM	IRRIGATION CANAL	G		G		E	E		G		F	E			G	E	G	E		E	G	G	
S374 0000 0037	38	T T TRESTLE	PLENTYWOOD CR	G	G	G		G	G		G		G		G			G	P	G	G	F	P	G	
S404 0000 0198	110	CONT CONC T BM	SMOKE CR	G		G			G		G	G	G	G			G	G	G	G		G	F	G	

S438 0000 0252	78	STEEL I BEAM	E FK PORCUPINE	G	G	G			G		G		G		G			F		G	G	F		P	G		
S438 0000 0355	23	UNT T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			F		G	G	F		P	G		
S469 0000 0019	1159	STEEL GIRDER	MISSOURI R	G		G	G		G	G	G		G	G		G	G	G		F	G	G		F	G		
S480 0000 0030	1056	CONT PL GIRDER	MISSOURI R	E		E	E		E	E	E	E	E	E			E	E		E	E	E	E	E	E		
S480 0000 0138	29	STEEL I BEAM	LONGGRASS CR	P	C	P		P	F		G		G		F			P		F					P		X
S496 0000 0103	27	STEEL I BEAM	W FK SHOTGUN CR	P	P	P		P	P		G		G		F					F					P		X
S496 0000 0122	25	STEEL I BEAM	E FK SHOTGUN CR	F	G	G		G	G		G		G		G					G					G		
S496 0000 0140	26	STEEL I BEAM	DRAINAGE	G	G	G		G	G		G		G		G			P		F					G		
S496 0000 0172	22	CONCRETE BEAM	SHOTGUN CREEK	G	G	G		G	G		G		G					G		G					G		N
S514 0000 0003	176	CONT STEEL GIR	POPLAR R	F		G	G	G	G	G	G		G	G			G	G		G	G	G	F	F	G		
S514 0000 0191	245	PRE CONC BEAM	POPLAR R	F		E	E		E	E	G	G	G	E			E	E	E	E		E	E	G	E		
S515 0000 0088	92	PRE CONC BEAM	LAKE CR	G		G		E	E		G	G	G	E			G	E	G	E		G		G	G		
S528 0000 0108	75	ST PONY TRUSS	SAND CR	G	G	G		G	G		G		G		G	G	G	G		G	G			P	G		

S528 0000 0191	230	UNT T TRESTLE	PRAIRIE ELK CR	F	P	P	P	G	G	P	F	G		P			G		G	P		P		X
S537 0000 0023	272	ST HOWE TRUSS	MILK R	G	G	G		G	G		G	G	G	G	F	G	P	P	F	G	P	P	F	
S537 0000 0057	32	T TRESTLE	CASH CR	F	P	P		C	F		F	F		P					P	P	F	P	C	X

WOLF POINT DIVISION

P-1-3791-4474 125' T. T. Trestle Peoples Creek
It appears that the bridge piers heave and settle due to material conditions below the bridge. Maintenance Section crew keeps constant watch and repair on structure. Bridge not stable but safe.

P-1-3791-4583 186' Conc. T. Beam Great Northern R.R.
It appears that the end fills have pushed the bridge together at the expansion joint and the shoes are no longer working. This bridge is on a skew of about 30 degrees and the curb line has slipped about 1½" out of line. See photo.

P-1-4718-5004 114' T. T. Trestle Beaver Creek Overflow
The fifth stringer in from the north side in span 4 is cracked.

P-1-4718-5223 95' T. T. Trestle Beaver Creek Overflow
In span # 1 the 12th stringer from the left is cracked.

P-1-4718-5342 95' T. T. Trestle Mooney Coulee
In span # 5, stringer # 7 from left is split.

P-1-5972-6110 294' Steel Girders Poplar River
Bridge is in generally good condition except for rockers on the 2 piers and on the east end bent. (West bent is fixed). The rockers are tipped to the east, which causes the expansion joint to remain closed most of the time. Also the contraction joint on the west end is open quite wide. Two short send spans are concrete but are boxed in so it is not possible to check underside of deck or supports. See photo.

P-1-5972-6291 75' T. T. Trestle Box Elder Creek
Seventh stringer from the south side in center span is cracked. Cap on Bent # 3 is split.

P-1-5972-6391 163' Cont. Steel Girder Big Muddy River
Rockers at east end bent tipped towards east. Expansion joint at east end closed. Bridge rail on SW corner of bridge has been struck by traffic.

P-16-2206-2905 57' T. T. Trestle Wild Horse Creek Overflow
Stringer in center span, 5th from right is cracked.

WOLF POINT DIVISION

P-16-2206-2973 100' T. T. Trestle West Fork Alkali Creek
Stringer in span 1, seventh from left is cracked. Several other stringers show signs of cracking.

P-16-2206-3082 75' T. T. Trestle South Fork Taylor Creek
Stringer in Span 1, sixth one in from left, is broken.

P-16-2206-3108 100' T. T. Trestle Dodson South Canal
Cracked stringer in span 1, seventh from left.

P-22-0435-0467 19' T. T. Trestle Stockpass and Drainage
Piling at end bents are slipping out from under the caps and cap stringers are tipping back. Temporary braces have been put on piling, but tipped stringers should be corrected.

P-22-0435-0698 7' T. T. Trestle Stockpass
Piling, backwalls, and wingwalls have been charred quite badly by fire. Condition of this stockpass, at best, is only fair.

P-22-0886-0918 1169' Steel Truss Missouri River
At piers 3 and 4, where truss fastens to rocker shoe, there are angle irons either cracked or broken. These angle irons are cracked or broken on both sides of the rocker shoe. Also expansion joint at pier No. 7 is closed when temperature is + 30 degrees. Also, end fill under cap, bent No. 8, has eroded away and is causing settlement of south bridge approach.

P-32-0037-0081 89' Concrete T Beam Tule Creek
The two center bents that are in the water have severe scaling about $2\frac{1}{2}$" into the concrete, all the way around the columns just below the cap beams and at water level Reinforcing steel is exposed. See photos.

P-32-0037-0343 185' Steel Pony Truss West Fork of Poplar River
End bents. Fill on underside of cap has either settled or been washed away leaving a hollow area under the roadway which will cause settlement. Rockers at pier # 3 are tipped too far to the south as the temperature today is approximately +30 degrees. The expansion joint at pier 3 is open to within $\frac{1}{4}$" to $\frac{1}{2}$" of its maximum. The expansion joint at pier 2 (which is fixed) is closed to within $\frac{1}{4}$" of its maximum. It appears the center span is too far south. See photos.

WOLF POINT DIVISION

P-32-0037-0466 185' Steel Truss Poplar River
This bridge has transverse cracking on deck all the way across structure every couple of feet.

P-42-0000-0634 76' T. T. Trestle Galpin Coulee
It appears that the piles move up and down on the 2nd and 3rd bents. I believe it could be caused from the material beneath the structure. See photo.

P-42-0000-0704 38' T. T. Trestle Irrigation Canal
It appears that the canal is not cleaned out in the spring and water carries brush and etc. down the canal and it hangs up on the center pier causing backing plank encasing piles to be broken. Piles are good. No curbs are above the plant mix. I estimate 10" of plant mix on the deck. Railing needs paint. Bridge appears to be sound.

P-42-0000-0727 473' St. Thru Truss Milk River
The bracing on overhead truss on south end of bridge has been hit by high vehicle object and damaged. The shoes on expansion joint of pier 2 are rolled over. I don't believe the expansion joint is working, but instead the two piers are working back and forth. See photo.

M-249-0000-0072 57' T. T. Trestle Drainage
This structure has had a very bad fire underneath. Everything has been charred about $\frac{1}{2}$" to 3/4" into the wood. A high pressure gas line (MDU) goes under the structure and may have been the cause of the fire.

S-242-0000-0055 57' T. T. Trestle Circle Diamond Coulee
Cracked stringer in span No. 1, 6th from left side.

S-242-0000-0152 100' T. T. Trestle Cottonwood Creek
Pile on upstream side of bents have been damaged somewhat by ice during high water. Piles are also tipped somewhat.

S-243-0000-0059 146' Conc Slab Ford Milk River
The first 100' of the ford in the stream has had approximately 8" of concrete placed for deck over 16-24" R.C.P. From +75' to 100' about 4-24" R. C. P. have been squashed and deck settled. The repair work done was a concrete overlay built up to grade which is showing very poor condition. The last 46' has buckled up on the upstream side of the ford. About 8" of this structure is in very poor condition and should be replaced wiah a bridge. See photos.

WOLF POINT DIVISION

S-243-0000-0117 117' Steel I Beam Whitewater Creek

The piles at bent #3 are rotten and eating away, but newer pile are ahead. This bridge should be rebuilt from the bottom up. I recommend posting a load limit on structure. See photo.

S-248-0000-0029 278' St. Pony Truss East Fork Poplar River

Bent No. 4 (from east bridge end) has one pile that has nearly slipped out from under the cap. See photo. Also 1 pile has slipped some. Bent 3 rocker shoes at pier # 5 are tipped the wrong way and the expansion joint is closed. Tempature +05 degrees. Riprap at west end bent is very poor and end fill under bridge is nearly washed away.

S-248-0000-0105 75' T. T. Trestle Spring Creek

Rail on south side of bridge has been torn away by a car accident. Also, pile near channel were apparently not driven straight and do not sit straight under cap. This could cause problems in case of high water.

S-248-0000-0219 57' T. T. Trestle Drainage

Timber stringer, second one in from south side, has bad crack and will eventually break

S-248-0000-0290 200' T. T. Trestle West Fork of Poplar River

Sixth stringer in from south side at east end span is broken. The deck on this bridge has broken thru recently and been repaired. Quite a lot of the bracing on the stringers is loose.

S-251-0000-0207 25' T. T. Trestle Drainage

Number 7 stringer from left side is broken.

S-363-0000-0007 29' Steel I Beam Wagner Canal

The backwalls are good under the structure but the side's or wings which are part of the backwall are loose and could cause fill settlement. This structure is very unsafe due to no wheel guard, railing or markers to tell where the bridge is. I believe the bridge should have load limit. See photo.

S-363-0000-0013 219' St. Thru Truss Milk River

This bridge is very old, but the truss appears to be in fair condition, although there is no paint on it. The approach span on the north end is in critical condition and should be completely replaced to the main truss span. The first bent should be rebuilt to carry a proper distribution of deck. It appears the stringers are just laid back into a dirt fill and this has given way on the left side. This bridge needs maintenance badly. See photo.

WOLF POINT DIVISION

S-480-0000-0138 29' Steel I Beam Long Grass Creek
This bridge is in very poor shape. One pile is completly sheared off. Wingwalls have collapsed. Any heavy traffic could break this bridge down. I recommend it be replaced with a 48" culvert because a dam has been built 200' upstream from this location and the only water that goes under the bridge is seepage water from the dam. See photo.

S-496-0000-0103 27' Steel I Beam & Plank Deck West Fork of Shotgun Creek
Bridge is generally poor condition. Piles are untreated timber and appear to be decayed. Back walls are concrete and are in very poor condition. No curbs or rail. This bridge would not support heavy loads and should be replaced with a culvert. See photo.

S-528-0000-0191 230' Untreated Timber Trestle Prairie Elk Creek
This bridge is in very poor shape in the sub-structure. The upstream piling on just ½ of the piers are either broken or cracked and any surge of ice or highwater could cause this bridge to break down. The only apparent work done on this bridge since the last inspection 2 years ago seems to be in redecking with 2"x4" laid on side and new curb wheel guards. Also found 2 cracked stringers in Span # 2, stringer 1 and 2. Span # 9, stringer 7. Signs should be posted for safety of heavy vehicle traffic. See photos.

S-537-0000-0057 32' T. Trestle Cash Creek
This bridge is in very poor shape from piling to deck. Split piling have been replaced by mud sills. Wingwalls are breaking out This bridge should be replaced by new construction in 1969. See photos.

P-1-3791-4583

P-1-5972-6110

P-32-0037-0081

P-32-0037-0081

P-32-0037-0343

P-32-0037-0343

P-42-0000-0634

P-42-0000-0727

S-243-0000-0059

S-243-0000-0059

S-243-0000-0117

S-248-0000-0029

S-248-0000-0029

S-363-0000-0007

S-363-0000-0013

S-363-0000-0013

S-363-0000-0013

S-480-0000-0138

S-480-0000-0138

S-496-0000-0103

S-528-0000-0191

S-528-0000-0191

S-537-0000-0057

S-537-0000-0057

BILLINGS CONSTRUCTION DIVISION

							E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W			Z	Z1	
I	90	3746	3980	133	PRE CONC BEAM	INT-CO RD	F		E		E	E					E			E	E		E		E	F	G	G		X
I	90	3746	3980P	133	PRE CONC BEAM	INT-CO RD	G		E		E	E					E			E	E		E		E	P	G	G		
I	90	3746	4022	21	CONCRETE SLAB	JR INT-CO RD	G		E		F	E									E		E		G		G	G		X
I	90	3746	4031	16	CONC SLAB	JR GR SEP CO RD	G		E		F	E									E		E		G		G	G		X
I	90	3746	4033	558	RIV PL GIRDER	YELLOWSTONE R	G		E	E	E	E	E	E	E	E	E			E	G	G	F	E	G	E	G	E		X
I	90	3746	4037	249	STEEL GIRDER	NP RY	G		E		E	E					E			E	E		G		E	G	G	E		
I	90	3746	4046	16	CONC SLAB	JR GR SEP CO RD	F		E		G	E									E		E		E		G	E		
I	90	3746	4057	102	PRE CONC BEAM	BERRY CREEK	F		E		E	E		G	G	G	E			E	E		F		E	G	G	G		
I	90	3746	4140	76	CONCRETE T BEAM	KEYSER CR	G		G			G		G	G	G	G				P		G		F		P	G		
I	90	3746	4198	96	CONCRETE T BEAM	BROWN CR	G		G			G		G	G	G	G			G	G	G	G		G			G		
I	90	3746	4204	84	STEEL I BEAM	HENSLEY CR	F		F			F		G		G		G			G	G	G		G		P	F		
I	90	3746	4226	23	STEEL T BEAM	COVE IRR DT	F		G		F	G		G		G		G			G	G	G		F		P	G		
I	90	3746	4254	21	STEEL I BEAM	ALLEN CR	G		G		G	G		G	G	G		G			G	G	G		F		F	G		
I	90	3746	4268	100	CONT CONC T BM	BIG DITCH	F		G			G		G	G	G	G				G	G	G		G		F	G		
I	90	3746	4311	108	STEEL I BEAM	VALLEY CR	F		F			G		G	G	G		G			F	G	G		F		P	G		
I	90	3746	4328	123	PRE CONC BM	PARK CITY INT-10	E		E					E		E	E				E		E		E		E	E		
I	90	3746	4328P	123	PRE CONC BM	PARK CITY INT-10	E		E					E		E	E				E		E		E		E	E		
I	90	4328	4333	123	PRE CONC BM	SEP-CO RD	E		E					E		E	E				E		E		E		E	E		
I	90	4328	4333P	123	PRE CONC BM	SEP-CO RD	E		E					E		E	E				E		E		E		E	E		

I	90	4328	4375	123	PRE CONC BM	SEP-CO RD	E	E			E		E	E		E	E	E		E	E
I	90	4328	4375P	123	PRE CONC BM	SEP-CO RD	E	E			E		E	E		E	E	E		E	E
I	90	4328	4392	491	PRE CONC BM	W LAUREL INT-RY	E	E		E	E		E	E	E	E	E	E	E	E	E
I	90	4328	4392P	487	PRE CONC BM	W LAUREL INT-RY	E	E		E	E		E	E	E	E	E	E	E	E	E
I	90	4328	4396		UNDERPASS	SEP-CO RD	E	E					E	E							E
I	90	4328	4396A		UNDERPASS	SEP-CO RD	E	E					E	E							E
I	90	4328	4403	364	RIV PL GIR	S LAUREL INT-212	E	E	E		E		E	E		E	E	E		E	E
I	90	4328	4403P	364	RIV PL GIR	S LAUREL INT-212	E	E	E		E		E	E		E	E	E		E	E
I	90	4403	4417		UNDERPASS	SEP-CO RD	G	E		E				E	E		E	E	E	G	E
I	90	4403	4417A		UNDERPASS	SEP-CO RD	G	E		E				E	E		E	E	E	G	E
I	90	4403	4437	118	PRE CONC BEAM	INT-US 10	G	E		E				E	E	E	E	E	E	G	E
I	90	4403	4437P	118	PRE CONC BEAM	INT-US 10	G	E		E				E	E	E	E	E	E	G	E
I	90	4437	4442	40	PRE CONC BEAM	BBWA CANAL	G	E	E	E	G		G	E		E	E	E		G	E
I	90	4437	4442P	40	PRE CONC BEAM	BBWA CANAL	G	E	E	E	G		G	E		E	E	G		G	E
I	90	4437	4465	153	PRE CONC BEAM	SEP-OR 502	G	E		E				E	E	E	G	G	G	G	G
I	90	4437	4465P	153	PRE CONC BEAM	SEP-OR 502	G	E		E				E	E	E	G	G	F	G	G
I	90	4437	4489		UNDERPASS	SEP-OR 429	F	G		G				E	G	G	G		G	F	G
I	90	4437	4489A		UNDERPASS	SEP-OR 429	F	G		G				E	G	G	G		G	F	G
I	90	4437	4491	153	PRE CONC BEAM	CANYON CR	F	G		G	G	G	G	G	G	G	G	G	G	F	G

A	B			E	F	G	H		J			M	N	O		Q	R	S	T	U		W				Z	cc
I 90 4437 4491P	153	PRE CONC BEAM	CANYON CR	F		G			G		G	G	G	G			G	G		G		G	G	F	G		
I 90 4437 4517	82	PRE CONC BEAM	HOGAN SL	G		G			G		G		G	G			G	G		G		G	G	G	G		
I 90 4437 4517P	82	PRE CONC BEAM	HOGAN SL	G		G			G		G		G	G			G	G		G		G	G	G	G		
I 90 4437 4522	185	PRE CONC BEAM	W BILLINGS INT	G		E			E					E				E		G		E		E	E		
I 90 4437 4522P	185	PRE CONC BEAM	W BILLINGS INT	G		E			E					E				E		G		E		E	E		
I 90 4522 4524	195	PRE CONC BEAM	W BILLINGS INT	G		E			E					E				E		G		E		E	E		
I 90 4522 4524P	195	PRE CONC BEAM	W BILLINGS INT	G		E			E					E				E		G		E		E	E		
I 90 4522 4534		UNDERPASS	BILLINGS BLV SEP	G		E			E					E											E		
I 90 4522 4534A		UNDERPASS	BILLINGS BLV SEP	G		E			E					E											E		
I 90 4522 4555		UNDERPASS	SUGAR AVE SEP	G		E			E					E											E		
I 90 4522 4555A		UNDERPASS	SUGAR AVE SEP	G		E			E					E											E		
I 90 4522 4563		UNDERPASS*	27TH ST INT-SR 3	G		E			E					E											E		
I 90 4522 4563A		UNDERPASS*	27TH ST INT-SR 3	G		E			E					E											E		
I 90 4563 4568	148	PRE CONC BEAM	MT POWER RR SPUR	G		E			E					E				E		E		E		E	E		
I 90 4563 4568P	148	PRE CONC BEAM	MT POWER RR SPUR	G		E			E					E				E		E		E		E	E		
I 90 4563 4583	945	RIV PL GIRDER	YELLOWSTONE R	G		E	E		E		G	G	G	E			E	E	E	F		E	E	G	E		
I 90 4563 4583P	945	RIV PL GIRDER	YELLOWSTONE R	G		E	E		E		G	G	G	E			E	E	E	F		E	E	G	E		
I 90 4563 4591S	276	PRE CONC BEAM	LOCKWOOD INT-I94	G		E			E					E				E		E				E	E		
I 90 4591 4606	57	UNT T TRESTLE	DRY CR	G	G	G			G		G	F			P			F		G		F		F	F		X

I	90	4591	4698	69	CONCRETE SLAB	PRYOR CR	G		F		F	G		G	F			G			E		G		G		F	G	
I	90	4591	4700	55	CONCRETE SLAB	E FK PRYOR CR	G		G			G		G	F			G			E		G		G		F	G	
I	90	4591	4866	19	T T TRESTLE	STOCKPASS & DR	F	F	F		G	P						F			F		G		G		P	G	
I	90	4591	4907	57	UNT T TRESTLE	FLY CR	G	G	G			G		G	G			P			F		G		G		P	G	X
I	90	4591	4945	233	CONCRETE T BEAM	CB & Q RY	G		P			G					G			P	G		G		F	P		F	X
I	90	4591	4959	19	T T TRESTLE	STOCKPASS & DR	G	G	G		G	G				G		F			G		G		G		F	G	
I	90	4591	5005	38	T T TRESTLE	PERISTA CR	G	G	F		F	G		G		G		F			F		G	G	G		F	G	X
I	90	4591	5015	19	T T TRESTLE	STOCKPASS & DR	F	G	G		G	G		G		G		F			G		G		G		F	G	X
I	90	4591	5052	31	CONCRETE T BEAM	TWO LEGGIN CA	G	G	G			G		G	F	G					F		G		F			G	
I	90	5065	5086	578	STEEL TRUSS	BIG HORN R	G		G	G		G		G		G		G	G	G	F	G	G	G	G	P	P	G	X
I	90	5065	5137	118	PRE CONC BEAM	INT-CO RD	F		E			E					E			E	E		G		E		F	E	
I	90	5065	5137P	118	PRE CONC BEAM	INT-CO RD	F		E			E					E			E	E		G		E		F	E	
I	90	5065	5146	15	CONCRETE SLAB	JR GR SEP	G		E		P	E					E			E	E		G		E		F	G	X
I	90	5065	5196	133	PRE CONC BEAM	INT-CO RD	F		E			E					E			E	E		G		E		P	G	
I	90	5065	5196P	133	PRE CONC BEAM	INT-CO RD	G		E			E					E			E	E		G		G		P	G	
I	90	5065	5201	165	PRE CONC BEAM	LITTLE BIGHORN R	G		E	E		E	E	G	G	G	E			E	E		G		E		F	E	
I	90	5065	5201P	130	CONT ST GIRDER	LITTLE BIGHORN R	G		G	G	G	G	G	G	G	G	G			F	G	F	G		G	F	F	G	
I	90	5065	5214		UNDERPASS*	INT-US 212	F		E			E					E			E			E				G	E	
I	90	5065	5214A		UNDERPASS	INT-US 212	F		E			E					E			E			E				G	E	

A	B			E	F	G	H		J			M	N		P		R					W			Z	
I 90 5214 5221	156	CONCRETE T BEAM	LITTLE BIGHORN R	G			G		G	G	G	G	G	G			G	G	F	G		G		G	G	
I 90 5214 5280	156	CONCRETE T BEAM	LITTLE BIGHORN R	P			G		G	G	G	G	G	G			G	G	G	G		F		F	G	
I 90 5214 5338	136	CONCRETE T BEAM	LITTLE BIGHORN R	P			G		G	G	G	G	G	G			G	G	F	G		G		G	G	
I 90 5214 5409	64	CONCRETE T BEAM	LODGE GRASS CR	G			G		G	G	G	G	G	G			G	G	P	G		G		F	G	
I 90 5214 5501	120	CONT ST GIRDER	LITTLE BIGHORN R	F		G	G		G	G	G	G	G	G			F	G	F	G		G	F	P	G	
I 90 5214 5585	65	CONT ST GIRDER	PASS CR	F	G	G	G		G		G	G	G	G			G	G	G	G		G		G	G	
I 90 5214 5592	65	CONT ST GIRDER	PASS CR	F	G	G	G		G		G	G	G	G			G	G	G	G		G		G	G	
I 94 0000 0000		UNDERPASS	INT-I90 & US 87	E		E			E					E										E	E	
I 94 0000 0000A		UNDERPASS	INT-I 90 & US 87	E		E			E					E										E	E	
I 94 0000 0024	150	PRE CONC BM	JOHNSON LANE-SEP	G		E			E					E				E		E		E		E	E	
I 94 0000 0024P	150	PRE CONC BM	JOHNSON LANE-SEP	G		E			E					E				E		E		E		E	E	
I 94 0000 0037		UNDERPASS	PINE HILL INT	E		E			E					E										E	E	
I 94 0000 0037A		UNDERPASS	PINE HILL INT	E		E			E					E										E	E	
I 94 0000 0045	153	PRE CONC BM	SEP-CO RD	E		E			E					E				E		E		E		E	E	
I 94 0000 0045P	163	PRE CONC BM	SEP-CO RD	E		E			E					E				E		E		E		E	E	
I 94 0000 0095		PRE CONC BM	HUNTLEY INT	E		E			E					E										E	E	
I 94 0000 0095P		PRE CONC BM	HUNTLEY INT	E		E			E					E										E	E	
I 94 0000 0098	313	PRE CONC BEAM	PRYOR CR																							N

I 94 0000 0098P	313	PRE CONC BEAM	PRYOR CR												N
I 94 0000 0106	92	PRE CONC BM	PRYOR CR	E	E	E	E	E	E	E	E	E	E	E	
I 94 0000 0107	70	PRE CONC BM	HUNTLEY CANAL	E	E	E	E	E	E	E	E	E	E	E	
I 94 0000 0135	78	CAST CONC SLAB	SEP-CO RD												N
I 94 0000 0135P	78	CAST CONC SLAB	SEP-CO RD												N
I 94 0000 0181	128	PRE CONC BEAM	BALLANTINE INT												N
I 94 0000 0181P	128	PRE CONC BEAM	BALLANTINE INT												N
I 94 0000 0198	448	PRE CONC BEAM	CB & GRR-CO RD												N
I 94 0000 0198P	446	PRE CONC BEAM	CB & GRR-CO RD												N
I 94 0000 0207	154	PRE CONC BEAM	SEP-CO RD												N
I 94 0000 0207P	154	PRE CONC BEAM	SEP-CO RD												N
I 94 0000 0228	128	PRE CONC BEAM	SEP-CO RD												N
I 94 0000 0228P	118	PRE CONC BEAM	SEP-CO RD												N
I 94 0000 0237	107	PRE CONC BEAM	HUNTLEY CA												N
I 94 0000 0237P	117	PRE CONC BEAM	HUNTLEY CA												N
I 94 0000 0245		UNDERPASS	SEP-CO RD												N
I 94 0000 0245A		UNDERPASS	SEP-CO RD												N
I 94 0000 0265		UNDERPASS	POMPEYS PILLAR												N
I 94 0000 0265A		UNDERPASS	INT US 10												N

A	B			E	F	G	H			K	L	M	N	O	P	Q	R								Z	
I 94 0265 0287	125	T T TRESTLE	FLY CR	G	G	G	F		G	F	G		G		G			G	G	G	F	G		G	G	
I 94 0265 0306	57	T T TRESTLE	SAND CR	G	G	G			G		G	G	F		G			P	F	G	G	G		G	G	
I 94 0265 0330	57	T T TRESTLE	MILL CR	G	G	G			G		G	G	G		F			F	F	G	G	G		G	G	X
I 94 0265 0345	57	T T TRESTLE	KAISER CR	G	G	G			G		G	G	G		G			F	G	G	G	G		G	G	
I 94 0265 0361	57	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			F		G	G	G		G	G	
I 94 0265 0376	57	T T TRESTLE	SPRING CR	G	G	G			G		G	G	G		G			G	F	G	G	G		G	G	
I 94 0265 0406	106	STEEL GIRDER	AUTOMATIC CR	G		G			G		G	G	G	G			G	G	G	G		G	F	F	G	
I 94 0535 0558	580	RIV PL GIRDER	BIG HORN R	G		E	E		E	E	G	G	G	E			E	E	E	E	E	E	E	G	E	
I 94 0535 0568		UNDERPASS	INT-CO RD	G		E			E					E			E							G	E	
I 94 0535 0716	143	PRE CONC BM	HYSHAM INT-US 10	G		E			E					E			G	G		G		E		G	E	
I 94 0716 0754	188	PRE CONC BM	SARPY CR	E		E		E	E	E	E			E			E			E		E		E	E	
I 94 0716 0757		UNDERPASS	SARPY INT-OR 415	E		E			E					E			E							E	E	

P	2	4387	4387		UNDERPASS*	PARK CITY INT 10	E	E			E	E				E						E	
P	2	4387	4388		UNDERPASS*	PARK CITY INT 10	E	E			E	E				E						E	
P	2	4387	4389	34	STEEL I BEAM	BIG DITCH	G	G	F	G	G	G		G		G	G	G	G		P	G	
P	2	4387	4392	27	STEEL I BEAM	COVE IRR DT	G	G	G	G	G	G		G		P	G	G	P		F	G	
P	2	4387	4409	25	STEEL I BEAM	COVE IRR DT	G	G	G	G	G	G		G		G	G	G	P		F	G	
P	2	4387	4426	63	CONCRETE T BEAM	BIG DITCH	F	F	F	F	G	G	G			G	G	G	G			F	
P	2	4467	4500	269	STEEL GIRDER	NP RY	G	C		F			G		P	G	F	F	G	P	P	P	X
P	2	4467	4503		UNDERPASS	INT-I 90	G	E		E			E		E	E					E	E	
P	2	4467	4504		UNDERPASS	INT-I 90	G	E		E			E		E	E					E	E	
P	2	4595	4595		UNDERPASS*	W BILLINGS INT	E	E		E			E		E	E					E	E	
P	2	4595	4595A		UNDERPASS	W BILLINGS INT	E	E		E			E		E	E					E	E	
P	2	4595	4596		UNDERPASS	W BILLINGS INT	E	E		E			E		E	E					E	E	
P	2	4595	4596A		UNDERPASS*	W BILLINGS INT	E	E		E			E		E	E					E	E	
P	2	4595	4598		UNDERPASS	SEP OR 305	G	E		E			E		E	E					E	E	
P	2	4595	4598A		UNDERPASS	SEP OR 305	G	E		E			E		E	E					E	E	
P	2	4595	4599		UNDERPASS	SEP OR 305	G	E		E			E		E	E					E	E	
P	2	4595	4599A		UNDERPASS	SEP OR 305	G	E		E			E		E	E					E	E	
P	2	4611	4613	1711	PRE CONC BEAM	NP RY & US BYP	F	E	F	E			E		E	G		G	G	G	G	G	X
P	2	4611	4613P	1711	PRE CONC BEAM	NP RY & US BYP	F	E	F	E			E		E	G		G	G	G	G	G	X

							E	F	G				K	L	M	N		P	Q	R	S	T	U		W			Z		
P	2	4682	4688	63	T T TRESTLE	FIVE MILE CR	G	G	G			G		G	G	G		G			F	G	G	G	G		G	G		
P	2	4682	4695	67	T T TRESTLE	BL&I IRR DT	G	G	G	G		G		G	G	G		G			G	F	G	G	G		G	G		
P	2	4682	4699	11	T T TRESTLE	STOCK PASS	G	G	G		G	G						G			G		G	G	G		G	G		
P	2	4682	4704	59	T T TRESTLE	BL&I IRR DT	G	G	G	G		G		G	G	G		G			F	G	G	G	G		G	G		
P	2	4682	4705	11	T T TRESTLE	STOCK PASS	G	G	G		G	G						G			F		G	G	G		G	G		
P	2	4682	4710	25	T T TRESTLE	SEVEN MILE CR	G	G	G			G		G	G	G		G			F	G	G		G		G	G		
P	2	4682	4748	100	T T TRESTLE	TWELVE MILE CR	G	G	G			G		G		G		G			F	F	G	G	G		F	G		
P	2	4682	4770	1022	STEEL GIRDER	YELLOWSTONE R	G		G	G		G	G	G	G	G	G			G	G	G	G	G	F	F	P	G		
P	2	4682	4805	25	STEEL I BEAM	CUSTER COU	G		G		G	G		G		G		G			G	G	G	G	G			G		
P	2	4682	4814	14	CONCRETE SLAB	DRAINAGE	G		G			G		G	G	G		G					G				P	G		
P	2	4682	4869	24	STEEL I BEAM	ARROW CR.	G		F		F	F		G		G		G					G		F		P	G		X
P	2	4682	4941	268	ST. PONY TRUSS	NP RY	F		F			G					G	G	G	F	F	F	G	G	G	F	P	G		X
P	2	4682	4943	259	CONT STEEL BM	INT I-94																							N	
P	2	5383	5383R		UNDERPASS	HYSHAM INT I 94	E		G			E					E			E							E	E		
P	2	5383	5413	25	T T TRESTLE	IRR DT	F	G	G			G		G		G		G			F		G	G	G		F	G		
P	2	5383	5425	19	T T TRESTLE	STOCKPASS	F	G	G		P	G		G		G		F			P		G	G	P		P	G		X
P	2	5383	5428	19	T T TRESTLE	DRAINAGE	G	G	G		F	G		P		G		G			F		G	G	G		F	G		
P	2	5383	5442	57	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			F		G	G	F		F	G		
P	2	5383	5446	38	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		F			G		G	G	F		F	G		X

P	2	5383	5451	95	T T TRESTLE	SARPY CR	G	G	G	G		G	G	G		G		F		F	G	G	G	F		F	G	X
P	2	5383	5456	38	T T TRESTLE	DRAINAGE	F	G	G			G		G	P	G		F		G		G	G	F		G	G	X
P	2	5383	5460	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		F		G		G	G	F		G	G	X
P	2	5383	5491	76	T T TRESTLE	IRR DT	F	G	G			G		G		G		F		G		G	F	F		G	G	X
P	2	5383	5502	19	T T TRESTLE	STOCKPASS	F	G	G		P	F						G		F		G	G	F		G	G	
P	2	5383	5507	57	T T TRESTLE	IRR DT	G	G	G			F		G		G		F		G		G	G	F		F	G	X
P	2	5383	5508	19	T T TRESTLE	STOCKPASS	F	G	G			G		G		G		G		G		G	G	F		F	G	
P	2	5383	5511	19	T T TRESTLE	STOCKPASS	F	G	G			G		G	F	G		G		F		G	G	G		P	G	
P	2	7128	7130S		UNDERPASS*	I 90 PTW--US 10			E								E		E	E		E					E	
P	2	7128	7131S		UNDERPASS*	I 90 PTW-US 10			E								E		E	E		E					E	
P	2	7145	7155		UNDERPASS	NP RY	G		G		G	G					G		G	F				G		F	G	X
P	4	0000	0005	57	T T TRESTLE	USRS FRANNIE CA	G	G	G			G		G		G		G		G	G	G	G	G		G	G	
P	4	0000	0042	76	T T TRESTLE	SAGE CR	G	G	G		G	G	G	G		G		P		G	G	G	G	G		F	G	X
P	4	0000	0121	142	CONCRETE T BEAM	C8&Q RR	G		G			G					G			G		G		G			G	
P	4	0000	0225	19	T T TRESTLE	DRAINAGE	G	G	G		F	G		G		G		G		F		G		G		G	G	
P	4	0000	0235	57	T T TRESTLE	8RIDGER CR	G	G	G			F		G		G		F		G		G	G	G		F	G	X
P	4	0000	0237	300	STEEL GIRDER	CLARK-FK YELLO R	G		G	G		G	G	G		G	G		G	G	G	G	G	G	G	F	G	
P	4	0000	0242	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G		F		G		G		F	G	

P	4	0000	0245	19	T T TRESTLE	DRAINAGE	F	G	G			G		G	F	G		G			G		G		G		G	G	
P	4	0247	0256	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	F	G		F			F		G		F		F	G	
P	4	0247	0290	57	T T TRESTLE	SAND CR	F	G	G			F		G	F	G		G			G		G	P	F		F	G	X
P	4	0247	0306	19	T T TRESTLE	DRAINAGE-STK	G	G	G		G	G						G			F		F		F		F	G	
P	4	0247	0424	139	CONCRETE T BEAM	ROCK CR	E		E			E		E	E	E	E			G	E		G		E			E	X
P	4	0427	0526		UNDERPASS	NP RY	G		G		G	G					G	G		G	G	G					G	G	
P	4	0427	0529	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G		G		E	G	
P	4	0427	0535	496	STEEL TRUSS	YELLOWSTONE R	G		F	F		F	G	G		G			G	G	G	G	G	G	F		F	G	X
P	4	0427	0541		UNDERPASS*	LAUREL INT-I 90	E		E			E					E			E	E							E	
P	4	0541	0541		UNDERPASS*	LAUREL INT-I 90	E		E			E					E			E	E							E	
P	4	0541	0545		UNDERPASS	NPRY	G		G		P	G					G	G			P				F		P	G	X
P	16	1039	1039	276	PRE CONC BEAM	LOCKWOOD INT I90	G		E			E					E				E		E				E	E	
P	16	1039	1039T	276	PRE CONC BEAM	LOCKWOOD INT I90	G		E			E					E				E		E				E	E	
P	16	1039	1045	262	CONT STEEL BEAM	NP RY	G		G			G					G			P	F		G	F	F	P	P	F	
P	16	1039	1047	540	CONT STEEL TRUS	YELLOWSTONE R	G		F	G		G	G	G		G		G	G	G	F	F	F	F	F	F	F	F	X
P	16	1039	1049	35	CONC T BEAM	SEWER DT	G		G			G					G				F		G					G	X
P	16	1088	1091	57	T T TRESTLE	FIVE MILE CR	G	F	G			G		F		G		G			F	G	G	G	F		F	G	
P	16	1088	1097	39	STEEL I BEAM	BBWA CA	G	F	G			F		G		G		G			P	F	G		F		F	G	

A	B TOTAL LENGTH FEET	C MATERIAL … MAXIMUM SPAN	D NAME OF FEATURE	E END FILLS	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q	R	S CURBS	T MARKERS	U DECK	V	W	X	Y	Z	Z1	Z2
P 16 1088 1143	31	STEEL I BEAM	ELEVEN MILE CR	G	G	G			G		G		G		G			F		G		F		G	G		
P 16 1088 1148	38	T T TRESTLE	MID FK 12 MI CR	F	G	G			F		G		G		G			F		G		F		G	G		
P 16 1088 1151	38	T T TRESTLE	N FK 12 MILE CR	F	G	G			F		G		F		G			F		G	G	F		G	G		
P 16 1088 1203	57	T T TRESTLE	S FK CROOKED CR	G	G	G			F		G		G		G			F		F	G	F		G	G		
P 16 1088 1210	57	T T TRESTLE	N FK CROOKED CR	G	G	G			F		G		G		G			F		G	G	F		G	G		
P 16 1088 1245	57	T T TRESTLE	DRY WASH	G	G	G			F		G	G	G		G			F		G	G	F		G	G		
P 16 1088 1285	57	T T TRESTLE	DRAINAGE	G	G	G			F		G	G	G		G			F		G	G	F		G	G		
P 16 1088 1287	57	T T TRESTLE	DRAINAGE	G	G	G			F		G	F	G		G			F		G	G	F		G	G		
P 28 0000 0057	25	CONCRETE T 8EAM	DRAINAGE	G		G			G		G		G	G				G		G		G			G		
P 28 0000 0072	63	CONCRETE T 8EAM	W FK ROCK CR	G		G			G		G	G	G	G				G		G		G			G		
P 28 0000 0243	122	CONCRETE T 8EAM	ROCK CR	G		G			G		G	G	G	G				G	G	G		G			G		
P 28 0000 0343	123	STEEL I 8EAM	ROCK CR	F	F	P	F	F	P	G	F	G	G	G	P			G		G		G		F	C		X
P 28 0000 0348	38	T T TRESTLE	DRAINAGE	F	F	G			G		G		G		F			G		G	G	G		F	G		X
P 37 0000 0000	210	PRE CONC 8EAM	INT-I90	F		E			E					E			E	E		E		E		G	E		
P 37 0000 0013	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G	G	G		G			G		G	G	G		G	G		
P 37 0000 0030	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G		G	G	G		G	G		
P 37 0000 0081	76	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		P			G		G	G	G		F	G		X

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W			Z		
P 37 0000 0093	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		P			G		G	F	G		F	G		X
P 37 0000 0129	95	T T TRESTLE	W FK TULLOCK CR	G	G	G			F		G	G	G		P			G		G	F	G		G	G		X
P 37 0000 0147	76	T T TRESTLE	DRAINAGE	F	G	G			F		G	G	G		P			G		G	G	G		G	G		X
P 37 0000 0156	38	T T TRESTLE	DRAINAGE	G	G	G			F		G	F	G		P			G		G	G	G		G	G		X
P 37 0000 0165	38	T T TRESTLE	DRAINAGE	G	G	G			F		G	G	G		P			G		G	G	G		G	G		X
P 37 0000 0170	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		P			G		G	G	G		G	G		X
P 37 0000 0249	75	T T TRESTLE	ROSEBUD CR	G	G	G			G		G	G	G		F			G	G	G	G	G		G	G		X
P 37 0000 0255	38	T T TRESTLE	BUSBY CR	G	G	G			G		G	G	G		F			G	G	G	G	G		G	G		X
P 37 0000 0278	75	T T TRESTLE	PARK CR	G	G	G			G		G	G	G		F			G		G	G	G		G	G		X
P 37 0000 0283	100	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		F			G		G	G	G		G	G		X
P 37 0000 0293	75	T T TRESTLE	E PORCUPINE CR	G	G	G			G		G	G	G		F			G		G	G	G		G	G		X
P 37 0000 0303	75	T T TRESTLE	TWO MOON CR	G	G	G			G		G	G	G		P			G	G	G	G	G		G	G		X
P 37 0000 0313	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 37 0000 0321	75	T T TRESTLE	KILLSNIGHT CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		X
P 37 0000 0337	75	T T TRESTLE	RIDGEWALKER CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 37 0000 0367	95	T T TRESTLE	MUDDY CR	G	G	G			G		G		G		G			G	G	G	G	G		G	G		
P 48 0000 0009	25	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		F			P		G	G	F		P	G		
P 48 0000 0015	68	T T TRESTLE	DRAINAGE	G	G	G					G		F		G			F		G	G	F		P	G		

P	48	0000	0055	31	T T TRESTLE	LOW LINE DITCH	F	F	F			F		G		G		F		F		P		F	F	F	X
P	48	0000	0075	38	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G		G		G	G	G	F	G	
P	48	0000	0080	38	T T TRESTLE	LOW LINE DITCH	G	G	G			G		P		G		G		F		F	G	F	F	G	
P	48	0000	0083	57	T T TRESTLE	LOW LINE DITCH	G	G	G			G		G		G		G		F		G	G	F	F	G	
P	48	0000	0113	38	T T TRESTLE	DRAIN DITCH	G	G	G	G		G	G	G		F		G		F		G	G	F	G	G	
P	53	0000	0000	220	PRE CONC BEAM	27TH ST INT I90	G		E			E					E		E	E		E		E	E	E	
P	53	0000	0000T	220	PRE CONC 8EAM	27TH ST INT I90	G		E			E					E		E	E		E		E	E	E	
P	53	0013	0024	35	T T TRESTLE	8L&I CANAL	G	G	G		G	G		G		G		G		G		G		G	G	G	
P	53	0013	0097	95	T T TRESTLE	S FK ALKALI CR	F	G	G			G		G	G	G		G		F		G	G	G	G	G	
P	53	0013	0106	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G		G		G	G	G	F	G	
P	53	0013	0119	57	T T TRESTLE	N FK ALKALI CR	G	G	G			G		G	G	G		G		G	G	G	G	G	G	G	
P	53	0013	0145	76	T T TRESTLE	S FK FIVE MILE C	G	G	G			G		G	G	G		G		G		G	G	G	G	G	
P	53	0013	0147	57	T T TRESTLE	N FK FIVE MILE C	G	G	G			F		G	G	G		G		G		G	G	G	G	G	

						E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	
M308	0000	0001	62	STEEL I BEAMS	ROCK CR	G		F	F	G	G		G	G	G	G	G			F		G		P		P	G	X
M308	0147	0158	244	STEEL GIRDER	CLARK FORK	F		G	G		G	G	G	G	G	G			G	G	G	G		G	F	G	G	
M308	0147	0175	57	T T TRESTLE	SILVER TIP CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G	
M308	0147	0183	261	STEEL GIRDER	CLARK FORK	G		G	G		G	G	G	G	G	G			G	G		G		G	G	G	G	
M397	0000	0055	194	STEEL GIRDER	CLARK FORK	F		G	G	F	G		G	G	G	G			G			G		G		G	G	X

S302 0000 0090		UNDERPASS	GN RY	G		G								G			G							P	G		
S303 0000 0072	24	STEEL I BEAM	ARROW CR	F	C	P		P	F		G		G		P			P		G		P		P	P		X
S303 0000 0082	36	STEEL I BEAM	CANAL	G		G	G	G	G		G		G		G			F		F		G		G	G		
S303 0000 0104		UNDERPASS	I 90 SEP																							N	
S303 0000 0105		UNDERPASS	I 90 SEP																							N	
S303 0000 0150	23	ST I BM PILE	CANAL	G	G	G		F	F		G		G		G			P		F		P		G	G		
S303 0000 0159	25	T T TRESTLE	CANAL	G	G	G			G		P		G		G					G	F	F		F	G		
S305 0000 0036	120	CONT CONC T BM	CANYON CR	G		G			G		F	G	G	G			G	G	F	G		F		F	G		
S305 0000 0049	25	T T TRESTLE	BIG DITCH BBWA	G	G	G		G	G		G		G		G			G		G	G	G		G	G		
S305 0000 0101	29	T T TRESTLE	BBWA CANAL	F	G	G		G	G		G		G		G			G		G	G	G		G	G		
S305 0000 0112	190	PRE CONC BEAM	NP RY	G		E			E					E			E	E		E		E	E	G	E		
S305 0000 0112P	190	PRE CONC BEAM	NP RY	G		E			E					E			E	E		E		E	E	G	E		
S305 0000 0118	175	PRE CONC BEAMS	SEP US 10	G		E			E					E			E	E		E		E	E	G	E		
S305 0000 0118P	175	PRE CONC BEAMS	SEP US 10	G		E			E					E			E	E		E		E	E	G	E		
S306 0000 0036	30	STEEL I BEAM	KEYSER CR	G		G		G			G	F		G											F		
S306 0000 0058	95	T T TRESTLE	KEYSER CR	F	G	G	G	G	G	G	G	G			G			F	P	F	G	G		P	G		

S307 0000 0129	25	T T TRESTLE	W RED LODGE C	P	G	G		G	G		G		G		G		G	P	G	G	G		P	G	
S307 0000 0198	110	CONT CONCT BEAM	E ROSEBUD CR	P		G			G		G	G	G	G		G	G	G	G		G		G	G	
S307 0000 0262	153	PRE CONC BEAMS	E ROSEBUD CR	F		G	G		G		G	G	G	G		G	G	G	G		G	G	G	G	
S307 0000 0301	30	STEEL I BEAM	BUTCHER CR	G		G		G	G		G		G		G		G		G		G		F	G	
S307 0000 0349	50	T T TRESTLE	BEAVER CR	G	G	G		G	G		G	G	G		F		G	P	G	F	F		P	G	X
S307 0000 0435	63	T T TRESTLE	SHAYNE CR	G	G	G	G	G	G		G	G	G		C		G	P	G	G	G		P	G	X
S307 0000 0461	576	RIV PL GIRDERS	YELLOWSTONE R	P		G	G	G	G	G	G	G	G	G	G	G	G		G	G	G	G	F	G	
S310 0000 0008	562	RIV PL GIRD	YELLOWSTONE R	P		E	E		G	E	E	G	G	E		E	E	G	E	E	E	G	G	G	
S311 0000 0130	62	UNT T TRESTLE	DRAINAGE	G	P	F			F		P		G		F		P		F	F	P		P	P	X
S311 0000 0169	704	WELDED PL GIRD	YELLOWSTONE R	E		E	E	E		E	G	E		E		E	E	E	E		E	E	E	E	X
S311 0000 0202	88	T T TRESTLE	BUCKINGHAM COU	G	G	G			G		G	P	G		P		F	P	G	G	P		P	G	X
S311 0000 0237	95	T T TRESTLE	BOX ELDER CR	G	G	P			F		G		G		P		F	G	G	G	P		P	F	X
S313 0000 0018	25	T T TRESTLE	WILLIAMS CR	G	G	G		G	G		G	F	G		C		F		G	G	G		F	G	X
S313 0000 0055	45	T T TRESTLE	TWO LEGGIN CANAL	G	G	G		G	G		G		G		F		F		G	G	G		P	G	
S313 0000 0070	50	T T TRESTLE	TWO LEGGIN CANAL	G	G	G		G	G		G		G		F		F		G	G	F		P	G	
S313 0000 0072	57	T T TRESTLE	OVERFLOW DITCH	P	G	G		G	P		P				C		F		F	G	F		P	F	X

S313 0000 0075	576	RIV PL GIRDERS	BIG HORN R	G		G	G		G	G	G	G	G	G			G	G	G	G	G	G	G	G	G		
S313 0000 0230	64	T T TRESTLE	ROTTEN GRASS CR	F	G	G			G		G		G		P			G		G	G	P		P	F		X
S313 0000 0317	102	PRE CONC BEAM	SOAP CR	F		E		E	E		G	G	G	E			E	E	E	E		E		G	E		
S313 0000 0341	65	PRE CONC BEAM	INDIAN SERVICE C	F		E		E	E		G	G	G	E			E	E		E		E		G	E		
S329 0000 0017	537	STEEL TRUSS	YELLOWSTONE R	F		F	F	F		G	G	F	F	G	F	G	F	G		F	F	F	P	P	F		X
S329 0000 0022	59	STEEL TRESTLE	DUCK CR	G	G	G				G	G		G	G				G		G		P		P	G		
S329 0000 0024	40	STEEL I BEAM	DUCK CR	E		E		E			F				E					E		E		G	E		X
S384 0000 0005	183	PRE CONC BEAM	LIT BIG HORN R	G		E	E		E	E	P	G	G	E			E	E	F	E		E	E	F	E		
S384 0000 0139	92	PRE CONC BEAM	TULLOCK R																							N	
S415 0000 0020	142	PRE CONC BM	SARPY INT I94	E		E			E					E				E	E	E		E		E	E		
S415 0000 0037	25	T T TRESTLE	SARPY CR	G	G	G		P	F		G		G		G			P		F	G	P		P	G		
S415 0000 0093	25	UNT T TRESTLE	SARPY CR	P	P	P		P	F		G		G		F			P		F	G	P		P	P		
S415 0000 0184	36	UNT T & CONC	SARPY CR	G		G	G			G	P		G		P			P		F	P	P		P	F		
S416 0000 0010	215	PRE CONC BEAM	BILLINGS BLV SEP	G		E			E					E			E	E		E		E	E	E	E		
S416 0000 0023	766	STEEL TRUSS	YELLOWSTONE R	G		G	G		G	G	F		G		G	G	G	F	F	F	G	F	F	P	G		

S416 0000 0029	38	T T TRESTLE	BLUE CR	F	G	G		G	G	P		G		G			F	F	G	G	P		P	G	
S41B 0000 0005	64	T T TRESTLE	PASS CR	G	C	P			G	F		G		G					G	F	G		P	P	X
S41B 0000 0096	90	STEEL TRUSS	LIT BIGHORN R	G		G			G	G	G	G		G	G	G	G		G	G	G	G	G	G	
S419 0000 0001	26	STEEL I BEAM	OF E ROSEBUD CR	G		P		G	G	G		G		G					G		P		F	G	X
S419 0000 0002	56	ST PONY TRUSS	EAST ROSEBUD CR	G		P		F	F	G		G		G	G		G		G	G	F		F	G	X
S419 0000 0036	60	ST PONY TRUSS	WEST ROSEBUD CR	G		G				G	P	G		P	P		P		G	G	P		P	F	X
S419 0000 0199	176	REINF CONC GIR	STILLWATER R	P		G	G			G		G	G			G	G	G	G		G	G		G	X
S419 0000 0213	31	UNT T PONY TRUS	DRAINAGE	F		F		F	F	G		G		P	P				F		P		P	F	
S419 0000 0214	42	STEEL I BEAM	W FK STILLWATER	G		G		G	G	G		G	G	P					F		P		P	F	
S420 0000 0002	24	STEEL I BEAM	DRAINAGE	F		G		G	G	G		G		G					G		P		P	G	
S420 0000 0003	95	STEEL TRUSS	ROSEBUD CR	G		P		G	G	G	P	G		G	G	G	F		G	G	P	F	P	G	X
S429 0000 0002	457	PRE CONC BEAMS	SEP-I90	G		G			G				E			G	G		G		G	G	F	G	
S429 0000 0012	133	PRE CONC BEAMS	CANYON CR	G		G			G	G	G	G	G			G	G	G	G		F	G	P	G	
S429 0000 0017	29	T T TRESTLE	BBWA CANAL	G	G	G		G	G	G		G		G			G		G	G	G		P	G	

S463 0000 0157	101	PRE CONC BEAM	ROTTEN GRASS CR	G		E		E	E	E		E		E	E	E		E	E	E	
S463 0000 0411	5B	T T TRESTLE	BIG HDRN CANAL	G	G	G		G	P		G		P			G	G	G	P	G	X
S502 0000 0001		UNDERPASS	BEETDUMP SEP-I90	G		E		E				E		E						E	
S502 0000 0002		UNDERPASS	BEETDUMP SEP-I90	G		E		E				E		E						E	
S502 0000 0004	24	STEEL I BEAM	BBWA CANAL	G		G	G	G	G		G		G		G	G		G	G	G	
S502 0000 0005	30	STEEL I BEAM	BBWA CANAL	G		G	G	F	G		P		G		G	G		P	P	G	X
S522 0000 0019	70	PRE CONC BEAM	HUNTLEY CANAL	E		E	E	E		E		E			E	E		E	E	E	
S522 0000 0021	92	PRE CDNC BEAM	PRYOR CR.	E		E	E	E		E		E			E	E		E	E	E	
S522 0000 0023		UNDERPASS	HUNTLEY INT I-94	E		E		E				E							E	E	
S522 0000 0024		UNDERPASS	HUNTLEY INT I-94	E		E		E				E							E	E	
S532 0000 0009	35	STEEL&CONCRETE	BIG DITCH	E		E	E		E		E	E			E	E		E	E	E	
S532 0000 007B	152	PRE CONC BEAM	CANYON CR	E		E	E		E		E	E			E	E		E	E	E	
S535 0000 001B	32	STEEL I BEAM	BBWA CANAL	F		G	C	G	G		G		G		F	G		C	P	F	

BILLINGS DIVISION

I-90-3746-3980 133' Pre Conc Beam Int. Co. Road
East end bent has settled considerably.

I-90-3746-4022 21' Concrete Slab Jr. Int. Co. Road
Retaining walls on all four corners have pushed out at the top 1½" to 2½" while remaining stationary at the bottom.

I-90-3746-4031 16' Concrete Slab Jr. Int. Co. Road
Retaining walls on all four corners have pushed out at the top 1" to 1½" while remaining stationary at the bottom.

I-90-3746-4033 558' Riv. Pl. Girder Yellowstone River
There are numerous cracks in the deck. These cracks run in no particular direction. (random cracking)

I-90-4591-4606 57' Unt. T. Trestle Dry Creek
One cracked stringer, 5th from north in center span.

I-90-4591-4907 57' Unt. T. Trestle Fly Creek
Six cracked stringers. Numbers 5, 6, 8, 9, from north in east span. Number 3 from north in center span. Number 12 from North in west span.

I-90-4591-4945 233' Concrete T. Beam CB & Q Ry
Probably due to bent settlement the 3rd span has shifted 5 5/8 inches to the west. See photo. Due to this shift the rocker shoes for expansion joint are about 2 inches out of original position. See photo.

I-90-4591-5005 38' T. T. Trestle Perista Creek
One cracked stringer, number 7 from north on east span.

I-90-4591-5015 19' T. T. Trestle Stockpass & Dr
One cracked stringer, number 9 from south. One piece of backing plank poor.

I-90-5065-5086 578' Steel Truss Big Horn River
End portals, intermediate portals and all intermediate cross sections have been hit numerous times. As a result of this coupled with a very poor paint job the structure is an eyesore to the public.

I-90-5065-5146 15' Concrete Slab Jr. Gr. Separation
Retaining walls on all four corners have pushed out at the top approximately 1 inch while remaining stationary at the bottom.

BILLINGS DIVISION

I-90-0119-0200 24' Steel I Beam Arrow Creek
Concrete is deteriorating around footings and lower part of backwall.

I-94-0119-0272 268' St. Pony Truss N.P. Ry.
Light scale is occurring on top portion of bents.

I-94-0119-0336 57' T T Trestle Mill Creek
One cracked stringer, number 7 from south in the center span.

P-2-4467-4500 269' Steel Girder N.P. Ry.
Spalling is critical on north end bent around shoes. There is very little room for expansion, possibly caused by south end bent moving in at the top.

P-2-4611-4613 1711' Pre Conc Beam N.P. Ry. & US Bypass
Retaining wall on west end of structure has moved out about 3 inches.

P-2-4611-4613P 1711' Pre Conc Beam N.P. Ry & US Bypass
Retaining wall on west end of structure has moved out about 2 inches.

P-2-5383-5425 19' T T Trestle Stockpass
One cracked stringer, number 3 from south.

P-2-5383-5446 38' T T Trestle Drainage
One cracked stringer, number 8 from north in east span.

P-2-5383-5451 95' T T Trestle Sarpy Creek
One cracked stringer, number 5 from north in west span.

P-2-5383-5456 38' T T Trestle Drainage
Two cracked stringers, number 7 from north in west span. Number 4 from north in east span.

P-2-5383-5460 57' T T Trestle Drainage
Two cracked stringers, number 3 from north in center span, number 8 from north in east span.

P-2-5383-5491 76' T T Trestle Irrigation Ditch
One cracked stringer, number 8 from north in east span.

BILLINGS DIVISION

P-2-5383-5507 57' T T Trestle Irrigation Ditch
Two cracked stringers, number 5 from north in west span, number 8 from north in center span.

P-2-7145-7155 Underpass N.P. Ry
There is a constant seepage of water to the concrete roadway from the side walls, probably due to high water table. There is some light surface spalling on the curbs and walls.

P-4-0000-0042 76' T T Trestle Sage Creek
Nine cracked stringers.

P-4-0000-0235 57' T T Trestle Bridger Creek
One cracked stringer, number 6 from west in south span.

P-4-0000-0290 57' T T Trestle Sand Creek
One piece of bracing is broken.

P-4-0000-0424 139' Concrete T Beam Rock Creek
This structure has been widened by contractor, 1968.

P-4-0427-0535 496' Steel Truss Yellowstone River
The corner abutments are scaling from a light to a severe degree.

P-4-0541-0545 Underpass N.P. Ry.
The retaining walls and curbs are scaling from a light to a heavy degree.

P-16-1039-1047 540' Cont Steel Truss Yellowstone River
The corner abutments are scaling from a light to a severe degree. Severe cracks also exist. Near the north end of this structure two verticle uprights have been struck and are in poor condition. These members are directly opposite of each other. On one side the rivets have been torn loose from the rail while on the other side the upright has a cut in the angle about 2 inches long. Both uprights are twisted badly. This appears to be the result of two separate incidents as both members are bent in the direction with traffic.

P-16-1039-1049 35' Conc T Beam Sewer Ditch
This structure no longer serves as a drain. The rails have been removed and the upper end has been filled.

BILLINGS DIVISION

P-28-0000-0343 123' Steel I Beam Rock Creek
The south span of this structure has untreated timbers which are in very poor condition. H beam piling has been driven in this span as well as the north end of structure. The backing plan on both ends of this structure is poor. See photo.

P-28-0000-0348 38' T. T. Trestle Drainage
Two cracked stringers, number 2 and 7 from east in south span.

P-37-0000-0081 76' T.T.Trestle Drainage
Seven cracked stringers.

P-37-0000-0093 57' T.T.Trestle Drainage
Four cracked stringers.

P-37-0000-0129 95' T. T. Trestle W. Fk. Tullock Creek
Four cracked stringers.

P-37-0000-0147 76' T. T. Trestle Drainage
Four cracked stringers.

P-37-0000-0156 38' T. T. Trestle Drainage
Five cracked stringers.

P-37-0000-0165 38' T. T. Trestle Drainage
Four cracked stringers.

P-37-0000-0170 57' T. T. Trestle Drainage
Three cracked stringers.

P-37-0000-0249 75' T. T. Trestle Rosebud Creek
Two cracked stringers.

P-37-0000-0255 38' T. T. Trestle Busby Creek
One cracked stringer.

BILLINGS DIVISION

P-37-0000-0278 75' T. T. Trestle Park Creek
One cracked stringer.

P-37-0000-0283 100' T. T. Trestle Drainage
Two cracked stringers.

P-37-0000-0293 75' T. T. Trestle East Porcupine Creek
Two cracked stringers.

P-37-0000-0303 75' T. T. Trestle Two Moon Creek
Four cracked stringers.

P-37-0000-0321 75' T. T. Trestle Killsnight Creek
One cracked stringer.

P-48-0000-0055 31' T. T. Trestle Low Line Ditch
This structure was partially burned about 20 years ago. A charred condition exists on the stringers, piles and backwalls. As a result of this fire, piling for a center bent was driven. Both ends of the cap on this center bent are beginning to rot.

M-308-0000-0001 62' Steel I Beam Rock Creek
The rail on this bridge is poor. There is a guy wire from a power pole attached to this rail.

M-397-0000-0055 194' Steel Girder Clark Fork
Basically this structure is in good condition. However because of the 16' 8" horizontal clearance it constitutes a safety hazard.

S-303-0000-0072 24' Steel I Beam Arrow Creek
The # 2 bent has 2 pilings completely rotted off. Several alternate stringers (3" x 12") are cracked.

S-307-0000-0349 50' T. T. Trestle Beaver Creek
One cracked stringer, number 6 from east in north span.

S-307-0000-0435 63' T. T. Trestle Shayne Creek
One cracked stringer, number 5 from west in center span. This is a diagonal crack and is critical.

BILLINGS DIVISION

S-311-0000-0130 62' Unt. T. Trestle Drainage
One pile in each bent is untreated and is in poor condition.

S-311-0000-0202 88' T. T. Trestle Buckingham Coulee
Three cracked stringers, number 7 from west in north span. Number 5 and 6 from west in 2nd span from north. Riprap on south end is poor.

S-311-0000-0237 95' T. T. Trestle Box Elder Creek
Two cracked stringers, number 8 from north in east span. Number 8 from north in 2nd span from east. This bridge has been jacked up at bent # 4 and #5 but has continued to sink and is about 6" low again on the south side.

S-313-0000-0018 25' T. T. Trestle Williams Creek
One cracked stringer, number 9 from east.

S-313-0000-0072 57' T. T. Trestle Overflow Ditch
Number 7 stringer from east in south span is cracked, number 8 stringer from east in south span is broken.

S-313-0000-0230 64' T. T. Trestle Rotten Grass Creek
Four cracked stringers. Numbers 4, 5, and 6 from west in north span. Number 8 from west in center span. This stringer has been repaired before but needs further attention.

S-329-0000-0017 537' Steel Truss Yellowstone River
This structure has an unusual alignment which may be caused from pier settlement.

S-418-0000-0005 64' T. T. Trestle Pass Creek
Number 1 pile on upstream side in bent 2 is broken. This was reported in the 1966 Bridge Condition report and still reamins in a critical condition.

S-419-0000-0001 26' Steel I Beam Overflow Rusebud Creek
The southwest corner of bent 2 is becoming undermined.

S-419-0000-0002 56' Steel Pony Truss East Rosebud Creek
Both bents are becoming undermined.

BILLINGS DIVISION

S-419-0000-0036 60' Steel Pony Truss West Rosebud Creek
Two cracked stringers, number 5 from north in west span. Number 3 from north in 2nd span from east. The riprap on the west end is poor. Three hangers on this bridge are broken loose from the gusset plate on the top of truss. This was reported in the 1966 Bridge Condition report but still remains in critical condition. See photo.

S-419-0000-0199 176' Reinforced Conc. Girder Stillwater River
The northwest end fill is approaching a critical condition. There is a cavity behind the bent. Also the fill around the corner abutment is very poor. See photo.

S-420-0000-0003 95' Steel Truss Rosebud Creek
On bent # 1 the concrete has eroded about 2 to 4 inches in depth just above the footing about 1/3 of the way across the bent. The riprap around bent # 1 is poor.

S-463-0000-0411 58' T. T. Trestle Big Horn Canal
The 7th stringer from the south on the east span is cracked.

S-502-0000-0005 30' Steel I Beam B.B.W.A. Canal
The concrete is deteriorating on the southwest corner of bent # 1 on the old section of the structure.

I-90-4591-4945

I-90-4591-4945

P-16-1039-1047

P-16-0000-0343

S-419-0000-0036

S-419-0000-0199

MILES CITY CONSTRUCTION DIVISION

I	94	0716	0856	180	PRE CONC BM	SEP-CO RD-RES CR	G		E			E		G	G	G	E			E	E		E		E		E	E
I	94	0716	0913		UNDERPASS	COLSTRIP INT-315	F		E			E					E			E	E		E		E		E	E
I	94	0716	091B	394	PRE CONC 8M	NP RY-ARMELLS CR	F		E			E		G	E	G	E			E	E		E		E		E	E
I	94	0716	0959	220	PRE CONC 8M	SMITH CR	G		E			E		G	E	G	E			E	E		E		E		E	E
I	94	0972	1079	123	ST PONY TRUSS	ROSE8UD CR	G		G	G		G		G		G		G	G	F	G		G	G	F		G	G
I	94	0972	1097	76	T T TRESTLE	8UTTE CR	F	F	F			G		G	G	G		F			F	G	G	F	F		F	F
I	94	0972	1154	114	T T TRESTLE	SWEENEY CR	F	F	F			F		G		G		F			F	E	G	G		F	F	F
I	94	0972	1182	95	T T TRESTLE	COAL CR	G	G	F			F		G	G	G		F			F	G	G	G	F		F	F
I	94	0972	1194	17	CONCRETE SLA8	JR GR SEP-STK	F		E		G	E									E		E		E		G	E
I	94	0972	1229	82	PRE CONC 8EAM	GRAVEYARD CR	G		E			E		G	G	G	E			E	E		E		E	F	G	E
I	94	0972	1305		UNDERPASS	INT-CO RD	G		E			E					E			E	E		E		E	G	G	E
I	94	0972	1330		UNDERPASS	INT-CO RD	G		E			E					E			E	E		E		E	G	G	E
I	94	0972	1381	17	CONCRETE SLAB	JR GR SEP-STK	G		E		E	E									E		E		E		G	E
I	94	0972	1391	17	CONCRETE SLA8	JR GR SEP-STK	G		E		E	E									E		E		E		G	E
I	94	0972	1398		UNDERPASS*	W INT-US 10	G		E			E					E			E	E		E		E		G	E
I	94	0972	1398A		UNDERPASS	W INT-US 10	G		E			E					E			E	E		E		E		G	E
I	94	1398	1408	17	CONCRETE SLA8	JR GR SEP-STK	G		E		E	E									E		E		E		G	E
I	94	1398	1413	290	RIV PL GIRDER	TONGUE R	G		E	E		E	E	G	G	G	E	E		E	E		E	E	E	G	G	E
I	94	1398	1422	153	PRE CONC 8EAM	SEP-CO RD	G		E			G					E			G	F		E		E	F	G	E

								F	G	H		J	K	L	M	N	O													
I	94	1398	1425	158	PRE CONC BEAM	INT-US 312	G		E			E					E			G	E		E		E	F	G	E		X
I	94	1425	1431	21	CONCRETE SLAB	JR GR SEP-CD RD	G		E		E	E									E		E		E		G	E		
I	94	1425	1443	21	CONCRETE SLAB	JR GR SEP-CD RD	G		E		E	E									E		E		E		G	E		
I	94	1425	1450	14	CONC SLAB	JR GR SEP	G		E		E	E									E		G		E		F	G		
I	94	1425	1454		UNDERPASS*	BAKER INT-US 12	G		E			E					E			E	G		E		E	G	G	E		
I	94	1454	1489	15	CONCRETE SLAB	JR GR SEP-STK	G		E		E	E									E		E		E		G	E		
I	94	1454	1505	21	CONCRETE SLAB	JR GR SEP-CD RD	G		E		E	E									E		E		E		G	E		
I	94	1531	1625	171	T T TRESTLE	COTTONWOOD CR	G	F	F			G		G	G	G		F			G	G	G	F	F		P	F		
I	94	1531	1639	57	T T TRESTLE	MILES CR	G	G	G					P		P		G			G	G	G	G	F		F	G		
I	94	1531	1659	38	T T TRESTLE	MACKS CR	G	G	G			G		G	G	G		G			G	G	G	G	G		F	G		

P	2	5383	5536	19	T T TRESTLE	DRAINAGE	F	G	G			G		G		G		G			G		G	G	G		G	G
P	2	5383	5546	19	T T TRESTLE	DRAINAGE	G	G	G			F		G	G	G		G			F		G	G	F		F	G
P	2	5383	5552	100	T T TRESTLE	RESERVATION CR	G	G	G	G		G	G	G	G	G		G			F	G	G	G	G		G	G
P	2	5383	5566	19	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			F		G	G	F		F	G
P	2	5383	5594	65	STEEL I BEAM	WYANT COV	F		G			G		G	G	G	G				F	G	G		F			G
P	2	5383	5614	129	CONC T BEAM	ARMELLS CR	G		G	G		G	G	G	G	G	G				G	G	G		G			G
P	2	5383	5630	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		G	G
P	2	5383	5643	57	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		F	G
P	2	5383	5655	89	STEEL I BEAM	SMITH CR	G		G			G		G	G	G	G				G	G	G		G		G	G
P	2	6096	6096	268	STEEL GIRDER	W INT-I 94	G		E			E					E			E	E		E		E		G	E
P	2	6096	6104	311	ST PLATE GIRDER	NP RY	G		G			G					G			G	G	F	G	G	G	G	G	G
P	2	6096	6118	300	STEEL GIRDER	TONGUE R	F		G	G		G	G	G	F	G	G	G		G	G	G	G	G	G	F	P	G
P	2	6123	6126		UNDERPASS	NPRY	F		F		F	F						G		G	F	F		G	F		F	F
P	2	6146	6161	168	PRE CONC BEAM	BAKER INT-I 94	G		E			E					E			E	G		E		E	G	G	E
P	2	6161	6169	57	T T TRESTLE	KIRCHER CR	G	G	G			F		G	F	G		G			G	G	G	G	G		G	G
P	2	6161	6186	57	T T TRESTLE	DRY WASH	F	G	G			F		G	F	G		G			G		G	G	G		G	G
P	2	6161	6194	76	T T TRESTLE	BENSLEY CR	G	G	G					G	G	G		G			G	G	G	G	F		G	G
P	2	6161	6243	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		G	G
P	2	6161	6274	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G		G	G	G		G	G

	NUMBER	CONTROL SECTION	BRIDGE MILEPOST	TOTAL LENGTH FEET	MATERIAL & TYPE	NAME OF FEATURE CROSSED	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIPRAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
		A		B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	2	6161	6291	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		F	G		
P	2	6161	6298	76	T T TRESTLE	MEADOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	2	6161	6305	76	T T TRESTLE	ASH CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		
P	2	6161	6322	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G		G	G	G		F	G		
P	2	6161	6328	38	T T TRESTLE	LI COTTONWOOD CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	2	6161	6336	7	T T TRESTLE	STOCKPASS	G	G	F		G	G						G			G		G	G	G		F	G		
P	2	6161	6340	76	T T TRESTLE	COTTONWOOD CR	G	G	G			F		G		G		G			G		G	G	G		G	G		
P	2	6161	6374	57	T T TRESTLE	S FK SMITH CR	G	G	G			G		G	F	G		G			G		G	G	G		F	G		
P	2	6161	6380	95	T T TRESTLE	SMITH CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	2	6161	6402	57	T T TRESTLE	DRY WASH	G	G	G			G		G		G		G			G		G	G	F		P	G		
P	2	6161	6417	76	T T TRESTLE	SMITH CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	2	6161	6419	554	STEEL TRUSS	POWDER R	F		F	F		G	G	G	G	G		G	F	F	G	G	G	P	G	F	P	F		
P	2	6161	6688	200	STEEL GIRDER	O FALLON CR	G		G	G		G	G	G	G	G		G		G	G	G	G	G	G	F	F	G		
P	2	6161	6716	57	T T TRESTLE	HAY CR	G	G	G			G		G	F	G		G			G	G	G	G	G		G	G		
P	14	1694	2079	38	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	F		G			G		G	G	F		G	G		
P	14	1694	2094	95	T T TRESTLE	HOME CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P	14	1694	2160	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G		G	G	G		G	G		
P	14	1694	2161	57	T T TRESTLE	HOME CR	G	G	G			G		G	G	G		G			G	G	G	G	G		G	G		

P	14	1694	2165	57	T	T	TRESTLE	HOME CR	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G
P	14	1694	2168	57	T	T	TRESTLE	HOME CR	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G
P	14	1694	2170	38	T	T	TRESTLE	HOME CR	G	G	G	G	G		G	G	G	G	G	G	G	G	G
P	14	1694	2199	57	T	T	TRESTLE	DRY WASH	G	G	G	G	G		G	F	F	G	G	G	G	G	G
P	14	1694	2237	38	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	F	G	G	F		G	G	G	G	G
P	14	1694	2246	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	F	G	F		G	G	G	F	G
P	14	1694	2273	57	T	T	TRESTLE	DRY WASH	G	G	G	G	G	G	G	F	G		G	G	G	G	G
P	14	1694	2293	25	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	F	F	G	F		G	G	G	G	G
P	14	1694	2359	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G		G	G	G		G	G	G	G	G
P	14	1694	2381	38	T	T	TRESTLE	DRAINAGE	G	G	G	G	G		G	G	G		G	G	G	G	G
P	14	1694	2389	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	F	G	G	G		G	G	G	G	G
P	14	1694	2398	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G		G	G	G		G	G	G	G	G
P	14	1694	2437	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	G	G	G		G	G	G	G	G
P	14	1694	2453	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	G	G	F		G	G	G	G	G
P	14	1694	2463	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	G	G	F		G	G	G	F	G
P	14	1694	2505	100	T	T	TRESTLE	HORSE CR	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G
P	14	1694	2521	57	T	T	TRESTLE	ANDERSON CR	G	G	G	G	G	F	G	G	G	G	G	G	G	G	G
P	14	1694	2530	38	T	T	TRESTLE	DRAINAGE	F	G	G	G	G	G	G	G	F		G	G	F	G	G
P	14	1694	2545	19	T	T	TRESTLE	DRAINAGE-STK P	F	G	G	G	G	G	G	G	G		G	G	G	G	G

CONTROL BRIDGE NUMBER A	TOTAL LENGTH FEET B	DESCRIPTIVE FEATURES MATERIAL & TYPE C	NAME OF FEATURE CROSSED D	SUBSTRUCTURE END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	SUPERSTRUCTURE GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILS W	EXPANSION X	PAINT Y	GENERAL Z	NOTES Z1	REMARKS Z2
P 14 1694 2570	19	T T TRESTLE	STOCKPASS	F	G	G			G						G			F		G	G	G		G	G		
P 14 1694 2572	122	STEEL GIRDER	PORCUPINE CR	G	G	G	G		G	G	G	G	G	G	G			F	G	G	G	G		G	G		
P 14 1694 2574	57	T T TRESTLE	DRAINAGE	G	G	F			G		G	G	G		G			F		G	G	G		G	G		
P 14 1694 2583	19	T T TRESTLE	STOCKPASS	F	G	G			G		G	G	G		G			F		G	G	G		G	G		
P 14 1694 2585	11	T T TRESTLE	STOCKPASS	F	G	G		G	G		G		G		G			G		G	G	G		G	G		
P 14 1694 2598	38	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			F		G	G	F		G	G		
P 14 1694 2603	11	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G		G	G	G		G	G		
P 14 1694 2615	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 14 1694 2620	19	T T TRESTLE	DRAINAGE	G	G	F			F		G	G	G		G			F		G	G	F		F	G		
P 14 1694 2625	95	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			G		G	G	F		F	G		
P 14 1694 2626	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			F		G	G	F		G	G		
P 14 1694 2628	19	T T TRESTLE	GREASEWOOD CR	F	G	G			G		G	G	G		G			F	G	G	G	F		F	G		
P 14 1694 2648	38	T T TRESTLE	MCGRAWS COULEE	G	G	G			G		G	G	G		G			F	F	G	G	F		F	G		
P 14 1694 2703	825	STEEL GIRDER	YELLOWSTONE R-RR	G		E	E		E	G	G	G	G	E	E		E	G	G	E	E	G	G	F	E		
P 18 0000 0010	971	STEEL GIRDER	YELLOWSTONE R	F		G	G	G	G	G	F	G	G	G	G		G	G	P	G		G	F	F	G		
P 18 0000 0039	164	CONCRETE BEAM	S FK SUNDAY CR	G		G	G		G	G	G	G	G	G			G	G	E	G		G		G	G		
P 18 0000 0110	122	PRE CONC BEAM	N FK SUNDAY CR	F		G			G		G	G	G	G			G	G	E	G	G	G		G	G		
P 18 0000 0178	102	PRE CONC BEAM	GRIMES CR	G		G			G		G	G	G	G			G	G	E	G	G	G	G	G	G		

P	18	0000	0251	95	T T TRESTLE	DRY HOUSE CR	G	P	P			F	G	G	G	G		F			F	E	F	F	G		G	F
P	18	0000	0351	38	T T TRESTLE	ROCK SPRINGS CR	F	F	F			F		G	G	G		F			F		F	F	G		G	G
P	23	0000	0021		UNDERPASS*	INT-I 94	G		E			E					E			G	E		E		E	F	G	E
P	23	0021	0027	50	T T TRESTLE	IRRIGATION CANAL	G	G	G	F		G		F	P	G		G			G		G	G	G		F	G
P	23	0021	0033	19	UNT T TRESTLE	STOCKPASS	G	G	G			G		G	G	G		G			G		G	G	G		F	G
P	23	0021	0067	57	T T TRESTLE	COWLES CR	G	G	G			G		G	G	G		G			G		G	G	G		F	G
P	23	0021	0073	38	T T TRESTLE	IRRIGATION CANAL	G	G	G	F		G		F	G	G		G			G		G	G	G		F	G
P	23	0021	0082	50	T T TRESTLE	IRRIGATION CANAL	G	G	G	F		G		G	F	F		G			G		G	G	G		P	G
P	23	0021	0087	95	T T TRESTLE	LOG CR	G	G	G			G		F	F	G		G			G		G	G	G		F	G
P	23	0021	0095	76	T T TRESTLE	MILLS CR	G	G	G			G	G	G		F		G			G		G	G	G		F	G
P	23	0021	0103	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		F	G
P	23	0021	0108	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		F	G
P	23	0021	0112	76	T T TRESTLE	SQUAW CR	G	G	G			G		G	G	G		G			G		G	G	G		F	G
P	23	0021	0159	138	PRE CONC BEAM	PUMPKIN CR	E		E			E		G	G	G	E			E	E	E	E		E		G	E
P	23	0021	0282	38	T T TRESTLE	DRAINAGE	G	G	G			G		F	P	G		G			G		G	G	F		F	G
P	23	0021	0293	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		F	G
P	23	0021	0300	57	T T TRESTLE	FIRE CR	G	G	G			G		G	G	G		G			G		F	G	G		F	G
P	23	0021	0313	38	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
	DESCRIPTIVE FEATURES			CONDITION RATING																							
				SUBSTRUCTURE											SUPERSTRUCTURE												
BRIDGE NUMBER	TOTAL LENGTH FEET	MATERIAL AND TYPE MAXIMUM SPAN	NAME OF FEATURE CROSSED (River, Creek, Canal, Irrigation Ditch, Railroad, Highway, Separation)	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK		RAILING			GENERAL CONDITION		REMARKS
P 23 0021 0328	38	T T TRESTLE	DRAINAGE	G	G	G			G		F		F		F			G		F	G	G		G	G		
P 23 0021 0338	57	T T TRESTLE	MAGGIE CR	G	F	G			F		G	P	G		G			G	G	G	G	G		F	G		
P 23 0021 0343	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		G	G	G		F	G		
P 23 0021 0352	57	T T TRESTLE	DRAINAGE	F	G	G			F		G	F	G		G			G		G	G	G		F	G		
P 23 0021 0358	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G		F	G	G		F	G		
P 23 0021 0367	38	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		G	G		
P 23 0021 0383	19	T T TRESTLE	DRAINAGE	F	G	G			G		G		F		G			G		G		G		F	G		
P 23 0021 0389	38	T T TRESTLE	DRAINAGE	F	F	F			F		G	G	G		G			G		F	G	G		E	F		
P 23 0021 0400	57	T T TRESTLE	969 CR	G	G	G			G		G		G		G			G		F		G		F	G		
P 23 0021 0404	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						F			G		G	G	G		G	G		
P 23 0021 0412	57	T T TRESTLE	BETZ CR	F	G	G			G		G	G	G		G			G		G	G	G		F	G		
P 23 0021 0421	38	T T TRESTLE	COTTONWOOD CR	G	G	G			G		G	G	G		G			G		G	G	G		F	G		
P 23 0021 0431	57	T T TRESTLE	BASIN CR	F	G	G			F		G		G		G			G		F	G	G		G	G		
P 23 0021 0434	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G		F	G	G		G	G		
P 23 0021 0445	95	T T TRESTLE	PUMPKIN CR	G	G	G	G		G	G	F	G	F		G			G	G	F	G	G		F	G		
P 23 0021 0451	57	T T TRESTLE	DRAINAGE	F	G	G			G		G	G	G		G			G		F	G	G		F	G		
P 23 0021 0475	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G		G	G	G		E	G		
P 23 0021 0582	76	T T TRESTLE	DRAINAGE	F	G	G			G		G		G		G			G		G	G	G		G	G		
P 23 0021 0601	38	T T TRESTLE	LOST SOLDIER CR	G	G	G			G		G		G		G			G		G	G	G		G	G		

P 23 0021 0614	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G
P 23 0021 0643	19	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		G	G
P 23 0021 0668	57	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G			G	G
P 23 0021 0698	114	T T TRESTLE	MIZPAH CR	G	G	G	G		G	G	G	G	G		G			G	G	F	G	G		F	G
P 23 0021 0706	57	T T TRESTLE	DRAINAGE	G	G	G			G		G		G		G			G		G	G	G		F	G
P 23 0021 0728	38	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G
P 23 0762 0791	19	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			F		P	G	P		P	F
P 23 0762 0795	57	T T TRESTLE	DRAINAGE	G	G	G					G	G	G		G			G		F	G	G		F	G
P 23 0762 0805	592	CONT ST TRUSS	POWDER R	F		G	G		G	G	F	G	G		G	G	G	F	G	G	G	G	G	P	G
P 23 0831 0844	19	T T TRESTLE	DRAINAGE	G	G	G		F	F		G		G		G			G		G	G	G		F	G
P 23 0831 0868	297	STEEL TRUSS	LITTLE POWDER R	G	G	G	G		G	G	G	G	G		F	F	G	F	F	G	F	F	G	F	G
P 23 0831 0872	114	T T TRESTLE	E FORK CR	G	G	G	F		F	G	G	G	G		G			F		G	F	F		F	F
P 23 0831 1264	92	CONCRETE GIRDER	WILLOW CR	G	G	G			G		G		G	G			G	G	F	G		G		F	G
P 23 0831 1344	102	PRE CONC BEAM	THOMPSON CR	F		E	E	E	E	E	G	G	G	E			E	E	E	E		E		E	E
P 23 0831 1361	142	PRE CONC BEAM	LIT MISSOUR R	F		E	E	E	E	E	G	G	G	E			E	E	G	G		E		G	E
P 37 0000 0420	75	T T TRESTLE	LAME DEER CR	F	G	G			G		G	G	G		G			F		F	G	G		F	G
P 37 0000 0614	200	CONT ST GIRDER	TONGUE R	F		G	G		G	G	G	G	G	G			G	G	G	G		G	G	G	G
P 37 0000 0631	112	T T TRESTLE	OTTER CR	G	G	G			F		G		G		G			G	G	G	G			F	G

CONTROL NUMBER A	TOTAL LENGTH FEET B	MATERIAL & TYPE MAXIMUM SPAN C	NAME OF FEATURE CROSSED D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALL J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILINGS W	EXPANSION X	PAINT Y	GENERAL CONDITION Z	NOT INSPECTED Z1	REMARKS Z2
P 37 0000 0635	7	T T TRESTLE	STOCKPASS	G		G		G	G						G					G		G		G	G		
P 37 0000 0639	7	T T TRESTLE	STOCKPASS	G		G		G	G						G					G		P		F	G		
P 37 0000 0661	10	T T TRESTLE	STOCK PASS	G		F		G	F						G					G					G		
P 37 0000 0670	6	T T TRESTLE	STOCKPASS	G		G		G	G						G					G					G		
P 37 0000 0674	81	T T TRESTLE	E FK OTTER CR	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 37 0000 0724	38	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		
P 37 0000 0732	7	T T TRESTLE	STOCKPASS	G		G		G	G						G					G					G		
P 37 0000 0735	38	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G		G	G		

S315 0000 0136	113	T T TRESTLE	ROSEBUD CR	G	G	G	G		G	G	G		G		G			G	G	G	G	G	P	G	
S315 0000 0154	100	T T TRESTLE	MILLER COULEE	G	G	G			G		G	G	G		G			G	P	G	G	G	P	G	
S315 0000 0263	57	T T TRESTLE	STOCKER CR	G	G	G		G	G		F		G		G			G	P	G	G	G	G	G	
S315 0000 0292	38	T T TRESTLE	CORRAL CR	G	G	G			G		G	G	G		G			G	F	G	G	G	G	G	
S315 0000 0306	38	T T TRESTLE	MCGILVREY CR	G	G	G		G	G		G	G	G		G			G	F	G	G	G	G	G	
S315 0000 0339	57	T T TRESTLE	SEVEN MILE CR	G	G	G			G		G	P	G		G			G	F	G	G	G	G	G	
S315 0000 0364	76	T T TRESTLE	DRAINAGE	G	G	G			G		G	G	G		G			G		G	G	G	G	G	
S315 0000 0383	125	T T TRESTLE	E FK ARMELLS CR	G	G	G			G		F	G	G		F			G	G	G	G	G	G	G	X
S315 0000 0386	57	T T TRESTLE	SHEEP CR	G	G	G			G		G		G		G			G		G	G	G	G	G	
S315 0000 0438	92	PRE CONC BEAM	ARMELLS CR	P		E	E		E	E	G	G	G	E			E	E		E		E	E	E	
S315 0000 0512	143	PRE CONC BEAM	COLSTRIP INT 194	F		E			E					E			E	E		E		E	E	E	
S320 0000 0022	95	T T TRESTLE	COTTONWOOD CR	C	G	G			G		G	F	G		C			F			G	F	P	F	X
S320 0000 0051	36	STEEL I BEAM	STATION CR	G		F		F	F		G		G		F			F		F		P	P	F	
S320 0000 0053	202	ST PONY TRUSS	OFALLON CR	F		F	F	P	F	G	G		G		G	F	F	G		G	G	P	P	F	
S332 0000 0009	138	PRE CONC BEAMS	PUMPKIN CR	F		E			E		G	G	F	E			E	E	G	G		E	G	E	
S332 0000 0105	38	T T TRESTLE	ASH CR	G	G	G			G		F		G		G			G	G	G	G	G	G	G	X
S332 0000 0106	38	T T TRESTLE	ASH CR OVERFLOW	G	G	G		G	G		G		G		G			G	G	G	G	G	G	G	X

CONTROL NUMBER A	TOTAL LENGTH FEET B	MATERIAL & TYPE C	NAME OF FEATURE CROSSED D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILING W	EXPANSION X	PAINT Y	GENERAL Z	NOT INSPECTED Z1	REMARKS Z2
S332 0000 0109	38	T T TRESTLE	ASH CR OVERFLOW	G	G	G		G	G		F		G		G			G	G	G	G	G		G	G		
S332 0000 0138	25	T T TRESTLE	JACK CR	G	G	G		G	G		G		G		F			G	G	G	G	G		G	G		X
S332 0000 0157	25	T T TRESTLE	BROWN CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S332 0000 0173	38	T T TRESTLE	HADDOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S332 0000 0198	38	T T TRESTLE	FOSTER CR	G	G	G		G	G		P		F		G			F	G	G	G	G		G	G		
S332 0000 0396	214	PRE CONC BEAMS	TONGUE R	G		E	E		E		F	G	G	E		E	E	E	E	E		G		G	E		
S333 0000 0081	23	STEEL I BEAM	DRAINAGE	G	F	F			P		G		G		G					P		P		P	P		
S333 0000 0142	39	STEEL I BEAM	STREVELL CR	G	G	G		G	G		G		G		G			F		F		F		F	F		
S333 0000 0160	138	ST THRU TRUSS	MIZPAH CR			F										G								P			
S391 0000 0037	45	T T TRESTLE	SAND CR	F	G	G			G		G	E	G		G			G		G	G	G		P	G		
S391 0000 0078	60	ST PONY TRUSS	ROUGH CR	F	G	F			F		G		G		C	G	G	P		F	F	F		P	F		
S391 0000 0359		FORD	POWDER R																							N	
S391 0000 0393	31	STEEL I BEAM	HORSE CR																							X	X
S402 0000 0045	251	STEEL TRUSS	LITTLE POWDER R	G	G	G	G		G	G	F	G	F		G	G	G	G	P	G	G	G	F	P	G		
S446 0000 0004	867	STEEL TRUSS	YELLOWSTONE R	F	P	P	F	P	P	F	G		G		P	F	F	P		P	F	P		P	P		

PLANNING SURVEY BRIDGE CONDITION REPORT

RATINGS

Columns E thru Z

E = Excellent
G = Good
F = Fair
P = Poor
C = Critical

Column Z

N = New
R = To be Removed
U = Unable to Inspect

Column Z2

X = Written Explanation

CONTROL BRIDGE NUMBER A	TOTAL LENGTH FEET B	DESCRIPTIVE FEATURES MATERIAL & TYPE MAXIMUM SPAN C	NAME OF FEATURE D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W			Z	Z	Z
S446 0000 0061	38	T T TRESTLE	SAND CR	G	E	E		E	E		G		F		E			G		G	E	G		F	G		
S447 0000 0051	75	ST PRATT TRUSS	ROSEBUD CR	G		G		G	G		G		G		G	G				F	F	P		P	G		
S447 0000 0094	58	UNT T TRESTLE	DRAINAGE	F	P	P		P	F		G		G		P			P		P		P		P	P		
S447 0000 0172	96	STEEL I BEAM	DRAINAGE	G		F	F	F	F		F		G		G			P		F		P		P	F		
S447 0000 0224	31	STEEL I BEAM	DRAINAGE	G		F		F	F		G		G		G			P		F		P		P	F		
S447 0000 0427	31	STEEL I BEAM	LAY CR	F		F		F	F		G		G		G			P		F		F		P	F		
S484 0000 0034	102	PRE CONC BEAM	OTTER CR	G		E			E		G	G	G	E			E	E	G	E		E		G	E		
S484 0000 0236	90	STEEL TRUSS	OTTER CR	F	G	P			F		G		G		F	G	G		G	P	F	P		P	P		
S484 0000 0254	45	ST PONY TRUSS	OTTER CR	F	F	F					G		G		F	G	G	P		F	F	F		P	F		
S484 0000 0258	35	STEEL TRUSS	BEAR CR	F	G	F			F		G		G		G	G		F		P	F	F		P	F		
S489 0000 0037	198	PRE CONC BEAM	SUNDAY CR	F		G	G		G	G	F	G	G	G			G	G	X	G	G	G	G	G	G		
S544 0000 0003	107	ST HOWE TRUSS	POWDER R	P		F		F	F		G		G		P	G	G	P		F		P		P	P		X
S544 0000 0342	34	STEEL I BEAM	E FK SCOTT CR	F	F	C		P	P		G		G		G			P		P		P		P	C		X

MILES CITY DIVISION

I-94-1398-1425 158' Pre. Conc. Beam Int. US 312
Exposed joint bent 3 is not solid. Cover plate has been rebolted and is in fair condition. Rubber joint over bent 2 has failed on the slab and curbs.

S-315-0000-0383 125' Treated Timber Trestle East Fork Armells Creek
Sixth stringer from the left on span 3 is broken and needs replacing. See photo.

S-320-0000-0022 95' Treated Timber Trestle Cottonwood Creek
There is a broken water line at bent 10 washing out the end fill. Broken stringer in span 4, 7th from left.

S-332-0000-0105 38' Treated Timber Trestle Ash Creek
Nuts should be tightened on all bents.

S-332-0006-0106 38' Treated Timber Trestle Ash Creek Overflow
Nuts should be replaced and tightened on bents 1 and 2.

S-332-0000-0138 25' Treated Timber Trestle Jack Creek
Two cracked stringers.

S-391-0000-0393 31' Steel I Beam Horse Creek
Unable to reach this bridge to make inspection due to high water.

S-544-0000-0003 107' Steel Truss Little Powder River
Bridge is in poor condition. One stringer is broken and four stringers show signs of rotting. Twenty lineal feet of railing is missing and the remaining portion is in poor condition. Paint is in poor condition. An 8 ton load limit is posted, although much heavier oil drilling equipment has been using this bridge making it unsafe. See photos.

S-544-0000-0342 34' Steel I. Beam East Fork Scott Creek
Bridge is in unsafe condition. On bent 1 (west end) the pile cap is overturning on the piling. Two deck plans are missing and the remaining planks are in poor condition. The Left railing has been damaged and leaning over. See photo.

S-315-0000-0383

S-544-0000-0003

S-544-0000-0003

S-544-0000-0342

LEWISTOWN CONSTRUCTION DIVISION

P 11 0605 1024	7	T T TRESTLE	STOCKPASS	G	G	G	G	G						G		G	G	G	G			G	G	
P 11 0605 1037	38	T T TRESTLE	LOST CR	F	G	G	P	P		G		G		G		G	G	G	G	G		G	G	
P 11 0605 1044	38	T T TRESTLE	S FK 16 MILE CR	G	G	G	G	G		G	F	G		G		G	G	G	G	G		G	G	
P 11 0605 1050	245	CONT ST GIRDER	CMSTP&P RR-CR	F		G	G	G		G	G	G	G		G	F	G	F	G	G	G	F	F	
P 11 0605 1122	57	T T TRESTLE	S FK SMITH R	G	G	G	G	G		G		G		G		G	G	G	G	G		G	G	
P 11 0605 1124	19	T T TRESTLE	STOCKPASS	G	G	G	G	F		G		G		G		G	G	G	G	G		G	G	
P 11 0605 1131	57	T T TRESTLE	S FK SMITH R	G	G	G	G	G	G	G		G		G		G	G	G	G	G		G	G	
P 11 0605 1142	7	T T TRESTLE	STOCKPASS	G	G	G	G	G		G		G		G			G	G	G				G	
P 11 1175 1176	76	T T TRESTLE	S FK SMITH R	P	G	G	G	G		G		G		G		G	G	G	G	G		G	G	
P 11 1175 1185	19	T T TRESTLE	STOCKPASS-DR	G	G	G	G	G		G		G		G		G	G	G	G	G		G	G	
P 11 1175 1204	19	T T TRESTLE	DRAINAGE	G	G	G	G	G		G		G		G		G	G	G	G	G		G	G	
P 11 1291 1295	38	T T TRESTLE	N FK SMITH R	G	G	G	G	G		G		G		G		G	G	G	G	G		G	G	
P 11 1291 1471	69	T T TRESTLE	SHEEP CR	G	G	G	G	G		G	G	G		G		G	G	G	G	G		G	G	
P 14 0000 0117	19	UNT T TRESTLE	DRAINAGE	G	G	P	P	P		G		G		F		F	G	G	P	F		F	P	X
P 14 0000 0119	38	T T TRESTLE	DEEP CR	G	F	G	G	G	G	F		G		G		F	G	G	G	P		F	F	X
P 14 0000 0148	19	T T TRESTLE	DEEP CR	G	G	G	F	G		G		G		G		F	G	G	G	F		F	G	X
P 14 0000 0151	39	T T TRESTLE	DEEP CR	G	F	G	F	G		G		G		F		F	G	G	F	F		F	F	X
P 14 0000 0173	39	T T TRESTLE	DEEP CR	G	G	G	F	G		F	G	G		G		F	G	G	F	F		F	F	X

A	B FEET	C	D	E END FILLS	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TRUSS	R SHOES	S CURBS	T	U DECK	V	W	X	Y	Z	Z1	Z2 REMARKS
P 14 0000 0196	19	T T TRESTLE	DEEP CR	F		G		F	F		G		G		G			F	G	G	G	F		F	F		X
P 14 0000 0198	19	T T TRESTLE	DEEP CR	G		G		G	G		G		G		G			F	G	G	G	F		F	G		X
P 14 0000 0240	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0000 0246	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						F			G	G	G	G	G		G	G		X
P 14 0000 0295	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0000 0304	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0489	25	T T TRESTLE	FOUR MILE CR	G	G	G		G	G		G	G	G		G			G	F	G	G	G		G	G		
P 14 0449 0530	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0661	76	T T TRESTLE	FLAGSTAFF CR	G	G	F		G	G		G		G		G			G	G	G	G	G		G	G		X
P 14 0449 0667	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		G	G		
P 14 0449 0682	76	T T TRESTLE	COOPER CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 14 0449 0695	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 14 0449 0707	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		G	G		
P 14 0449 0730	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		G	G		
P 14 0449 0763	95	T T TRESTLE	N FK MUSSELSHELL	G	G	G		G	G	G	F		G		G			G	G	G	G	G		G	G		
P 14 0449 0764	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		X
P 14 0449 0773	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0778	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 14 0449 0784	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		

P 14 0449 0789	19	T T TRESTLE	STOCKPASS	G	G	G	G	G						G		G	G	G	G	G		G	G	
P 14 0449 0794	19	T T TRESTLE	STOCKPASS	G	G	G	G	G						G		G	G	G	G	G		G	G	
P 14 0449 0802	7	T T TRESTLE	STOCKPASS	G	G	G	G	G						G		G	G	G	G	G		G	G	
P 14 0449 0808	7	T T TRESTLE	STOCKPASS	G	G	G	G	G						G		G	G	G	G	G		G	G	
P 14 0449 0812	7	T T TRESTLE	STOCKPASS	G	G	G	G	G						G		G	G	G	G	G		G	G	
P 14 0449 0822	57	T T TRESTLE	DAISY DEAN CR	G	G	G	G	G		G		G		G		G	G	G	G	G		G	G	
P 14 0449 0848	57	T T TRESTLE	WILLIS COU	F	G	G	G	G		G	F	G		G		G	G	G	G	G		G	G	
P 14 0449 0881	65	CONT CONC SLAB	HAYMAKER CR	G		G	G	G		G	G	G				G	G	G		G		G	G	
P 14 0995 1005	204	CONT STEEL BEAM	CMSTP&P RR	P		G	G	G			G		G		G	G	G	G	G	G	G	G	G	
P 14 1008 1092	19	T T TRESTLE	STOCKPASS	G	G	G	G	G						G		G	G	G	P	G		G	G	
P 14 1008 1106	19	T T TRESTLE	DRAINAGE	G	G	G	G	G		G		G		G		G	G	G	P	G		G	G	
P 14 1008 1322	38	T T TRESTLE	DRAINAGE	P	G	G	G	G		G		G		G		G	G	G	F	F		G	G	
P 14 1008 1336	114	T T TRESTLE	CARELESS CR	P	G	G	G	G	G	P		P		G		G	G	G	G	G		G	G	X
P 14 1008 1337	7	T T TRESTLE	STOCKPASS	P	G	G	G	G						G		G	G	G	G	G		G	G	
P 14 1008 1344	7	T T TRESTLE	STOCKPASS	F	G	G	G	G						G		G	G	G	G	G		G	G	
P 14 1008 1352	7	T T TRESTLE	STOCKPASS	F	G	G	G	G						G		G	G	G	G	G		G	G	
P 14 1008 1358	57	T T TRESTLE	DRAINAGE	P	G	G	G	G		G	F	G		G		G	G	G	G	G		G	G	
P 14 1008 1393	7	T T TRESTLE	STOCKPASS	G	G	G	G	G						G		G	G	G	G	G		G	G	
P 14 1008 1397	57	T T TRESTLE	NINE MILE CR	G	G	G	G	G		G	P	G		G		G	G	G	G	G		G	G	

					DE CRI[illegible] E [illegible] R		C[illegible]ND TI[illegible] R[illegible]																							
					MAX MUM [illegible]AN Also [illegible] structure [illegible] [illegible] by typ[illegible] underpass [illegible]	R[illegible]er Creek, [illegible] [illegible] Drainage, Railro[illegible] [illegible]tways, interchange [illegible] Repor[illegible]	SUBST[illegible]UCTURE																							
A[illegible] NUMBER	CONTROL JUNCTION	M[illegible]	BR[illegible] DESCRIP[illegible]	TOTAL LENGTH FEET			END F[illegible]LS	PILES	BENTS	PIERS	WINGW[illegible]LLS	BA[illegible]KWA[illegible]	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDER[illegible]	STR[illegible]NGE[illegible]	TR[illegible]	SHOES	CURBS	MAR[illegible]	D[illegible]	BRA[illegible]	HA[illegible]NG	EXP		GENERAL COND	NOT INSPECTED	REM[illegible]KS
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	14	1008	1398		UNDERPASS	GN RY	G		G		G	G					G			G		G	G	G			G	G		
P	14	1008	1403	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	14	1008	1431	76	T T TRESTLE	FIVE MILE CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	14	1008	1444	95	T T TRESTLE	DRAINAGE	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	14	1460	1462	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1460	1474	57	T T TRESTLE	TWIN COULEE	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P	14	1460	1476	57	T T TRESTLE	TWIN COULEE	P	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1486	76	T T TRESTLE	DRAINAGE	P	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1523	76	T T TRESTLE	DEAN CREEK	P	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1531	7	T T TRESTLE	STOCKPASS	P	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1460	1547	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1613	95	T T TRESTLE	CURRANT CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1460	1641	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	14	1460	1658	75	T T TRESTLE	POLE CR	G		P		G	G		G	G	G	G				G	G	G	G	G		G	P		X
P	14	1694	1746	76	T T TRESTLE	WILLOW CR	P	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1755	76	T T TRESTLE	MUSSELSHELL R	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1763	76	T T TRESTLE	MUSSELSHELL R	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	14	1694	1771	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	14	1694	1774	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		

P	14	1694	1790	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	
P	14	1694	1806	38	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	
P	14	1694	1820	11	T	T	TRESTLE	STOCKPASS	F	G	G	G	G				G	G	G	G	G	G	G	G	
P	14	1694	1824	19	T	T	TRESTLE	STOCKPASS	F	G	G	G	G				G	G	G	G	G	G	G	G	
P	14	1694	1828	76	T	T	TRESTLE	DRAINAGE	F	G	G	G	G	G	G	G	G	G	G	G	G	G	G	G	
P	14	1694	1840	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G	F	G	G	G	G	G	P	F	G	G	
P	14	1694	1854	11	T	T	TRESTLE	STOCKPASS	G	G	G	G	G	G		G	G	G	G	G	G	G	G	G	
P	14	1694	1860	57	T	T	TRESTLE	DRAINAGE	P	G	G	G	G	G		G	G	G	G	G	G	G	G	G	
P	14	1694	1871	11	T	T	TRESTLE	STOCKPASS	P	G	G	G	G		F		G	G	G	G	G	G	G	G	
P	14	1694	1888	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G		G	G		G	G	G	G	G	G	
P	14	1694	1896	11	T	T	TRESTLE	STOCKPASS	G	G	G	G	G				G		G	G	G	G	G	G	
P	14	1694	1903	25	T	T	TRESTLE	IRRIGATION CANAL	G	G	G	G	G	G		G	G		G	G	G	G	G	G	
P	14	1694	1913	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G		G	G		G	G	G	G	G	G	
P	14	1694	1919	76	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G		G	G		G	G	G	G	G	G	
P	14	1694	1930	57	T	T	TRESTLE	DRAINAGE	G	G	G	G	G	G		G	G		G	G	G	G	G	G	
P	14	1694	1945	95	T	T	TRESTLE	DRAINAGE	P	G	G	G	G	G		G	G		G	G	G	G	G	G	X
P	14	1694	1954	19	T	T	TRESTLE	STOCKPASS	G	G	G	G	G		G		G		G	G	G	G	G	G	
P	14	1694	1956	19	T	T	TRESTLE	DRAINAGE & STK P	F	G	G	G	G	G	G	G	G		G	G	G	G	G	G	
P	14	1694	1964	57	T	T	TRESTLE	DRAINAGE	P	G	G	G	G	G	G	G	G		G	G	G	G	G	G	X

A	B TOTAL LENGTH FEET	C MAIN STRUCTURE TYPE MAXIMUM SPAN	D NATURE OF FEATURE CROSSED	E FND FILLS	F PILES	G BENTS	H PIERS	I WINGWALLS	J BACKWALLS	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TRUSS	R SHOES	S CURBS	T MARKERS	U DECK	V BRACING	W RAILING	X	Y PAINT	Z GENERAL CONDITION	Z1 NOT INSPECTED	Z2 REMARK
P 14 1694 1966	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G				G	G	G	G		G	G		X
P 14 1694 1993	11	T T TRESTLE	STOCKPASS & DR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 14 1694 2000	38	T T TRESTLE	DRAINAGE	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 14 1694 2015	57	T T TRESTLE	OLD RIVER CH	G	G	G		G	G		G	P	G		G			G	G	G	G	G		G	G		
P 14 1694 2030	19	T T TRESTLE	STOCKPASS	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 14 1694 2039	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		X
P 14 1694 2052	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 14 1694 2071	224	CONT ST GIRDER	MUSSELSHELL R	G		G	G	G	G	G	G	F	G	G			G	G	G	G	G	G	G	G	G		
P 15 0000 0085	82	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	G	G		G	G	G	G		
P 15 0000 0093	82	PRE CONC BEAM	OTTER CR	G		G		G	G		F	G	G	G			G	G	G	G		G	F	G	G		
P 15 0000 0103	82	PRE CONC BEAM	OTTER CR	G		G		G	G		G	G	G	G			G	G	G	G		G	F	G	G		
P 15 0000 0108	82	PRE CONC BEAM	OTTER CR	G	G	G		G	G		G	G	G	G			G	G	G	G		G		G	G		
P 15 0000 0219	57	T T TRESTLE	MCCARTHY CR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 15 0000 0241	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 0000 0262	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		G	G		
P 15 0000 0267	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 0000 0291	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 0000 0292	57	T T TRESTLE	FOX COU	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		

A	FEET B		D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Zc
P 15 0000 0303	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 15 0000 0308	57	T T TRESTLE	SURPRISE CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0000 0317	57	T T TRESTLE	SUN CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0000 0336	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P 15 0000 0349	57	T T TRESTLE	WOLF CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0363	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P 15 0000 0372	38	T T TRESTLE	N FK SKULL CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0374	38	T T TRESTLE	S FK SKULL CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0389	57	T T TRESTLE	COYOTE CR	G	G	G		G	G		G		G		G			F	G	G	G	G		G	G		
P 15 0000 0394	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P 15 0000 0400	57	T T TRESTLE	WILLOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0422	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0000 0431	38	T T TRESTLE	SAGE CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 15 0000 0442	38	T T TRESTLE	DRAINAGE	C	G	G		G	G		G	F	G		G			G	G	G	G	F		G	G		X
P 15 0000 0457	38	T T TRESTLE	DRY CR	P	G	G		G	G		G	P	G		G			G	G	G	G	G		G	G		
P 15 0000 0460	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 0000 0488	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 0000 0569	123	CONCRETE T BEAM	GN RY	G		G		G	G					G			G	G	G	G		G		G	G		
P 15 0000 0582	159	CONCRETE T BEAM	JUDITH R	F		G	P	G	G	G	P	F	G	G			G	G	G	G		G			F		X

F A SYSTEM	F A ROUTE NUMBER	CONTROL JUNCTION MILE	BRIDGE MILEPOST TO TENTHS	TOTAL LENGTH FEET	MATERIAL & TYPE MAXIMUM SPAN	NAME OF FEATURE PASSED	END FILLS	PILES	BENTS	PIERS	WINGWALLS	BACKWALLS	ICE BREAKERS	DRIFT	RIP RAP	SCOUR	GIRDERS	STRINGERS	TRUSS	SHOES	CURBS	MARKERS	DECK	BRACING	RAILING	EXPANSION	PAINT	GENERAL CONDITION	NOT INSPECTED	REMARKS
A				B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z1	Z2
P	15	0000	0625	120	CONCRETE T BEAM	ROSS FORK CR	P		G	G	G	G	G	G	F	G	G			G	G	G	G		G			G		X
P	15	0000	0631	38	T T TRESTLE	OLSON CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	15	0000	0638	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P	15	0649	0694	38	T T TRESTLE	DRY COU	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	15	0649	0696	38	T T TRESTLE	ROCK CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	15	0649	0719	38	T T TRESTLE	LITTLE ROCK CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	15	0649	0726	57	T T TRESTLE	KING COU	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	15	0649	0739	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G		G		G	G		
P	15	0649	0741	57	T T TRESTLE	BEAVER CR	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	15	0649	0751	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G			G		G	G		
P	15	0649	0755	75	T T TRESTLE	COTTONWOOD CR	F	G	G		G	G		F	G	G		G			G	G	G	G	G		G	G		
P	15	0793	0796	165	CONCRETE T BEAM	CMSTP&P RR	F		F		G	G					F			F	F	G	F		G			F		X
P	15	0793	0822	30	STEEL & CONC	BIG SPRING CR	G		N		N	N						N			G		G					G		X
P	15	0823	0824	25	CONCRETE T BEAM	MILL DITCH	G		F		F	F		G		G	G				P		F		G			G		X
P	15	0823	0842	57	T T TRESTLE	BOYD CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	15	0823	0862	57	T T TRESTLE	BOYD CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	15	0823	0872	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	15	0823	0909	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			P	G	G	G			G	G		
P	15	0823	0955	38	T T TRESTLE	DRAINAGE	G	G	G		F	G	G			G		G			F	G	G	G			G	G		

A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Z
P 15 0823 0996	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G				G	G	G			G	G		
P 15 0823 1008	57	T T TRESTLE	DRAINAGE	G	G	G		F	G				G		G			G	G	G	G			G	G		
P 15 0823 1038	25	T T TRESTLE	DRAINAGE	G	G	G		G	G			G	G		G			G	G	G	G			G	G		
P 15 0823 1053	57	T T TRESTLE	N FK MCDONALD CR	G	G	G		G	G			G	G		G			G	G	G	G			G	G		
P 15 0823 1067	38	T T TRESTLE	DRAINAGE	G	G	G		G	G			G	G		G			G	G	G	G			G	G		
P 15 0823 1074	57	T T TRESTLE	DRAINAGE	G	G	G		G	G			G	G		G			G	G	G	G			G	G		
P 15 0823 1078	100	T T TRESTLE	IRRIGATION RES	G	G	G		G	G			G			G			G	G	G	G	G		G	G		
P 15 0823 1094	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0823 1105	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0823 1107	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0823 1110	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0823 1118	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 0823 1125	100	T T TRESTLE	S FK MCDONALD CR	G	G	G		G	G		F	G	G		G			G	G	G	G	G		G	G		
P 15 1129 1172	92	PRE CONC BEAM	MCDONALD CR	G		G	G	G	G	G	F	G	G	G			G	G	G	G	G	G	G	G	G		
P 15 1129 1200	76	T T TRESTLE	BRIGGS COU	G	G	G		G	G		G		G		G				G	G	G	G	G	G	G		
P 15 1129 1453	184	CONCRETE T BEAM	BOX ELDER CR	P		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G		
P 15 1129 1579	38	T T TRESTLE	DRAINAGE	F	G	G		G	G			G	G		G			G	G	G	G	G		G	G		
P 15 1129 1584	436	STEEL TRUSS	MUSSELSHELL R	F		G	F	G	G	G	G	G	G			G	F	F	G	F	G	G	G	G	G		X
P 15 1129 1613	114	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		

NG S[illegible] B [illegible] CONT

P - Poor
C - Critical
[illegible] - Unable to Inspect

CONTROL NUMBER (F. A. SYSTEM, F. A. ROUTE, NUMBER, CONTROL, BRIDGE LOCATION) A	TOTAL LENGTH FEET B	MATERIAL & TYPE MAXIMUM SPAN C	NAME OF FEATURE CROSSED D	END FILLS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRA[illegible] V	RAILINGS W	EXPAN[illegible] X	PAINT Y	GENERAL CONDITION Z	NOT INSPECTED 21	REMARKS 22
P 15 1129 1698	132	PRE CONC BEAM	CALF CR	E		E	E	E	E	E	E	E	E	E			E	E	E	E		E		E	E		
P 15 1129 1735	57	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	F	G	G	G		G	G		
P 15 1129 1750	57	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 1129 1772	38	T T TRESTLE	DRAINAGE	P	G	G		G	G		G	P	G		G			G	G	G	G	G		G	G		
P 15 1129 1792	19	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 1129 1800	19	T T TRESTLE	STOCKPASS	F	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 15 1129 1816	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 1129 1832	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 15 1129 1842	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 15 1129 1846	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		F	G		
P 15 1129 1849	7	T T TRESTLE	STOCKPASS	P	G	G		G	G						G			G	G	G	G	G		G	G		
P 15 1129 1878	95	T T TRESTLE	DUGOUT COU	G	G	G		G	G			G			G			G	G	G	G	G		P	G		
P 15 1129 1891	19	T T TRESTLE	STOCKPASS	G	G	G		G	G			G			G			G	G	G	G	G		F	G		
P 15 1129 1903	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		F	G		
P 15 1129 1910	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 15 1129 1912	95	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 15 1129 1923	114	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P 15 1129 1934	95	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
P 15 1129 1942	95	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		

	B	C	D	E	F	G	H		J	K	L	M	N	O	P	Q	R	S	T	U	V	W					2
P 15 1129 1969	95	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P 15 1129 1973	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P 15 1129 1989	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P 15 1129 2001	162	STEEL GIRDER	BIG DRY CR	G	G	G	G	G	G	G	G	G	G	G	G		G	G	G	G	G	G	G	P	G		
P 15 1129 2007	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P 15 1129 2025	76	T T TRESTLE	DRAINAGE	F	G	G		G	G		G	E	G		G			G	G	G	G	G		P	G		
P 15 1129 2035	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		F	G		
P 15 1129 2050	57	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		F	G		
P 15 1129 2056	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		P	G		
P 15 1129 2063	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		F	G		
P 15 1129 2078	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 15 1129 2087	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 15 1129 2092	19	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		F	G		
P 15 1129 2105	95	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 15 1129 2112	114	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 15 2121 2123	161	STEEL BEAM	BIG DRY CR	P	G	G	G	G	G	F	G	G	G	G	G		G	G	G	G	G	G	P	P	G		
P 15 2121 2152	63	T T TRESTLE	VALE CR	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 15 2121 2177	63	T T TRESTLE	DRY WASH	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		
P 15 2121 2198	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		F	G		

[illegible]

Unable to inspect

CONTROL BRIDGE NUMBER F A	F A R T NUMBER	CONTROL JUNCTION	BRIDGE MILEPOST	TOTAL LENGTH FEET B	DESCRIPTIVE FEATURES MATERIAL & TYPE MAXIMUM SPAN – Also Structures not carrying road by type of facility Underpass, Tunnel, Ferry C	NAME OF FEATURE CROSSED River, Creek, Canal, Irrigation or Ditch Drainage, Railroad, Highways, Other bridges and Separation, Etc. D	END ... E	... F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILING W	EXP... X	PAINT Y	GENERAL CONDITION Z	NOT INSPECTED Z1	REMARK Z2
P	15	2121	2212	63	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	15	2121	2224	63	T T TRESTLE	DRY WASH	G	G	G		G	G		G	E	G		G			G	G	G	G	G		F	G		
P	15	2121	2235	76	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	15	2121	2265	396	CONT STEEL BEAM	BIG DRY CR	G	G	G	G	G	G	G	G	G	G	G	G		F	G	G	G	G	G	P	F	G		
P	15	2121	2275	125	T T TRESTLE	L-S CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	15	2121	2299	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		F	G		
P	16	1088	1308	38	T T TRESTLE	DRAINAGE	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		X
P	16	1088	1318	57	T T TRESTLE	DRAINAGE	F	G	G		P	G		G		G		G			G	G	G	G	G		G	G		X
P	16	1088	1332	19	T T TRESTLE	DRAINAGE & STK P	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	16	1088	1336	75	T T TRESTLE	RAZOR CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	16	1088	1515	229	CONT STEEL BEAM	MUSSELSHELL R	G		G	G	G	G	G	P	P	P	G			G	G	G	G	G	G	G	G	G		
P	16	1088	1519	168	STEEL TRUSS	CMSTP&P RY	G		G		G	G							G	G	G	G	G	G	G	P	F	G		
P	16	1539	1612	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	F		G	G		
P	16	1539	1621	76	T T TRESTLE	S WILLOW CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P	16	1539	1633	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	16	1539	1642	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P	16	1539	1687	95	T T TRESTLE	WILLOW CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P	16	1539	1729	7	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		

							E	F	G	H		J	K		M	N	O	P	Q	R	S	T		V	W	X		Z	ZZ
P	16	1539	1924	57	T T TRESTLE	ELK CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P	16	1991	1998	92	PRE CONC BEAM	MCDONALD CR	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G	
P	16	1991	2009	82	PRE CONC BEAM	CHIPPEWA CR	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G	
P	16	1991	2047	92	PRE CONC BEAM	FORDS CR	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G	
P	16	1991	2070	82	PRE CONC BEAM	LIT BOX ELDER CR	G		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G	
P	16	1991	2103	92	PRE CONC BEAM	S FK BEAR CR	G		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G	
P	16	1991	2160	82	PRE CONC BEAM	N FK BEAR CR	G		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G	
P	16	2206	2211	75	T T TRESTLE	OF BOX ELDER CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G	
P	16	2206	2405	173	PRE CONC BEAM	ARMELLS CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G	G	G	G	
P	16	2206	2420	69B	STEEL GIRDER	MISSOURI R	P		G	G	G	G	G	F	G	G	G			G	G	G	G	G	G	G	F	G	X
P	18	0000	0779	153	CONCRETE T BEAM	SAND CREEK	G		G	G	G	G	G	G	G	G	G			G	G	G	G	G	G	G	F	G	
P	43	0000	0001	34	CONCRETE SLAB	BIG SPRING CR	G		G		G	G		G		G					G	G	G	G	G		G	G	
P	43	0003	0007	63	CONCRETE T BEAM	BIG SPRING CR	G		P	F	F	F		G	G	F	F				F		F		F			F	X
P	43	0003	0100	38	T T TRESTLE	WARM SPRINGS CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	43	0003	0379	57	T T TRESTLE	BOX ELDER CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G	
P	43	0003	0385	57	T T TRESTLE	BOX ELDER CR	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G	

A	TOTAL LENGTH FEET B	DESCRIPTIVE FEATURES MATERIAL & TYPE MAXIMUM SPAN Also Structures not carrying road by type of facility Underpass Tunnel Ferry C	NAME OF FEATURE CROSSED River, Creek, Canal, Irrigation Ditch, Drainage, Railroad, Highways, Interchanges and Separations, Etc. D	END FLOORS E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILING W	EXPANSION JOINTS X	PAINT Y	GENERAL CONDITION Z	NOT INSPECTED Z1	REMARKS Z2
P 45 0000 0291	113	T T TRESTLE	FISH CR	G	G	G		G	G	G	F	G	G		G			G	G	G	G	G		G	G		
P 45 0000 0316	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 45 0000 0328	29	CONC & ST I BM	S FK AMERICAN FK	G		G		G	G		G	G	P		G			G	G	G	G	G		G	G		
P 45 0000 0330	40	CONCRETE T BEAM	AMERICAN FK	G		G		G	G		G	G	F		G			G	G	G	G	G			G		
P 45 0000 0365	25	T T TRESTLE	DRY WASH	G		G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 45 0000 0370	25	T T TRESTLE	LEBO CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 45 0000 0381	25	T T TRESTLE	SPRING CR	P	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 45 0000 0403	7	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G				G		
P 45 0000 0434	190	CONT ST CANT	MUSSELSHELL R	F		G	G	G	G	G	G	G	G	G			G	G	G	G	G	G	G	F	G		X
P 45 0000 0437	186	ST PONY TRUSS	CMSTP&P RR	F		G		G	G			G				G	G	G	G	G	G	G	F	F	G		
P 45 0453 0460	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0468	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0487	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0492	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0549	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0621	15	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0628	200	CONT ST GIRDER	GN RY	P		G		G	G					G			G	G	G	G	G	G	G	G	G		
P 45 0453 0658	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 45 0453 0662	25	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		

P 45 0453 0668	19	T T TRESTLE	ROSS FK	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 45 0453 0687	19	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 45 0453 0731	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0733	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0754	25	T T TRESTLE	BUFFALO CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 45 0453 0796	57	T T TRESTLE	LITTLE TROUT CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 45 0453 0821	241	CONCT BEAM	CMST P&P RY	F		G		G	G					G			G	G	G	G	G	G			G		
P 45 0453 0825	11	T T TRESTLE	STOCKPASS	G	G	G		G	G						G			G	G	G	G	G		G	G		
P 45 0453 0830	19	T T TRESTLE	OLSON CR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 53 0013 0347	19	T T TRESTLE	STOCKPASS	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 53 0013 0368	57	T T TRESTLE	DRY WASH	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
P 53 0013 0372	25	T T TRESTLE	DRY WASH	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
P 53 0013 0392	76	T T TRESTLE	DRY WASH	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		X
P 53 0013 0398	95	T T TRESTLE	PAINTED ROBE CR	G	G	G		G	G		G	F	G		G			G	G	G	G	G		G	G		
P 53 0013 0448	101	PRE CONC BEAM	BIG COULEE CR	F		G		G	G		G	G	G	G			G	G	G	G		G	G	G	G		
P 53 0013 0454	143	PRE CONC BEAM	MUSSELSHELL R	G		G	F	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G		X
P 53 0013 0463	11	T T TRESTLE	STOCKPASS	F	G	G		G	G						G			G	G	G	G	G		G	G		

DESCRIPTIVE FEATURES

CONDITION RATING

A	FEET B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	ZZ
M230 0000 0611	57	T T TRESTLE	WOLF CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
M244 0000 0024	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	E	G		G			G	G	G	G	G		G	G		
M244 0000 0058	133	T T TRESTLE	FLATWILLOW CR	G	G	G		G	G	G	G	F	G		G			G	G	G	G	G		G	G		X
M244 0000 0121	38	T T TRESTLE	PIKE CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		G	G		
M244 0000 0123	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
M244 0000 0185	76	T T TRESTLE	YELLOW WATER CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
M244 0000 0233	125	T T TRESTLE	MCDONALD CR	G	G	G		G	G	G	F	G	G		G			G	G	G	G	G		G	G		

				E	F	G	H		J	K		M	N	O			R	S	T	U	V	W	X		Z		ZZ
S235 0000 0004	50	CONCRETE SLAB	WARM SPRINGS CR																							R	
S235 0000 0033	38	T T TRESTLE	WARM SPRINGS CR	G	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S235 0000 0085	38	T T TRESTLE	IRRIGATION CANAL	P	F	F		G	G		F		G		G			G		G	G				G		X
S235 0000 0090	95	T T TRESTLE	WARM SPRINGS CR	P	G	G		G	G		F		G		G			G		G	G	F		P	G		
S235 0000 0100	95	T T TRESTLE	WARM SPRINGS CR	P	G	G		G	G		G	G	G		G			G		G	G	F		P	G		
S235 0000 0175	177	STEEL GIRDER	JUDITH R	F		G	G	G	G	G	P		G	G			G	G	G	G	G	G	G	G	G		X
S235 0000 0179	175	T T TRESTLE	SAGE CR	G	G	G		G	G		F	F	G		G			G	G	G	F	G		G	G		
S235 0000 0225	57	T T TRESTLE	DRY WOLF CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S235 0000 0299	76	T T TRESTLE	WOLF CR	F	G	G		G	G		G		G		G			G		G	G	G		G	G		X
S235 0000 0364	38	T T TRESTLE	COFFEE CR	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S236 0000 0042	38	T T TRESTLE	DOG CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
S236 0000 0063	38	T T TRESTLE	LITTLE DOG CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
S236 0000 0095	38	T T TRESTLE	DOG CR	G	G	G		G	G		G		G		G			G	G	G	G	G		P	G		
S236 0000 0101	57	T T TRESTLE	DOG CR	G	G	G		G	G		G	G	G		G			G	G	G	G	G		P	G		
S237 0000 0019	50	HOWE ST TRUSS	BIG SPRING CR	G		P		F	F		G		G			F				F	P	P		G	F		X
S238 0000 0004	49	REINF CONC SLAB	MILL DITCH	G	G	G		G	G		G	G	G					G		G		F		P	G		X

PLANNING SURVEY [illegible] CONDITION REPORT

CONTROL NUMBER A	TOTAL LENGTH FEET B	DESCRIPTIVE FEATURES MATERIAL & TYPE C	NAME D	FND E	PILES F	BENTS G	PIERS H	WINGWALLS I	BACKWALLS J	ICE BREAKERS K	DRIFT L	RIP RAP M	SCOUR N	GIRDERS O	STRINGERS P	TRUSS Q	SHOES R	CURBS S	MARKERS T	DECK U	BRACING V	RAILING W	X	PAINT Y	GENERAL CONDITION Z	NOT INSPECTED Z1	REMARKS Z2
S239 0000 0031	65	PRE CONC BEAM	JUDITH R	G		G		G	G		G		G	G			G	G		G		G		G	G		
S294 0000 0125	50	T T TRESTLE	SAWMILL CR	G	G	G		G	G		G		G		G			G	G	G	F	G		P	G		
S294 0000 0225	75	CONT STEEL GIR	COTTONWOOD CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G		G	G		
S294 0000 0272	31	T T TRESTLE	OF MUSSELSHELL R	G	G	G		G	G						G			G	G	G	G	G		P	G		
S294 0000 0273	100	T T TRESTLE	S FK MUSSELSHELL	G	G	G		G	G	G	P	G	G		G			G	G	G	G	G		P	G		
S296 0000 0003	112	PRE CONC BEAM	MUSSELSHELL R	G		G	G	G	G	G	P	G	G	G			G	G	G	G		G		G	G		
S296 0000 0094	30	UNT T TRESTLE	BIG ELK CR	F	F	F		F	G		G		G		G				F	F	P	P		P	F		
S297 0000 0009	57	T T TRESTLE	DEADMANS BASIN	G	G	G		G	G		G		G		G			G		G	G	G		G	G		
S299 0000 0044	102	PRE CONC BEAM	CARELESS CR	G		G	G	G	G		G	G	G	G				G	G	G	G	G		G	G		
S300 0000 0002	142	PRE CONC BEAMS	MUSSELSHELL R	G		G	G	G	G	G	P	G	G	G			G	G	G	G	G	G		G	G		
S300 0000 0012	63	T T TRESTLE	FISH CR	F	G	G		G	G		P	F	F		G			G	G	G	G	G		G	G		
S300 0000 0081	49	UNT T TRESTLE	BIG COULEE	G	F	F		F	F		G		G		G			F		F	F				F		
S300 0000 0089	40	ST QUEEN TRUSS	BIG COULEE	F	G	F		P	P		G		G			F				F	F	F		P	P	X	

				E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T	U	V	W	X	Y	Z	Z	Zz
S309 0000 0040	38	T T TRESTLE	DRAINAGE	G	G	G		G	G		G	G	G		G			G		G	G	G		P	G		X
S310 0000 0427	193	PRE CONC BEAMS	MUSSELSHELL R	G		G	G	G	G	G	G	G	G	G			G	G	G	G		G	G	G	G		
S360 0000 0004	29	T T TRESTLE	N FK SMITH R	F	G	G		G	G		G		G		G			G	G	G	G	G		G	G		
S360 0000 0163	61	PRATT ST TRUSS	SMITH R	G		P		P	P		G		G		G	P	P	F		G	P	P		P	P		X
S381 0000 0004	150	STEEL GIRDER	MUSSELSHELL R	G		G	G	G	G	G	P	G	G	G			G	G		G	G	G	G	G	G		
S381 0000 0044	38	T T TRESTLE	HARPER COULEE	G	G	G		G	G	G	G		G		G			G		G	G	G		P	G		
S394 0000 0005	130	STEEL GIRDER	MUSSELSHELL R	G		G	G	G	G	G	F	F	G	G			G	G		G	G	G		G	G		
S427 0000 0122	38	T T TRESTLE	OTTER CR	G	G	G		G	G		F		G		G			G	G	G	G	G		G	G		
S466 0000 0002	75	PRE CONC BEAM	E FK SPRING CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G		G	G		
S466 0000 0014	32	UNTR T TRESTLE	SPRING CR	F	F	F		F	F		G		F		G					F	F	F		P	F		X
S500 0000 0123	28	UNT T TRESTLE	DRAINAGE	P	F	F		P	F		G		G		F					P	P				P		X
S500 0000 0300	132	PRE CONC BEAM	FLATWILLOW CR	G		G	G	G	G	G	P	G	G	G			G	G		G		G	G	G	G		

A NUMBER	B FEET	C	D	E END	F PIL	G BENTS	H PIERS	I WINGWALLS	J BACKWALL	K ICE BREAKERS	L DRIFT	M RIP RAP	N SCOUR	O GIRDERS	P STRINGERS	Q TRUSS	R SHOES	S CURBS	T MARKER	U DE	V BRA	W RA	X	Y	Z
S505 0000 0064	163	PRE CONC BEAM	BIG SPRING CR	G		G		G	G		G	G	G	G			G	G	G	G	G	G		G	G
S505 0000 0123	75	ST PONY TRUSS	JUDITH R	G		F		F	F		G		G			F	P			F	F	F		G	F
S543 0000 0027	48	UNTR TIMBER	VAIL CR	G	P	P		P	P		G		G		P					F	P				P

LEWISTOWN DIVISION

P-14-0000-0117 19' Untreated Timber Trestle Drainage
Structure not inspected during 1968. Bridge condition rating taken from 1966 inspection report.

P-14-0000-0119 38' Treated Timber Trestle Deep Creek
Structure not inspected during 1968. Bridge condition rating taken from 1966 inspection report.

P-14-0000-0148 19' Treated Timber Trestle Deep Creek
Structure not inspected during 1968. Bridge condition rating taken from 1966 inspection report.

P-14-0000-0151 39' Treated Timber Trestle Deep Creek
Structure not inspected during 1968. Bridge condition rating taken from 1966 inspection report.

P-14-0000-0173 39' Treated Timber Trestle Deep Creek
Structure not inspected during 1968. Bridge condition rating taken from 1966 inspection report.

P-14-0000-0196 19' Treated Timber Trestle Deep Creek
Structure not inspected during 1968. Bridge condition rating taken from 1966 inspection report.

P-14-0000-0198 19' Treated Timber Trestle Deep Creek
Structure not inspected during 1968. Bridge condition rating taken from 1966 inspection report.

P-14-0000-0246 7' Treated Timber Trestle Stockpass
One stringer cracked from cap notch back.

P-14-0449-0661 76' Treated Timber Trestle Flagstaff Creek
Fill is pushing end bent and starting to roll cap over.

P-14-0449-0764 19' Treated Timber Trestle Stockpass
One badly cracked stringer.

LEWISTOWN DIVISION

P-14-1008-1336 114' Treated Timber Trestle Careless Creek
Vertical bank under backwalls. Drift collected at piers.

P-14-1460-1658 75' Treated Timber Trestle Pole Creek
Columns are being eaten off by alkalie at low water line. Re-bar is exposed and rusting. See photo.

P-14-1694-1945 95' Treated Timber Trestle Drainage
One cracked stringer, span 4.

P-14-1694-1964 57' Treated Timber Trestle Drainage
Vertical dirt bank under end backing plank.

P-14-1694-1966 11' Treated Timber Trestle Stockpass
Crack in cap.

P-14-1694-2039 76' Treated Timber Trestle Drainage
One stringer has a bad crack.

P-15-0000-0442 38' Treated Timber Trestle Drainage
A cavity has developed under the roadway surface on the west bridge approach fill.

P-15-0000-0582 159' Concrete T. Beam Judith River
The concrete has spalled to the point where the reinforcing steel is exposed on the down stream end of pier # 5. Some bearing haunches are cracked on the girders. Places along the deck and curb edges have deteriorated to the point where the reinforcing steel is exposed. See photo.

P-15-0000-0625 120' Concrete T Beam Ross Fork Creek
A cavity has developed behind the backwall and under the roadway surface on both ends of the bridge.

P-15-0793-0796 165' Concrete T. Beam C.M. ST. P. P. Ry
Stirrups are exposed on bottom of haunches of intermediate bents. Some girder haunches cracked.

LEWISTOWN DIVISION

P-15-0793-0822 30' Steel & Concrete Big Spring Creek
Structure not inspected.

P-15-0823-0824 25' Concrete T Beam Mill Ditch
One girder spalled at haunch. Curbs badly spalled. General spalling at water line on backwall. See photos.

P-15-1129-1584 436' Steel Truss Musselshell River
Three nuts on shoe bearing pins drifting off. Spalling concrete on caping of piers and curbs.

P-16-1088-1308 38' Treated Timber Trestle Drainage
About 2½ ft vertical fill under backwall at both end bents.

P-16-1088-1318 57' Treated Timber Trestle Drainage
One cracked stringer, two wingwalls broken.

P-16-2206-2420 698' Steel Girder Missouri River
One nut on rocker on span 2 at bent 2 has turned off a couple turns.

P-43-0003-0007 63' Concrete T. Beam Big Spring Creek
General spalling on edges and at water line on backwall. Water is all routed through one span. Honeycomb in bottom of girders showing reinforcing bar. See photo.

P-45-0000-0434 190' Cont. St. Cant. Musselshell River
North end bent has no berm. See photo.

P-53-0013-0392 76' T. T. Trestle Dry Wash
One stringer cracked.

P-53-0013-0454 143' Pre. Conc. Beam Musselshell River
Anchor bolt has cracked concrete away from one pier.

M-244-0000-0058 133' Treated Timber Trestle Flatwillow Creek
One broken stringer, span 3.

LEWISTOWN DIVISION

S-235-0000-0085 38' Treated Timber Trestle Irrigation Canal
This structure is in the process of being rebuilt.

S-235-0000-0175 177' Steel Girder Judith River
Deck has one spalled spot in span 1.

S-235-0000-0299 76' Treated Timber Trestle Wolf Creek
Structure has one cracked stringer in span 4.

S-237-0000-0019 50' St. Howe Truss Big Spring Creek
One nut gone from a vertical member at top chord connection.

S-238-0000-0004 49' Concrete Slab Mill Ditch
One end post has been hit and damaged. Rail is bent.

S-300-0000-0089 40' Steel Truss Big Coulee
Backwall planks badly rotted. No paint left on steel. See photo.

S-309-0000-0040 38' Treated Timber Trestle Drainage
One stringer cracked.

S-306-0000-0163 61' Steel Truss Smith River
Rail bent, backwall and wings crumbling. Truss has been hit. Members are bent and patched. Nuts on pins are loose. Posted 20 ton limit. See photo.

S-466-0000-0014 32' Untreated Timber Trestle Spring Creek
Creek has undercut the end fill on south end behind backing planks.

S-500-0000-0123 28' Untreated Timber Drainage
Deck planks in bad shape.

S-505-0000-0123 75' Steel Pony Truss Judith River
No paint left on steel.

S-543-0000-0027 48' Untreated Timber Vail Creek
One broken stringer, no rail, no markers, cobbled up construction. See photos.

P-14-1460-1658

P-15-0000-0582

P-15-0823-0824

P-15-0823-0824

P-43-0003-0007

P-45-0000-0434

S-300-0000-0089

S-543-0000-0027

S-543-0000-0027
